

Request For Information

Submitted By: Aaron Chamberlain

Title: CSII

Region: III

Institution: CIM

Project Name: Replace Roofs (Program Phase 1 - 4)

Title: Roof Replacement - Phase 1 Facility B

RFI#: 009

Date: 9/10/2025

Needed By: 10/1/2025

CCM Proj. # I-001123

A/E Proj. # 22-090



RFI Description – Correctional Construction Mentorship Program (CCM)

CCM request to verify attached Pg.A2.5 Keynote 13 highlighted and circled slopes are correct for Tapered Insulation Cricket. Multiple slopes on new work show sloping into Mechanical Rooms and away from drains. Please Advise. Field Staff Verified existing slopes to roof drains and flat area around Mechanical Room using a laser level. See Attached Drawings. Please verify slopes directions.

Location: Plan Set 22-090, FAC B UNIT 2

Attachments

Plan(s) Sht/Detail: 22-090 Pg.A2.5, Keynote 13

Specification: N/A

Submittals: N/A

Shop Drawings: Field provided slopes of existing condition to roof

Product Data: N/A

Memo / Letter: N/A

Images: N/A

Other: N/A

drains

Response To RFI – Architecture and Engineering Section

The slopes shown on the drawings need correction and are being corrected by the consultant. The new slopes will need to drain to the existing roof drains and the consultant will refine the drawings to indicate this. A CB with the corrected slopes/slope directions will be issued once this information is completed.

Attachments

Plan(s) Sht/Detail: N/A

Specification: N/A

Submittals: N/A

Shop Drawings: N/A

Product Data: N/A

Memo / Letter: N/A

Images: N/A

Other: N/A


Response By: Eileen Tumlin, Senior Architect

Date: 9/15/2025

Access Compliance Review for Attachment: Not Required

SFM Approval for Attachment: Required

Timestamp of Response: [Final A/E

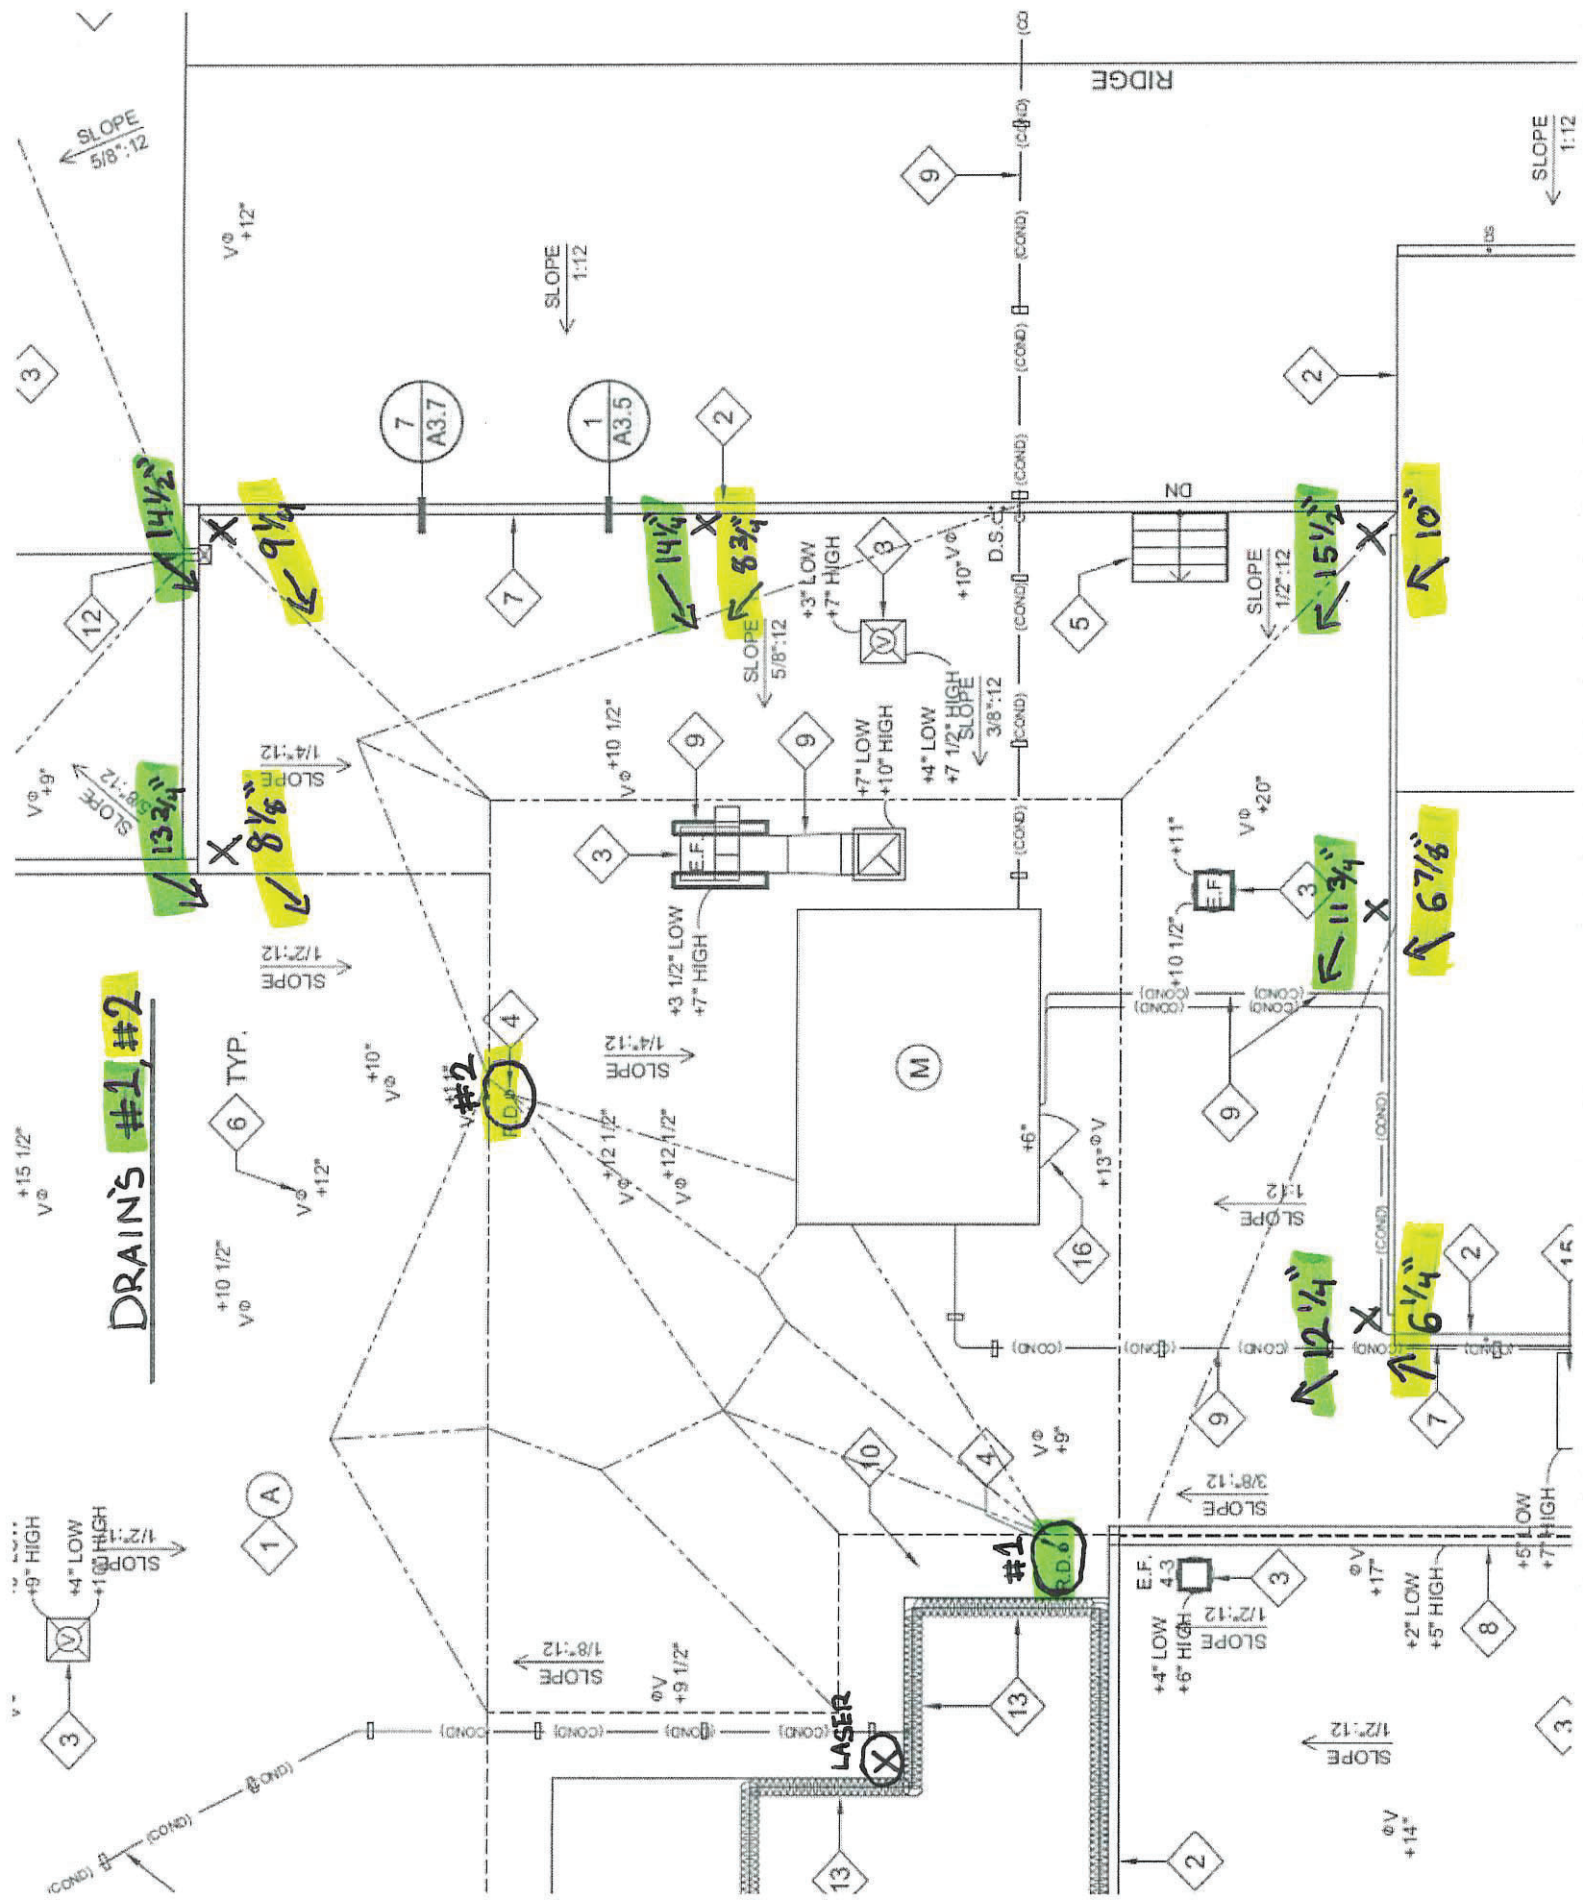

FLAT SECTION

