ID	Task Name	Duration	Start	Finish	Predecessors
1	**Togus EHRM Construction - NTP 2/3/2026 (523 Working Days, 730 Calendar Days)**	**523 days**	**Mon 2/2/26**	**Wed 2/2/28**	
2	**Submittals for Materials & Equipment**	**60 days**	**Mon 2/2/26**	**Fri 4/24/26**	
3	Submittal Process	60 days	Mon 2/2/26	Fri 4/24/26	
4	**Lead-Time Long-Lead Materials & Equipment**	**120 days**	**Mon 4/27/26**	**Fri 10/9/26**	**3**
5	Lead Time - Light Gauge Steel	30 days	Mon 4/27/26	Fri 6/5/26	3
6	Lead Time - MCR Flooring	60 days	Mon 4/27/26	Fri 7/17/26	3
7	Lead Time - UPS	120 days	Mon 4/27/26	Fri 10/9/26	3
8	Lead Time - Fire Protection Equipment	60 days	Mon 4/27/26	Fri 7/17/26	3
9	Lead Time - Data Cable & Fiber	60 days	Mon 4/27/26	Fri 7/17/26	3
10	Lead Time - Electrical Panels, Electrical Wire and Cabling	60 days	Mon 4/27/26	Fri 7/17/26	3
11	Lead Time - CRAC and compressors	120 days	Mon 4/27/26	Fri 10/9/26	3
12	Lead Time - Architectural - Doors & Hardware	60 days	Mon 4/27/26	Fri 7/17/26	3
13	**Site and Utility Work**	**80 days**	**Mon 7/20/26**	**Fri 11/6/26**	
14	Trenching for New Exterior Fiber Runs	10 days	Mon 7/20/26	Fri 7/31/26	9
15	Install New Ductbanks	15 days	Mon 8/3/26	Fri 8/21/26	14
16	Install New Exterior Fiber Loops	10 days	Mon 8/24/26	Fri 9/4/26	15
17	Install Exterior Electrical	30 days	Mon 7/20/26	Fri 8/28/26	10
18	Patch Asphalt	5 days	Mon 8/24/26	Fri 8/28/26	16SS
19	Patch Concrete	5 days	Mon 8/24/26	Fri 8/28/26	16SS
20	Restore Landscaping	10 days	Mon 9/7/26	Fri 9/18/26	16
21	Housekeeping pads	5 days	Mon 7/20/26	Fri 7/24/26	17SS
22	Install Condensing Units	5 days	Mon 10/12/26	Fri 10/16/26	11,21
23	Install CRAC piping to TRs	20 days	Mon 10/12/26	Fri 11/6/26	22SS
24	**New Main Computer Room (MCR)**	**395 days**	**Mon 4/27/26**	**Fri 10/29/27**	
25	Survey and Layout	5 days	Mon 4/27/26	Fri 5/1/26	3
26	Erosion Control	4 days	Mon 5/4/26	Thu 5/7/26	25
27	Clear and Grub	5 days	Fri 5/8/26	Thu 5/14/26	26
28	Excavation, Rock Removal	30 days	Fri 5/15/26	Thu 6/25/26	27
29	Retaining Wall Earthwork	7 days	Fri 6/26/26	Mon 7/6/26	28
30	Retaining Wall Formwork	5 days	Tue 7/7/26	Mon 7/13/26	29
31	Pour Retaining Wall	5 days	Tue 7/14/26	Mon 7/20/26	30
32	Underground Utilities, Stub Out	20 days	Tue 7/21/26	Mon 8/17/26	31
33	Subgrade Preparation	8 days	Tue 8/18/26	Thu 8/27/26	32
34	Foundation Formwork	14 days	Fri 8/28/26	Wed 9/16/26	33
35	Pour Foundation	7 days	Thu 9/17/26	Fri 9/25/26	34
36	Slab On Grade Preparation	11 days	Mon 9/28/26	Mon 10/12/26	35
37	Pour Slab on Grade	3 days	Tue 10/13/26	Thu 10/15/26	36
38	Structural Steel	40 days	Fri 10/16/26	Thu 12/10/26	37
39	New Exterior Walls	40 days	Fri 12/11/26	Thu 2/4/27	38
40	Roof	15 days	Fri 2/5/27	Thu 2/25/27	38,39
41	New interior walls, floors, doors	40 days	Fri 2/26/27	Thu 4/22/27	40
42	Install Electrical Panels	20 days	Fri 4/23/27	Thu 5/20/27	41
43	Install Power Distribution	10 days	Fri 5/21/27	Thu 6/3/27	10,42
44	Install UPS Units	10 days	Fri 6/4/27	Thu 6/17/27	7,43
45	Test UPS Units	5 days	Fri 6/18/27	Thu 6/24/27	44
46	Install Lighting	5 days	Fri 6/4/27	Thu 6/10/27	10,43
47	Install CRAC Units	14 days	Fri 5/21/27	Wed 6/9/27	41,42,11
48	Security	5 days	Fri 5/21/27	Thu 5/27/27	41,42
49	Fire suppression, FEC	21 days	Fri 4/23/27	Fri 5/21/27	41
50	Telecom racks and switches	40 days	Fri 5/21/27	Thu 7/15/27	41,42
51	Cable Tray and raceways	16 days	Fri 7/16/27	Fri 8/6/27	50,9
52	New Data Drops	5 days	Mon 8/9/27	Fri 8/13/27	51
53	Land Data Cabling On Switches	7 days	Mon 8/16/27	Tue 8/24/27	52
54	Test New Data Cabling and Outlets	3 days	Wed 8/25/27	Fri 8/27/27	53
55	DDC	1 day	Mon 8/30/27	Mon 8/30/27	47,48,49,53,54
56	Migrate MCR	30 days	Tue 8/31/27	Mon 10/11/27	55
57	Clean and punch	14 days	Tue 10/12/27	Fri 10/29/27	56
58	**Building 200/200E - TR#7A**	**65 days**	**Mon 7/20/26**	**Fri 10/16/26**	
59	ICRA	2 days	Mon 7/20/26	Tue 7/21/26	12,5
60	Abatement	3 days	Wed 7/22/26	Fri 7/24/26	59
61	Demolition	3 days	Mon 7/27/26	Wed 7/29/26	60
62	New walls, floors, doors	5 days	Thu 7/30/26	Wed 8/5/26	12,61,5
63	Install CRAC	5 days	Mon 10/12/26	Fri 10/16/26	62,11
64	Electrical and Lighting	5 days	Thu 8/6/26	Wed 8/12/26	62,10
65	Security	5 days	Thu 8/6/26	Wed 8/12/26	62,10
66	Fire suppression, FEC	3 days	Thu 8/6/26	Mon 8/10/26	62,8
67	Telecom racks and switches	3 days	Thu 8/6/26	Mon 8/10/26	62,9
68	Cable Tray and raceways	3 days	Tue 8/11/26	Thu 8/13/26	67
69	New cable from outlets to TRs	5 days	Fri 8/14/26	Thu 8/20/26	68
70	New outlet connections	3 days	Fri 8/21/26	Tue 8/25/26	69
71	Land cable on switches	2 days	Wed 8/26/26	Thu 8/27/26	70
72	Test new telecom outlets / system	2 days	Fri 8/28/26	Mon 8/31/26	71
73	DDC	1 day	Tue 9/1/26	Tue 9/1/26	72
74	Demo old cable	3 days	Tue 9/1/26	Thu 9/3/26	72
75	Clean and punch	3 days	Fri 9/4/26	Tue 9/8/26	74
76	**Building 200/200E - TR#7B**	**37 days**	**Wed 9/9/26**	**Thu 10/29/26**	
77	ICRA	2 days	Wed 9/9/26	Thu 9/10/26	75
78	Abatement	3 days	Fri 9/11/26	Tue 9/15/26	77
79	Demolition	3 days	Wed 9/16/26	Fri 9/18/26	78
80	New walls, floors, doors	5 days	Mon 9/21/26	Fri 9/25/26	12,5,79
81	Install CRAC	5 days	Mon 10/12/26	Fri 10/16/26	80,11
82	Electrical and Lighting	5 days	Mon 9/28/26	Fri 10/2/26	80,10
83	Security	5 days	Mon 9/28/26	Fri 10/2/26	80,10
84	Fire suppression, FEC	3 days	Mon 9/28/26	Wed 9/30/26	80,8
85	Telecom racks and switches	3 days	Mon 9/28/26	Wed 9/30/26	80,9
86	Cable Tray and raceways	3 days	Thu 10/1/26	Mon 10/5/26	85
87	New cable from outlets to TRs	5 days	Tue 10/6/26	Mon 10/12/26	86
88	New outlet connections	3 days	Tue 10/13/26	Thu 10/15/26	87
89	Land cable on switches	2 days	Fri 10/16/26	Mon 10/19/26	88
90	Test new telecom outlets / system	2 days	Tue 10/20/26	Wed 10/21/26	89
91	DDC	1 day	Thu 10/22/26	Thu 10/22/26	90
92	Demo old cable	3 days	Thu 10/22/26	Mon 10/26/26	90
93	Clean and punch	3 days	Tue 10/27/26	Thu 10/29/26	92
94	**Building 200/200E - TR#8A**	**37 days**	**Fri 10/30/26**	**Mon 12/21/26**	
95	ICRA	2 days	Fri 10/30/26	Mon 11/2/26	93
96	Abatement	3 days	Tue 11/3/26	Thu 11/5/26	95
97	Demolition	3 days	Fri 11/6/26	Tue 11/10/26	96
98	New walls, floors, doors	5 days	Wed 11/11/26	Tue 11/17/26	12,97,5
99	Install CRAC	5 days	Wed 11/18/26	Tue 11/24/26	98,11
100	Electrical and Lighting	5 days	Wed 11/18/26	Tue 11/24/26	98,10
101	Security	5 days	Wed 11/18/26	Tue 11/24/26	98,10
102	Fire suppression, FEC	3 days	Wed 11/18/26	Fri 11/20/26	98,8
103	Telecom racks and switches	3 days	Wed 11/18/26	Fri 11/20/26	98,9
104	Cable Tray and raceways	3 days	Mon 11/23/26	Wed 11/25/26	103
105	New cable from outlets to TRs	5 days	Thu 11/26/26	Wed 12/2/26	104
106	New outlet connections	3 days	Thu 12/3/26	Mon 12/7/26	105
107	Land cable on switches	2 days	Tue 12/8/26	Wed 12/9/26	106
108	Test new telecom outlets / system	2 days	Thu 12/10/26	Fri 12/11/26	107
109	DDC	1 day	Mon 12/14/26	Mon 12/14/26	108
110	Demo old cable	3 days	Mon 12/14/26	Wed 12/16/26	108
111	Clean and punch	3 days	Thu 12/17/26	Mon 12/21/26	110
112	**Building 200/200E - TR#9A**	**37 days**	**Tue 12/22/26**	**Wed 2/10/27**	
113	ICRA	2 days	Tue 12/22/26	Wed 12/23/26	111
114	Abatement	3 days	Thu 12/24/26	Mon 12/28/26	113
115	Demolition	3 days	Tue 12/29/26	Thu 12/31/26	114
116	New walls, floors, doors	5 days	Fri 1/1/27	Thu 1/7/27	12,115,5
117	Install CRAC	5 days	Fri 1/8/27	Thu 1/14/27	116,11
118	Electrical and Lighting	5 days	Fri 1/8/27	Thu 1/14/27	116,10
119	Security	5 days	Fri 1/8/27	Thu 1/14/27	116,10
120	Fire suppression, FEC	3 days	Fri 1/8/27	Tue 1/12/27	116,8
121	Telecom racks and switches	3 days	Fri 1/8/27	Tue 1/12/27	116,9
122	Cable Tray and raceways	3 days	Wed 1/13/27	Fri 1/15/27	121
123	New cable from outlets to TRs	5 days	Mon 1/18/27	Fri 1/22/27	122
124	New outlet connections	3 days	Mon 1/25/27	Wed 1/27/27	123
125	Land cable on switches	2 days	Thu 1/28/27	Fri 1/29/27	124
126	Test new telecom outlets / system	2 days	Mon 2/1/27	Tue 2/2/27	125
127	DDC	1 day	Wed 2/3/27	Wed 2/3/27	126
128	Demo old cable	3 days	Wed 2/3/27	Fri 2/5/27	126
129	Clean and punch	3 days	Mon 2/8/27	Wed 2/10/27	128
130	**Building 200/200E - TR#9B**	**37 days**	**Thu 2/11/27**	**Fri 4/2/27**	
131	ICRA	2 days	Thu 2/11/27	Fri 2/12/27	129
132	Abatement	3 days	Mon 2/15/27	Wed 2/17/27	131
133	Demolition	3 days	Thu 2/18/27	Mon 2/22/27	132
134	New walls, floors, doors	5 days	Tue 2/23/27	Mon 3/1/27	12,133,5
135	Install CRAC	5 days	Tue 3/2/27	Mon 3/8/27	134,11
136	Electrical and Lighting	5 days	Tue 3/2/27	Mon 3/8/27	134,10
137	Security	5 days	Tue 3/2/27	Mon 3/8/27	134,10
138	Fire suppression, FEC	3 days	Tue 3/2/27	Thu 3/4/27	134,8
139	Telecom racks and switches	3 days	Tue 3/2/27	Thu 3/4/27	134,9
140	Cable Tray and raceways	3 days	Fri 3/5/27	Tue 3/9/27	139
141	New cable from outlets to TRs	5 days	Wed 3/10/27	Tue 3/16/27	140
142	New outlet connections	3 days	Wed 3/17/27	Fri 3/19/27	141
143	Land cable on switches	2 days	Mon 3/22/27	Tue 3/23/27	142
144	Test new telecom outlets / system	2 days	Wed 3/24/27	Thu 3/25/27	143

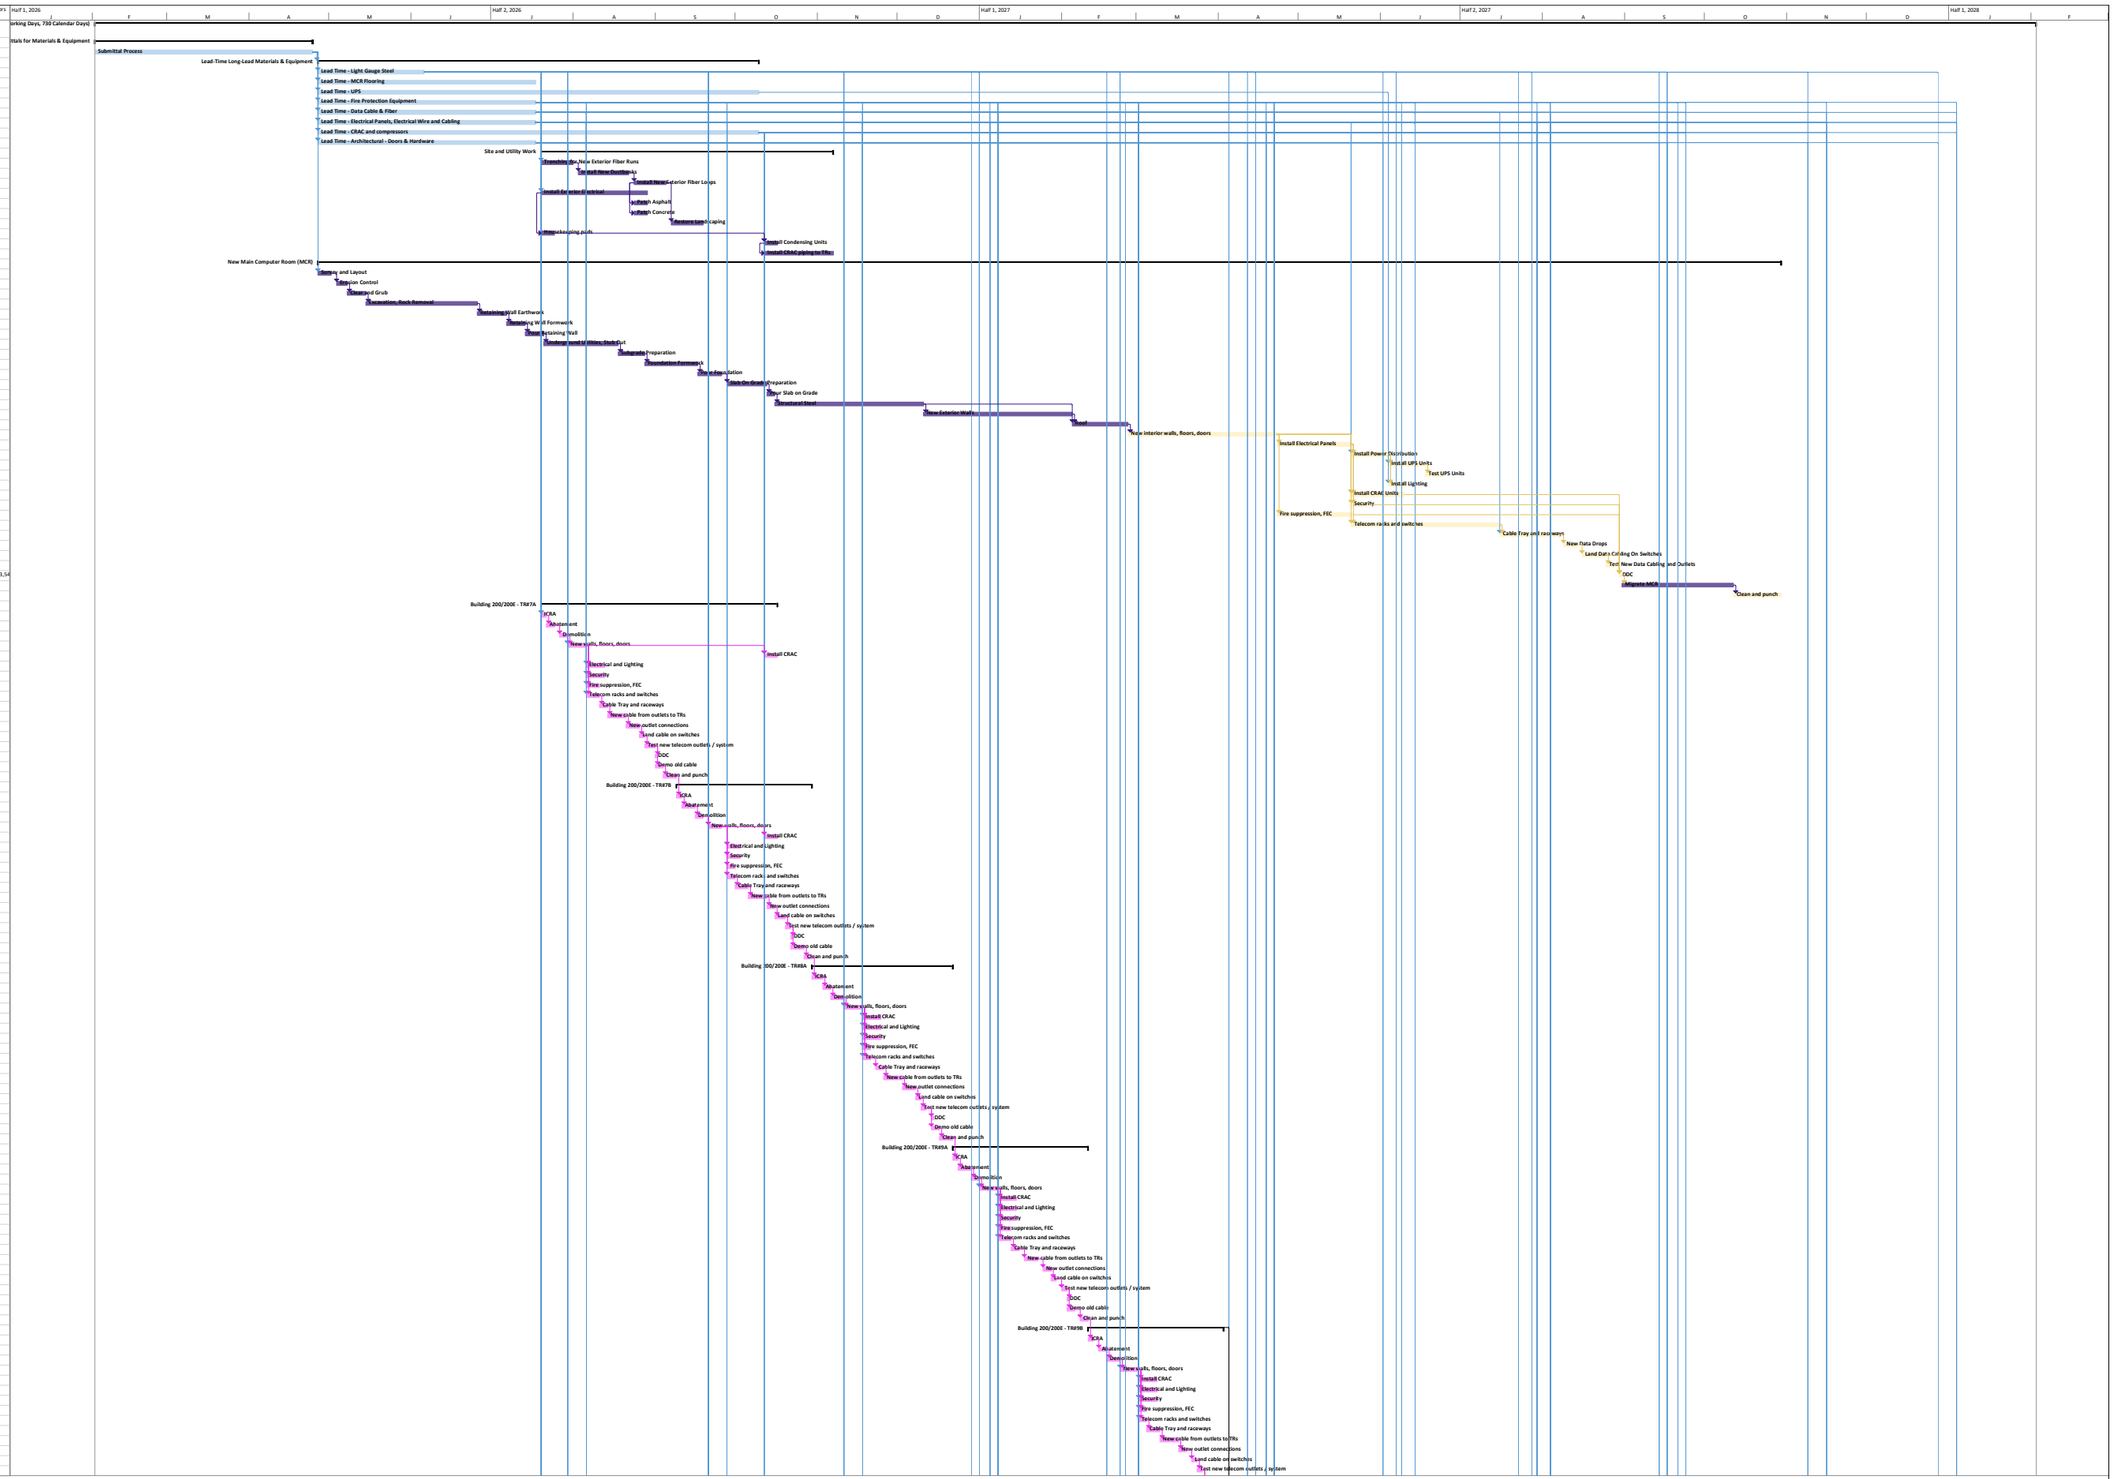

Togus EHRM
Reissued 12-22-2025

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress

ID	Task Name	Duration	Start	Finish	Predecessors
145	DDC	1 day	Fri 3/26/27	Fri 3/26/27	144
146	Demo old cable	3 days	Fri 3/26/27	Tue 3/30/27	144
147	Clean and punch	3 days	Wed 3/31/27	Fri 4/2/27	146
148	**Building 200/200E - TRR10A**	**37 days**	**Mon 4/5/27**	**Tue 5/25/27**	
149	ICRA	2 days	Mon 4/5/27	Tue 4/6/27	12,130,5
150	Abatement	3 days	Wed 4/7/27	Fri 4/9/27	149
151	Demolition	3 days	Mon 4/12/27	Wed 4/14/27	150
152	New walls, floors, doors	5 days	Thu 4/15/27	Wed 4/21/27	12,151,5
153	Install CRAC	5 days	Thu 4/22/27	Wed 4/28/27	152,11
154	Electrical and Lighting	5 days	Thu 4/22/27	Wed 4/28/27	152,10
155	Security	5 days	Thu 4/22/27	Wed 4/28/27	152,10
156	Fire suppression, FEC	3 days	Thu 4/22/27	Mon 4/26/27	152,8
157	Telecom racks and switches	3 days	Thu 4/22/27	Mon 4/26/27	152,9
158	Cable Tray and raceways	3 days	Tue 4/27/27	Thu 4/29/27	157
159	New cable from outlets to TRs	5 days	Fri 4/30/27	Thu 5/6/27	158
160	New outlet connections	3 days	Fri 5/7/27	Tue 5/11/27	159
161	Land cable on switches	2 days	Wed 5/12/27	Thu 5/13/27	160
162	Test new telecom outlets / system	2 days	Fri 5/14/27	Mon 5/17/27	161
163	DDC	1 day	Tue 5/18/27	Tue 5/18/27	162
164	Demo old cable	3 days	Tue 5/18/27	Thu 5/20/27	162
165	Clean and punch	3 days	Fri 5/21/27	Tue 5/25/27	164
166	**Building 200/200E - TRR10B**	**37 days**	**Wed 5/26/27**	**Thu 7/15/27**	
167	ICRA	2 days	Wed 5/26/27	Thu 5/27/27	165
168	Abatement	3 days	Fri 5/28/27	Tue 6/1/27	167
169	Demolition	3 days	Wed 6/2/27	Fri 6/4/27	168
170	New walls, floors, doors	5 days	Mon 6/7/27	Fri 6/11/27	12,169,5
171	Install CRAC	5 days	Mon 6/14/27	Fri 6/18/27	170,11
172	Electrical and Lighting	5 days	Mon 6/14/27	Fri 6/18/27	170,10
173	Security	5 days	Mon 6/14/27	Fri 6/18/27	170,10
174	Fire suppression, FEC	3 days	Mon 6/14/27	Wed 6/16/27	170,8
175	Telecom racks and switches	3 days	Mon 6/14/27	Wed 6/16/27	170,9
176	Cable Tray and raceways	3 days	Thu 6/17/27	Mon 6/21/27	175
177	New cable from outlets to TRs	5 days	Tue 6/22/27	Mon 6/28/27	176
178	New outlet connections	3 days	Tue 6/29/27	Thu 7/1/27	177
179	Land cable on switches	2 days	Fri 7/2/27	Mon 7/5/27	178
180	Test new telecom outlets / system	2 days	Tue 7/6/27	Wed 7/7/27	179
181	DDC	1 day	Thu 7/8/27	Thu 7/8/27	180
182	Demo old cable	3 days	Thu 7/8/27	Mon 7/12/27	180
183	Clean and punch	3 days	Tue 7/13/27	Thu 7/15/27	182
184	**Building 200/200E - TRR11**	**37 days**	**Fri 7/16/27**	**Mon 9/6/27**	
185	ICRA	2 days	Fri 7/16/27	Mon 7/19/27	183
186	Abatement	3 days	Tue 7/20/27	Thu 7/22/27	185
187	Demolition	3 days	Fri 7/23/27	Tue 7/27/27	186
188	New walls, floors, doors	5 days	Wed 7/28/27	Tue 8/3/27	12,187,5
189	Install CRAC	5 days	Wed 8/4/27	Tue 8/10/27	188,11
190	Electrical and Lighting	5 days	Wed 8/4/27	Tue 8/10/27	188,10
191	Security	5 days	Wed 8/4/27	Tue 8/10/27	188,10
192	Fire suppression, FEC	3 days	Wed 8/4/27	Fri 8/6/27	188,8
193	Telecom racks and switches	3 days	Wed 8/4/27	Fri 8/6/27	188,9
194	Cable Tray and raceways	3 days	Mon 8/9/27	Wed 8/11/27	193
195	New cable from outlets to TRs	5 days	Thu 8/12/27	Wed 8/18/27	194
196	New outlet connections	3 days	Thu 8/19/27	Mon 8/23/27	195
197	Land cable on switches	2 days	Tue 8/24/27	Wed 8/25/27	196
198	Test new telecom outlets / system	2 days	Thu 8/26/27	Fri 8/27/27	197
199	DDC	1 day	Mon 8/30/27	Mon 8/30/27	198
200	Demo old cable	3 days	Mon 8/30/27	Wed 9/1/27	198
201	Clean and punch	3 days	Thu 9/2/27	Mon 9/6/27	200
202	**Building 200/200E - TRR12**	**37 days**	**Tue 9/7/27**	**Wed 10/27/27**	
203	ICRA	2 days	Tue 9/7/27	Wed 9/8/27	201
204	Abatement	3 days	Thu 9/9/27	Mon 9/13/27	203
205	Demolition	3 days	Tue 9/14/27	Thu 9/16/27	204
206	New walls, floors, doors	5 days	Fri 9/17/27	Thu 9/23/27	12,205,5
207	Install CRAC	5 days	Fri 9/24/27	Thu 9/30/27	206,11
208	Electrical and Lighting	5 days	Fri 9/24/27	Thu 9/30/27	206,10
209	Security	5 days	Fri 9/24/27	Thu 9/30/27	206,10
210	Fire suppression, FEC	3 days	Fri 9/24/27	Tue 9/28/27	206,8
211	Telecom racks and switches	3 days	Fri 9/24/27	Tue 9/28/27	206,9
212	Cable Tray and raceways	3 days	Wed 9/29/27	Fri 10/1/27	211
213	New cable from outlets to TRs	5 days	Mon 10/4/27	Fri 10/8/27	212
214	New outlet connections	3 days	Mon 10/11/27	Wed 10/13/27	213
215	Land cable on switches	2 days	Thu 10/14/27	Fri 10/15/27	214
216	Test new telecom outlets / system	2 days	Mon 10/18/27	Tue 10/19/27	215
217	DDC	1 day	Wed 10/20/27	Wed 10/20/27	216
218	Demo old cable	3 days	Wed 10/20/27	Fri 10/22/27	216
219	Clean and punch	3 days	Mon 10/25/27	Wed 10/27/27	218
220	**Building 200/200E - TRR13**	**65 days**	**Mon 7/20/26**	**Fri 10/16/26**	
221	ICRA	2 days	Mon 7/20/26	Tue 7/21/26	12,5
222	Abatement	3 days	Wed 7/22/26	Fri 7/24/26	221
223	Demolition	3 days	Mon 7/27/26	Wed 7/29/26	222
224	New walls, floors, doors	5 days	Thu 7/30/26	Wed 8/5/26	12,223,5
225	Install CRAC	5 days	Mon 10/12/26	Fri 10/16/26	224,11
226	Electrical and Lighting	5 days	Thu 8/6/26	Wed 8/12/26	224,10
227	Security	5 days	Thu 8/6/26	Wed 8/12/26	224,10
228	Fire suppression, FEC	3 days	Thu 8/6/26	Mon 8/10/26	224,8
229	Telecom racks and switches	3 days	Thu 8/6/26	Mon 8/10/26	224,9
230	Cable Tray and raceways	3 days	Tue 8/11/26	Thu 8/13/26	229
231	New cable from outlets to TRs	5 days	Fri 8/14/26	Thu 8/20/26	230
232	New outlet connections	3 days	Fri 8/21/26	Tue 8/25/26	231
233	Land cable on switches	2 days	Wed 8/26/26	Thu 8/27/26	232
234	Test new telecom outlets / system	2 days	Fri 8/28/26	Mon 8/31/26	233
235	DDC	1 day	Tue 9/1/26	Tue 9/1/26	234
236	Demo old cable	3 days	Tue 9/1/26	Thu 9/3/26	234
237	Clean and punch	3 days	Fri 9/4/26	Tue 9/8/26	236
238	**Building 202 - TRR207E**	**37 days**	**Wed 9/9/26**	**Thu 10/29/26**	
239	ICRA	2 days	Wed 9/9/26	Thu 9/10/26	237
240	Abatement	3 days	Fri 9/11/26	Tue 9/15/26	239
241	Demolition	3 days	Wed 9/16/26	Fri 9/18/26	240
242	New walls, floors, doors	5 days	Mon 9/21/26	Fri 9/25/26	12,241,5
243	Install CRAC	5 days	Mon 10/12/26	Fri 10/16/26	242,11
244	Electrical and Lighting	5 days	Mon 9/28/26	Fri 10/2/26	242,10
245	Security	5 days	Mon 9/28/26	Fri 10/2/26	242,10
246	Fire suppression, FEC	3 days	Mon 9/28/26	Wed 9/30/26	242,8
247	Telecom racks and switches	3 days	Mon 9/28/26	Wed 9/30/26	242,9
248	Cable Tray and raceways	3 days	Thu 10/1/26	Mon 10/5/26	247
249	New cable from outlets to TRs	5 days	Tue 10/6/26	Mon 10/12/26	248
250	New outlet connections	3 days	Tue 10/13/26	Thu 10/15/26	249
251	Land cable on switches	2 days	Fri 10/16/26	Mon 10/19/26	250
252	Test new telecom outlets / system	2 days	Tue 10/20/26	Wed 10/21/26	251
253	DDC	1 day	Thu 10/22/26	Thu 10/22/26	252
254	Demo old cable	3 days	Thu 10/22/26	Mon 10/26/26	252
255	Clean and punch	3 days	Tue 10/27/26	Thu 10/29/26	254
256	**Building 204 - TRR19**	**37 days**	**Fri 10/30/26**	**Mon 12/21/26**	
257	ICRA	2 days	Fri 10/30/26	Mon 11/2/26	255
258	Abatement	3 days	Tue 11/3/26	Thu 11/5/26	257
259	Demolition	3 days	Fri 11/6/26	Tue 11/10/26	258
260	New walls, floors, doors	5 days	Wed 11/11/26	Tue 11/17/26	12,259,5
261	Install CRAC	5 days	Wed 11/18/26	Tue 11/24/26	260,11
262	Electrical and Lighting	5 days	Wed 11/18/26	Tue 11/24/26	260,10
263	Security	5 days	Wed 11/18/26	Tue 11/24/26	260,10
264	Fire suppression, FEC	3 days	Wed 11/18/26	Fri 11/20/26	260,8
265	Telecom racks and switches	3 days	Wed 11/18/26	Fri 11/20/26	260,9
266	Cable Tray and raceways	3 days	Mon 11/23/26	Wed 11/25/26	265
267	New cable from outlets to TRs	5 days	Thu 11/26/26	Wed 12/2/26	266
268	New outlet connections	3 days	Thu 12/3/26	Mon 12/7/26	267
269	Land cable on switches	2 days	Tue 12/8/26	Wed 12/9/26	268
270	Test new telecom outlets / system	2 days	Thu 12/10/26	Fri 12/11/26	269
271	DDC	1 day	Mon 12/14/26	Mon 12/14/26	270
272	Demo old cable	3 days	Mon 12/14/26	Wed 12/16/26	270
273	Clean and punch	3 days	Thu 12/17/26	Mon 12/21/26	272
274	**Building 205 - TRR20**	**37 days**	**Thu 12/17/26**	**Fri 2/5/27**	
275	ICRA	2 days	Thu 12/17/26	Fri 12/18/26	272
276	Abatement	3 days	Mon 12/21/26	Wed 12/23/26	275
277	Demolition	3 days	Thu 12/24/26	Mon 12/28/26	276
278	New walls, floors, doors	5 days	Tue 12/29/26	Mon 1/4/27	12,5,277
279	Install CRAC	5 days	Tue 1/5/27	Mon 1/11/27	278,11
280	Electrical and Lighting	5 days	Tue 1/5/27	Mon 1/11/27	278,10
281	Security	5 days	Tue 1/5/27	Mon 1/11/27	278,10
282	Fire suppression, FEC	3 days	Tue 1/5/27	Thu 1/7/27	278,8
283	Telecom racks and switches	3 days	Tue 1/5/27	Thu 1/7/27	278,9
284	Cable Tray and raceways	3 days	Fri 1/8/27	Tue 1/12/27	283
285	New cable from outlets to TRs	5 days	Wed 1/13/27	Tue 1/19/27	284
286	New outlet connections	3 days	Wed 1/20/27	Fri 1/22/27	285
287	Land cable on switches	2 days	Mon 1/25/27	Tue 1/26/27	286
288	Test new telecom outlets / system	2 days	Wed 1/27/27	Thu 1/28/27	287
289	DDC	1 day	Fri 1/29/27	Fri 1/29/27	288

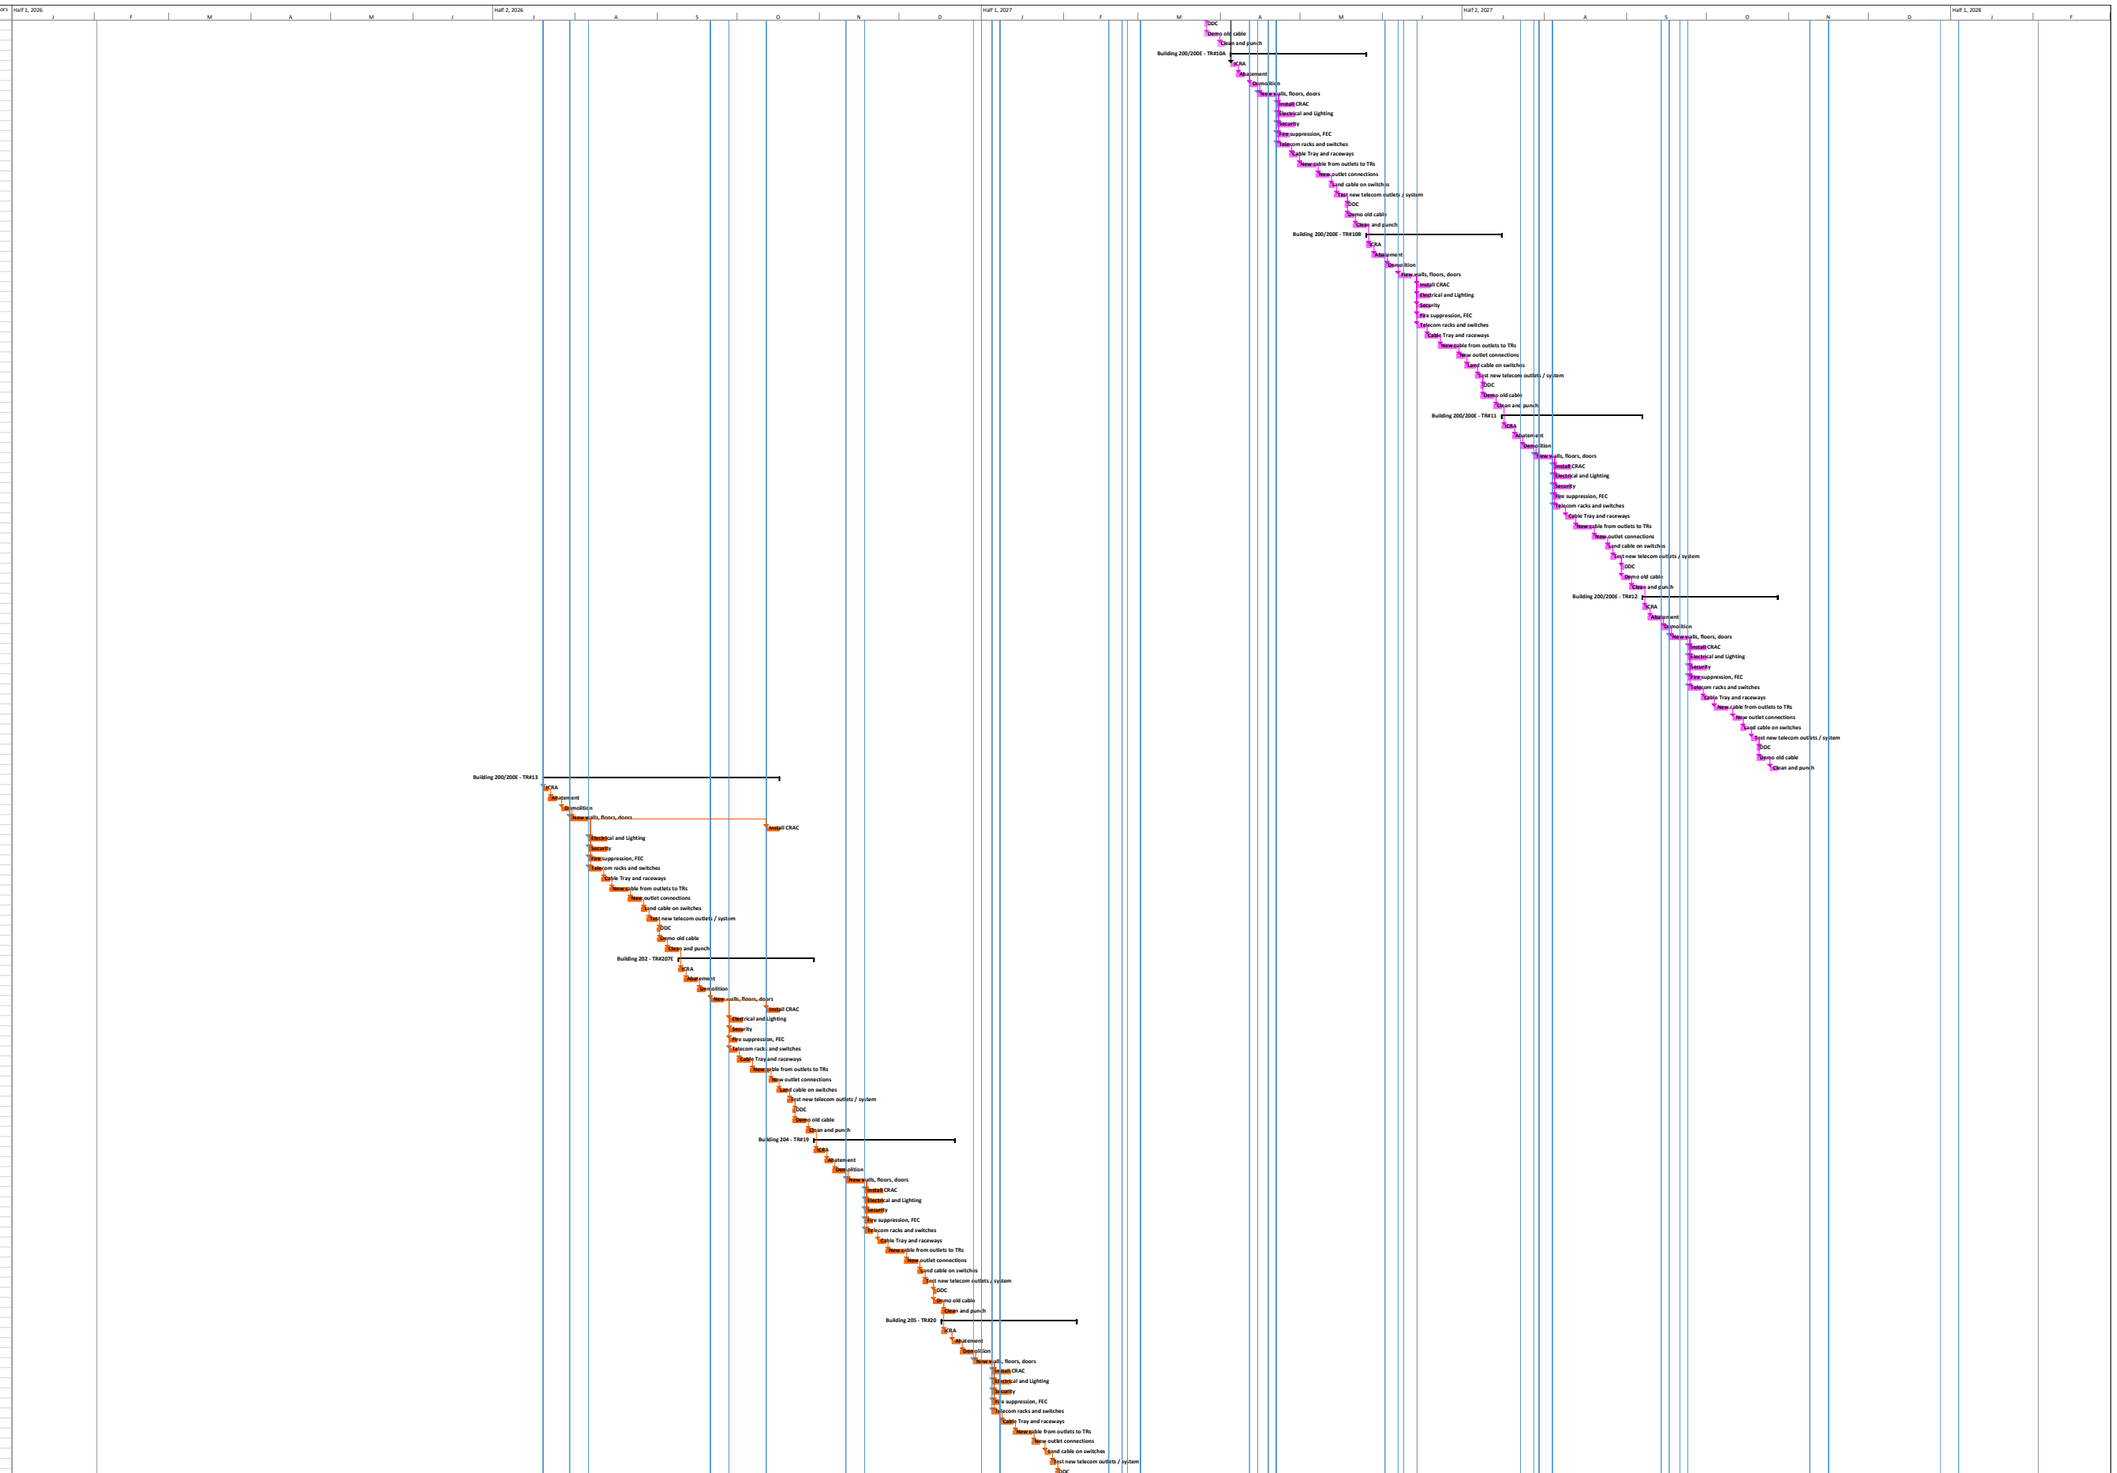

Togus EHRM
Reissued 12-22-2025

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress

ID	Task Name	Duration	Start	Finish	Predecessors
290	Demo old cable	3 days	Fri 1/29/27	Tue 2/2/27	288
291	Clean and punch	3 days	Wed 2/3/27	Fri 2/5/27	290
292	**Building 205 - TRR21**	**37 days**	**Mon 2/8/27**	**Tue 3/30/27**	
293	ICRA	2 days	Mon 2/8/27	Tue 2/9/27	291
294	Abatement	3 days	Wed 2/10/27	Fri 2/12/27	293
295	Demolition	3 days	Mon 2/15/27	Wed 2/17/27	294
296	New walls, floors, doors	5 days	Thu 2/18/27	Wed 2/24/27	12,5,295
297	Install CRAC	5 days	Thu 2/25/27	Wed 3/3/27	296,11
298	Electrical and Lighting	5 days	Thu 2/25/27	Wed 3/3/27	296,10
299	Security	5 days	Thu 2/25/27	Wed 3/3/27	296,10
300	Fire suppression, FEC	3 days	Thu 2/25/27	Mon 3/1/27	296,8
301	Telecom racks and switches	3 days	Thu 2/25/27	Mon 3/1/27	296,9
302	Cable Tray and raceways	3 days	Tue 3/2/27	Thu 3/4/27	301
303	New cable from outlets to TRs	5 days	Fri 3/5/27	Thu 3/11/27	302
304	New outlet connections	3 days	Fri 3/12/27	Tue 3/16/27	303
305	Land cable on switches	2 days	Wed 3/17/27	Thu 3/18/27	304
306	Test new telecom outlets / system	2 days	Fri 3/19/27	Mon 3/22/27	305
307	ODC	1 day	Tue 3/23/27	Tue 3/23/27	306
308	Demo old cable	3 days	Tue 3/23/27	Thu 3/25/27	306
309	Clean and punch	3 days	Fri 3/26/27	Tue 3/30/27	308
310	**Building 205 - TRR22**	**37 days**	**Wed 3/31/27**	**Thu 5/20/27**	
311	ICRA	2 days	Wed 3/31/27	Thu 4/1/27	309
312	Abatement	3 days	Fri 4/2/27	Tue 4/6/27	311
313	Demolition	3 days	Wed 4/7/27	Fri 4/9/27	312
314	New walls, floors, doors	5 days	Mon 4/12/27	Fri 4/16/27	12,313,5
315	Install CRAC	5 days	Mon 4/19/27	Fri 4/23/27	314,11
316	Electrical and Lighting	5 days	Mon 4/19/27	Fri 4/23/27	314,10
317	Security	5 days	Mon 4/19/27	Fri 4/23/27	314,10
318	Fire suppression, FEC	3 days	Mon 4/19/27	Wed 4/21/27	314,8
319	Telecom racks and switches	3 days	Mon 4/19/27	Wed 4/21/27	314,9
320	Cable Tray and raceways	3 days	Thu 4/22/27	Mon 4/26/27	319
321	New cable from outlets to TRs	5 days	Tue 4/27/27	Mon 5/3/27	320
322	New outlet connections	3 days	Tue 5/4/27	Thu 5/6/27	321
323	Land cable on switches	2 days	Fri 5/7/27	Mon 5/10/27	322
324	Test new telecom outlets / system	2 days	Tue 5/11/27	Wed 5/12/27	323
325	ODC	1 day	Thu 5/13/27	Thu 5/13/27	324
326	Demo old cable	3 days	Thu 5/13/27	Mon 5/17/27	324
327	Clean and punch	3 days	Tue 5/18/27	Thu 5/20/27	326
328	**Building 206 - TRR23**	**400 days**	**Mon 7/26/26**	**Fri 1/28/28**	
329	ICRA	2 days	Fri 5/21/27	Mon 5/24/27	327
330	Abatement	3 days	Tue 5/25/27	Thu 5/27/27	329
331	Demolition	3 days	Fri 5/28/27	Tue 6/1/27	330
332	New walls, floors, doors	5 days	Wed 6/2/27	Tue 6/8/27	12,5,331
333	Install CRAC	5 days	Wed 6/9/27	Tue 6/15/27	332,11
334	Electrical and Lighting	5 days	Wed 6/9/27	Tue 6/15/27	332,10
335	Security	5 days	Wed 6/9/27	Tue 6/15/27	332,10
336	Fire suppression, FEC	3 days	Wed 6/9/27	Fri 6/11/27	332,8
337	Telecom racks and switches	3 days	Wed 6/9/27	Fri 6/11/27	332,9
338	Cable Tray and raceways	3 days	Mon 6/14/27	Wed 6/16/27	337
339	New cable from outlets to TRs	5 days	Thu 6/17/27	Wed 6/23/27	338
340	New outlet connections	3 days	Thu 6/24/27	Mon 6/28/27	339
341	Land cable on switches	2 days	Tue 6/29/27	Wed 6/30/27	340
342	Test new telecom outlets / system	2 days	Thu 7/1/27	Fri 7/2/27	341
343	ODC	1 day	Mon 7/5/27	Mon 7/5/27	342
344	Demo old cable	3 days	Mon 7/5/27	Wed 7/7/27	342
345	Clean and punch	3 days	Thu 7/8/27	Mon 7/12/27	344
346	**Building 206 - TRR24**	**400 days**	**Mon 7/26/26**	**Fri 1/28/28**	
347	ICRA	2 days	Tue 7/13/27	Wed 7/14/27	345
348	Abatement	3 days	Thu 7/15/27	Mon 7/18/27	347
349	Demolition	3 days	Tue 7/20/27	Thu 7/22/27	348
350	New walls, floors, doors	5 days	Fri 7/23/27	Thu 7/29/27	349,12,5
351	Install CRAC	5 days	Fri 7/30/27	Thu 8/5/27	350,11
352	Electrical and Lighting	5 days	Fri 7/30/27	Thu 8/5/27	350,10
353	Security	5 days	Fri 7/30/27	Thu 8/5/27	350,10
354	Fire suppression, FEC	3 days	Fri 7/30/27	Tue 8/3/27	350,8
355	Telecom racks and switches	3 days	Fri 7/30/27	Tue 8/3/27	350,9
356	Cable Tray and raceways	3 days	Wed 8/4/27	Fri 8/6/27	355
357	New cable from outlets to TRs	5 days	Mon 8/9/27	Fri 8/13/27	356
358	New outlet connections	3 days	Mon 8/16/27	Wed 8/18/27	357
359	Land cable on switches	2 days	Thu 8/19/27	Fri 8/20/27	358
360	Test new telecom outlets / system	2 days	Mon 8/23/27	Tue 8/24/27	359
361	ODC	1 day	Wed 8/25/27	Wed 8/25/27	360
362	Demo old cable	3 days	Wed 8/25/27	Fri 8/27/27	360
363	Clean and punch	3 days	Mon 8/30/27	Wed 9/1/27	362
364	**Building 206 - TRR25**	**400 days**	**Mon 7/26/26**	**Fri 1/28/28**	
365	ICRA	2 days	Thu 9/2/27	Fri 9/3/27	363
366	Abatement	3 days	Mon 9/6/27	Wed 9/8/27	365
367	Demolition	3 days	Thu 9/9/27	Mon 9/13/27	366
368	New walls, floors, doors	5 days	Tue 9/14/27	Mon 9/20/27	367,12,5
369	Install CRAC	5 days	Tue 9/21/27	Mon 9/27/27	368,11
370	Electrical and Lighting	5 days	Tue 9/21/27	Mon 9/27/27	368,10
371	Security	5 days	Tue 9/21/27	Mon 9/27/27	368,10
372	Fire suppression, FEC	3 days	Tue 9/21/27	Thu 9/23/27	368,8
373	Telecom racks and switches	3 days	Tue 9/21/27	Thu 9/23/27	368,9
374	Cable Tray and raceways	3 days	Fri 9/24/27	Tue 9/28/27	373
375	New cable from outlets to TRs	5 days	Wed 9/29/27	Tue 10/5/27	374
376	New outlet connections	3 days	Wed 10/6/27	Fri 10/8/27	375
377	Land cable on switches	2 days	Mon 10/11/27	Tue 10/12/27	376
378	Test new telecom outlets / system	2 days	Wed 10/13/27	Thu 10/14/27	377
379	ODC	1 day	Fri 10/15/27	Fri 10/15/27	378
380	Demo old cable	3 days	Fri 10/15/27	Tue 10/19/27	378
381	Clean and punch	3 days	Wed 10/20/27	Fri 10/22/27	380
382	**Building 207 - TRR26**	**400 days**	**Mon 7/26/26**	**Fri 1/28/28**	
383	ICRA	2 days	Mon 7/26/26	Tue 7/21/26	12,5
384	Abatement	3 days	Wed 7/22/26	Fri 7/24/26	383
385	Demolition	3 days	Mon 7/27/26	Wed 7/29/26	384
386	New walls, floors, doors	5 days	Thu 7/30/26	Wed 8/5/26	385,12,5
387	Install CRAC	5 days	Mon 10/12/26	Fri 10/16/26	386,11
388	Electrical and Lighting	5 days	Thu 8/6/26	Wed 8/12/26	386,10
389	Security	5 days	Thu 8/6/26	Wed 8/12/26	386,10
390	Fire suppression, FEC	3 days	Thu 8/6/26	Mon 8/10/26	386,8
391	Telecom racks and switches	3 days	Thu 8/6/26	Mon 8/10/26	386,9
392	Cable Tray and raceways	3 days	Tue 8/11/26	Thu 8/13/26	391
393	New cable from outlets to TRs	5 days	Fri 8/14/26	Thu 8/20/26	392
394	New outlet connections	3 days	Fri 8/21/26	Tue 8/25/26	393
395	Land cable on switches	2 days	Wed 8/26/26	Thu 8/27/26	394
396	Test new telecom outlets / system	2 days	Fri 8/28/26	Mon 8/31/26	395
397	ODC	1 day	Tue 9/1/26	Tue 9/1/26	396
398	Demo old cable	3 days	Tue 9/1/26	Thu 9/3/26	396
399	Clean and punch	3 days	Fri 9/4/26	Tue 9/8/26	398
400	**Building 207 - TRR28**	**400 days**	**Mon 7/26/26**	**Fri 1/28/28**	
401	ICRA	2 days	Wed 9/9/26	Thu 9/10/26	399
402	Abatement	3 days	Fri 9/11/26	Tue 9/15/26	401
403	Demolition	3 days	Wed 9/16/26	Fri 9/18/26	402
404	New walls, floors, doors	5 days	Mon 9/21/26	Fri 9/25/26	403,12,5
405	Install CRAC	5 days	Mon 10/12/26	Fri 10/16/26	404,11
406	Electrical and Lighting	5 days	Mon 9/28/26	Fri 10/2/26	404,10
407	Security	5 days	Mon 9/28/26	Fri 10/2/26	404,10
408	Fire suppression, FEC	3 days	Mon 9/28/26	Wed 9/30/26	404,8
409	Telecom racks and switches	3 days	Mon 9/28/26	Wed 9/30/26	404,9
410	Cable Tray and raceways	3 days	Thu 10/1/26	Mon 10/5/26	409
411	New cable from outlets to TRs	5 days	Tue 10/6/26	Mon 10/12/26	410
412	New outlet connections	3 days	Tue 10/13/26	Thu 10/15/26	411
413	Land cable on switches	2 days	Fri 10/16/26	Mon 10/19/26	412
414	Test new telecom outlets / system	2 days	Tue 10/20/26	Wed 10/21/26	413
415	ODC	1 day	Thu 10/22/26	Thu 10/22/26	414
416	Demo old cable	3 days	Thu 10/22/26	Mon 10/26/26	414
417	Clean and punch	3 days	Tue 10/27/26	Thu 10/29/26	416
418	**Building 208 - TRR29**	**400 days**	**Mon 7/26/26**	**Fri 1/28/28**	
419	ICRA	2 days	Fri 10/30/26	Mon 11/2/26	417
420	Abatement	3 days	Tue 11/3/26	Thu 11/5/26	419
421	Demolition	3 days	Fri 11/6/26	Tue 11/10/26	420
422	New walls, floors, doors	5 days	Wed 11/11/26	Tue 11/17/26	421,12,5
423	Install CRAC	5 days	Wed 11/18/26	Tue 11/24/26	422,11
424	Electrical and Lighting	5 days	Wed 11/18/26	Tue 11/24/26	422,10
425	Security	5 days	Wed 11/18/26	Tue 11/24/26	422,10
426	Fire suppression, FEC	3 days	Wed 11/18/26	Fri 11/20/26	422,8
427	Telecom racks and switches	3 days	Wed 11/18/26	Fri 11/20/26	422,9
428	Cable Tray and raceways	3 days	Mon 11/23/26	Wed 11/25/26	427
429	New cable from outlets to TRs	5 days	Thu 11/26/26	Wed 12/2/26	428
430	New outlet connections	3 days	Thu 12/3/26	Mon 12/7/26	429
431	Land cable on switches	2 days	Tue 12/8/26	Wed 12/9/26	430
432	Test new telecom outlets / system	2 days	Thu 12/10/26	Fri 12/11/26	431
433	ODC	1 day	Mon 12/14/26	Mon 12/14/26	432
434	Demo old cable	3 days	Mon 12/14/26	Wed 12/16/26	432

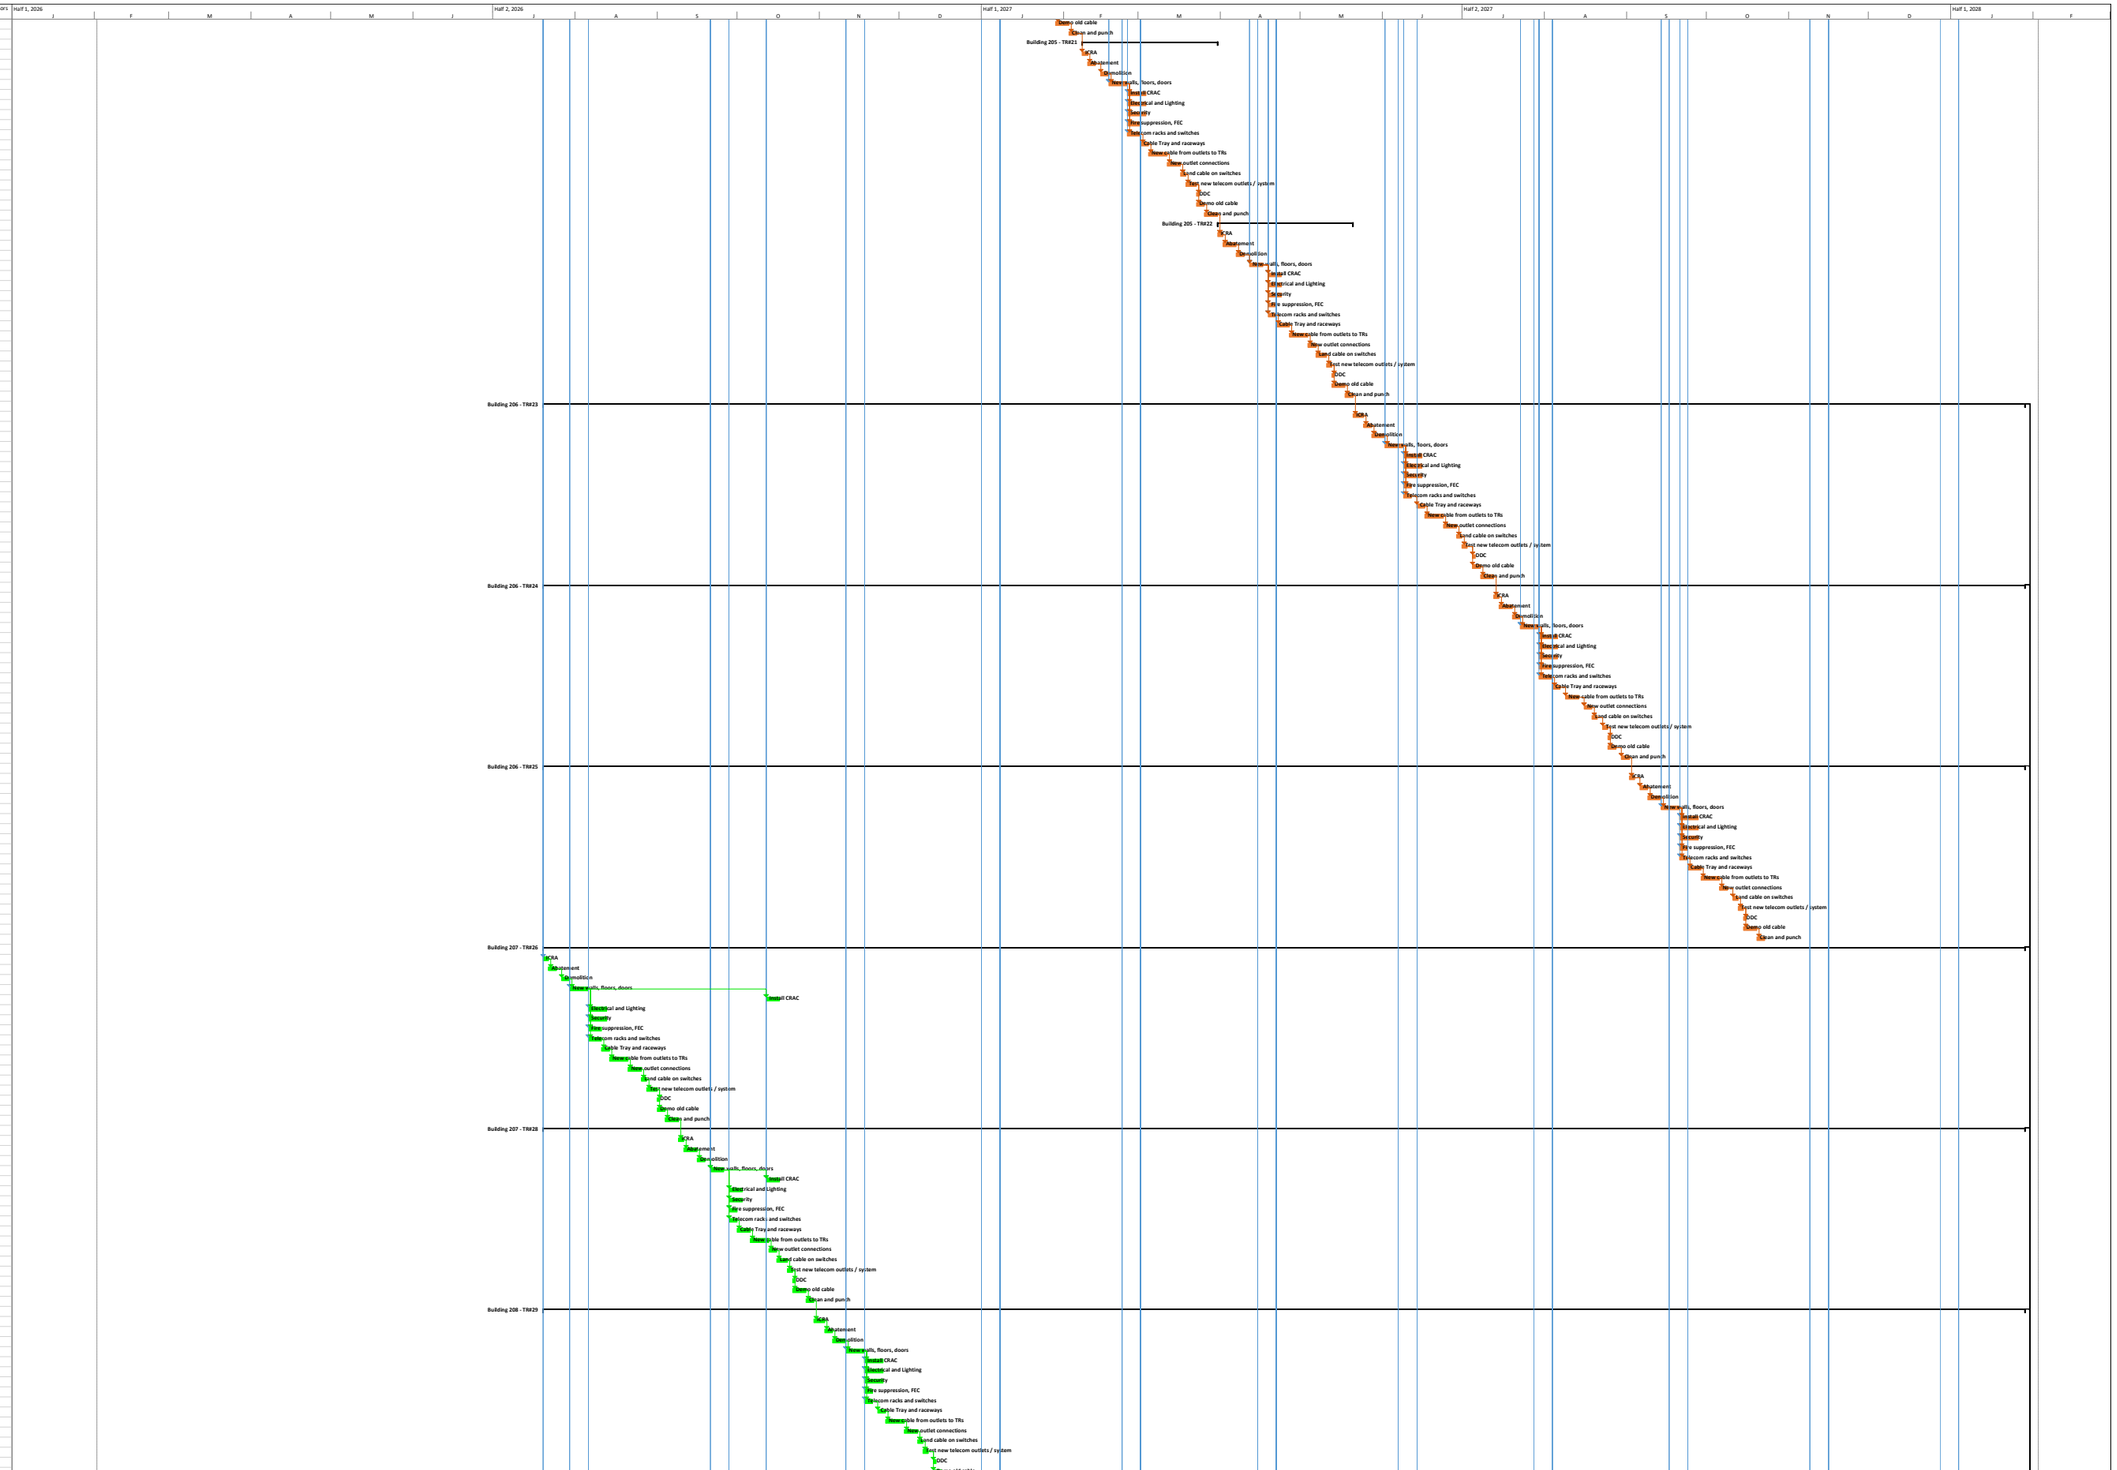

Togus EHRM
Reissued 12-22-2025

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress

ID	Task Name	Duration	Start	Finish	Predecessors
435	Clean and punch	3 days	Thu 12/17/26	Mon 12/21/26	434
436	**Building 209 - TR#30**	**400 days**	**Mon 7/20/26**	**Fri 1/28/28**	
437	ICRA	2 days	Tue 12/22/26	Wed 12/23/26	435
438	Abatement	3 days	Thu 12/24/26	Mon 12/28/26	437
439	Demolition	3 days	Tue 12/29/26	Thu 12/31/26	438
440	New walls, floors, doors	5 days	Fri 1/1/27	Thu 1/7/27	439,12,5
441	Install CRAC	5 days	Fri 1/8/27	Thu 1/14/27	440,11
442	Electrical and Lighting	5 days	Fri 1/8/27	Thu 1/14/27	440,10
443	Security	5 days	Fri 1/8/27	Thu 1/14/27	440,10
444	Fire suppression, FEC	3 days	Fri 1/8/27	Tue 1/12/27	440,8
445	Telecom racks and switches	3 days	Fri 1/8/27	Tue 1/12/27	440,9
446	Cable Tray and raceways	3 days	Wed 1/13/27	Fri 1/15/27	445
447	New cable from outlets to TRs	5 days	Mon 1/18/27	Fri 1/22/27	446
448	New outlet connections	3 days	Mon 1/25/27	Wed 1/27/27	447
449	Land cable on switches	2 days	Thu 1/28/27	Fri 1/29/27	448
450	Test new telecom outlets / system	2 days	Mon 2/1/27	Tue 2/2/27	449
451	DOC	1 day	Wed 2/3/27	Wed 2/3/27	450
452	Demo old cable	3 days	Wed 2/3/27	Fri 2/5/27	450
453	Clean and punch	3 days	Mon 2/8/27	Wed 2/10/27	452
454	**Building 209 - TR#31**	**400 days**	**Mon 7/20/26**	**Fri 1/28/28**	
455	ICRA	2 days	Thu 2/11/27	Fri 2/12/27	453
456	Abatement	3 days	Mon 2/15/27	Wed 2/17/27	455
457	Demolition	3 days	Thu 2/18/27	Mon 2/22/27	456
458	New walls, floors, doors	5 days	Tue 2/23/27	Mon 3/1/27	457,12,5
459	Install CRAC	5 days	Tue 3/2/27	Mon 3/8/27	458,11
460	Electrical and Lighting	5 days	Tue 3/2/27	Mon 3/8/27	458,10
461	Security	5 days	Tue 3/2/27	Mon 3/8/27	458,10
462	Fire suppression, FEC	3 days	Tue 3/2/27	Thu 3/4/27	458,8
463	Telecom racks and switches	3 days	Tue 3/2/27	Thu 3/4/27	458,9
464	Cable Tray and raceways	3 days	Fri 3/5/27	Tue 3/9/27	463
465	New cable from outlets to TRs	5 days	Wed 3/10/27	Tue 3/16/27	464
466	New outlet connections	3 days	Wed 3/17/27	Fri 3/19/27	465
467	Land cable on switches	2 days	Mon 3/22/27	Tue 3/23/27	466
468	Test new telecom outlets / system	2 days	Wed 3/24/27	Thu 3/25/27	467
469	DOC	1 day	Fri 3/26/27	Fri 3/26/27	468
470	Demo old cable	3 days	Fri 3/26/27	Tue 3/30/27	468
471	Clean and punch	3 days	Wed 3/31/27	Fri 4/2/27	470
472	**Building 210 - TR#32**	**400 days**	**Mon 7/20/26**	**Fri 1/28/28**	
473	ICRA	2 days	Mon 4/5/27	Tue 4/6/27	471
474	Abatement	3 days	Wed 4/7/27	Fri 4/9/27	473
475	Demolition	3 days	Mon 4/12/27	Wed 4/14/27	474
476	New walls, floors, doors	5 days	Thu 4/15/27	Wed 4/21/27	475,12,5
477	Install CRAC	5 days	Thu 4/22/27	Wed 4/28/27	476,11
478	Electrical and Lighting	5 days	Thu 4/22/27	Wed 4/28/27	476,10
479	Security	5 days	Thu 4/22/27	Wed 4/28/27	476,10
480	Fire suppression, FEC	3 days	Thu 4/22/27	Mon 4/26/27	476,8
481	Telecom racks and switches	3 days	Thu 4/22/27	Mon 4/26/27	476,9
482	Cable Tray and raceways	3 days	Tue 4/27/27	Thu 4/29/27	481
483	New cable from outlets to TRs	5 days	Fri 4/30/27	Thu 5/6/27	482
484	New outlet connections	3 days	Fri 5/7/27	Tue 5/11/27	483
485	Land cable on switches	2 days	Wed 5/12/27	Thu 5/13/27	484
486	Test new telecom outlets / system	2 days	Fri 5/14/27	Mon 5/17/27	485
487	DOC	1 day	Tue 5/18/27	Tue 5/18/27	486
488	Demo old cable	3 days	Tue 5/18/27	Thu 5/20/27	486
489	Clean and punch	3 days	Fri 5/21/27	Tue 5/25/27	488
490	**Building 211 - TR#33**	**400 days**	**Mon 7/20/26**	**Fri 1/28/28**	
491	ICRA	2 days	Wed 5/26/27	Thu 5/27/27	489
492	Abatement	3 days	Fri 5/28/27	Tue 6/1/27	491
493	Demolition	3 days	Wed 6/2/27	Fri 6/4/27	492
494	New walls, floors, doors	5 days	Mon 6/7/27	Fri 6/11/27	493,12,5
495	Install CRAC	5 days	Mon 6/14/27	Fri 6/18/27	494,11
496	Electrical and Lighting	5 days	Mon 6/14/27	Fri 6/18/27	494,10
497	Security	5 days	Mon 6/14/27	Fri 6/18/27	494,10
498	Fire suppression, FEC	3 days	Mon 6/14/27	Wed 6/16/27	494,8
499	Telecom racks and switches	3 days	Mon 6/14/27	Wed 6/16/27	494,9
500	Cable Tray and raceways	3 days	Thu 6/17/27	Mon 6/21/27	499
501	New cable from outlets to TRs	5 days	Tue 6/22/27	Mon 6/28/27	500
502	New outlet connections	3 days	Tue 6/29/27	Thu 7/1/27	501
503	Land cable on switches	2 days	Fri 7/2/27	Mon 7/5/27	502
504	Test new telecom outlets / syste	2 days	Tue 7/6/27	Wed 7/7/27	503
505	DOC	1 day	Thu 7/8/27	Thu 7/8/27	504
506	Demo old cable	3 days	Thu 7/8/27	Mon 7/12/27	504
507	Clean and punch	3 days	Tue 7/13/27	Thu 7/15/27	506
508	**Building 212 - TR#34**	**400 days**	**Mon 7/20/26**	**Fri 1/28/28**	
509	ICRA	2 days	Mon 7/20/26	Tue 7/21/26	12,5
510	Abatement	3 days	Wed 7/22/26	Fri 7/24/26	509
511	Demolition	3 days	Mon 7/27/26	Wed 7/29/26	510
512	New walls, floors, doors	5 days	Thu 7/30/26	Wed 8/5/26	511,12,5
513	Install CRAC	5 days	Mon 10/12/26	Fri 10/16/26	512,11
514	Electrical and Lighting	5 days	Thu 8/6/26	Wed 8/12/26	512,10
515	Security	5 days	Thu 8/6/26	Wed 8/12/26	512,10
516	Fire suppression, FEC	3 days	Thu 8/6/26	Mon 8/10/26	512,8
517	Telecom racks and switches	3 days	Thu 8/6/26	Mon 8/10/26	512,9
518	Cable Tray and raceways	3 days	Tue 8/11/26	Thu 8/13/26	517
519	New cable from outlets to TRs	5 days	Fri 8/14/26	Thu 8/20/26	518
520	New outlet connections	3 days	Fri 8/21/26	Tue 8/25/26	519
521	Land cable on switches	2 days	Wed 8/26/26	Thu 8/27/26	520
522	Test new telecom outlets / sy	2 days	Fri 8/28/26	Mon 8/31/26	521
523	DOC	1 day	Tue 9/1/26	Tue 9/1/26	522
524	Demo old cable	3 days	Tue 9/1/26	Thu 9/3/26	522
525	Clean and punch	3 days	Fri 9/4/26	Tue 9/8/26	524
526	**Building 221 - TR#35**	**363 days**	**Wed 9/9/26**	**Fri 1/28/28**	
527	ICRA	2 days	Wed 9/9/26	Thu 9/10/26	525
528	Abatement	3 days	Fri 9/11/26	Tue 9/15/26	527
529	Demolition	3 days	Wed 9/16/26	Fri 9/18/26	528
530	New walls, floors, doors	5 days	Mon 9/21/26	Fri 9/25/26	529,12,5
531	Install CRAC	5 days	Mon 10/12/26	Fri 10/16/26	530,11
532	Electrical and Lighting	5 days	Mon 9/28/26	Fri 10/2/26	530,10
533	Security	5 days	Mon 9/28/26	Fri 10/2/26	530,10
534	Fire suppression, FEC	3 days	Mon 9/28/26	Wed 9/30/26	530,8
535	Telecom racks and switche	3 days	Mon 9/28/26	Wed 9/30/26	530,9
536	Cable Tray and raceways	3 days	Thu 10/1/26	Mon 10/5/26	535
537	New cable from outlets to T	5 days	Tue 10/6/26	Mon 10/12/26	536
538	New outlet connections	3 days	Tue 10/13/26	Thu 10/15/26	537
539	Land cable on switches	2 days	Fri 10/16/26	Mon 10/19/26	538
540	Test new telecom outlets /	2 days	Tue 10/20/26	Wed 10/21/26	539
541	DOC	1 day	Thu 10/22/26	Thu 10/22/26	540
542	Demo old cable	3 days	Thu 10/22/26	Mon 10/26/26	540
543	Clean and punch	3 days	Tue 10/27/26	Thu 10/29/26	542
544	**Building 323 - TR#36**	**326 days**	**Fri 10/30/26**	**Fri 1/28/28**	
545	ICRA	2 days	Fri 10/30/26	Mon 11/2/26	543
546	Abatement	3 days	Tue 11/3/26	Thu 11/5/26	545
547	Demolition	3 days	Fri 11/6/26	Tue 11/10/26	546
548	New walls, floors, doors	5 days	Wed 11/11/26	Tue 11/17/26	547,12,5
549	Install CRAC	5 days	Wed 11/18/26	Tue 11/24/26	548,11
550	Electrical and Lighting	5 days	Wed 11/18/26	Tue 11/24/26	548,10
551	Security	5 days	Wed 11/18/26	Tue 11/24/26	548,10
552	Fire suppression, FEC	3 days	Wed 11/18/26	Fri 11/20/26	548,8
553	Telecom racks and switch	3 days	Wed 11/18/26	Fri 11/20/26	548,9
554	Cable Tray and raceway	3 days	Mon 11/23/26	Wed 11/25/26	553
555	New cable from outlets	5 days	Thu 11/26/26	Wed 12/2/26	554
556	New outlet connections	3 days	Thu 12/3/26	Mon 12/7/26	555
557	Land cable on switches	2 days	Tue 12/8/26	Wed 12/9/26	556
558	Test new telecom outle	2 days	Thu 12/10/26	Fri 12/11/26	557
559	DOC	1 day	Mon 12/14/26	Mon 12/14/26	558
560	Demo old cable	3 days	Mon 12/14/26	Wed 12/16/26	558
561	Clean and punch	3 days	Thu 12/17/26	Mon 12/21/26	560
562	**Building 201 - TR#37A**	**289 days**	**Tue 12/22/26**	**Fri 1/28/28**	
563	ICRA	2 days	Tue 12/22/26	Wed 12/23/26	561
564	Abatement	3 days	Thu 12/24/26	Mon 12/28/26	563
565	Demolition	3 days	Tue 12/29/26	Thu 12/31/26	564
566	New walls, floors, do	5 days	Fri 1/1/27	Thu 1/7/27	565,12,5
567	Install CRAC	5 days	Fri 1/8/27	Thu 1/14/27	566,11
568	Electrical and Lightin	5 days	Fri 1/8/27	Thu 1/14/27	566,10
569	Security	5 days	Fri 1/8/27	Thu 1/14/27	566,10
570	Fire suppression, FEC	3 days	Fri 1/8/27	Tue 1/12/27	566,8
571	Telecom racks and sw	3 days	Fri 1/8/27	Tue 1/12/27	566,9
572	Cable Tray and race	3 days	Wed 1/13/27	Fri 1/15/27	571
573	New cable from out	5 days	Mon 1/18/27	Fri 1/22/27	572
574	New outlet connecti	3 days	Mon 1/25/27	Wed 1/27/27	573
575	Land cable on switch	2 days	Thu 1/28/27	Fri 1/29/27	574
576	Test new telecom ou	2 days	Mon 2/1/27	Tue 2/2/27	575
577	DOC	1 day	Wed 2/3/27	Wed 2/3/27	576
578	Demo old cable	3 days	Wed 2/3/27	Fri 2/5/27	576
579	Clean and punch	3 days	Mon 2/8/27	Wed 2/10/27	578

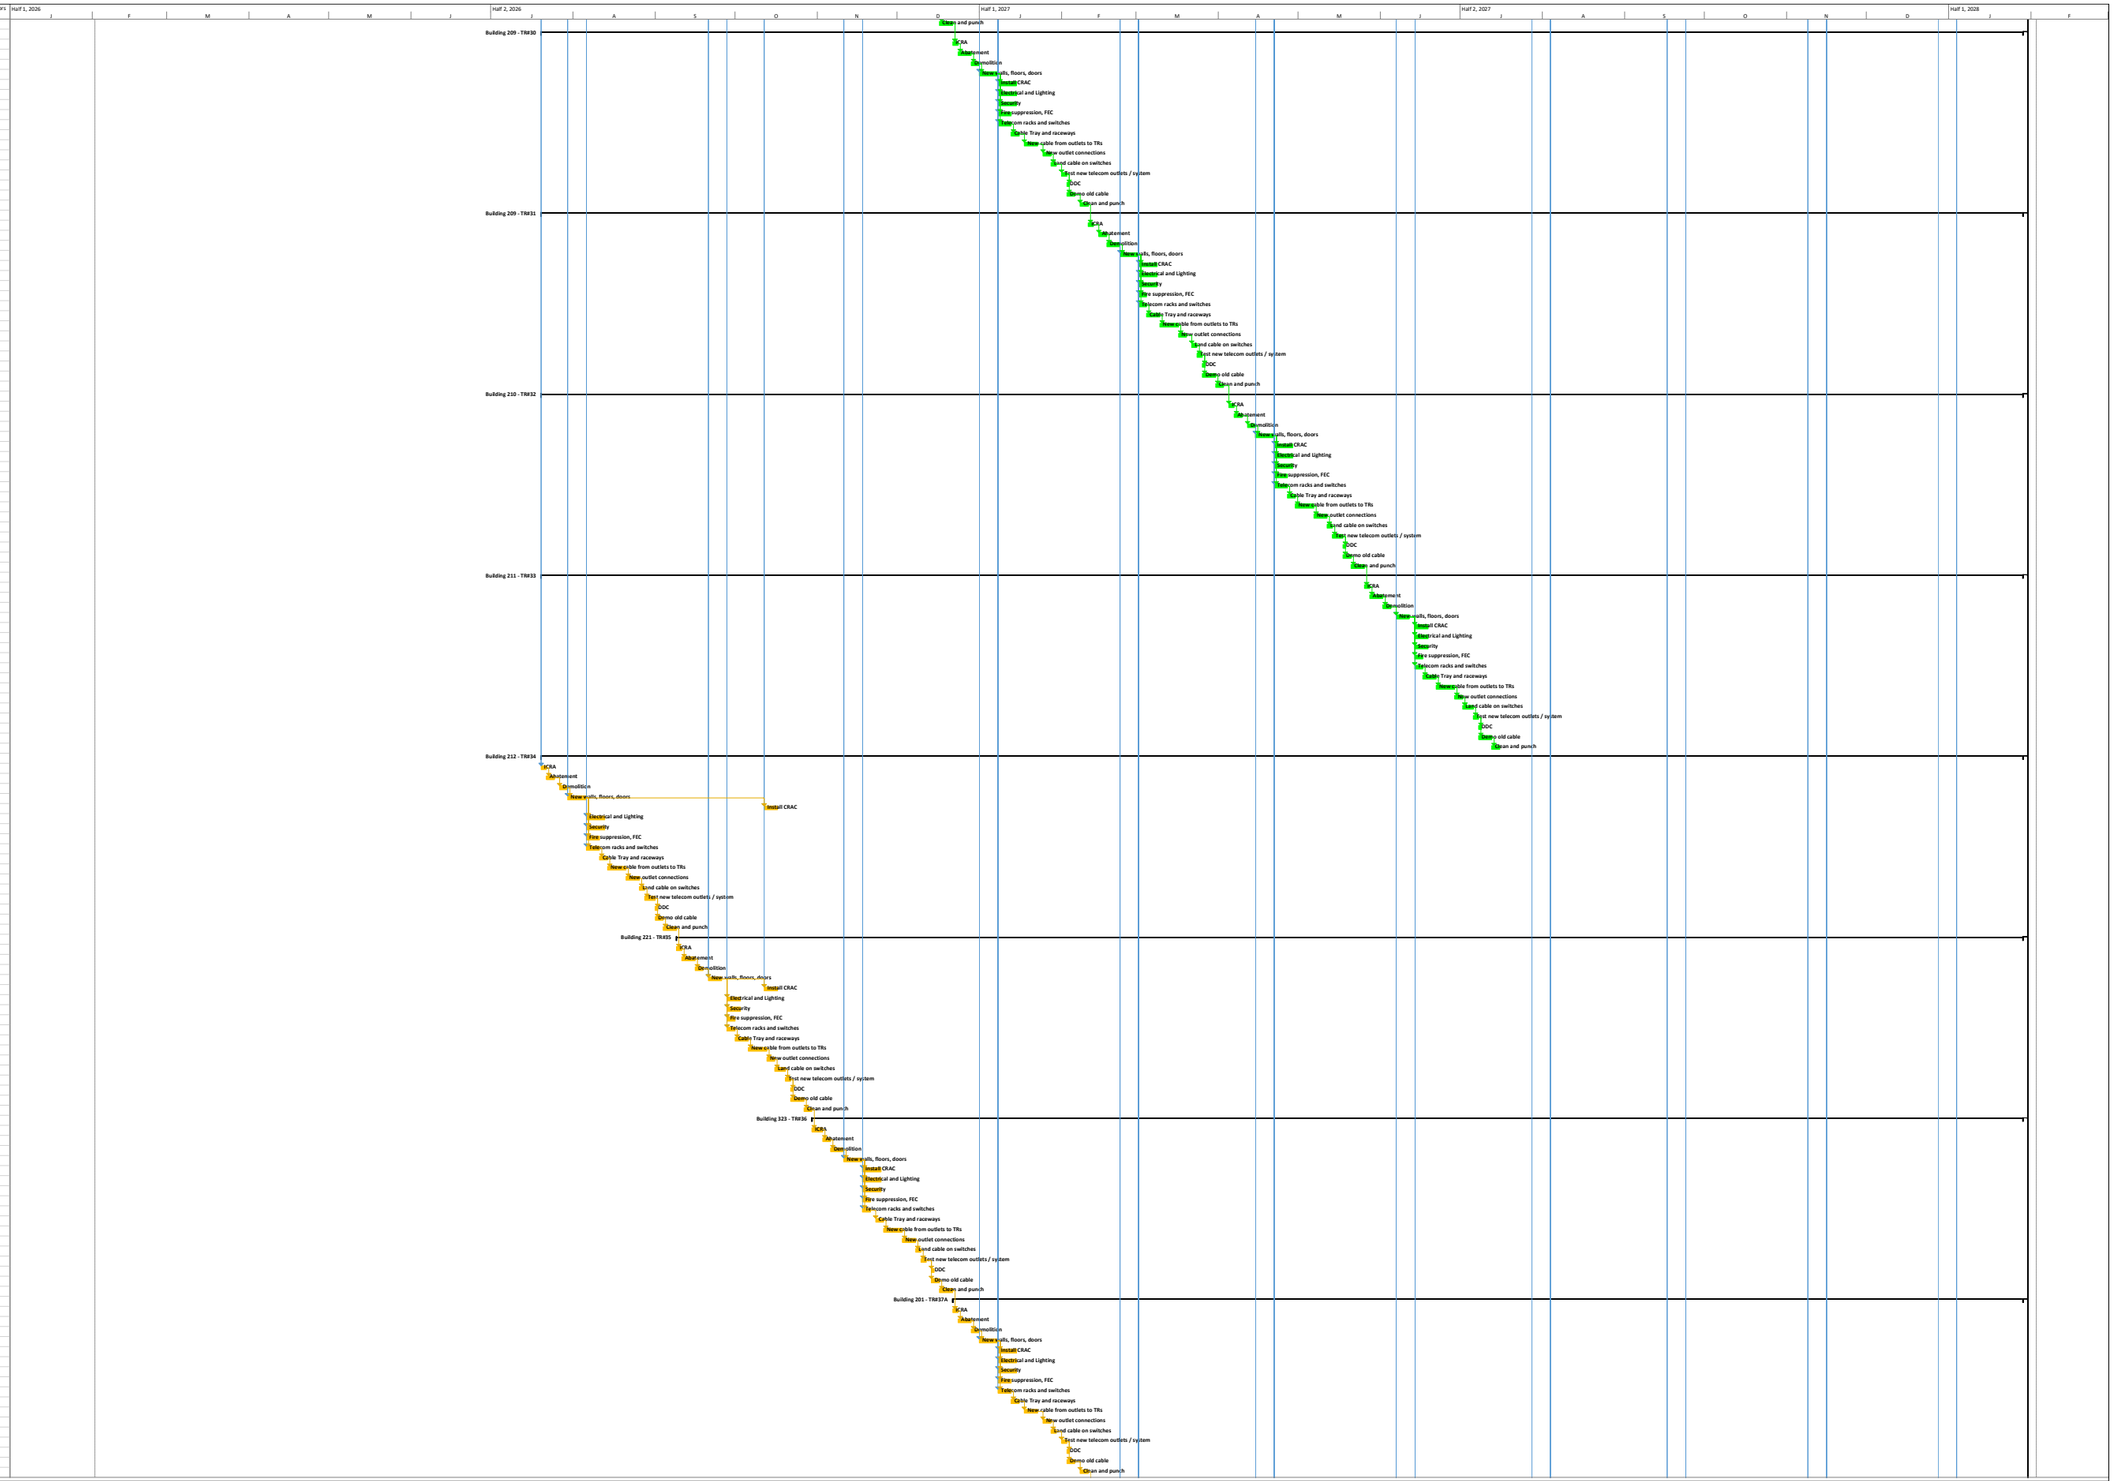

Togus EHRM
Reissued 12-22-2025

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress
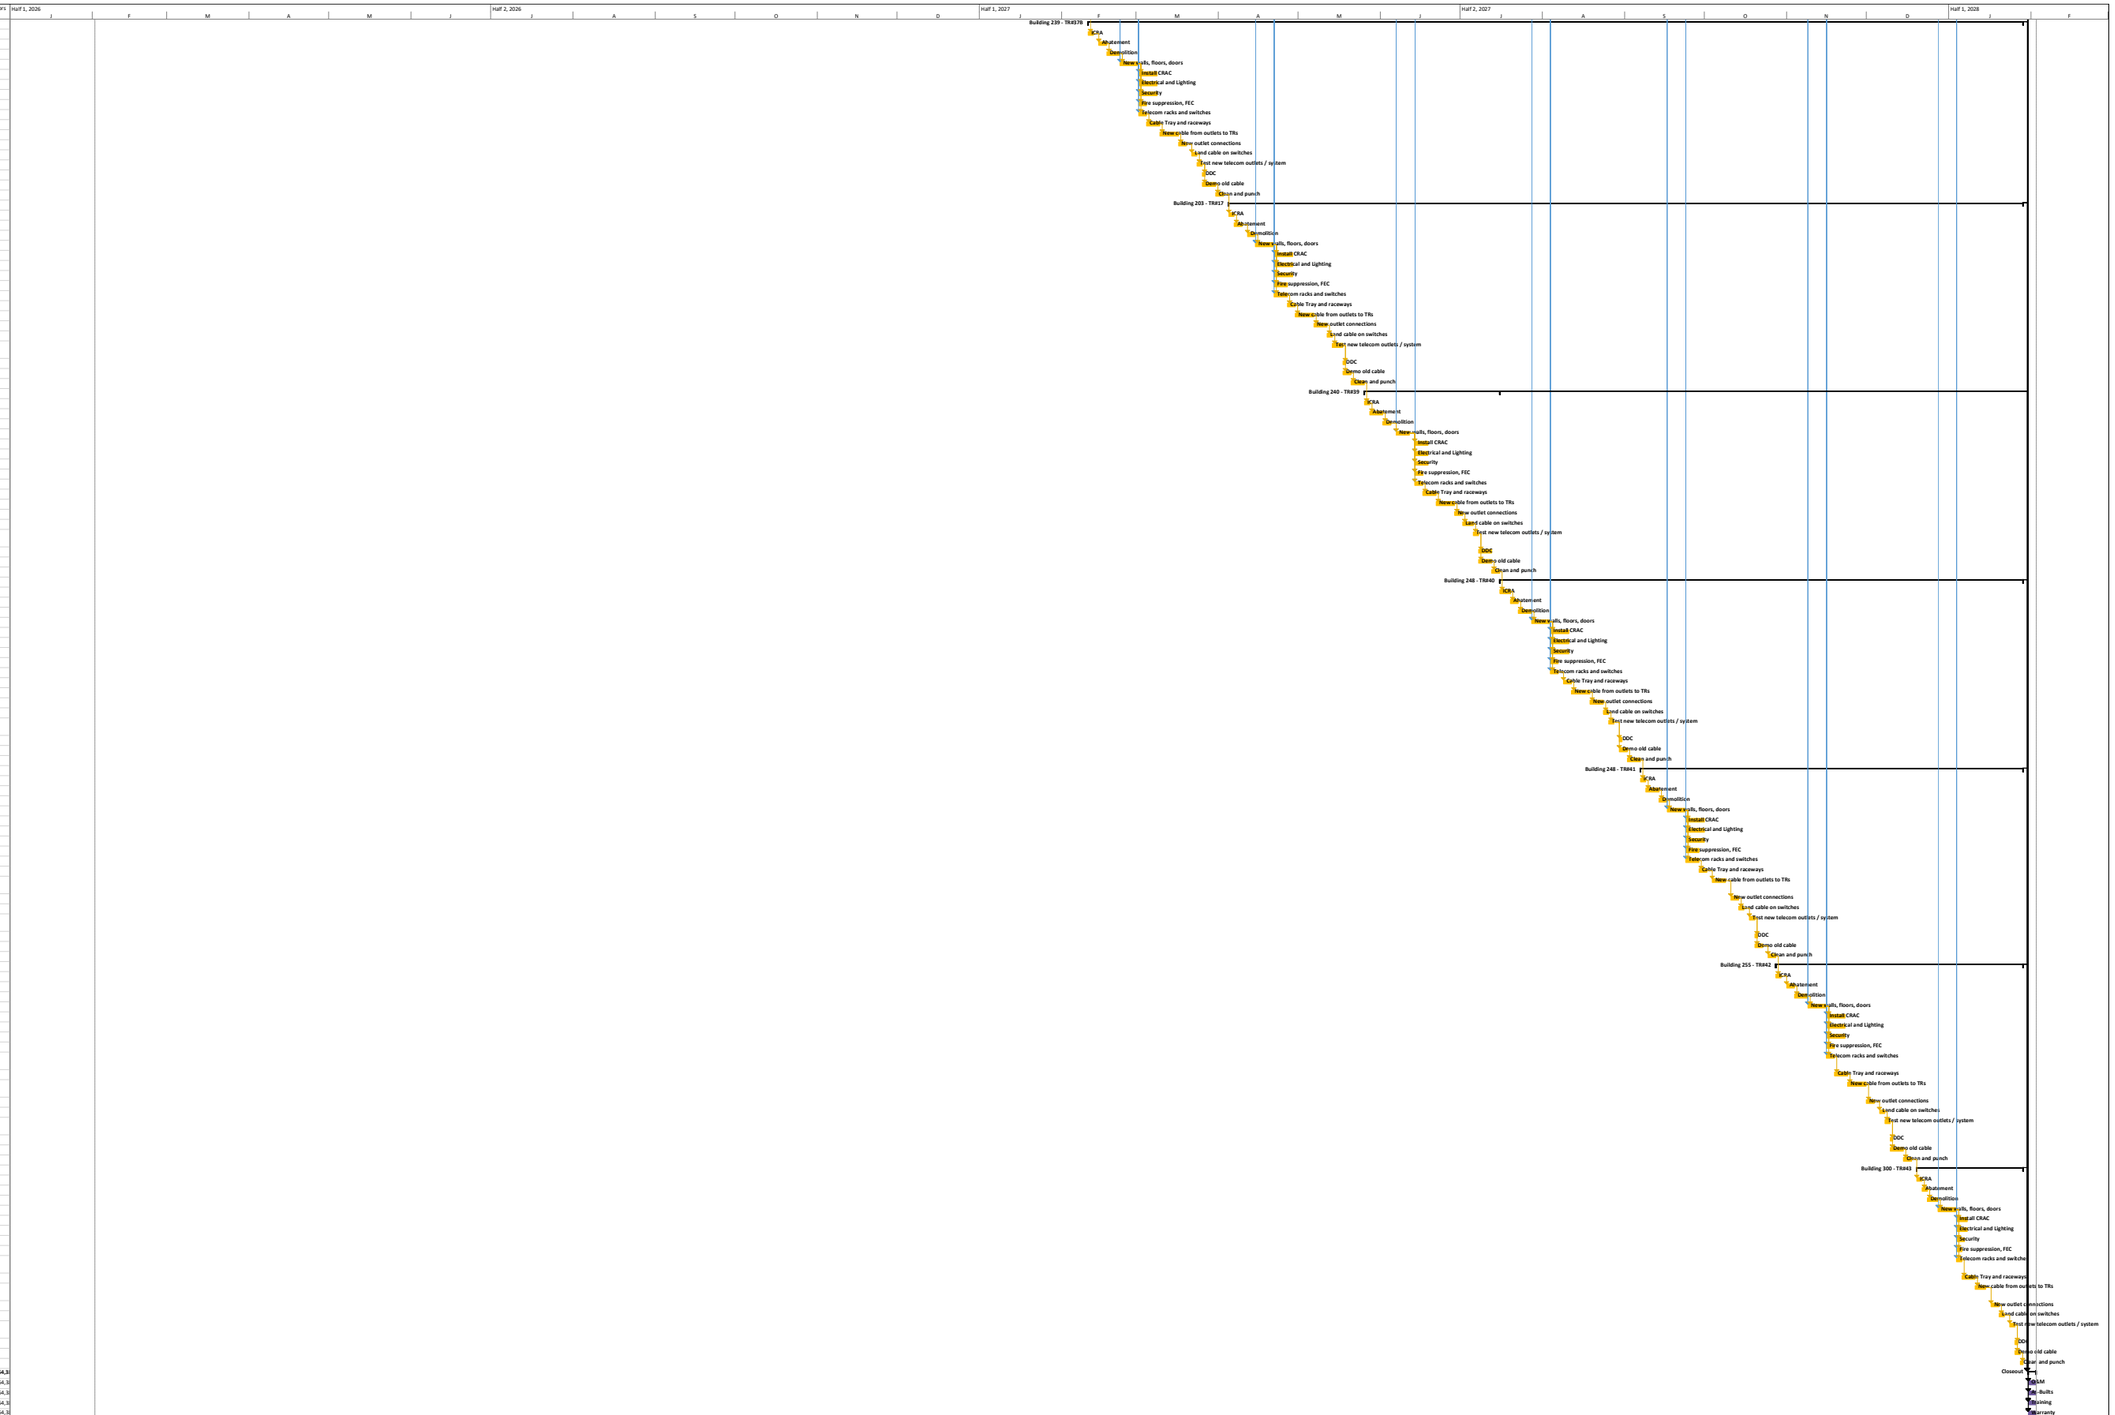
ID	Task Name	Duration	Start	Finish	Predecessors
580	**Building 239 - TR437**	**252 days**	**Thu 2/11/27**	**Fri 1/28/28**	
581	ICRA	2 days	Thu 2/11/27	Fri 2/12/27	579
582	Abatement	3 days	Mon 2/15/27	Wed 2/17/27	581
583	Demolition	3 days	Thu 2/18/27	Mon 2/22/27	582
584	New walls, floors,	5 days	Tue 2/23/27	Mon 3/1/27	583,12,5
585	Install CRAC	5 days	Tue 3/2/27	Mon 3/8/27	584,11
586	Electrical and Ligh	5 days	Tue 3/2/27	Mon 3/8/27	584,10
587	Security	5 days	Tue 3/2/27	Mon 3/8/27	584,10
588	Fire suppression, F	3 days	Tue 3/2/27	Thu 3/4/27	584,8
589	Telecom racks and	3 days	Tue 3/2/27	Thu 3/4/27	584,9
590	Cable Tray and ra	3 days	Fri 3/5/27	Tue 3/9/27	589
591	New cable from ou	5 days	Wed 3/10/27	Tue 3/16/27	590
592	New outlet conne	3 days	Wed 3/17/27	Fri 3/19/27	591
593	Land cable on swi	2 days	Mon 3/22/27	Tue 3/23/27	592
594	Test new telecom	2 days	Wed 3/24/27	Thu 3/25/27	593
595	DOC	1 day	Fri 3/26/27	Fri 3/26/27	594
596	Demo old cable	3 days	Fri 3/26/27	Tue 3/30/27	594
597	Clean and punch	3 days	Wed 3/31/27	Fri 4/2/27	596
598	**Building 203 - TR315**	**215 days**	**Mon 4/5/27**	**Fri 1/28/28**	
599	ICRA	2 days	Mon 4/5/27	Tue 4/6/27	597
600	Abatement	3 days	Wed 4/7/27	Fri 4/9/27	599
601	Demolition	3 days	Mon 4/12/27	Wed 4/14/27	600
602	New walls, floo	5 days	Thu 4/15/27	Wed 4/21/27	601,12,5
603	Install CRAC	5 days	Thu 4/22/27	Wed 4/28/27	602,11
604	Electrical and L	5 days	Thu 4/22/27	Wed 4/28/27	602,10
605	Security	5 days	Thu 4/22/27	Wed 4/28/27	602,10
606	Fire suppressio	3 days	Thu 4/22/27	Mon 4/26/27	602,8
607	Telecom racks	3 days	Thu 4/22/27	Mon 4/26/27	602,9
608	Cable Tray and	3 days	Tue 4/27/27	Thu 4/29/27	607
609	New cable from	5 days	Fri 4/30/27	Thu 5/6/27	608
610	New outlet con	3 days	Fri 5/7/27	Tue 5/11/27	609
611	Land cable on s	2 days	Wed 5/12/27	Thu 5/13/27	610
612	Test new telecom	2 days	Fri 5/14/27	Mon 5/17/27	611
613	DOC	1 day	Tue 5/18/27	Tue 5/18/27	612
614	Demo old cable	3 days	Tue 5/18/27	Thu 5/20/27	612
615	Clean and punc	3 days	Fri 5/21/27	Tue 5/25/27	614
616	**Building 240 - 137**	**days**	**Wed 5/26/27**	**Thu 7/15/27**	
617	ICRA	2 days	Wed 5/26/27	Thu 5/27/27	615
618	Abatement	3 days	Fri 5/28/27	Tue 6/1/27	617
619	Demolition	3 days	Wed 6/2/27	Fri 6/4/27	618
620	New walls, fl	5 days	Mon 6/7/27	Fri 6/11/27	619,12,5
621	Install CRAC	5 days	Mon 6/14/27	Fri 6/18/27	620,11
622	Electrical an	5 days	Mon 6/14/27	Fri 6/18/27	620,10
623	Security	5 days	Mon 6/14/27	Fri 6/18/27	620,10
624	Fire suppres	3 days	Mon 6/14/27	Wed 6/16/27	620,8
625	Telecom rac	3 days	Mon 6/14/27	Wed 6/16/27	620,9
626	Cable Tray a	3 days	Thu 6/17/27	Mon 6/21/27	625
627	New cable fr	5 days	Tue 6/22/27	Mon 6/28/27	626
628	New outlet c	3 days	Tue 6/29/27	Thu 7/1/27	627
629	Land cable o	2 days	Fri 7/2/27	Mon 7/5/27	628
630	Test new telecom	2 days	Tue 7/6/27	Wed 7/7/27	629
631	DOC	3 days	Thu 7/8/27	Mon 7/12/27	630
632	Demo old ca	3 days	Thu 7/8/27	Mon 7/12/27	630
633	Clean and p	3 days	Tue 7/13/27	Thu 7/15/27	632
634	**Building 248 - 1141**	**days**	**Fri 7/16/27**	**Fri 1/28/28**	
635	ICRA	2 days	Fri 7/16/27	Mon 7/18/27	633
636	Abatement	3 days	Tue 7/20/27	Thu 7/22/27	635
637	Demolition	3 days	Fri 7/23/27	Tue 7/27/27	636
638	New walls, fl	5 days	Wed 7/28/27	Tue 8/3/27	637,12,5
639	Install CRAC	5 days	Wed 8/4/27	Tue 8/10/27	638,11
640	Electrical an	5 days	Wed 8/4/27	Tue 8/10/27	638,10
641	Security	5 days	Wed 8/4/27	Tue 8/10/27	638,10
642	Fire suppres	3 days	Wed 8/4/27	Fri 8/6/27	638,8
643	Telecom rac	3 days	Wed 8/4/27	Fri 8/6/27	638,9
644	Cable Tray a	3 days	Mon 8/9/27	Wed 8/11/27	643
645	New cable fr	5 days	Thu 8/12/27	Wed 8/18/27	644
646	New outlet c	3 days	Thu 8/19/27	Mon 8/23/27	645
647	Land cable o	2 days	Tue 8/24/27	Wed 8/25/27	646
648	Test new telecom	2 days	Thu 8/26/27	Fri 8/27/27	647
649	DOC	1 day	Mon 8/30/27	Mon 8/30/27	648
650	Demo old ca	3 days	Mon 8/30/27	Wed 9/1/27	648
651	Clean and p	3 days	Thu 9/2/27	Mon 9/6/27	650
652	**Building 248**	**104 days**	**Tue 9/7/27**	**Fri 1/28/28**	
653	ICRA	2 days	Tue 9/7/27	Wed 9/8/27	651
654	Abatemen	3 days	Thu 9/9/27	Mon 9/13/27	653
655	Demolitio	3 days	Tue 9/14/27	Thu 9/16/27	654
656	New wall	5 days	Fri 9/17/27	Thu 9/23/27	655,12,5
657	Install Ch	5 days	Fri 9/24/27	Thu 9/30/27	656,11
658	Electrical	5 days	Fri 9/24/27	Thu 9/30/27	656,10
659	Security	5 days	Fri 9/24/27	Thu 9/30/27	656,10
660	Fire suppr	3 days	Fri 9/24/27	Tue 9/28/27	656,8
661	Telecom r	3 days	Fri 9/24/27	Tue 9/28/27	656,9
662	Cable Tra	3 days	Wed 9/29/27	Fri 10/1/27	661
663	New cable	5 days	Mon 10/4/27	Fri 10/8/27	662
664	New outl	3 days	Mon 10/11/27	Wed 10/13/27	663
665	Land cabl	2 days	Thu 10/14/27	Fri 10/15/27	664
666	Test new telecom	2 days	Mon 10/18/27	Tue 10/19/27	665
667	DOC	1 day	Wed 10/20/27	Wed 10/20/27	666
668	Demo old	3 days	Wed 10/20/27	Fri 10/22/27	666
669	Clean and	3 days	Mon 10/25/27	Wed 10/27/27	668
670	**Building 267**	**days**	**Thu 10/28/27**	**Fri 1/28/28**	
671	ICRA	2 days	Thu 10/28/27	Fri 10/29/27	669
672	Abatem	3 days	Mon 11/1/27	Wed 11/3/27	671
673	Demoli	3 days	Thu 11/4/27	Mon 11/8/27	672
674	New w	5 days	Tue 11/9/27	Mon 11/15/27	673,12,5
675	Install	5 days	Tue 11/16/27	Mon 11/22/27	674,11
676	Electric	5 days	Tue 11/16/27	Mon 11/22/27	674,10
677	Securit	5 days	Tue 11/16/27	Mon 11/22/27	674,10
678	Fire su	3 days	Tue 11/16/27	Thu 11/18/27	674,8
679	Telece racks	3 days	Tue 11/16/27	Thu 11/18/27	674,9
680	Cable T	3 days	Fri 11/19/27	Tue 11/23/27	679
681	New cable	5 days	Wed 11/24/27	Tue 11/30/27	680
682	New ou	3 days	Wed 12/1/27	Fri 12/3/27	681
683	Land c	2 days	Mon 12/6/27	Tue 12/7/27	682
684	Test new	2 days	Wed 12/8/27	Thu 12/9/27	683
685	DOC	1 day	Fri 12/10/27	Fri 12/10/27	684
686	Demo	3 days	Fri 12/10/27	Tue 12/14/27	684
687	Clean	3 days	Wed 12/15/27	Fri 12/17/27	686
688	**Buildin**	**30 days**	**Mon 12/20/27**	**Fri 1/28/28**	
689	ICRA	2 days	Mon 12/20/27	Tue 12/21/27	687
690	Aba	2 days	Wed 12/22/27	Thu 12/23/27	689
691	Dem	2 days	Fri 12/24/27	Mon 12/27/27	690
692	New	5 days	Tue 12/28/27	Mon 1/3/28	691,12,5
693	Insta	4 days	Tue 1/4/28	Fri 1/7/28	692,11
694	Elec	4 days	Tue 1/4/28	Fri 1/7/28	692,10
695	Sec	3 days	Tue 1/4/28	Thu 1/6/28	692,10
696	Fire	2 days	Tue 1/4/28	Wed 1/5/28	692,8
697	Tele rack	2 days	Tue 1/4/28	Wed 1/5/28	692,9
698	Cab	3 days	Thu 1/6/28	Mon 1/10/28	697
699	New cabl	4 days	Tue 1/11/28	Fri 1/14/28	698
700	New	3 days	Mon 1/17/28	Wed 1/19/28	699
701	Lan	2 days	Thu 1/20/28	Fri 1/21/28	700
702	Test new	2 days	Mon 1/24/28	Tue 1/25/28	701
703	DOC	1 day	Wed 1/26/28	Wed 1/26/28	702
704	Den	2 days	Wed 1/26/28	Thu 1/27/28	702
705	Clea	1 day	Fri 1/28/28	Fri 1/28/28	704
706	**Closeout**	**3 days**	**Mon 1/31/28**	**Wed 2/2/28**	**328,346,364,3**
707	O&M	3 days	Mon 1/31/28	Wed 2/2/28	328,346,364,3
708	As-Builts	3 days	Mon 1/31/28	Wed 2/2/28	328,346,364,3
709	Training	3 days	Mon 1/31/28	Wed 2/2/28	328,346,364,3
710	Warranty	3 days	Mon 1/31/28	Wed 2/2/28	328,346,364,3
