A. This project will renovate approximately 2,500 BGSF in the existing Kitchen.

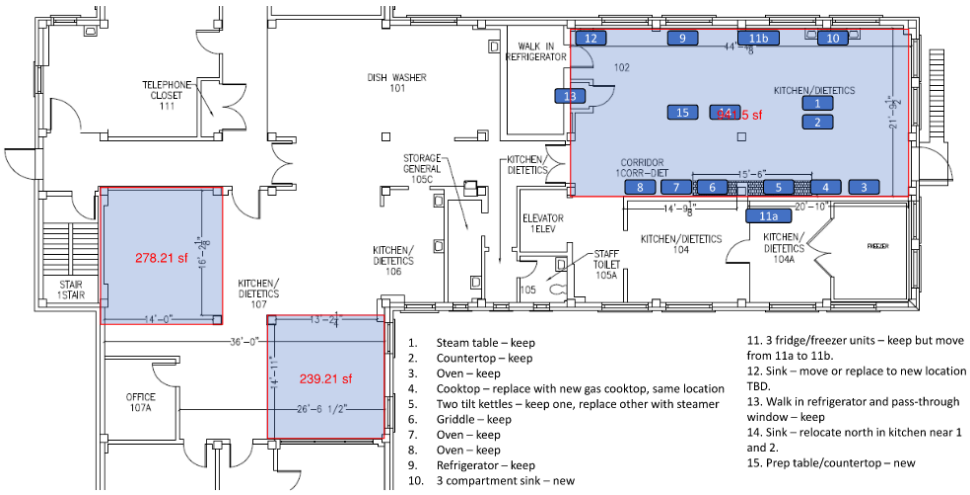

B. Project phasing will be utilized in this project to allow the NFS department to continue day to day operations with minimum hinderance. Refer to drawings in depth information.

1) Phasing

- Phase 1
  - Partial demolition of entry area into hot production/tray assembly line.
- Phase 2
  - Demolition and renovation of remaining hot production/tray assembly line and cold food prep.
- Phase 3
  - Demolition and renovation of Administration area.

SCHEDULE

The project is planned to be submitted to the VA for review and concurrence as follows:

VAMC WICHITA KS - Prepare Site for Choice Dining - VA Project #589A7-23-305

PROJECT DESIGN SCHEDULE

Project Start Date: 9/28/2023

Revised Schedule: 4/30/2024

Milestone	Progress	Start	Days for Review / Design	Review / Milestone Date	Days into Project
NTP DATE		**9/28/2023**			
Kick-Off Meeting	100%	9/27/2023	0	9/27/2023	0
SD Submittal	100%	9/28/2023	32	10/30/2023	32
SD Submittal Review	100%	10/30/2023	14	11/13/2023	46
DD 30% Submittal	100%	11/13/2023	21	12/4/2023	67
DD 30% Submittal Review	100%	12/4/2023	14	12/18/2023	81
DD 60% Submittal	100%	12/18/2023	28	1/15/2024	109
DD 60% Submittal Review	100%	1/15/2024	23	2/7/2024	132
CD 95% Contract Documents	100%	2/7/2024	21	2/28/2024	153
CD 95% Contract Documents Review	100%	2/28/2024	7	3/6/2024	160
DELAY-FIRE & LIFE SAFETY REVIEW	100%	3/6/2024		4/30/2024	
CD 100% Contract Documents	75%	5/1/2024	7	5/8/2024	223
CD 100% Contract Documents Review	0%	5/8/2024	7	5/15/2024	230
Final Document Delivery to VA	0%	5/15/2024	7	5/22/2024	237
