| ID | Task Mode | Task Name | Duration | Start | Finish | Predecessors |
|---|---|---|---|---|---|---|
| 1 | | **General** | **704 days** | **Tue 1/1/19** | **Fri 9/10/21** | |
| 3 | | stand up IPT | 60 days | Tue 1/1/19 | Mon 3/25/19 | 2SS-60 days |
| 2 | | Award | 1 day | Tue 3/26/19 | Tue 3/26/19 | |
| 4 | | Schedule 1st IPT meeting | 5 days | Wed 3/27/19 | Tue 4/2/19 | 2 |
| 6 | | Assign COR (leases) | 1 day | Wed 3/27/19 | Wed 3/27/19 | 2 |
| 7 | | Identify anticipated activation date | 1 day | Wed 3/27/19 | Wed 3/27/19 | 2 |
| 5 | | Inform IPT of high level action plan & timelines | 1 day | Wed 5/1/19 | Wed 5/1/19 | 8SS |
| 8 | | 1st Activation meeting | 1 day | Wed 5/1/19 | Wed 5/1/19 | 4FS+20 days |
| 10 | | **Charters and Plans** | **23 days** | **Wed 5/1/19** | **Fri 5/31/19** | |
| 11 | | Develop a Risk Management Plan | 23 days | Wed 5/1/19 | Fri 5/31/19 | 8SS |
| 12 | | Develop a Schedule Management Pl | 23 days | Wed 5/1/19 | Fri 5/31/19 | 8SS |
| 13 | | Develop Project Charter | 23 days | Wed 5/1/19 | Fri 5/31/19 | 8SS |
| 9 | | **1st patient day** | 1 day | Fri 9/10/21 | Fri 9/10/21 | 17FS+130 days |
| 44 | | **Acquisition** | **587 days?** | **Wed 6/12/19** | **Thu 9/9/21** | |
| 45 | | Develop Acquisition Plan | 30 days | Wed 6/12/19 | Tue 7/23/19 | 8SS+30 days |
| 55 | | **acquisition - Interior Design** | **516 days?** | **Thu 7/4/19** | **Thu 6/24/21** | |
| 60 | | **Furniture** | **463 days** | **Thu 7/4/19** | **Mon 4/12/21** | |
| 61 | | Create Furniture Plan | 180 days | Thu 7/4/19 | Wed 3/11/20 | 16FS-180 days |
| 62 | | Update SharePoint site for Furniture status - ongoing | 15 days | Thu 3/12/20 | Wed 4/1/20 | 61 |
| 63 | | Order furniture | 1 day | Thu 8/13/20 | Thu 8/13/20 | 17FF-150 days |
| 64 | | Deliver & Install Furniture | 22 days | Fri 3/12/21 | Mon 4/12/21 | 63FS+150 days |
| 65 | | **Artwork** | **336 days** | **Thu 3/12/20** | **Thu 6/24/21** | |
| 66 | | Create Artwork Plan | 110 days | Thu 3/12/20 | Wed 8/12/20 | 16 |

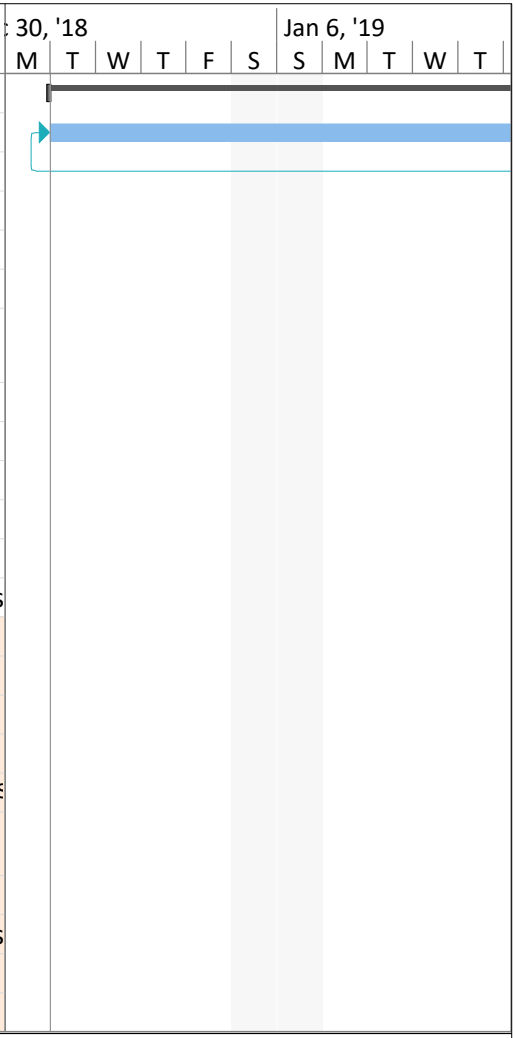


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

| ID | Task Mode | Task Name | Duration | Start | Finish | Predecessors |
|---|---|---|---|---|---|---|
| 67 | | Approval of Artwork plan by Direc | 20 days | Thu 8/13/20 | Wed 9/9/20 | 66 |
| 68 | | Artwork Plan approval from VISN | 20 days | Thu 9/10/20 | Wed 10/7/20 | 67 |
| 69 | | Update SharePoint site for Artwork status - ongoing | 15 days | Thu 10/8/20 | Wed 10/28/20 | 68 |
| 70 | | Order artwork | 1 day | Thu 10/29/20 | Thu 10/29/20 | 69 |
| 71 | | Deliver & Install Artwork | 120 days | Fri 1/8/21 | Thu 6/24/21 | 70FS+50 days |
| 56 | | office trash can acquisition | 30 days | Fri 1/29/21 | Thu 3/11/21 | 17FF |
| 58 | | clock acquisition | 30 days | Fri 1/29/21 | Thu 3/11/21 | 17FF |
| 57 | | deliver office trashcans to appropriate locations | 1 day? | Fri 3/12/21 | Fri 3/12/21 | 56 |
| 59 | | delivery and hang-up of clocks | 1 day? | Fri 3/12/21 | Fri 3/12/21 | 58 |
| 46 | | Update SharePoint - ongoing | 400 days | Mon 12/16/1 | Fri 6/25/21 | |
| 47 | | **Service Contracts** | **324 days** | **Mon 12/16/1** | **Thu 3/11/21** | |
| 48 | | Add list of contracts in support of Activation and operation, that need to be modified/awarded, to | 90 days | Mon 12/16/19 | Fri 4/17/20 | |
| 49 | | complete contracting activities to add service support | 90 days | Fri 11/6/20 | Thu 3/11/21 | 17FF,48 |
| 72 | | **All Acquisitions & Contents** | **321 days** | **Thu 12/19/19** | **Thu 3/11/21** | |
| 75 | | Confirm Acquisitions & contents | 60 days | Thu 12/19/19 | Wed 3/11/20 | 16FF |
| 76 | | acquisition of all other items | 180 days | Fri 7/3/20 | Thu 3/11/21 | 17FF |
| 73 | | shredder can acquisition | 30 days | Fri 1/29/21 | Thu 3/11/21 | 17FF |
| 74 | | step-on, large trash can acquisition | 30 days | Fri 1/29/21 | Thu 3/11/21 | 17FF |
| 50 | | **Deliveries** | **24 days?** | **Mon 2/15/21** | **Thu 3/18/21** | |

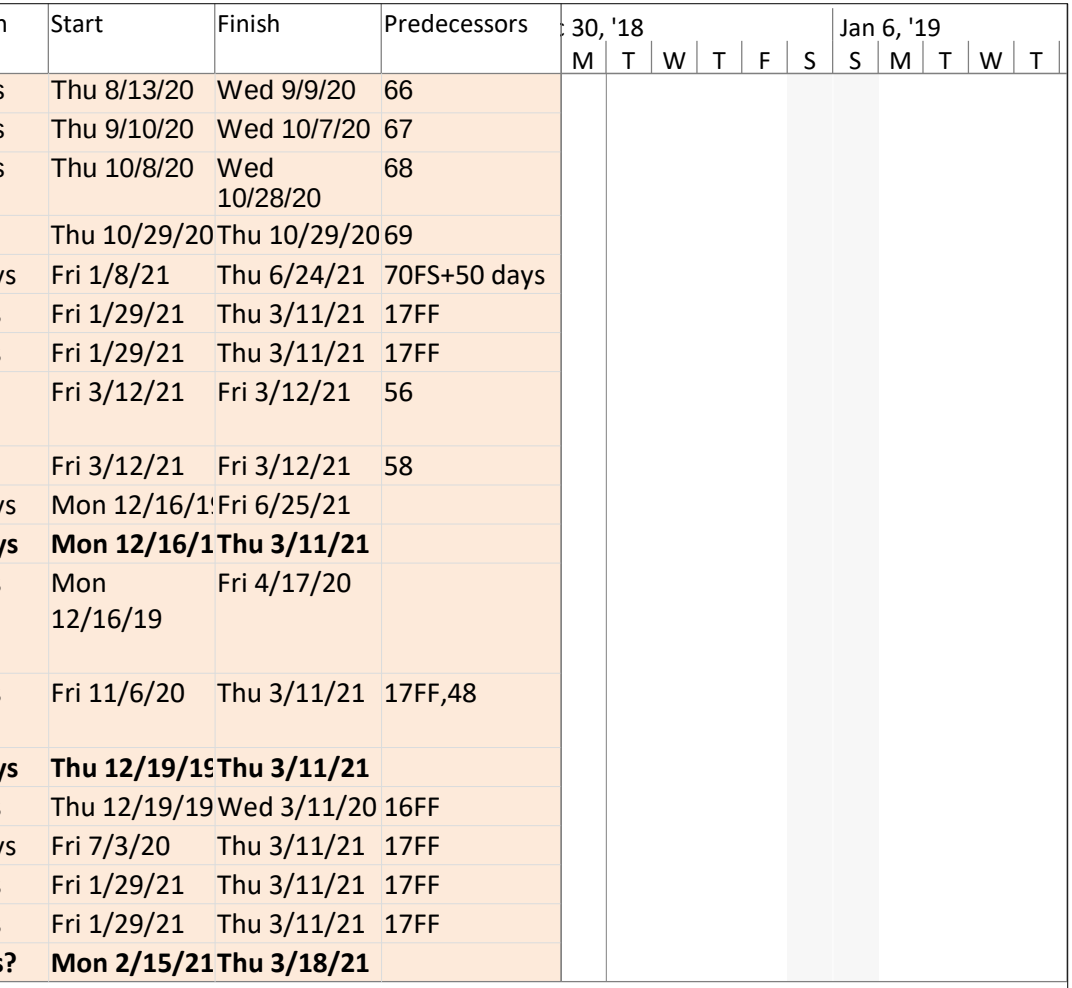


Project: Project WBS - Schedule
Date: Wed 2/24/21

Task
Split
Milestone
Summary
Project Summary
External Tasks
External Milestone
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
Deadline
Progress
Manual Progress

| ID | Task Mode | Task Name | Duration | Start | Finish | Predecessors |
|---|---|---|---|---|---|---|
| 53 | | Logistics to assign someone to meet deliveries and bring to assigned location | 20 days | Mon 2/15/21 | Fri 3/12/21 | 51FF |
| 51 | | deliver step-on, large trashcans to appropriate locations | 1 day? | Fri 3/12/21 | Fri 3/12/21 | 74 |
| 52 | | delivery of shredder cans | 1 day? | Fri 3/12/21 | Fri 3/12/21 | 73 |
| 54 | | Place Code Carts | 5 days | Fri 3/12/21 | Thu 3/18/21 | 17 |
| 77 | | **Starting Supplies** | **126 days** | **Fri 3/12/21** | **Fri 9/3/21** | |
| 78 | | Identify starting supply lists | 15 days | Fri 3/12/21 | Thu 4/1/21 | 17 |
| 79 | | Add Starting supply list to Acquisition plan | 15 days | Fri 4/2/21 | Thu 4/22/21 | 78 |
| 80 | | Order starting supplies | 10 days | Mon 7/19/21 | Fri 7/30/21 | 9FS-40 days |
| 81 | | Deliver starting supply list to appropriate spaces | 5 days | Mon 8/30/21 | Fri 9/3/21 | 9FF-5 days |
| 82 | | **Canteen** | **130 days?** | **Fri 3/12/21** | **Thu 9/9/21** | |
| 83 | | Canteen outfitting complete | 20 days | Fri 3/12/21 | Thu 4/8/21 | 17 |
| 84 | | Canteen stocked | 1 day? | Thu 9/9/21 | Thu 9/9/21 | 9FS-2 days |
| 85 | | **Installs** | **20 days** | **Mon 5/10/21** | **Fri 6/4/21** | |
| 86 | | Install checkpoint monitors | 5 days | Mon 5/10/21 | Fri 5/14/21 | 9FS-90 days |
| 87 | | install message boards | 5 days | Mon 5/10/21 | Fri 5/14/21 | 9FS-90 days |
| 88 | | Install phones | 15 days | Mon 5/10/21 | Fri 5/28/21 | 9FS-90 days |
| 89 | | Install computers | 20 days | Mon 5/10/21 | Fri 6/4/21 | 9FS-90 days |
| 90 | | build pyxis | 15 days | Mon 5/10/21 | Fri 5/28/21 | 9FS-90 days |
| 115 | | **Move** | **587 days?** | **Wed 6/12/19** | **Thu 9/9/21** | |
| 116 | | Develop Move Management Plan | 30 days | Wed 6/12/19 | Tue 7/23/19 | 8SS+30 days |




Project: Project WBS - Schedule
Date: Wed 2/24/21

| ID | Task Mode | Task Name | Duration | Start | Finish | Predecessors |
|---|---|---|---|---|---|---|
| 132 | | complete packing of clinics at old site | 1 day? | Mon 12/16/1 | Mon 12/16/1 | |
| 117 | | Move plan data entry | 150 days | Fri 8/14/20 | Thu 3/11/21 | 17FS-150 days |
| 119 | | Lock down move plan | 1 day? | Fri 3/12/21 | Fri 3/12/21 | 17 |
| 118 | | Determine move schedule | 15 days | Mon 3/15/21 | Fri 4/2/21 | 119 |
| 120 | | Union Notification of move plan | 30 days | Mon 3/15/21 | Fri 4/23/21 | 119 |
| 121 | | phone extensions assigned | 15 days | Mon 3/15/21 | Fri 4/2/21 | 119 |
| 124 | | arrange for additional staff to help with moves and unpacking | 20 days | Mon 3/15/21 | Fri 4/9/21 | 119 |
| 125 | | Boxes to services for packing | 10 days | Mon 3/15/21 | Fri 3/26/21 | 119 |
| 131 | | Furniture tag in old spaces | 20 days | Mon 3/15/21 | Fri 4/9/21 | 119 |
| 122 | | Provide staff with phone extensions for new locations | 15 days | Mon 4/5/21 | Fri 4/23/21 | 121 |
| 123 | | submit work orders for moves - OI&T and FMS | 5 days | Mon 4/5/21 | Fri 4/9/21 | 118 |
| 126 | | Phone Transfers - department 1 | 1 day | Thu 9/9/21 | Thu 9/9/21 | 127FF |
| 127 | | Move depart 1 | 1 day? | Thu 9/9/21 | Thu 9/9/21 | 9FS-2 days |
| 128 | | Phone Transfers - department 2 | 1 day? | Thu 9/9/21 | Thu 9/9/21 | 129FF |
| 129 | | Move depart 2 | 1 day? | Thu 9/9/21 | Thu 9/9/21 | 9FS-2 days |
| 130 | | Phone Transfers - department 3 | 1 day? | Thu 9/9/21 | Thu 9/9/21 | 133FF |
| 133 | | Move depart 3 | 1 day? | Thu 9/9/21 | Thu 9/9/21 | 9FS-2 days |
| 134 | | **Communication** | **628 days?** | **Wed 6/12/19** | **Fri 11/5/21** | |
| 135 | | Develop Communication Management Plan | 30 days | Wed 6/12/19 | Tue 7/23/19 | 8SS+30 days |
| 136 | | Public Affairs announcements | 400 days | Mon 4/27/20 | Fri 11/5/21 | 135,9FF+40 da |

Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

| ID | Task Mode | Task Name | Duration | Start | Finish | Predecessors |
|---|---|---|---|---|---|---|
| 143 | | Joint Commission Compliance items | 30 days | Wed 4/28/21 | Tue 6/8/21 | 36FF |
| 138 | | determine items needed for ribbon cutting | 5 days | Fri 4/30/21 | Thu 5/6/21 | 137FS-90 days |
| 139 | | Put ribbon cutting acquisitions on the Acq plan | 1 day | Fri 5/7/21 | Fri 5/7/21 | 138 |
| 141 | | Update Acquisition plan with ribbon cutting item procurement data | 60 days? | Fri 6/11/21 | Thu 9/2/21 | 140FF |
| 142 | | send out ribbon cutting invitations | 5 days | Fri 6/11/21 | Thu 6/17/21 | 137FS-60 days |
| 140 | | procure items needed for ribbon cuttir | 59 days | Mon 6/14/21 | Thu 9/2/21 | 137FS-59 days |
| 137 | | Dedication/ribbon cutting date | 1 day? | Thu 9/2/21 | Thu 9/2/21 | 9FS-7 days |
| 14 | | Building Prep | 377 days? | Wed 3/11/20 | Thu 8/19/21 | |
| 15 | | **Construction** | **262 days** | **Wed 3/11/20** | **Thu 3/11/21** | |
| 16 | | 100 % CDs | 1 day | Wed 3/11/20 | Wed 3/11/20 | 2FS+250 days |
| 17 | | building acceptance | 1 day | Thu 3/11/21 | Thu 3/11/21 | 16FS+260 days |
| 18 | | **RSA** | **51 days** | **Thu 3/12/20** | **Thu 5/21/20** | |
| 19 | | RSA agreement drafted | 37 days | Thu 3/12/20 | Fri 5/1/20 | 16 |
| 20 | | RSA agreement routed for signature | 14 days | Mon 5/4/20 | Thu 5/21/20 | 19 |
| 37 | | **Parking** | **50 days** | **Thu 3/12/20** | **Wed 5/20/20** | |
| 38 | | Name parking lots | 40 days | Thu 3/12/20 | Wed 5/6/20 | 16 |
| 39 | | Identification of gov't vehicle and black placard parking | 10 days | Thu 5/7/20 | Wed 5/20/20 | 38 |
| 40 | | **Building Number** | **351 days** | **Thu 3/12/20** | **Thu 7/15/21** | |
| 41 | | Assign building number | 25 days | Thu 3/12/20 | Wed 4/15/20 | 16 |
| 42 | | Assign Division Number | 80 days | Fri 11/6/20 | Thu 2/25/21 | 17FS-90 days |

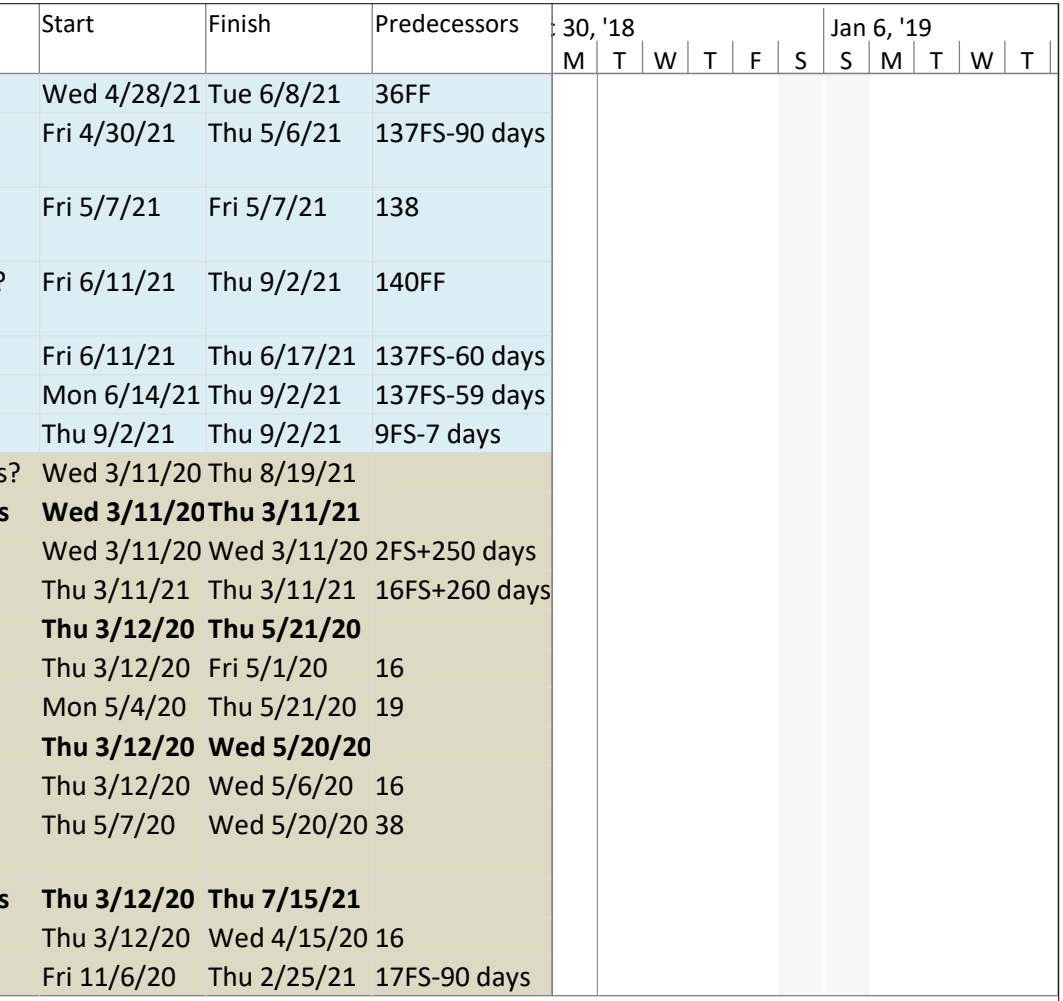


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

| ID | Task Mode | Task Name | Duration | Start | Finish | Predecessors |
|---|---|---|---|---|---|---|
| 43 | | Activate Division Number | 45 days | Fri 5/14/21 | Thu 7/15/21 | 17FS+45 days |
| 21 | | **Access** | **160 days** | **Fri 1/8/21** | **Thu 8/19/21** | |
| 22 | | Develop a master lock and key plan | 10 days | Fri 1/8/21 | Thu 1/21/21 | 17FS-45 days |
| 23 | | Develop a security plan for PIV acce | 10 days | Fri 1/8/21 | Thu 1/21/21 | 22SS |
| 24 | | work order for locks & keys | 2 days | Fri 2/5/21 | Mon 2/8/21 | 22FS+10 days |
| 25 | | PIV card readers programmed | 10 days | Fri 2/5/21 | Thu 2/18/21 | 22FS+10 days |
| 26 | | Keys made | 120 days | Tue 2/9/21 | Mon 7/26/21 | 24 |
| 28 | | staff notified of key pick-up | 1 day | Tue 7/27/21 | Tue 7/27/21 | 26 |
| 27 | | PIV card access provided to approved staff | 10 days | Fri 8/6/21 | Thu 8/19/21 | 25FS+120 days |
| 29 | | **Inspections, etc** | **78 days?** | **Fri 3/12/21** | **Tue 6/29/21** | |
| 30 | | Safety plans drafted & completed | 45 days | Fri 3/12/21 | Thu 5/13/21 | 17 |
| 32 | | Infection Control Inspections | 20 days | Fri 3/12/21 | Thu 4/8/21 | 17 |
| 33 | | Safety Inspection | 5 days | Fri 3/12/21 | Thu 3/18/21 | 17 |
| 34 | | Equipment Training | 20 days? | Fri 3/12/21 | Thu 4/8/21 | 17 |
| 35 | | EOC rounding | 1 day? | Fri 3/12/21 | Fri 3/12/21 | 17 |
| 36 | | Room Content Review Walk-thru | 2 days | Mon 6/7/21 | Tue 6/8/21 | 85,50 |
| 31 | | terminal clean | 15 days | Wed 6/9/21 | Tue 6/29/21 | 85,50,36 |
| 91 | | **Operations** | **465 days?** | **Mon 4/20/20** | **Fri 1/28/22** | |
| 92 | | **Develop Human Resource Plan** | **465 days?** | **Mon 4/20/20** | **Fri 1/28/22** | |
| 93 | | Staffing Call to impacted services | 20 days | Mon 4/20/20 | Fri 5/15/20 | 9FS-365 days |
| 94 | | Send packages to DAAS | 1 day? | Mon 5/18/20 | Mon 5/18/20 | 93 |
| 95 | | service meetings to discuss FTEE requests | 25 days | Mon 5/18/20 | Fri 6/19/20 | 93 |

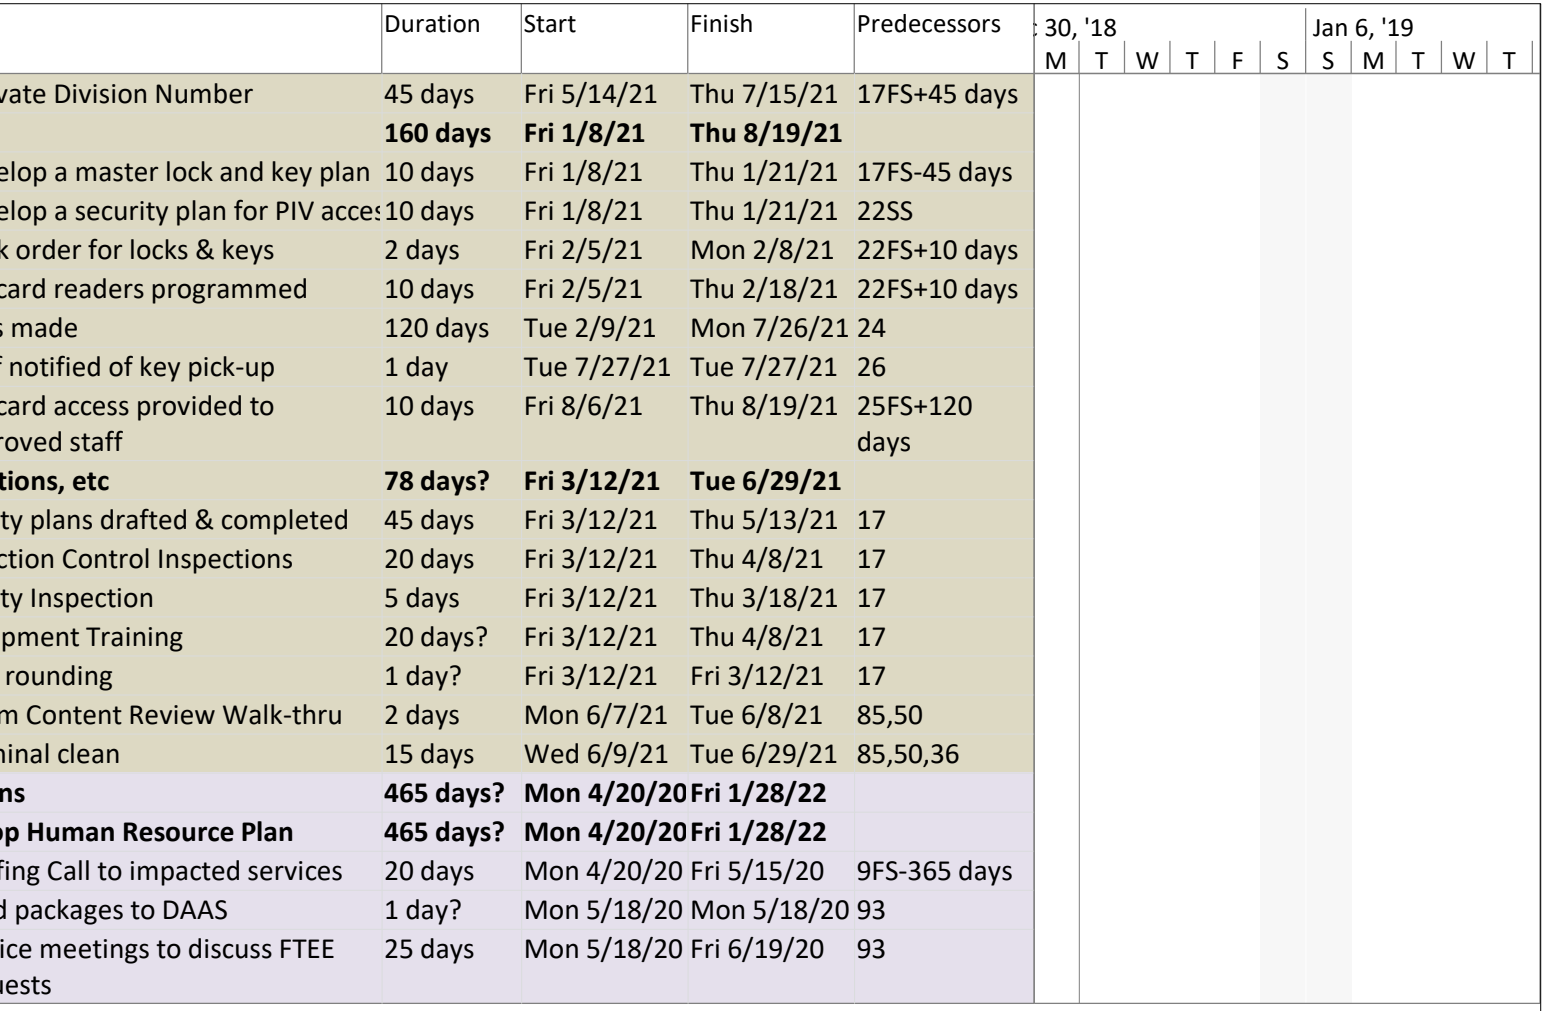


Project: Project WBS - Schedule
Date: Wed 2/24/21

Task
Split
Milestone
Summary
Project Summary
External Tasks
External Milestone
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
Deadline
Progress
Manual Progress

| ID | Task Mode | Task Name | Duration | Start | Finish | Predecessors |
|---|---|---|---|---|---|---|
| 96 | | Submit staffing requests to RMB | 90 days | Mon 6/22/20 | Fri 10/23/20 | 95 |
| 97 | | Update SharePoint FTEE tracker for approved positions | 7 days | Mon 10/26/20 | Tue 11/3/20 | 96 |
| 98 | | Update services of RMB results | 1 day | Mon 10/26/2 | Mon 10/26/2 | 96 |
| 99 | | Initiate FTEE recruitiment | 120 days? | Mon 2/15/21 | Fri 7/30/21 | 9FS-150 days |
| 100 | | Updates SharePoint FTEE tracker - ongoing | 250 days? | Mon 2/15/21 | Fri 1/28/22 | 9FS-150 days |
| 109 | | **Move Impacts** | **41 days** | **Mon 4/5/21** | **Mon 5/31/21** | |
| 110 | | request approval to close clinics (if needed) | 40 days | Mon 4/5/21 | Fri 5/28/21 | 118 |
| 111 | | Block clinics for move | 1 day | Mon 5/31/21 | Mon 5/31/21 | 110 |
| 112 | | **Day in the Life** | **58 days** | **Fri 6/4/21** | **Tue 8/24/21** | |
| 113 | | SimLearn Plan developed | 30 days | Fri 6/4/21 | Thu 7/15/21 | 17FS+60 days |
| 114 | | SimLearn exercises complete | 7 days | Mon 8/16/21 | Tue 8/24/21 | 9FS-20 days |
| 101 | | **CPRS** | **45 days** | **Mon 6/7/21** | **Fri 8/6/21** | |
| 102 | | Clinic changes provided to HAS and Informatics | 15 days | Mon 6/7/21 | Fri 6/25/21 | 9FS-70 days |
| 103 | | CPRS configuration changes comple | 15 days | Mon 6/28/21 | Fri 7/16/21 | 102 |
| 104 | | PRNS changes complete | 15 days | Mon 6/28/21 | Fri 7/16/21 | 102 |
| 105 | | Beds entered into VistA | 15 days | Mon 7/19/21 | Fri 8/6/21 | 103 |
| 106 | | clinic change letters sent to patients | 15 days | Mon 7/19/21 | Fri 8/6/21 | 103 |
| 107 | | send out pre-appointment letters | 15 days | Mon 7/19/21 | Fri 8/6/21 | 103 |
| 108 | | My HealtheVet e-mail follow-up | 15 days | Mon 7/19/21 | Fri 8/6/21 | 103 |
| 144 | | **Deactivation** | **53 days?** | **Fri 9/10/21** | **Tue 11/23/21** | **127,129,133** |

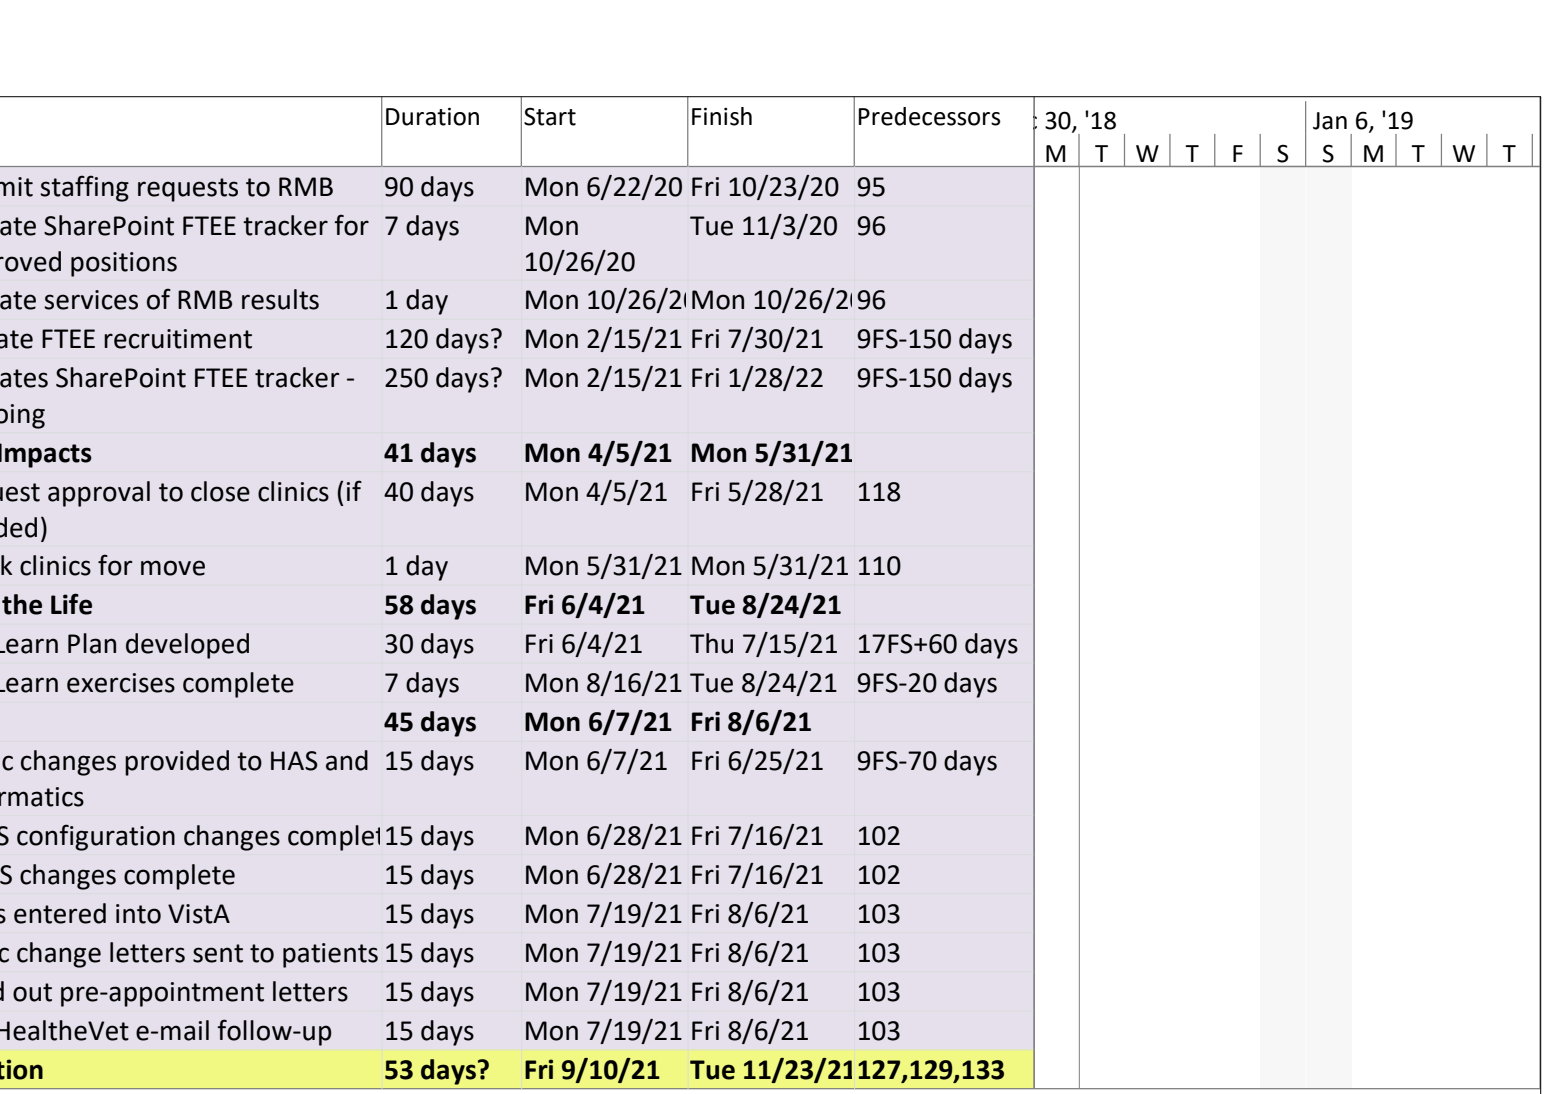


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

| ID | Task Mode | Task Name | Duration | Start | Finish | Predecessors |
|---|---|---|---|---|---|---|
| 145 | | team walks vacated space | 1 day | Fri 9/10/21 | Fri 9/10/21 | 127,129,133 |
| 146 | | Work order to change locks | 5 days | Fri 9/10/21 | Thu 9/16/21 | 127,129,133 |
| 147 | | Identify & tag remaining items | 25 days | Mon 9/13/21 | Fri 10/15/21 | 145 |
| 148 | | 2237s done to excess items | 1 day? | Mon 10/18/2 | Mon 10/18/2 | 147 |
| 149 | | Logistics to remove excessed items | 10 days | Tue 10/19/21 | Mon 11/1/21 | 148 |
| 150 | | EMS to remove trash | 5 days | Tue 11/2/21 | Mon 11/8/21 | 149 |
| 151 | | EMS to clean emptied space | 10 days | Tue 11/9/21 | Mon 11/22/2 | 150 |
| 152 | | return to space bank | 1 day | Tue 11/23/21 | Tue 11/23/21 | 151 |

Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | |
|---|---|---|---|
| Task | Inactive Task | Start-only | |
| Split | Inactive Milestone | Finish-only | |
| Milestone | Inactive Summary | Deadline | |
| Summary | Manual Task | Progress | |
| Project Summary | Duration-only | Manual Progress | |
| External Tasks | Manual Summary Rollup | | |
| External Milestone | Manual Summary | | |

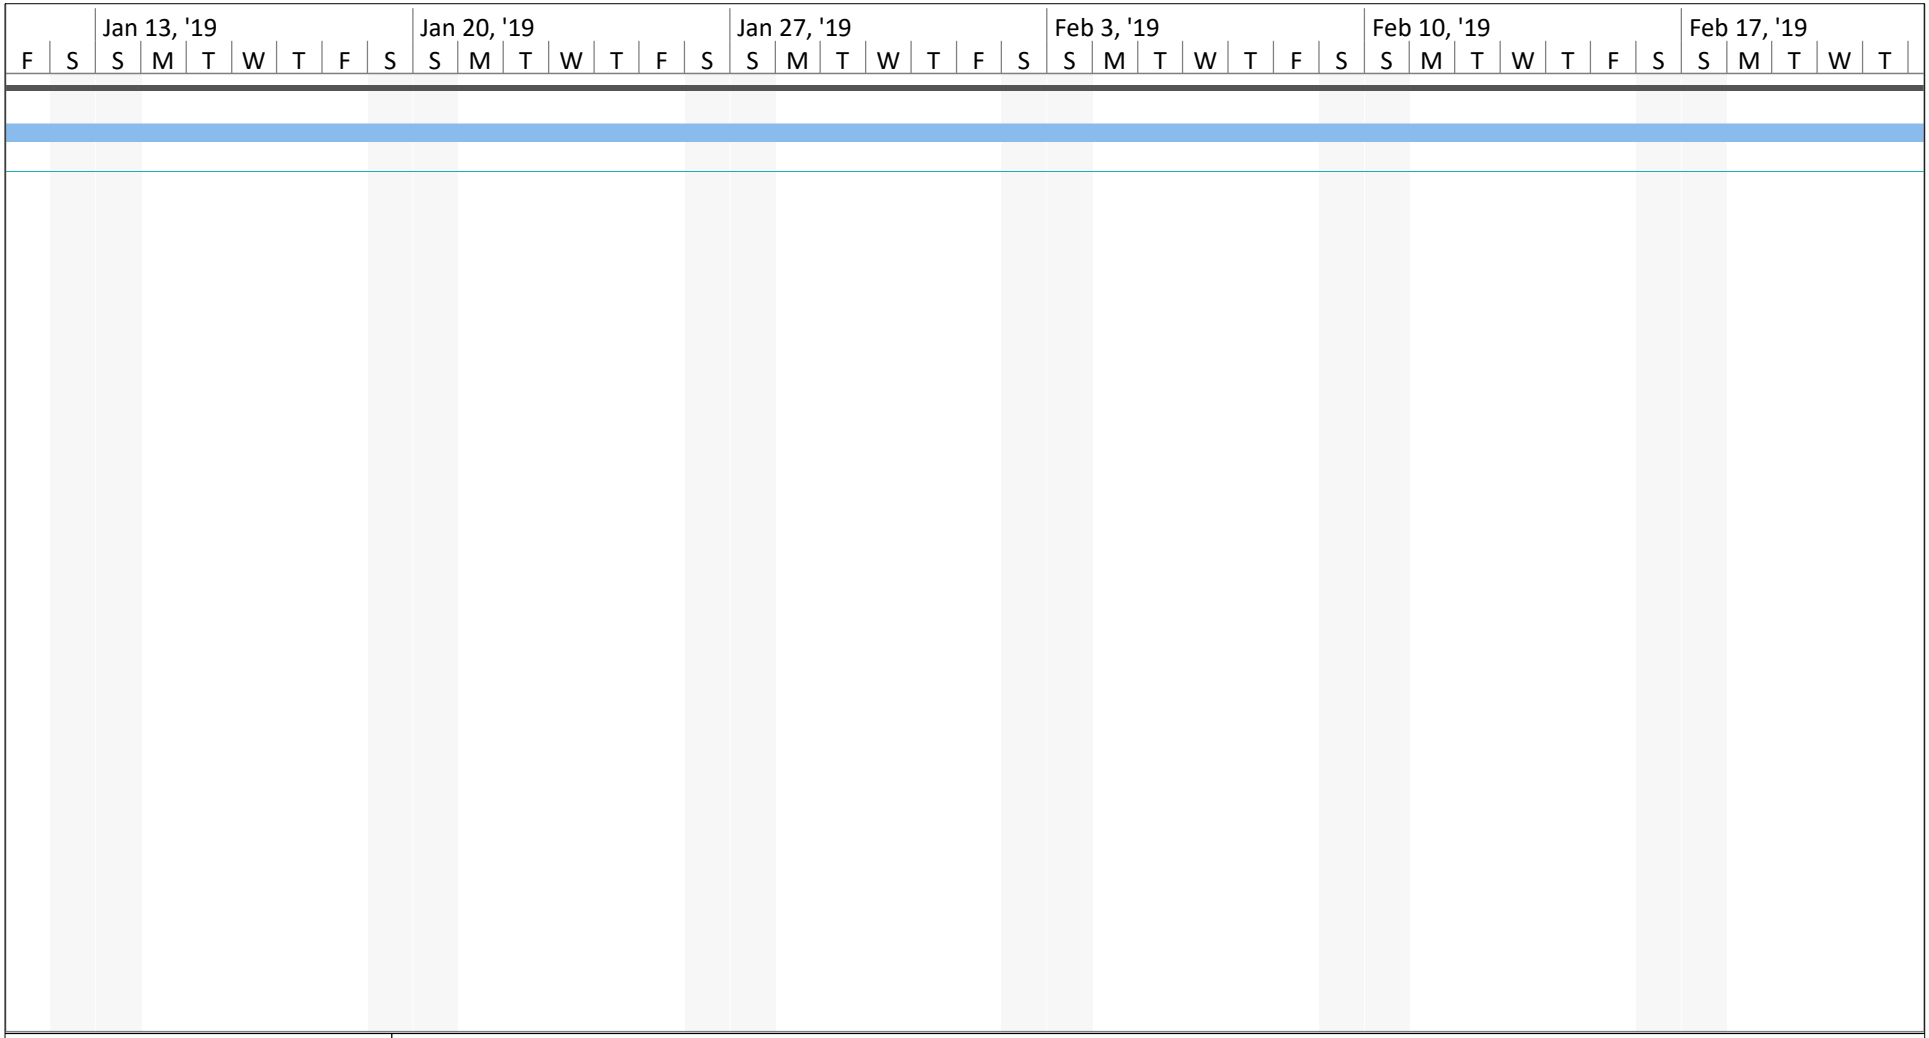


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

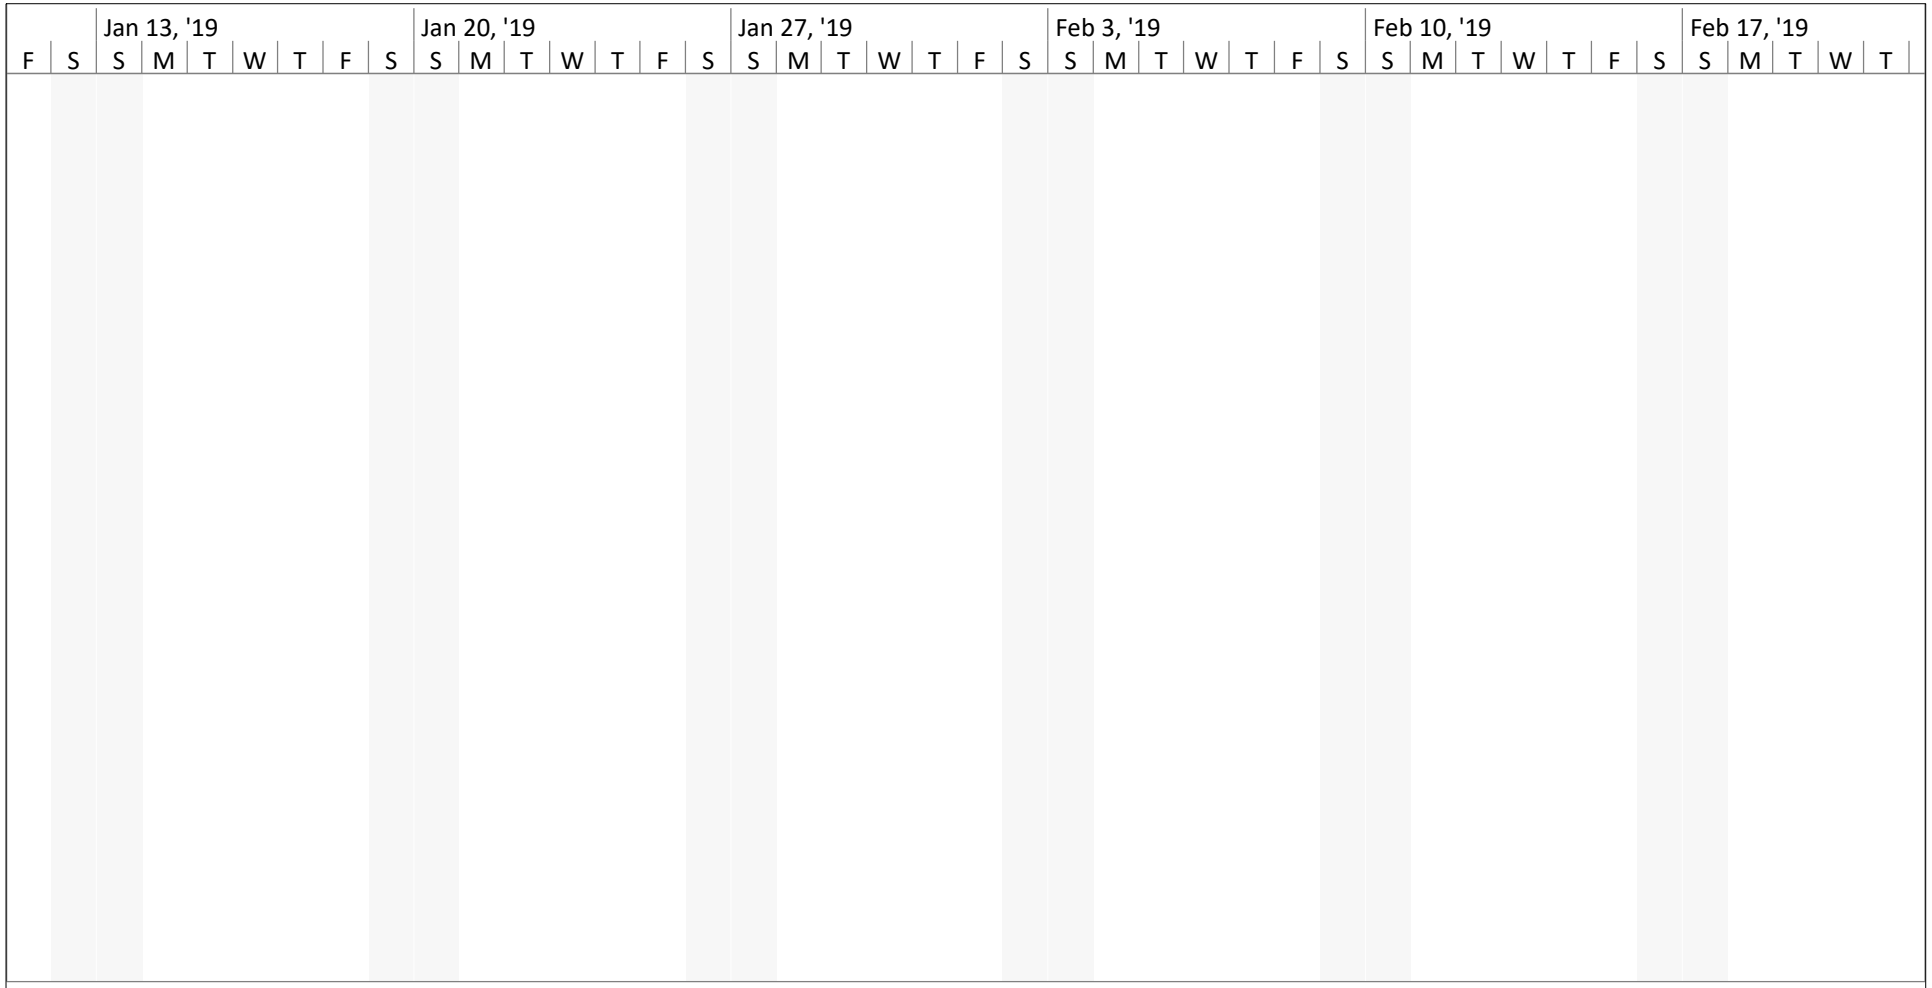


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

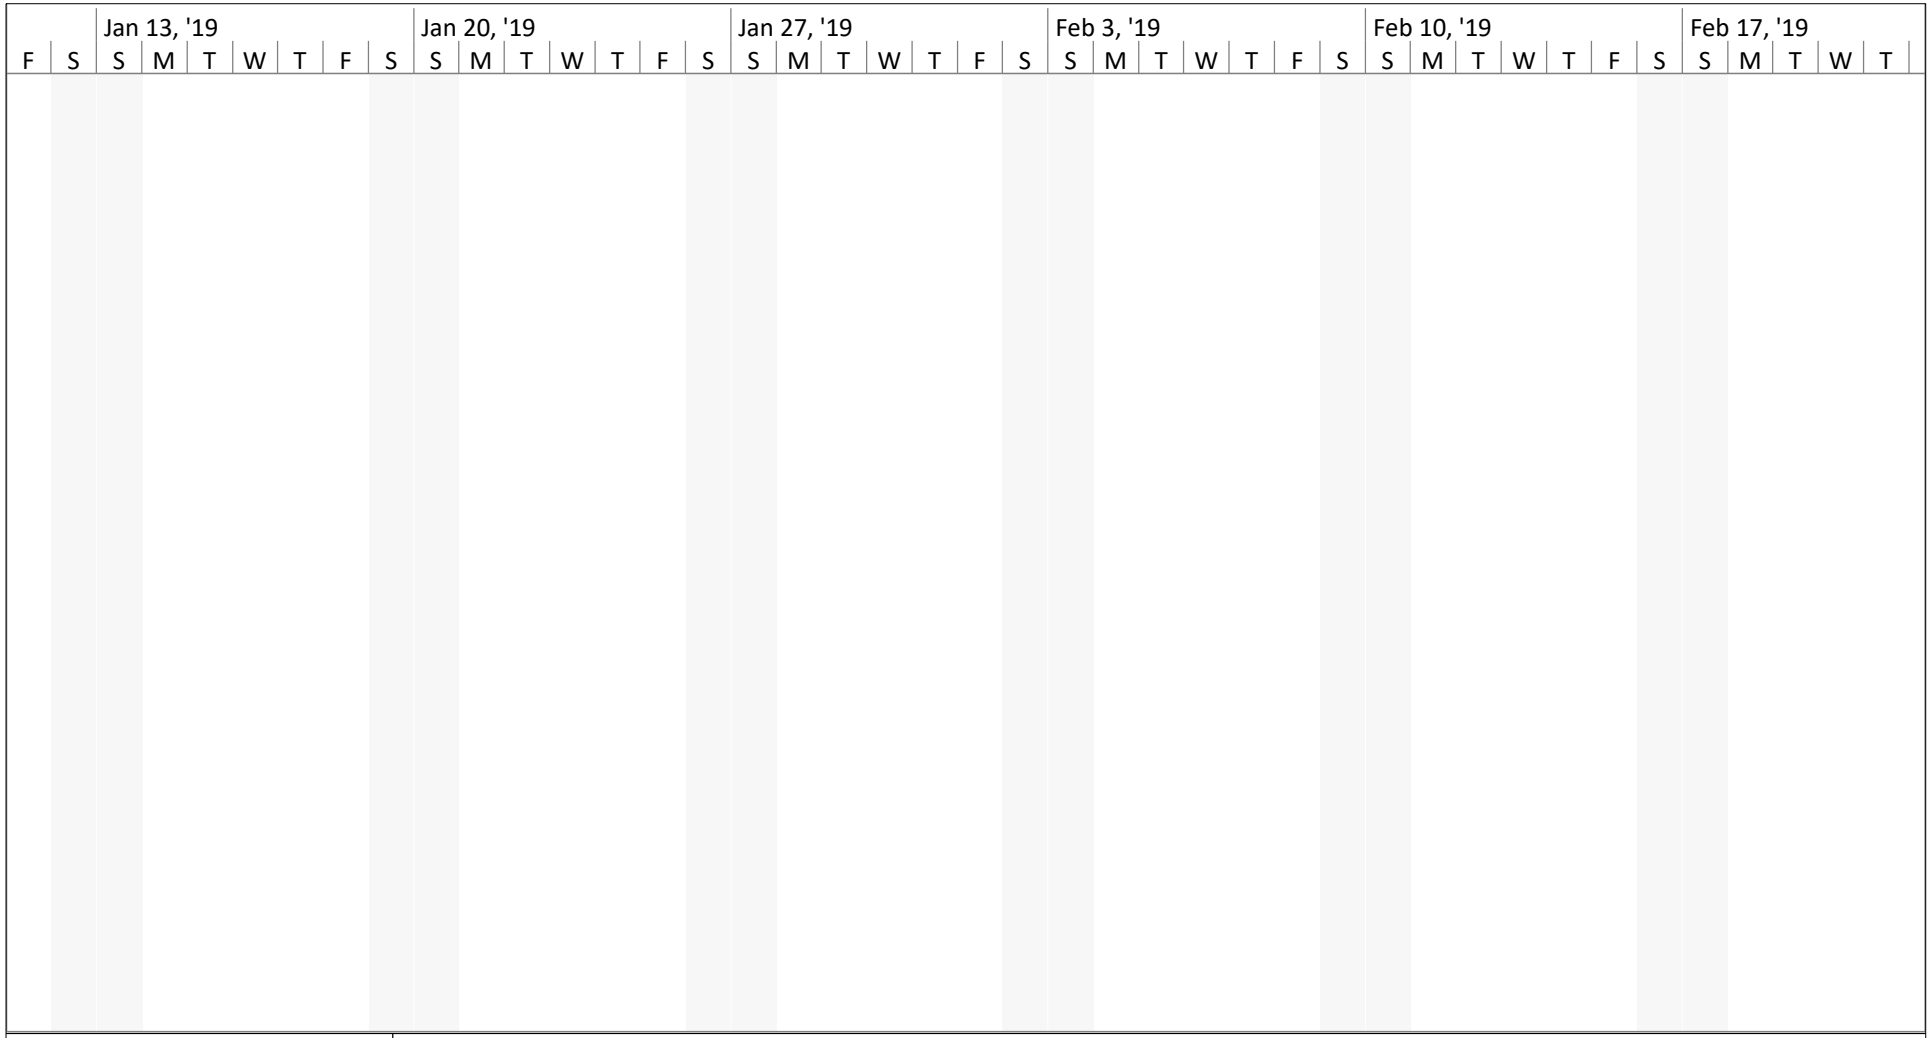


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

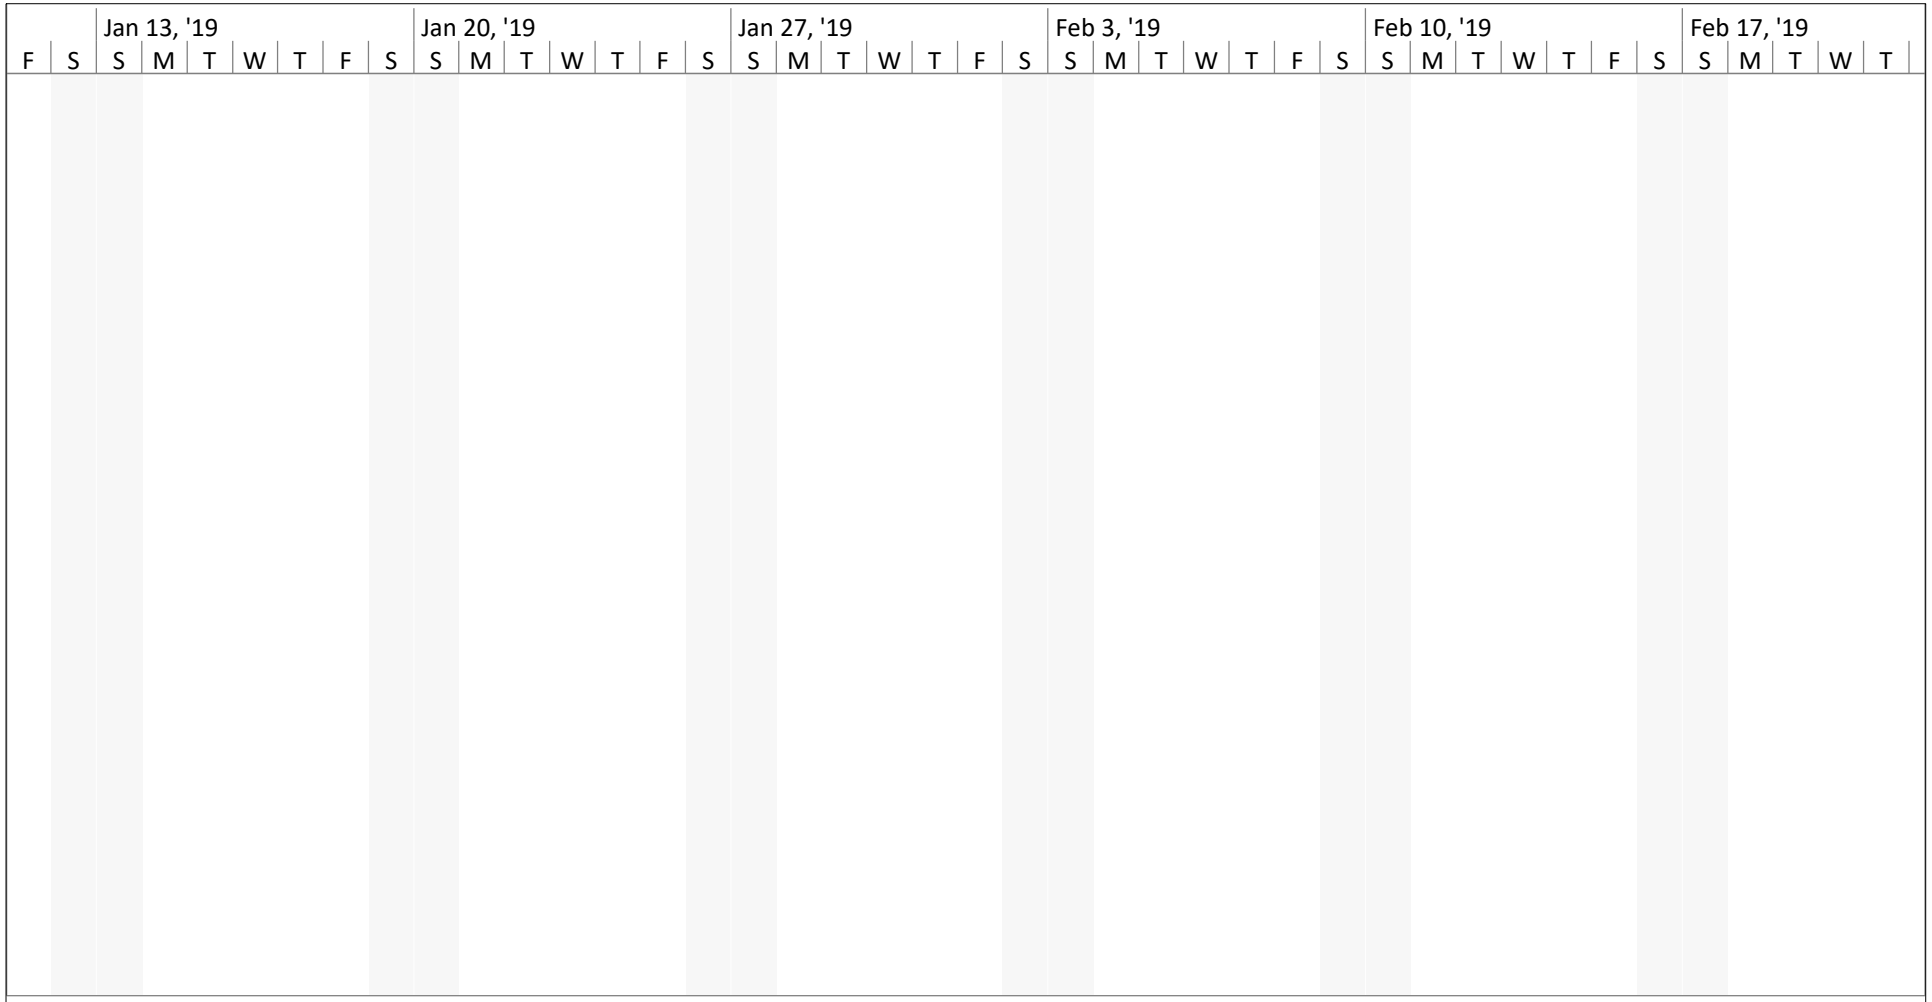


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

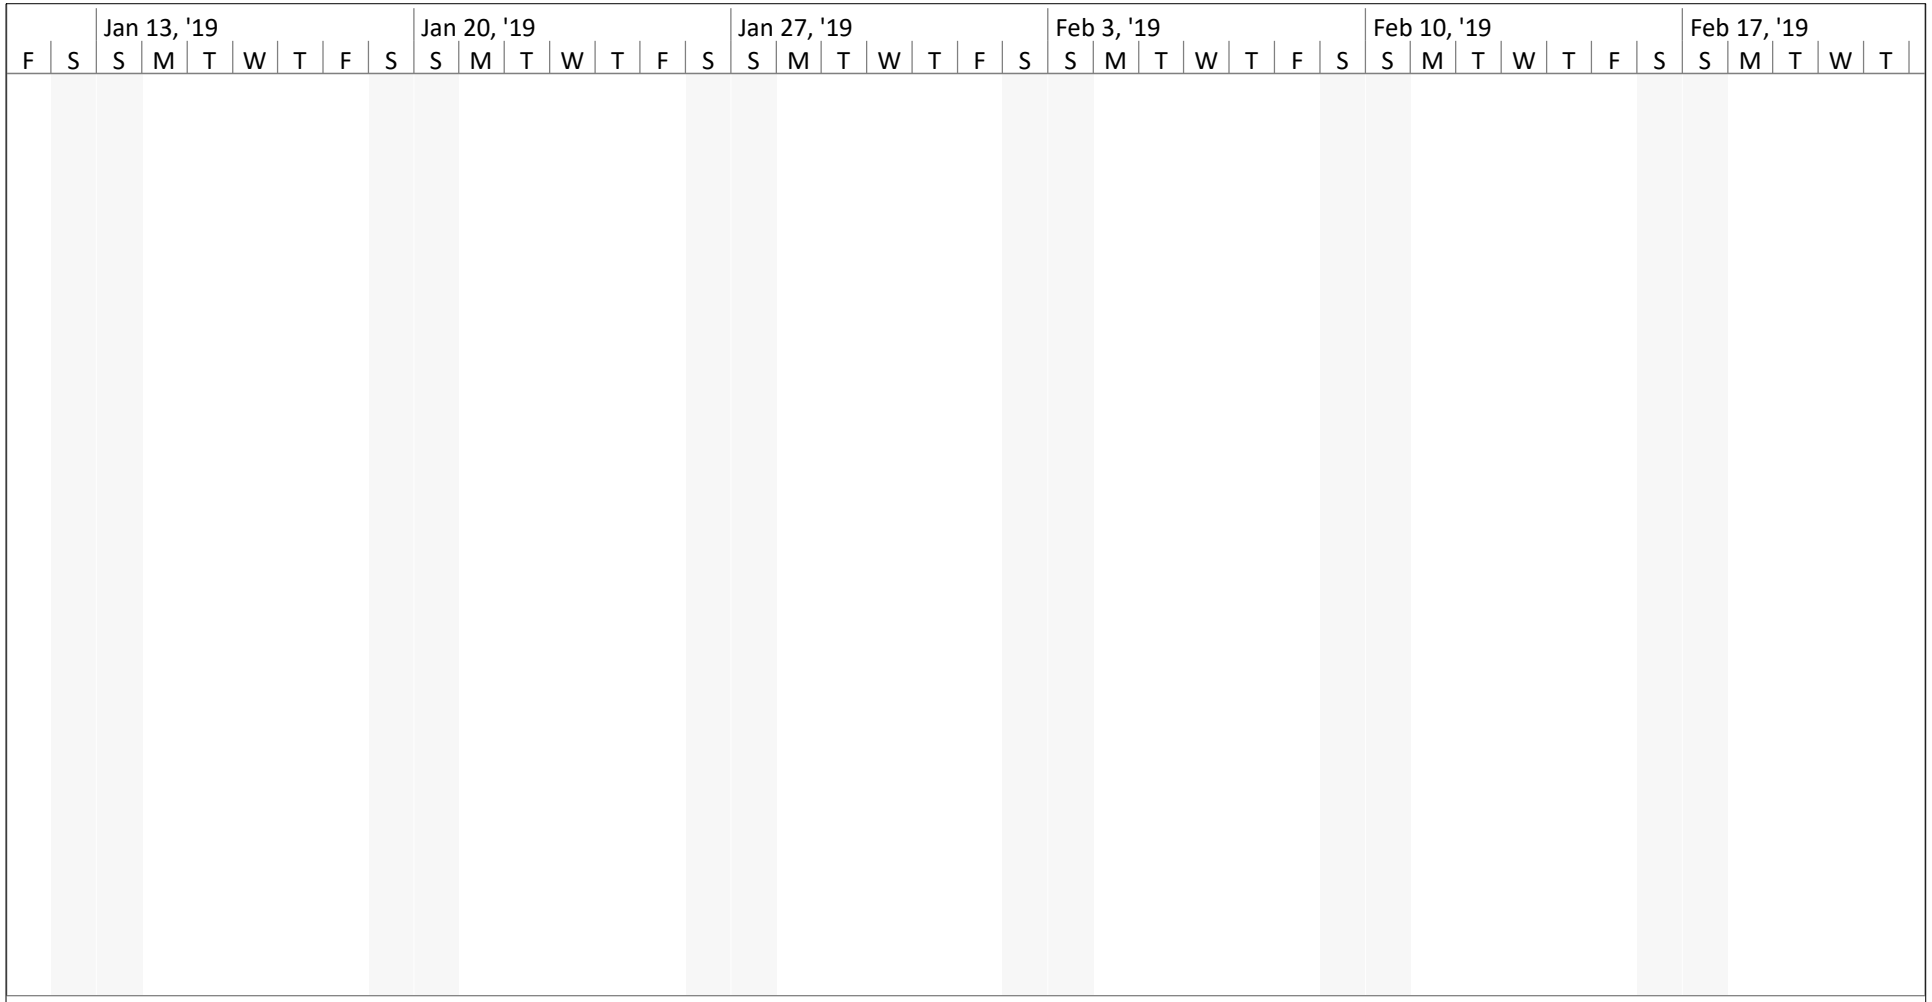


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

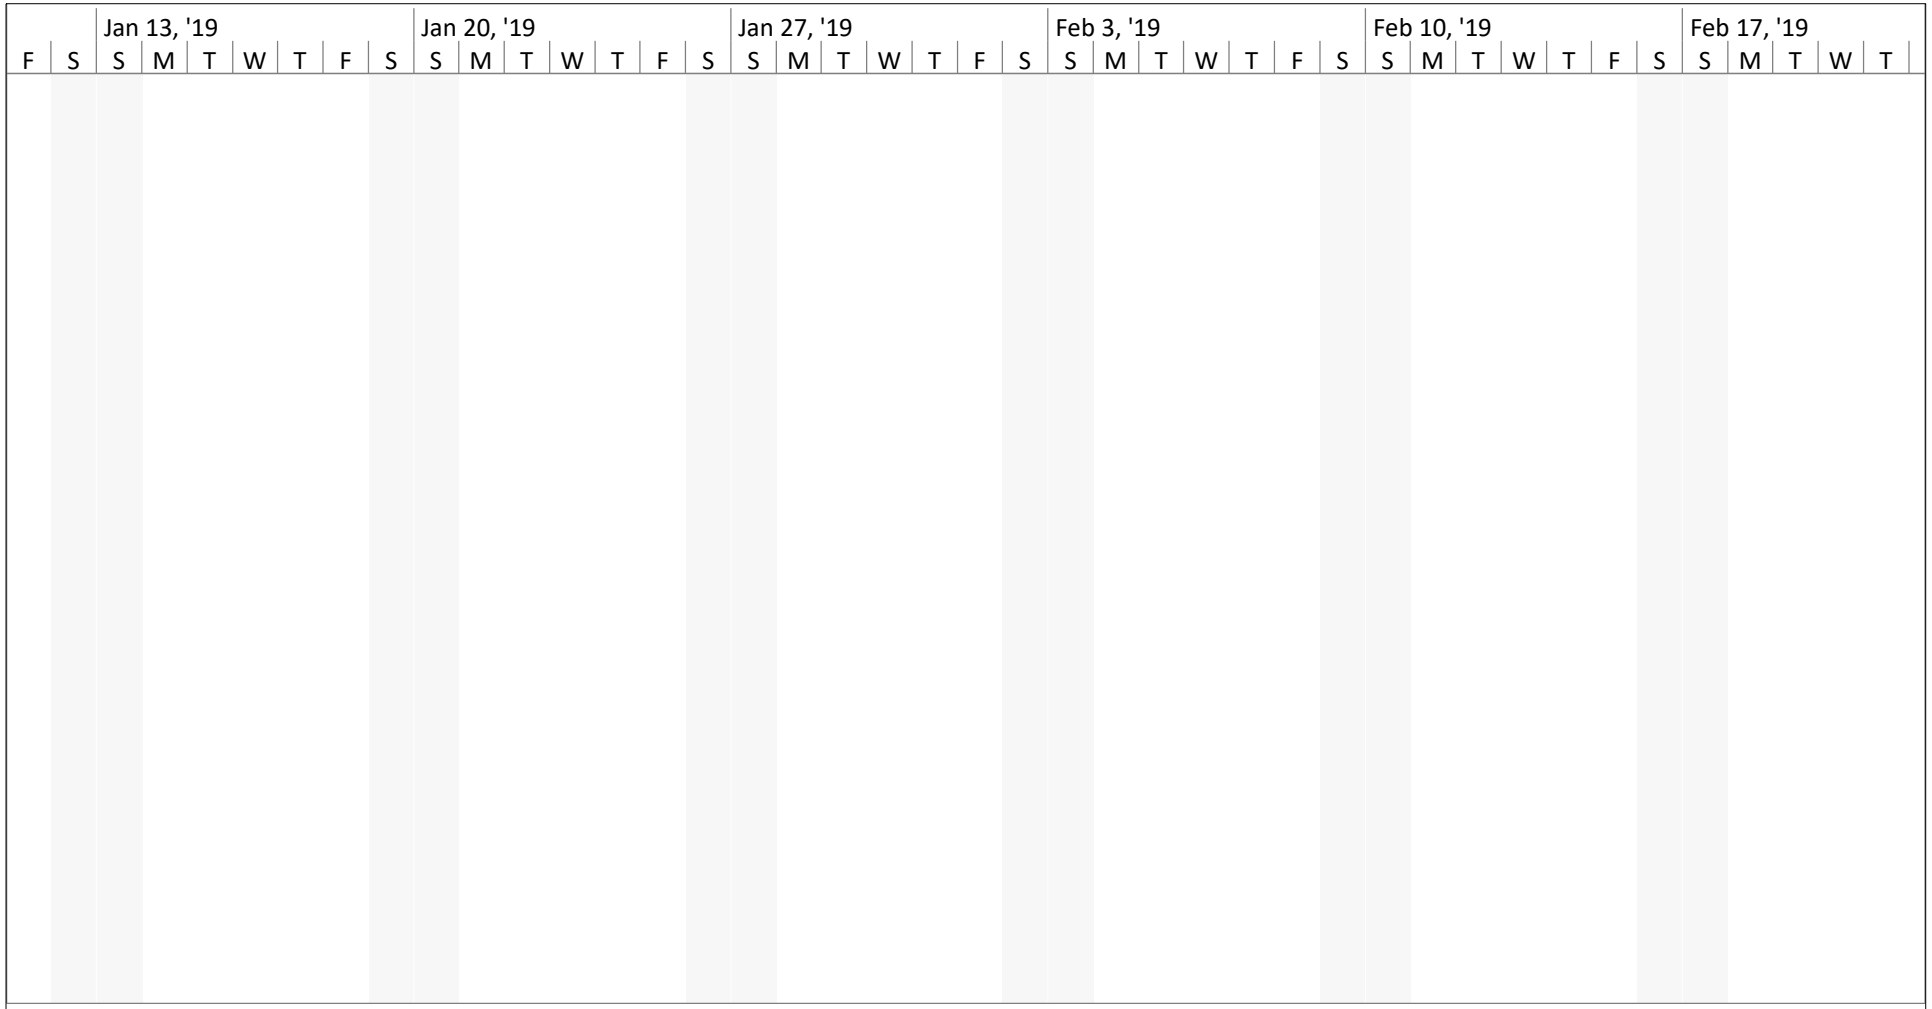


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

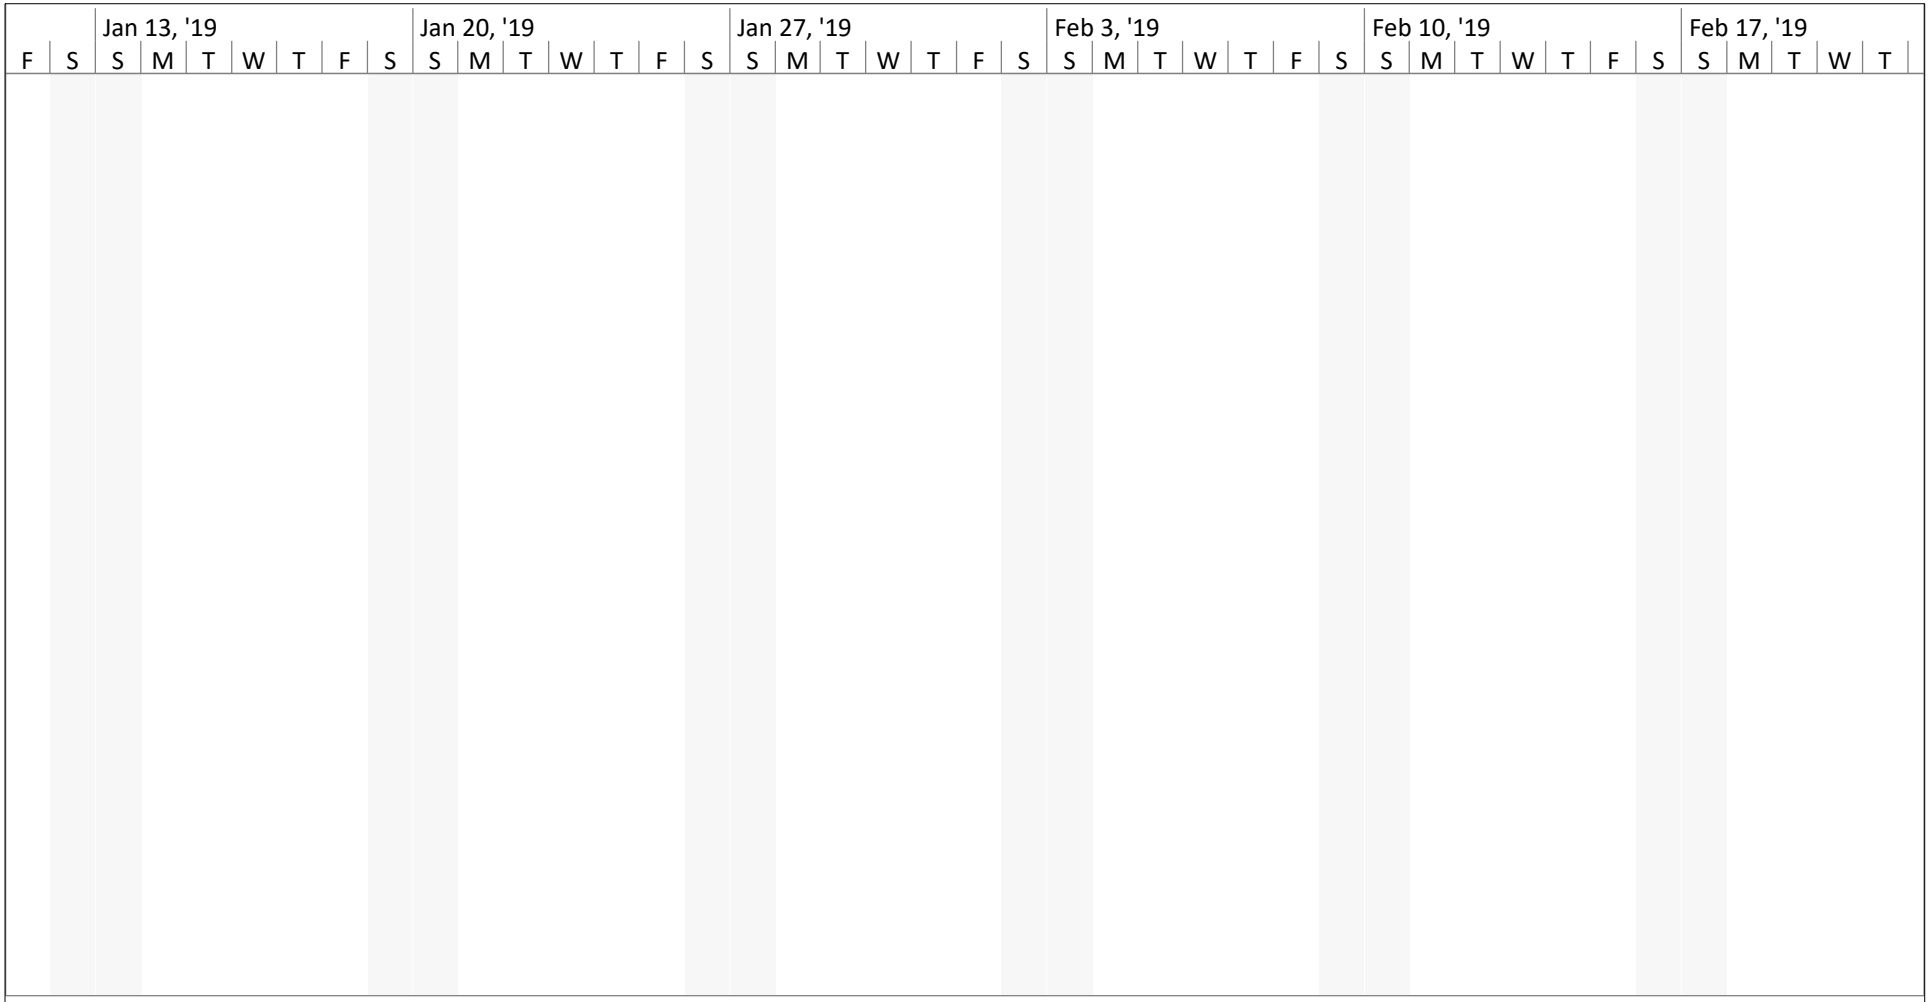


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |




Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

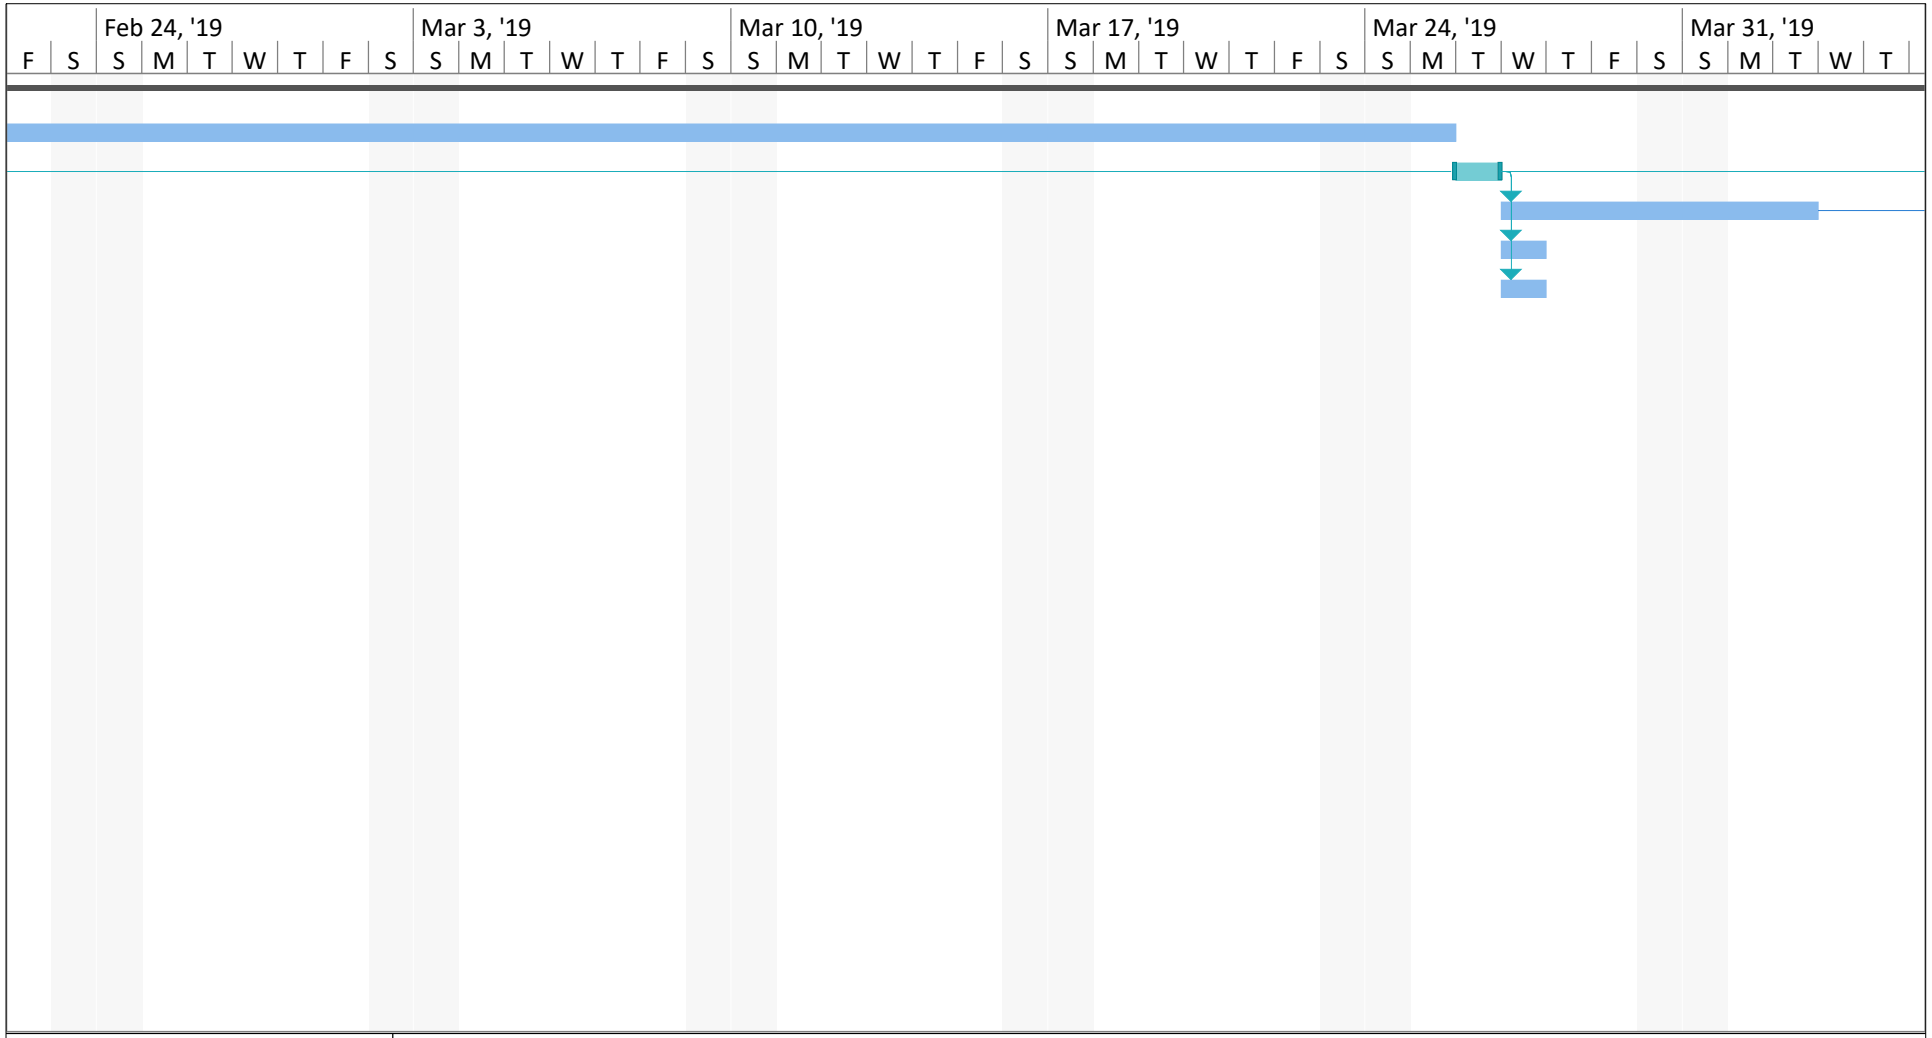


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

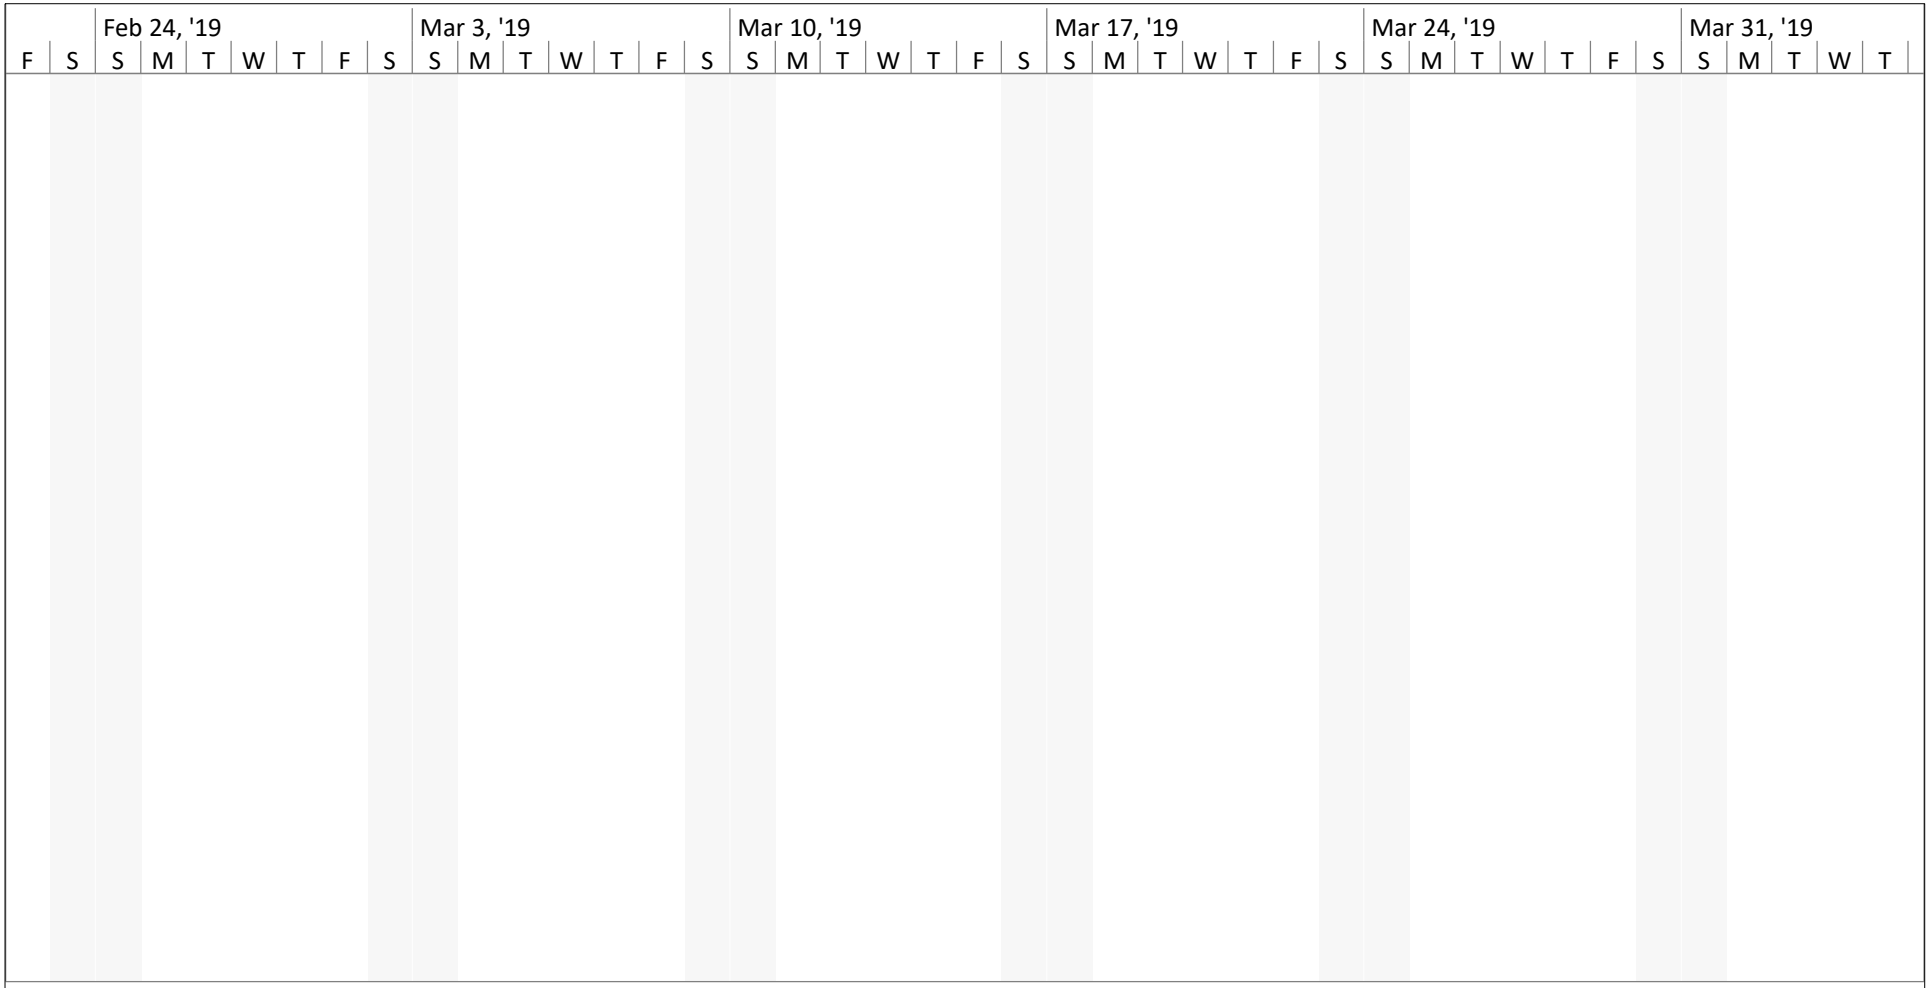


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

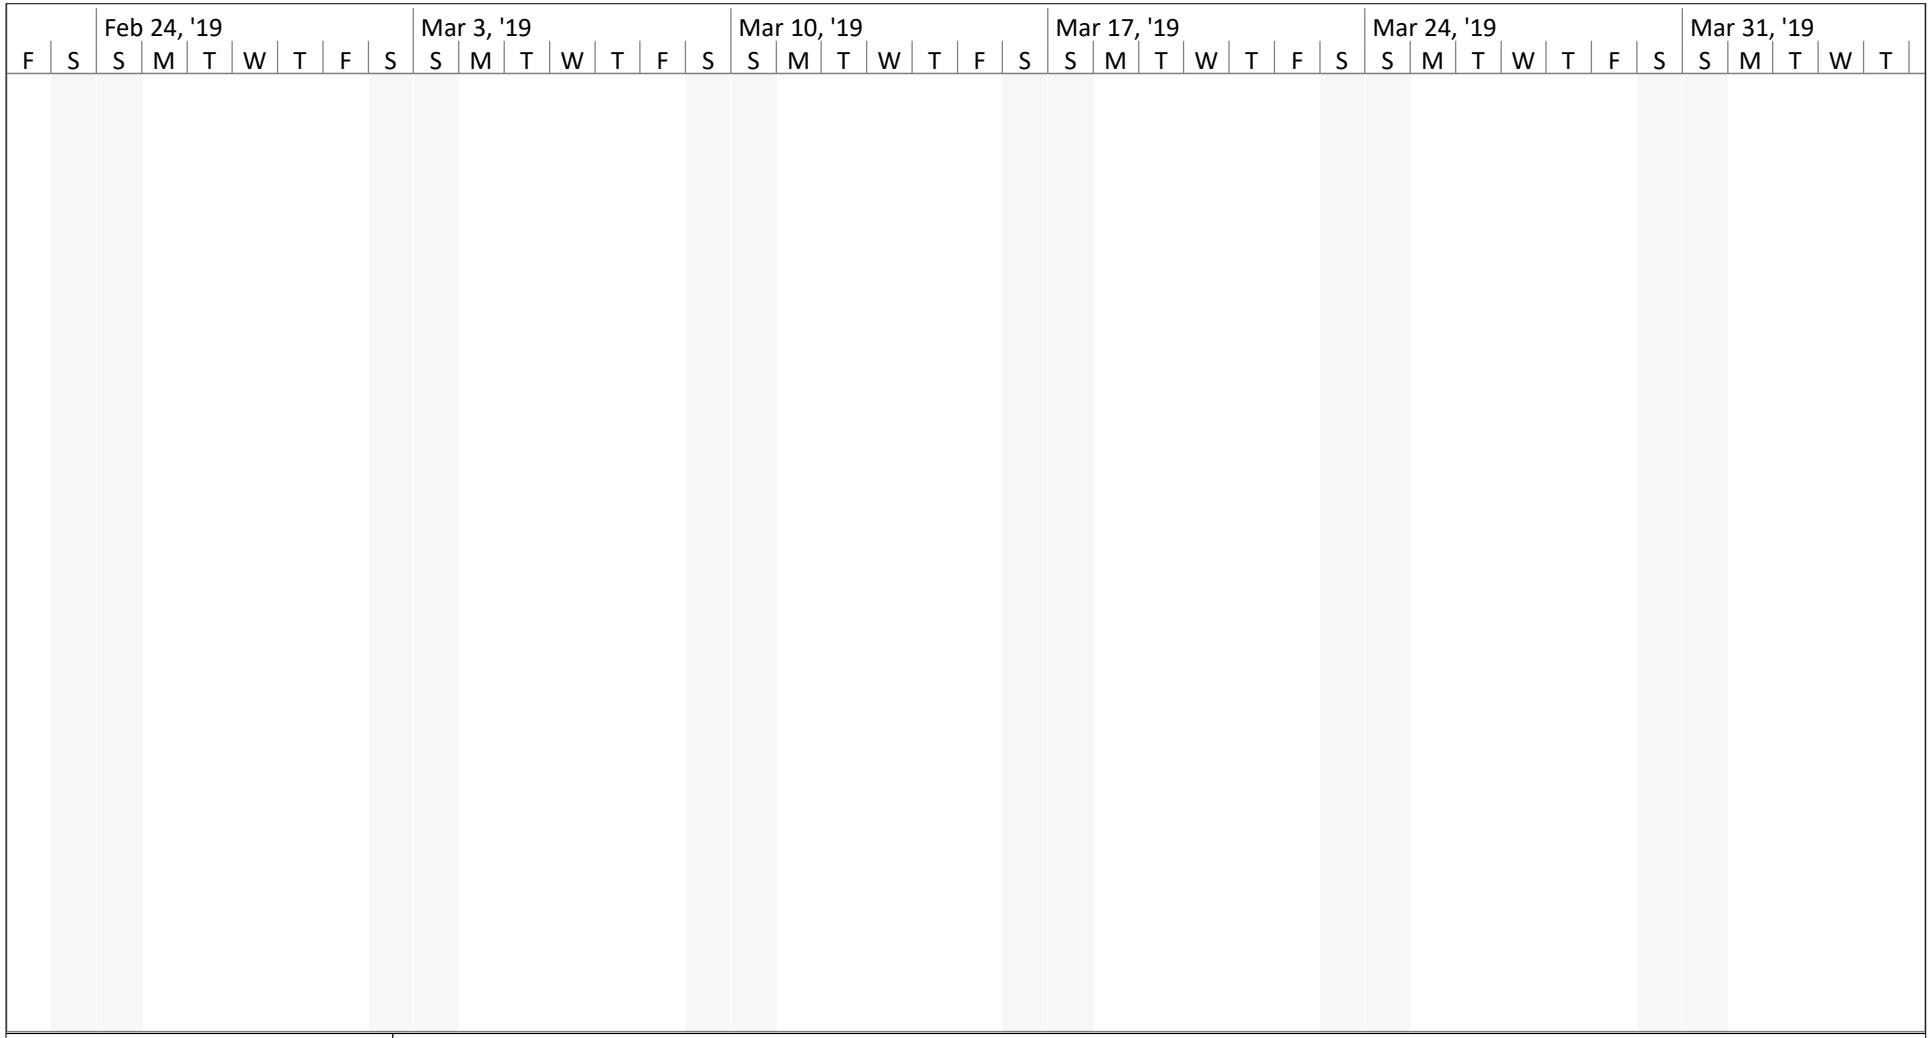


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

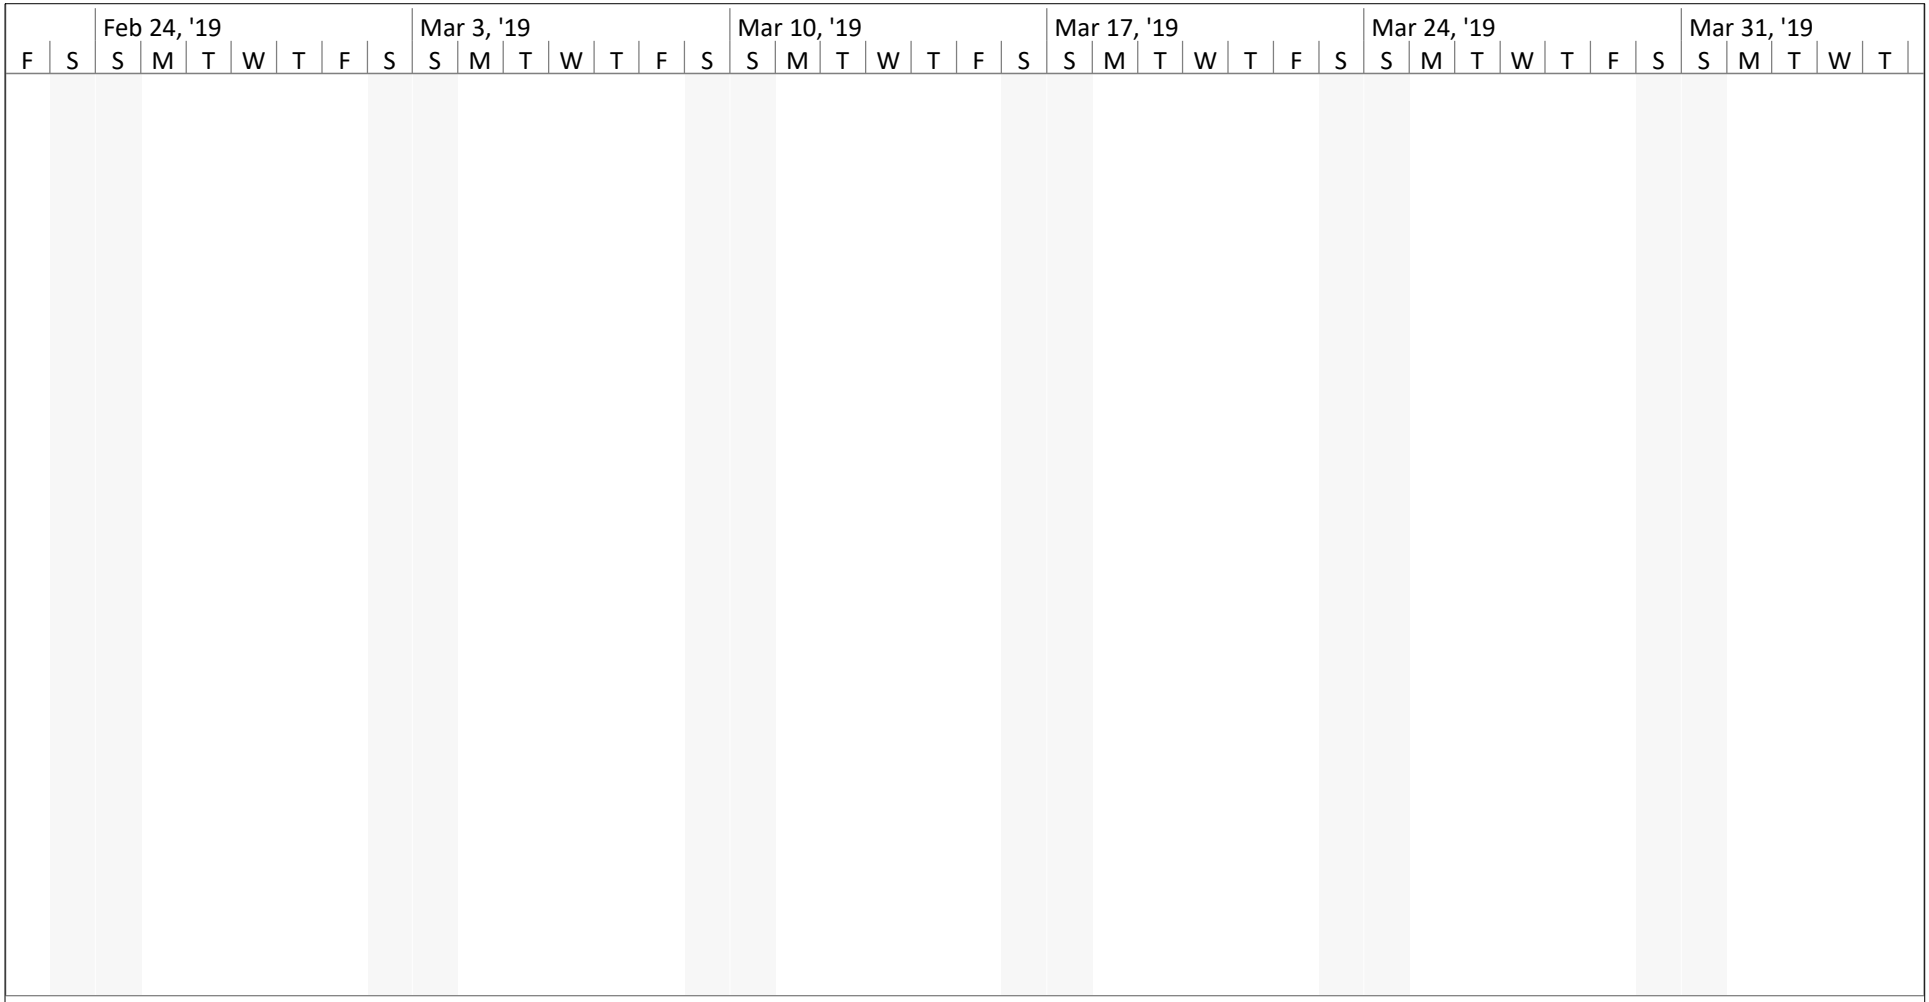


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

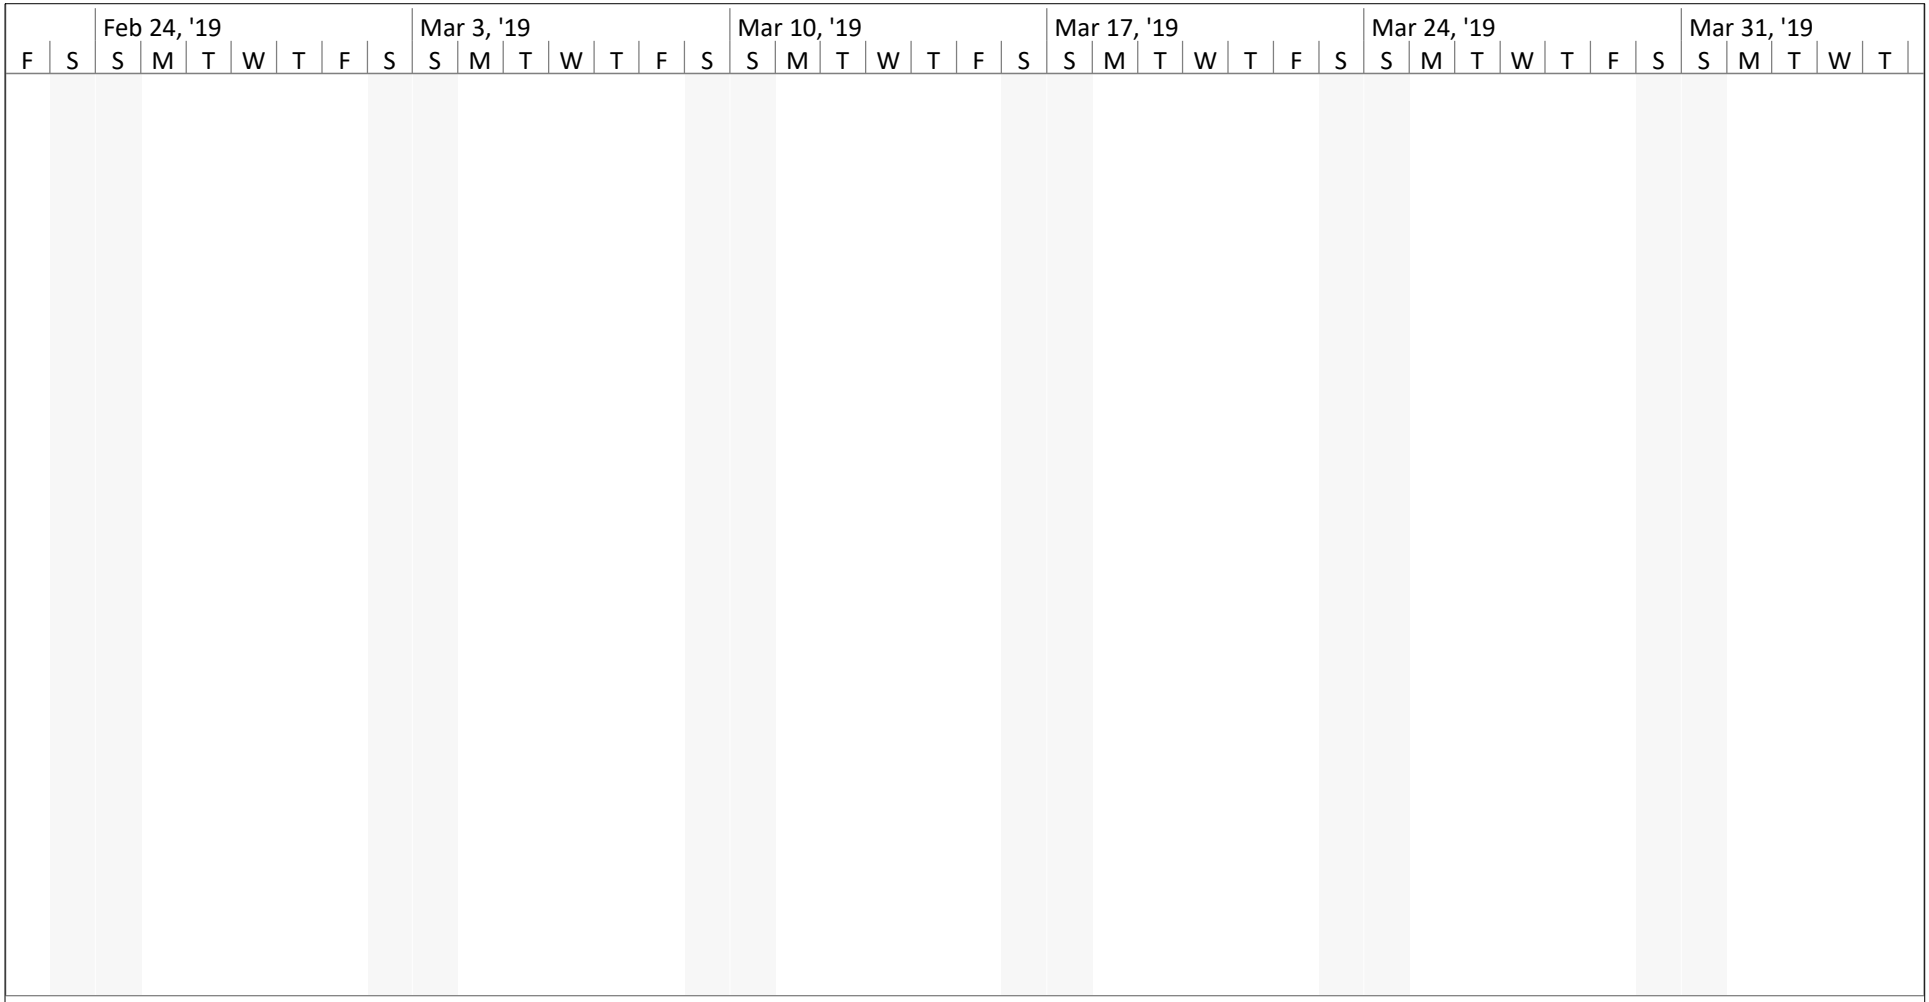


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

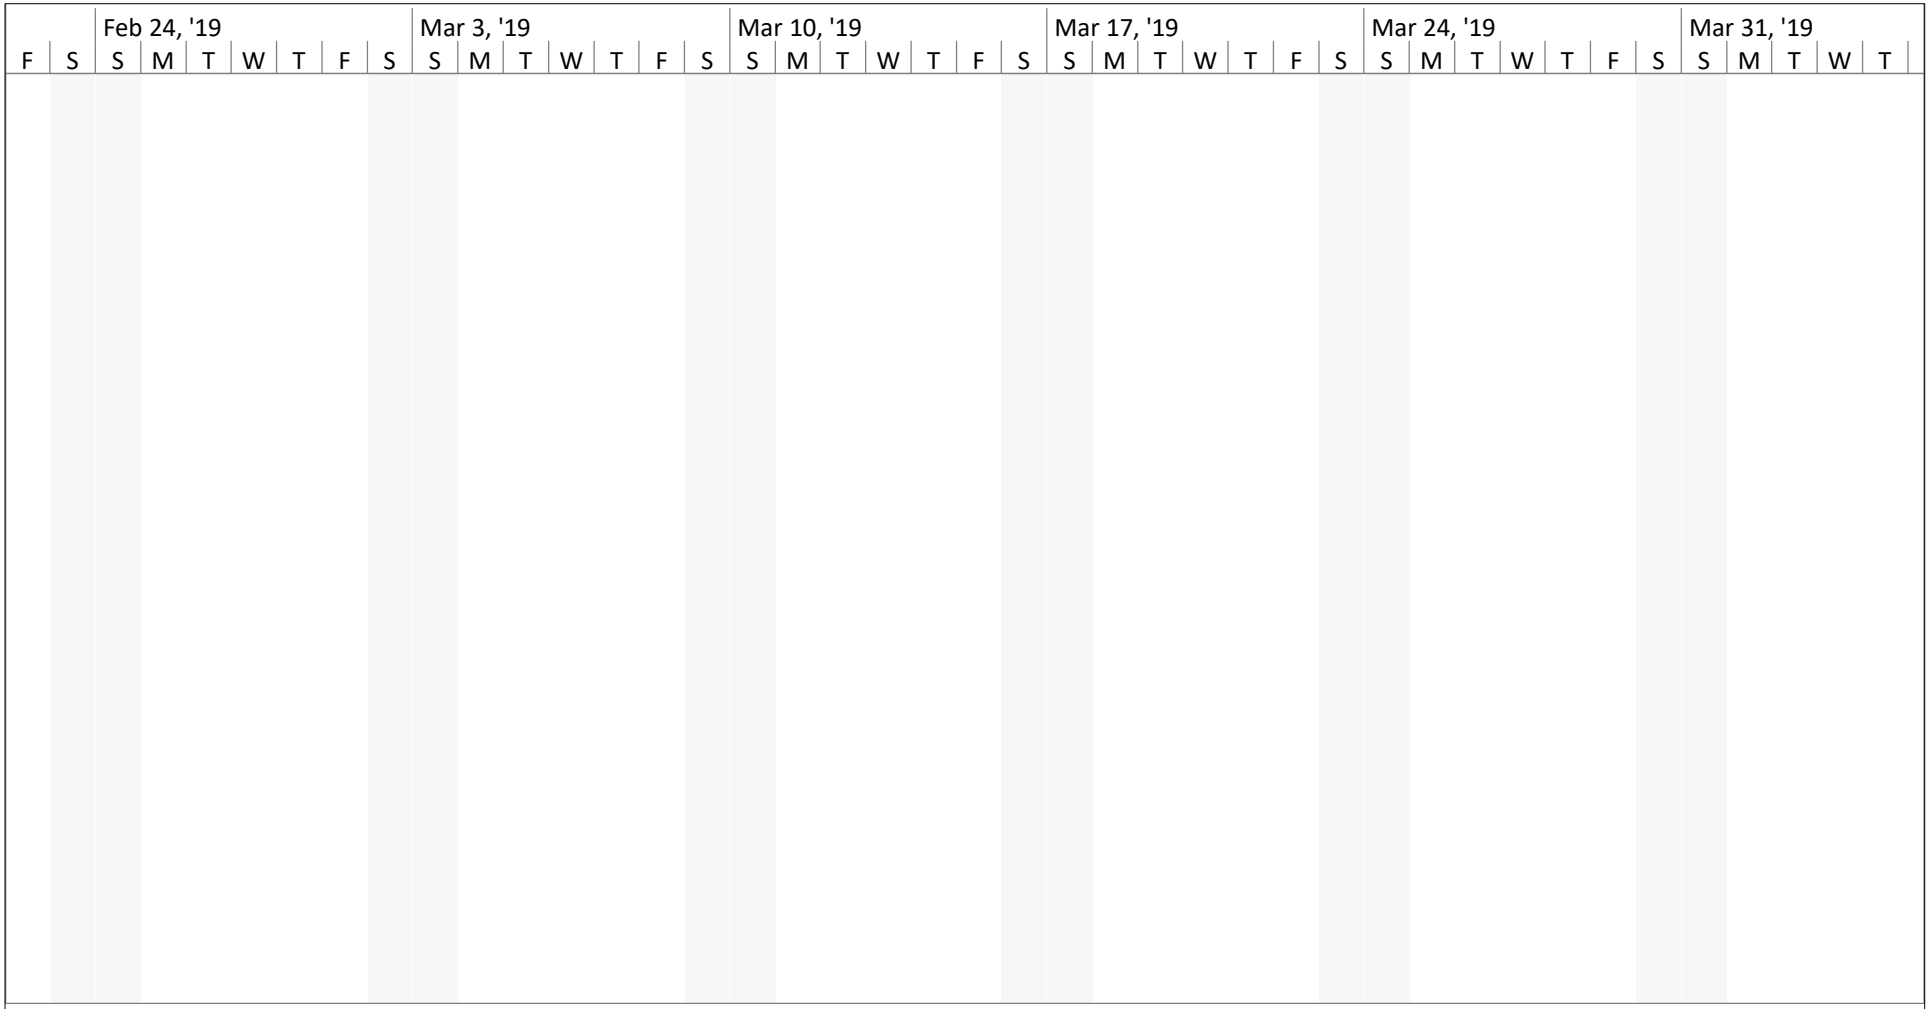


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

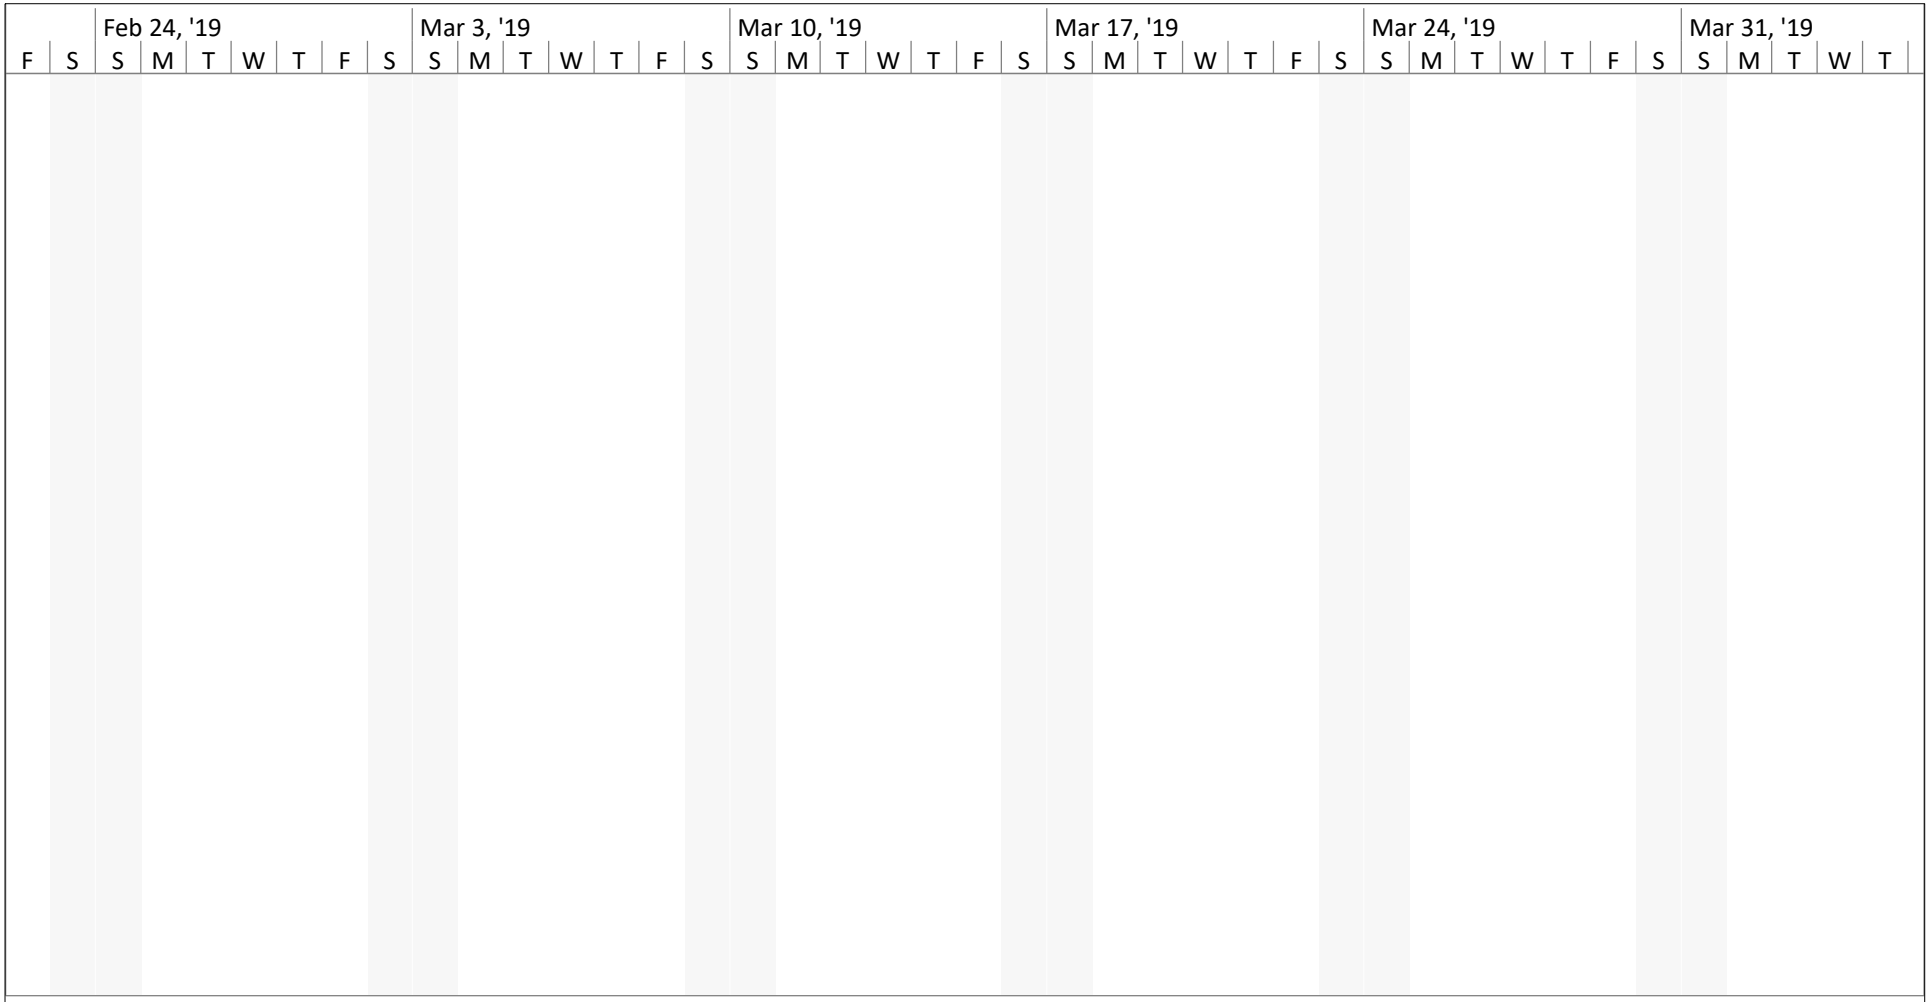


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |




Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

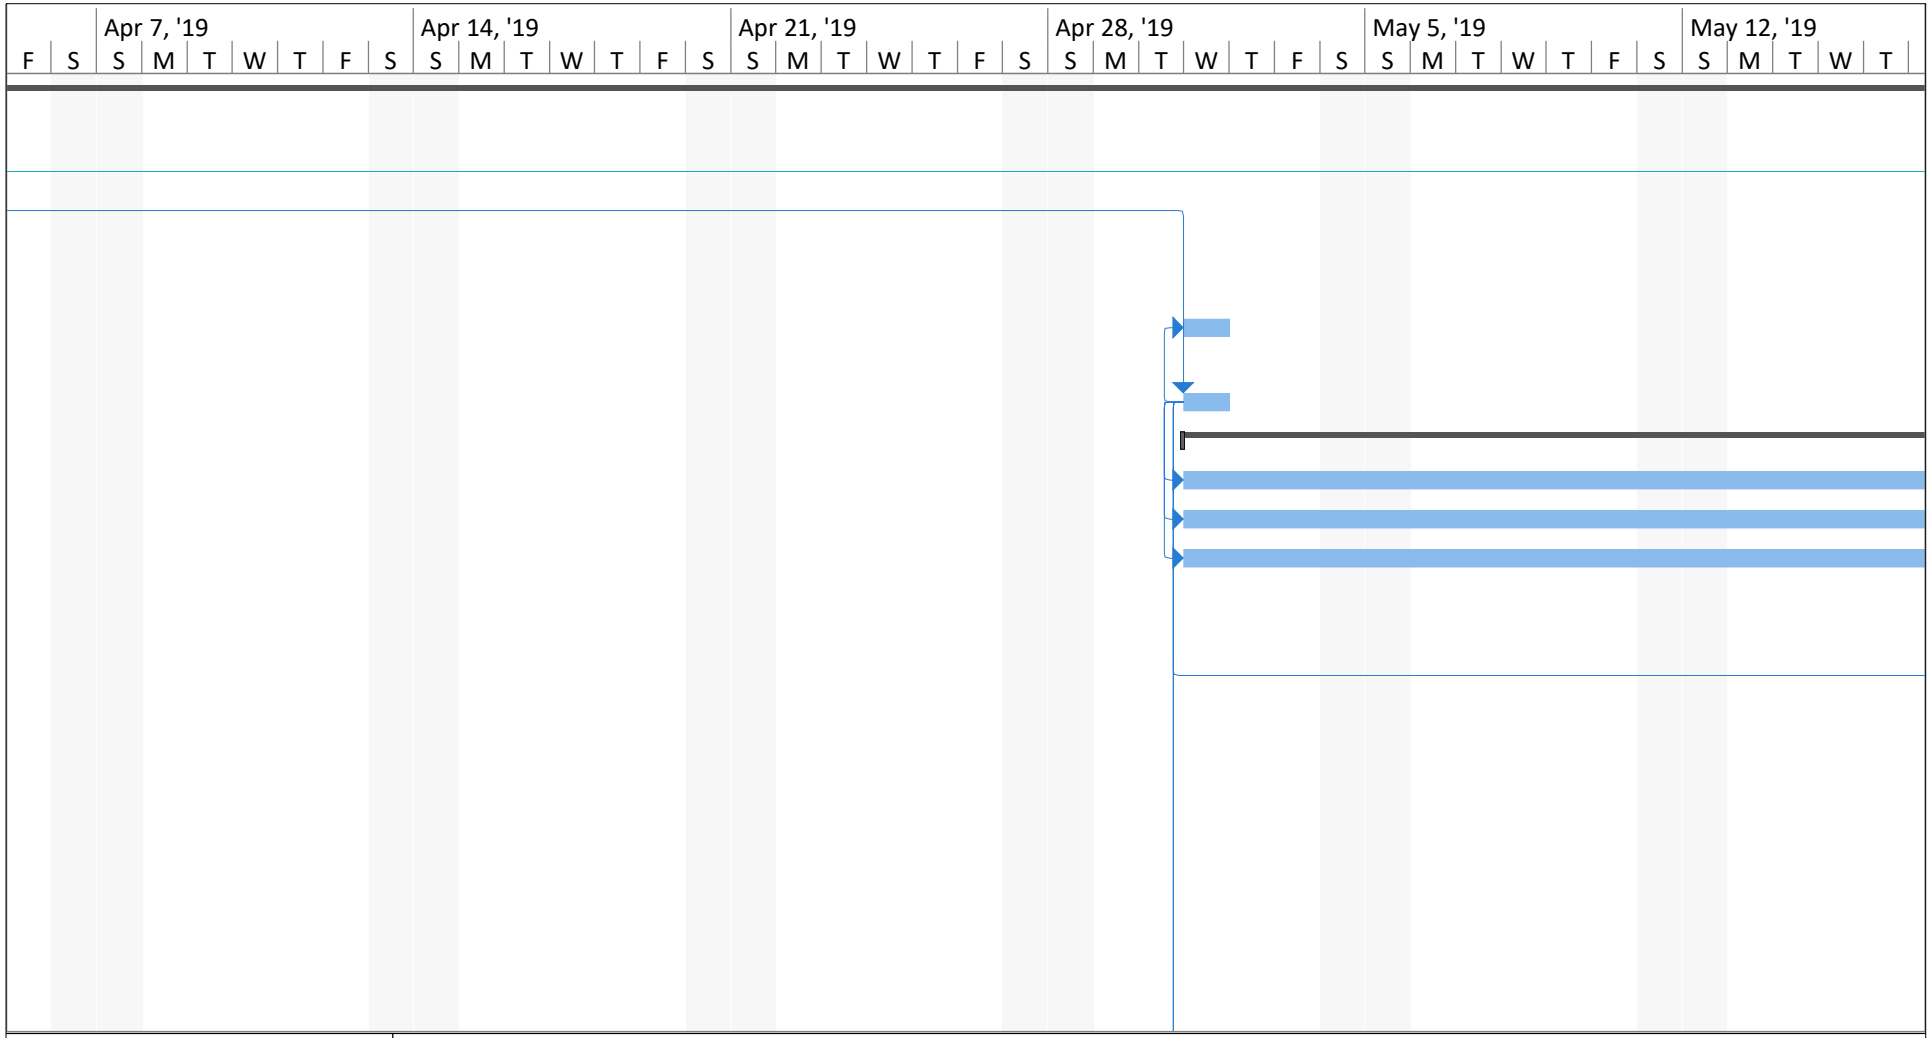


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

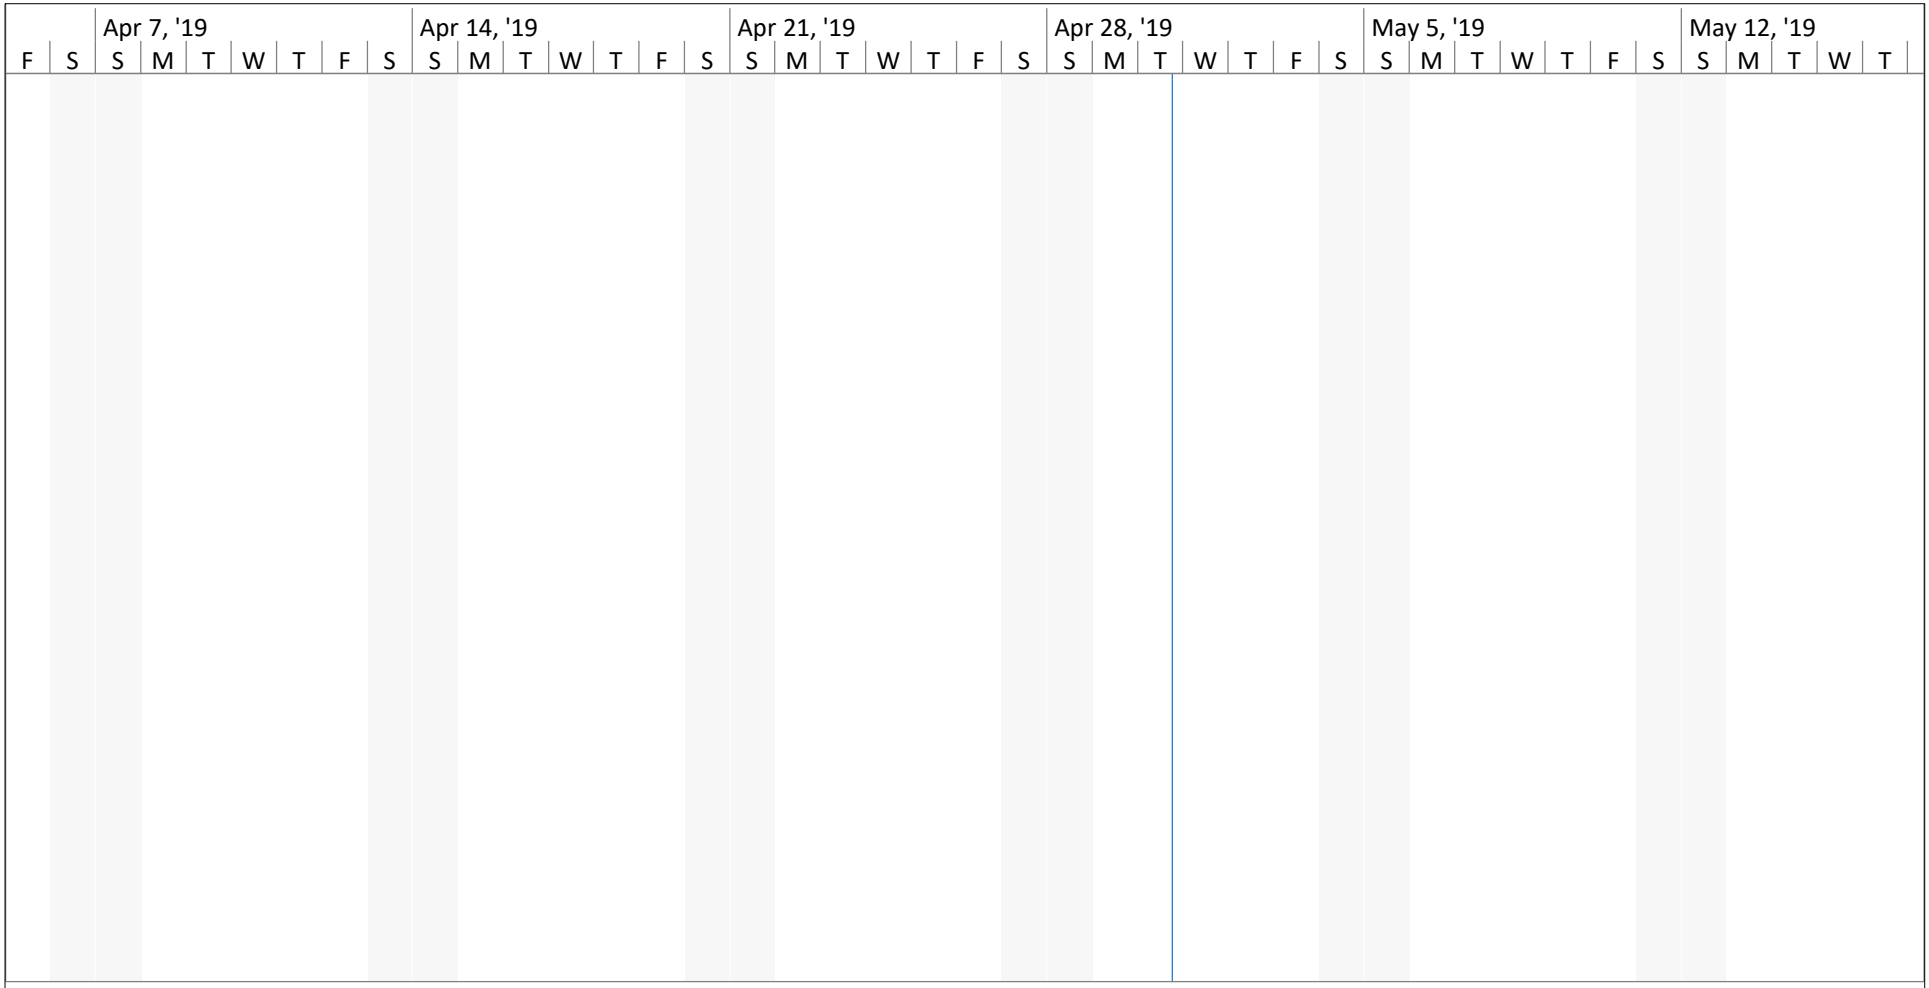


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

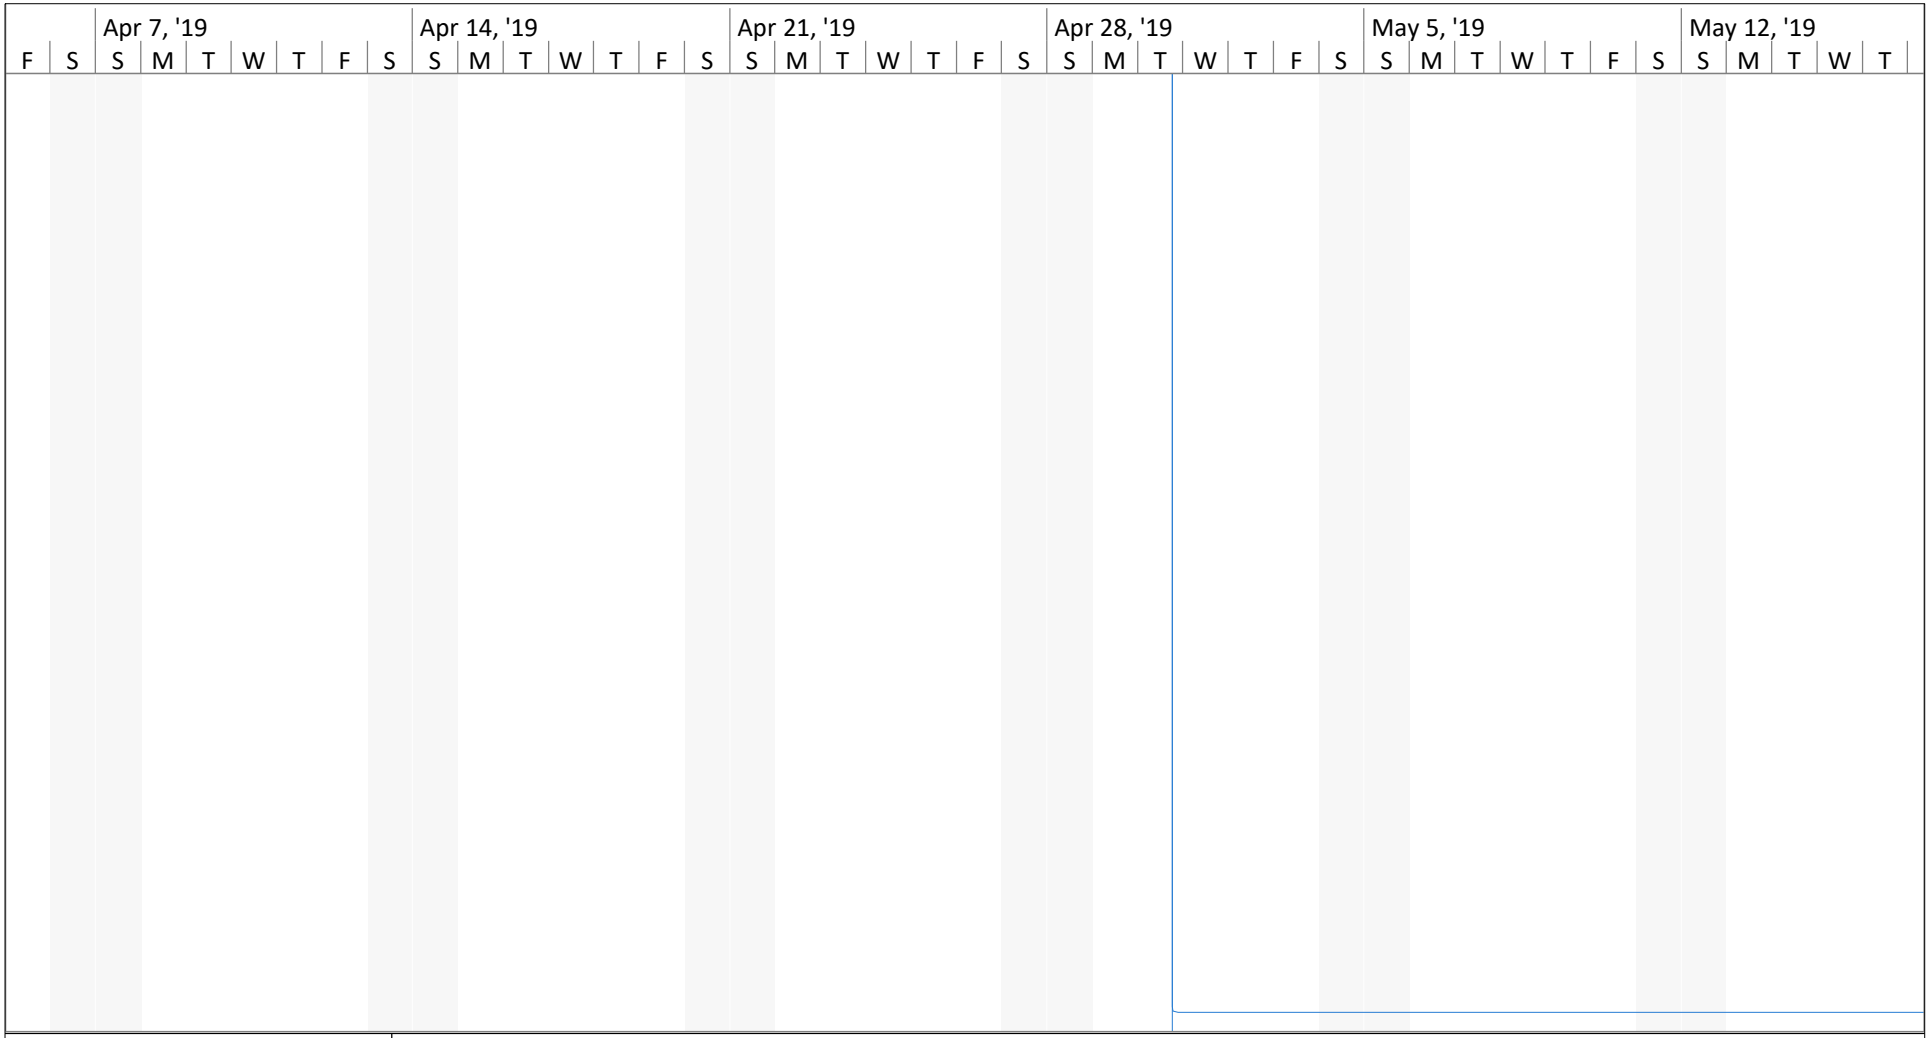


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

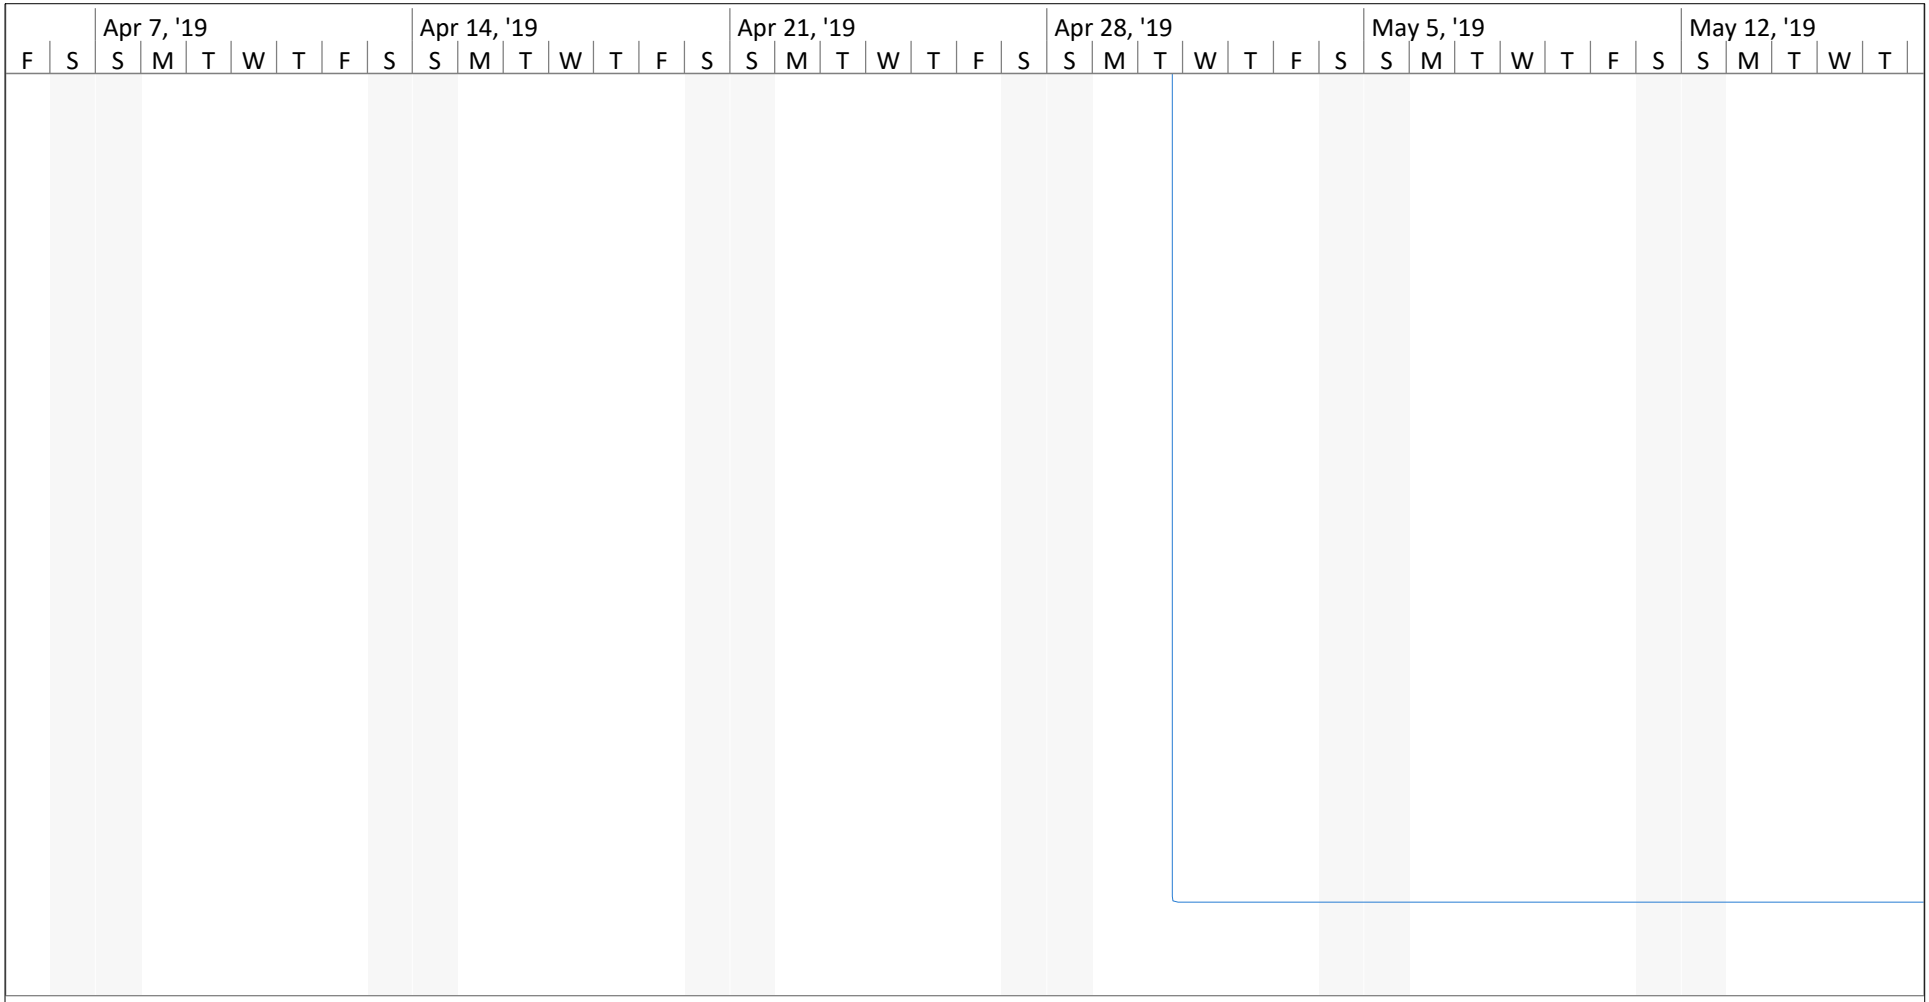


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

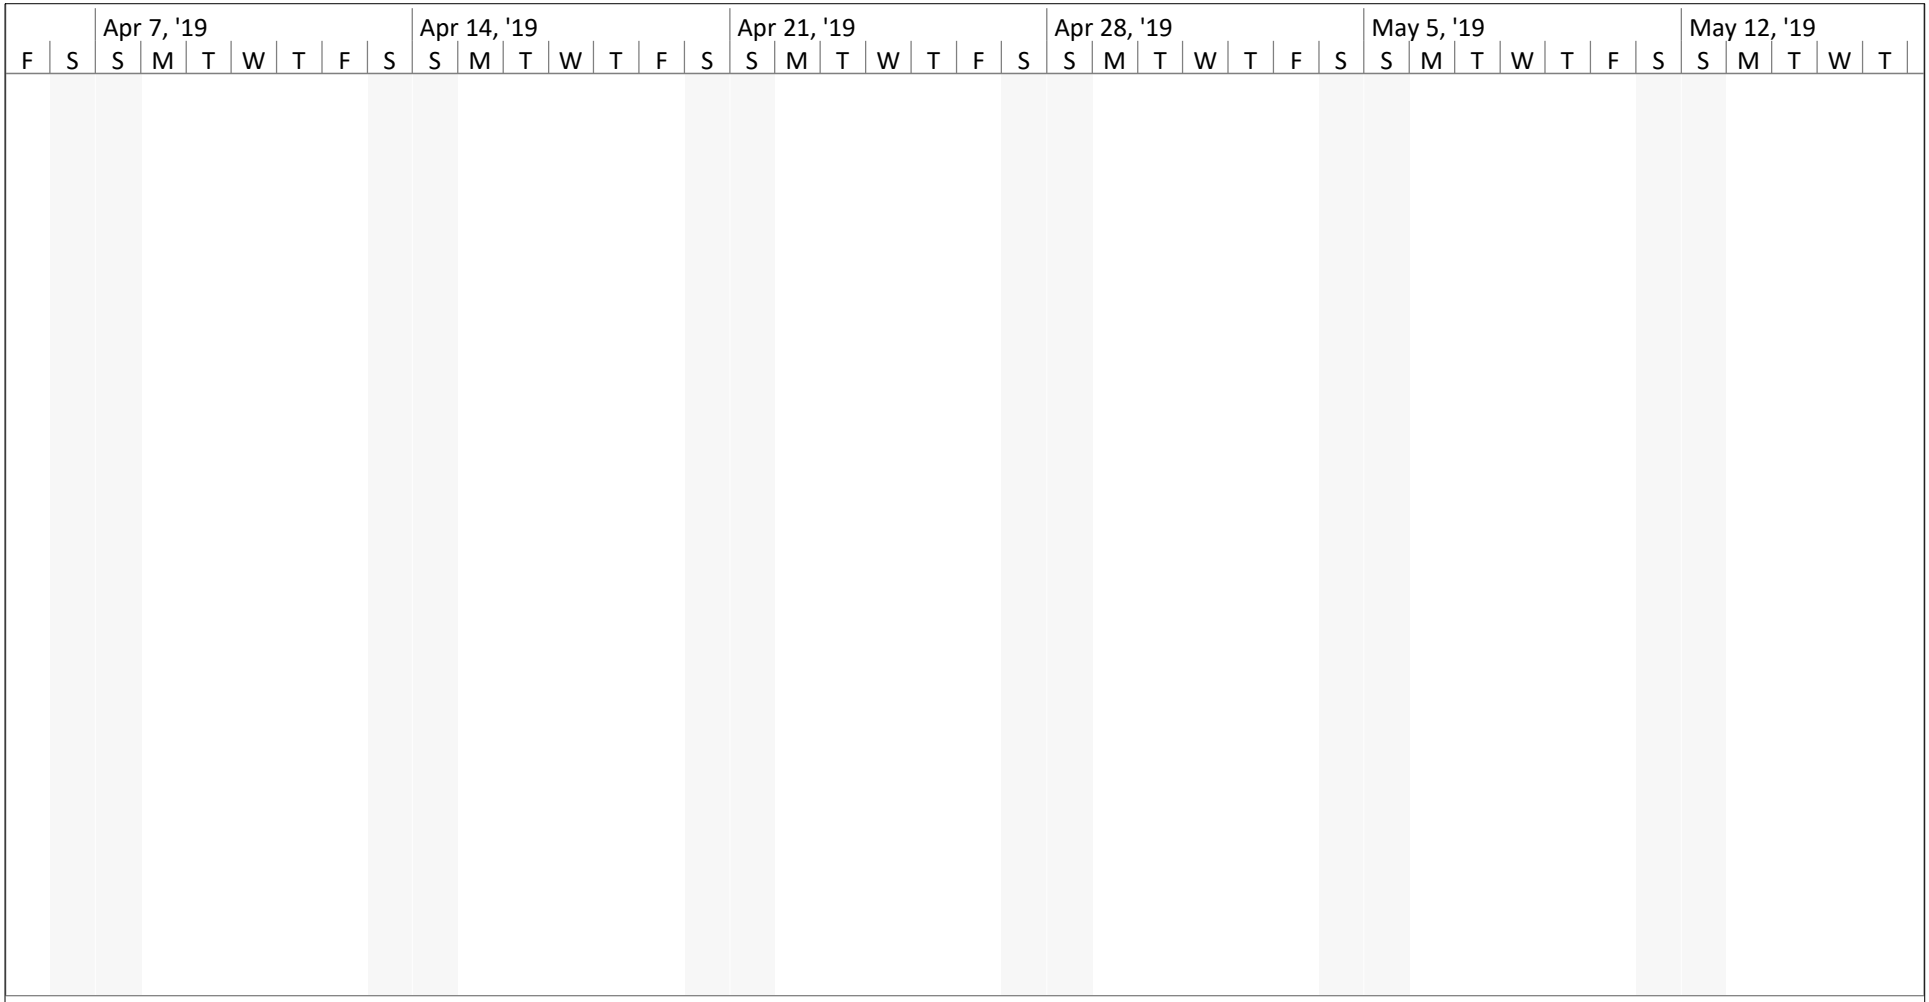


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

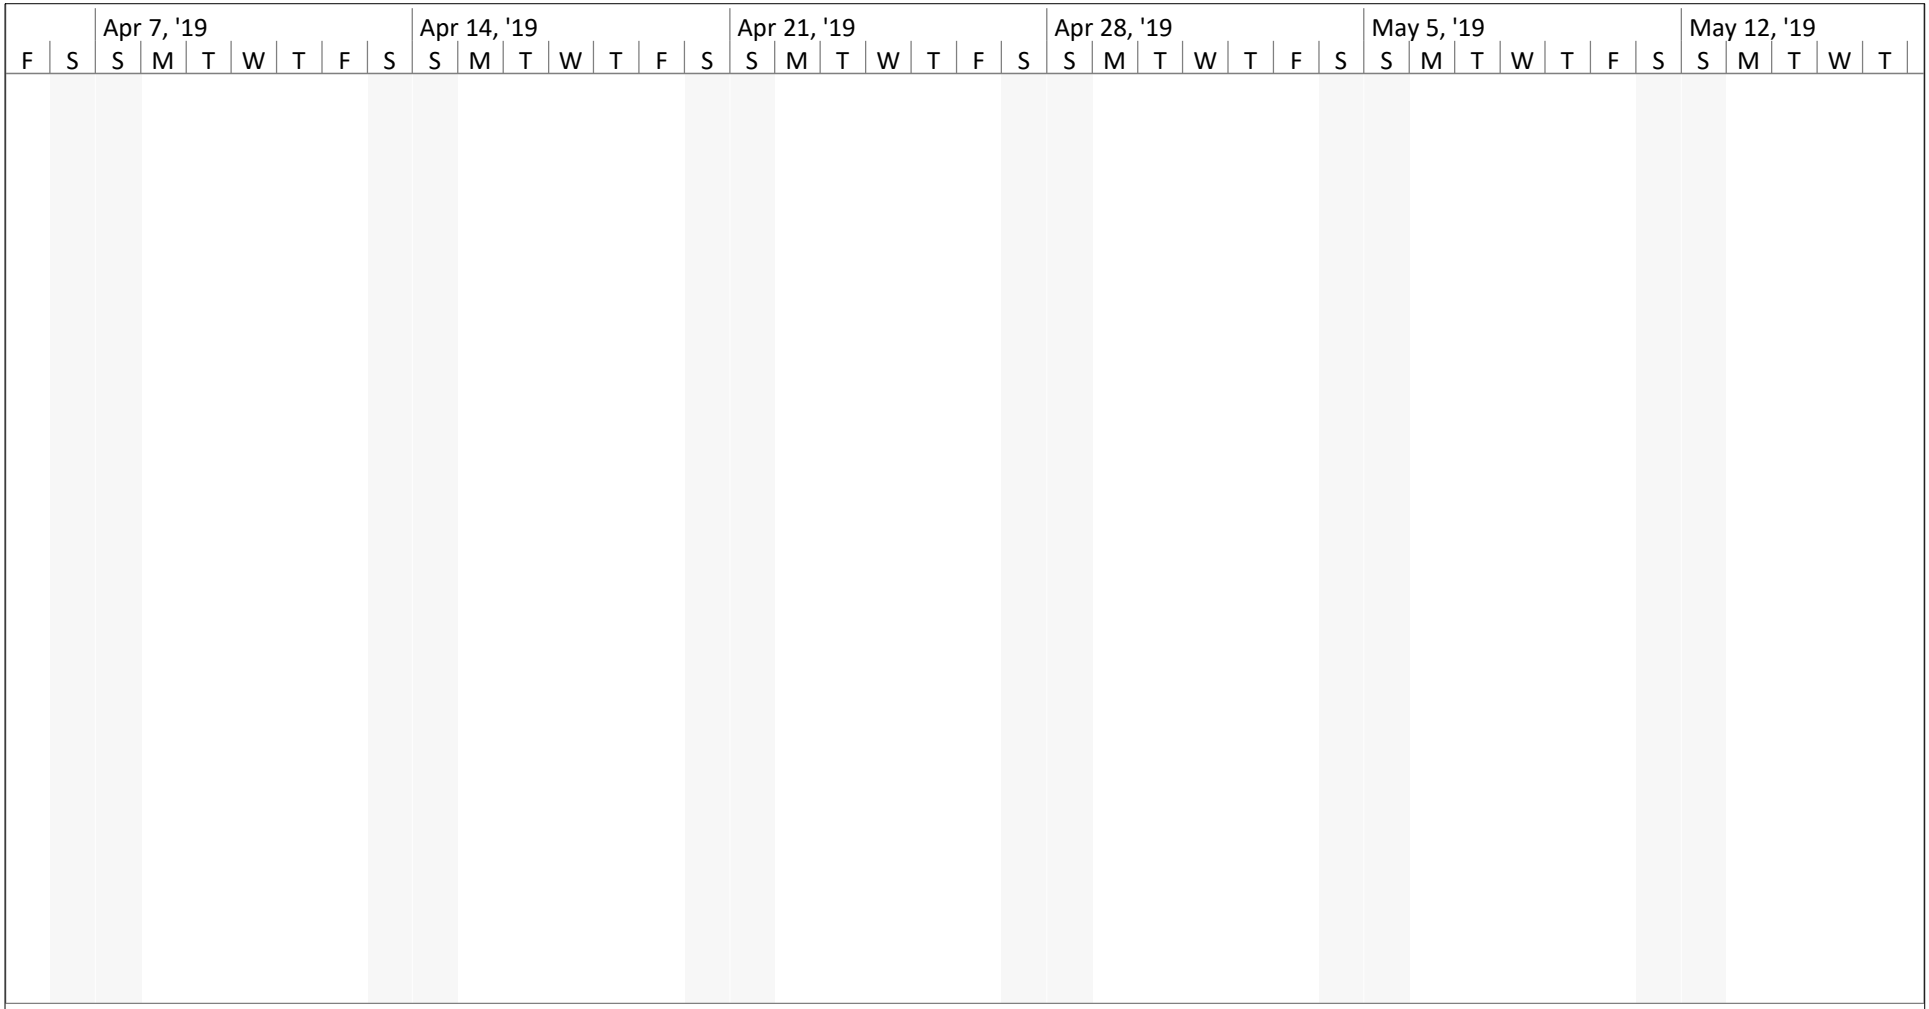


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

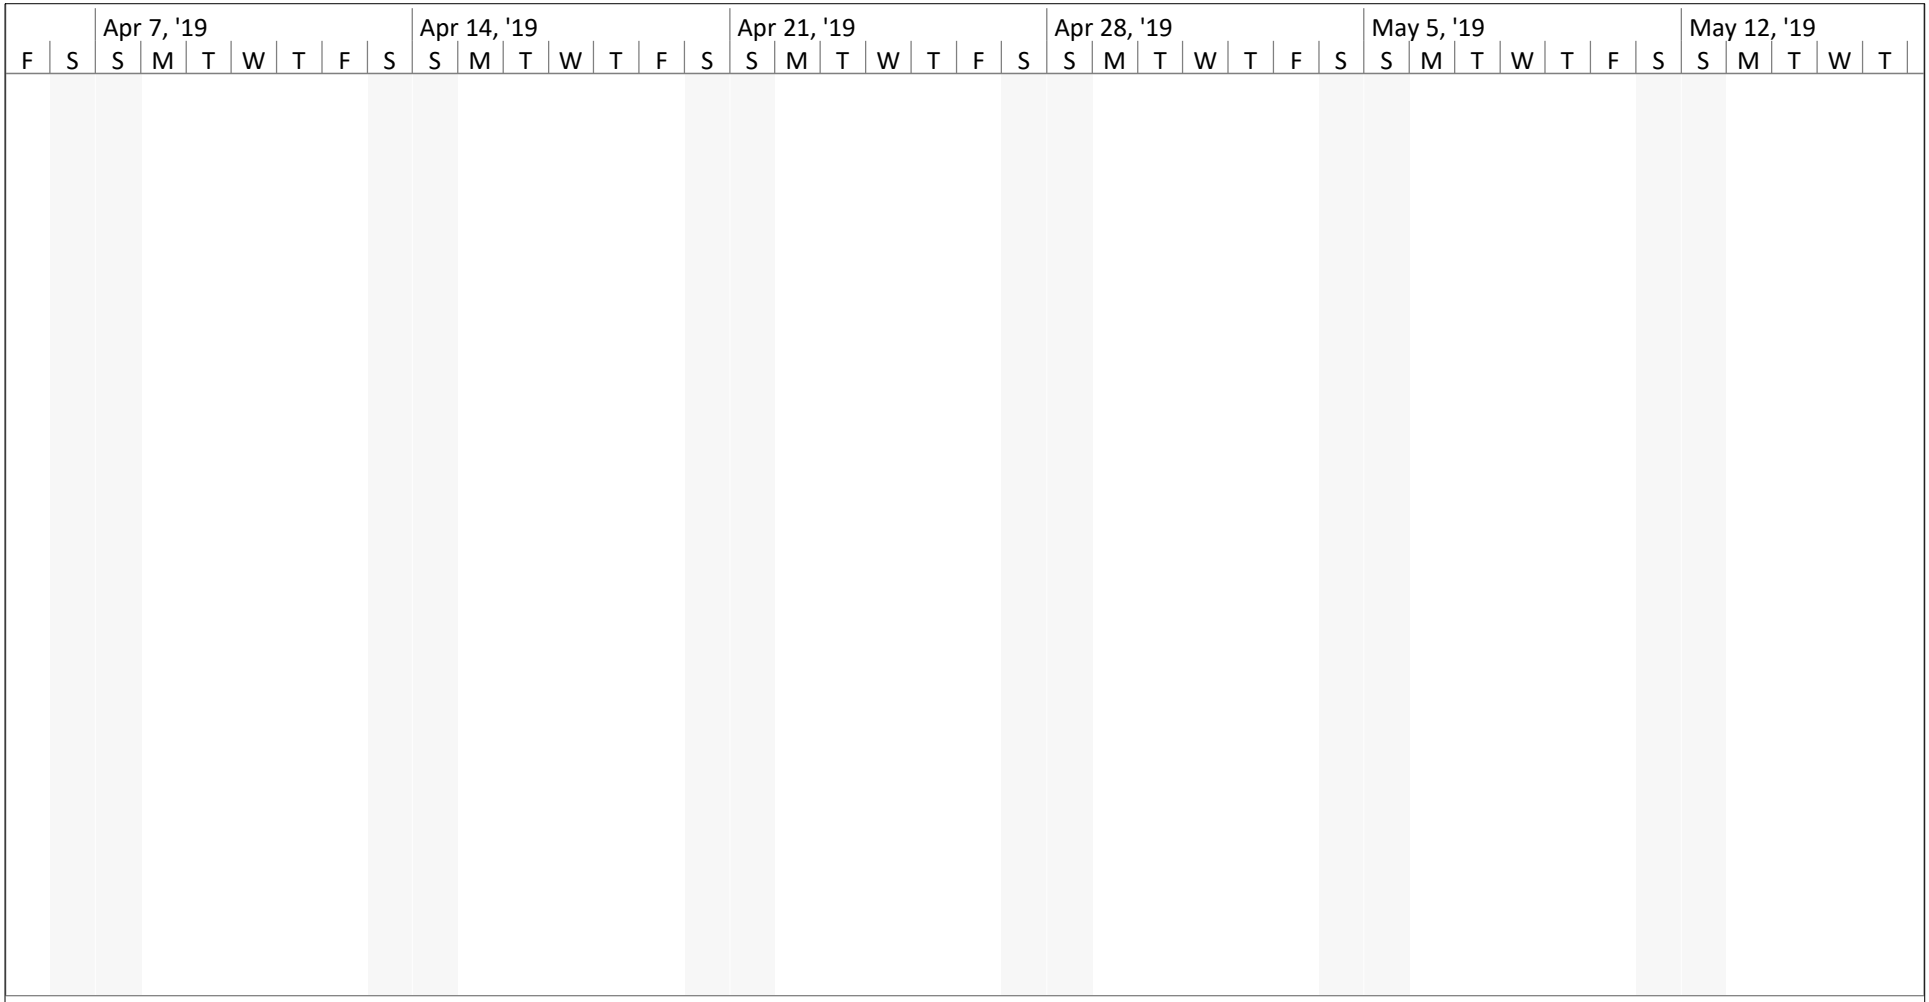


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |




Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

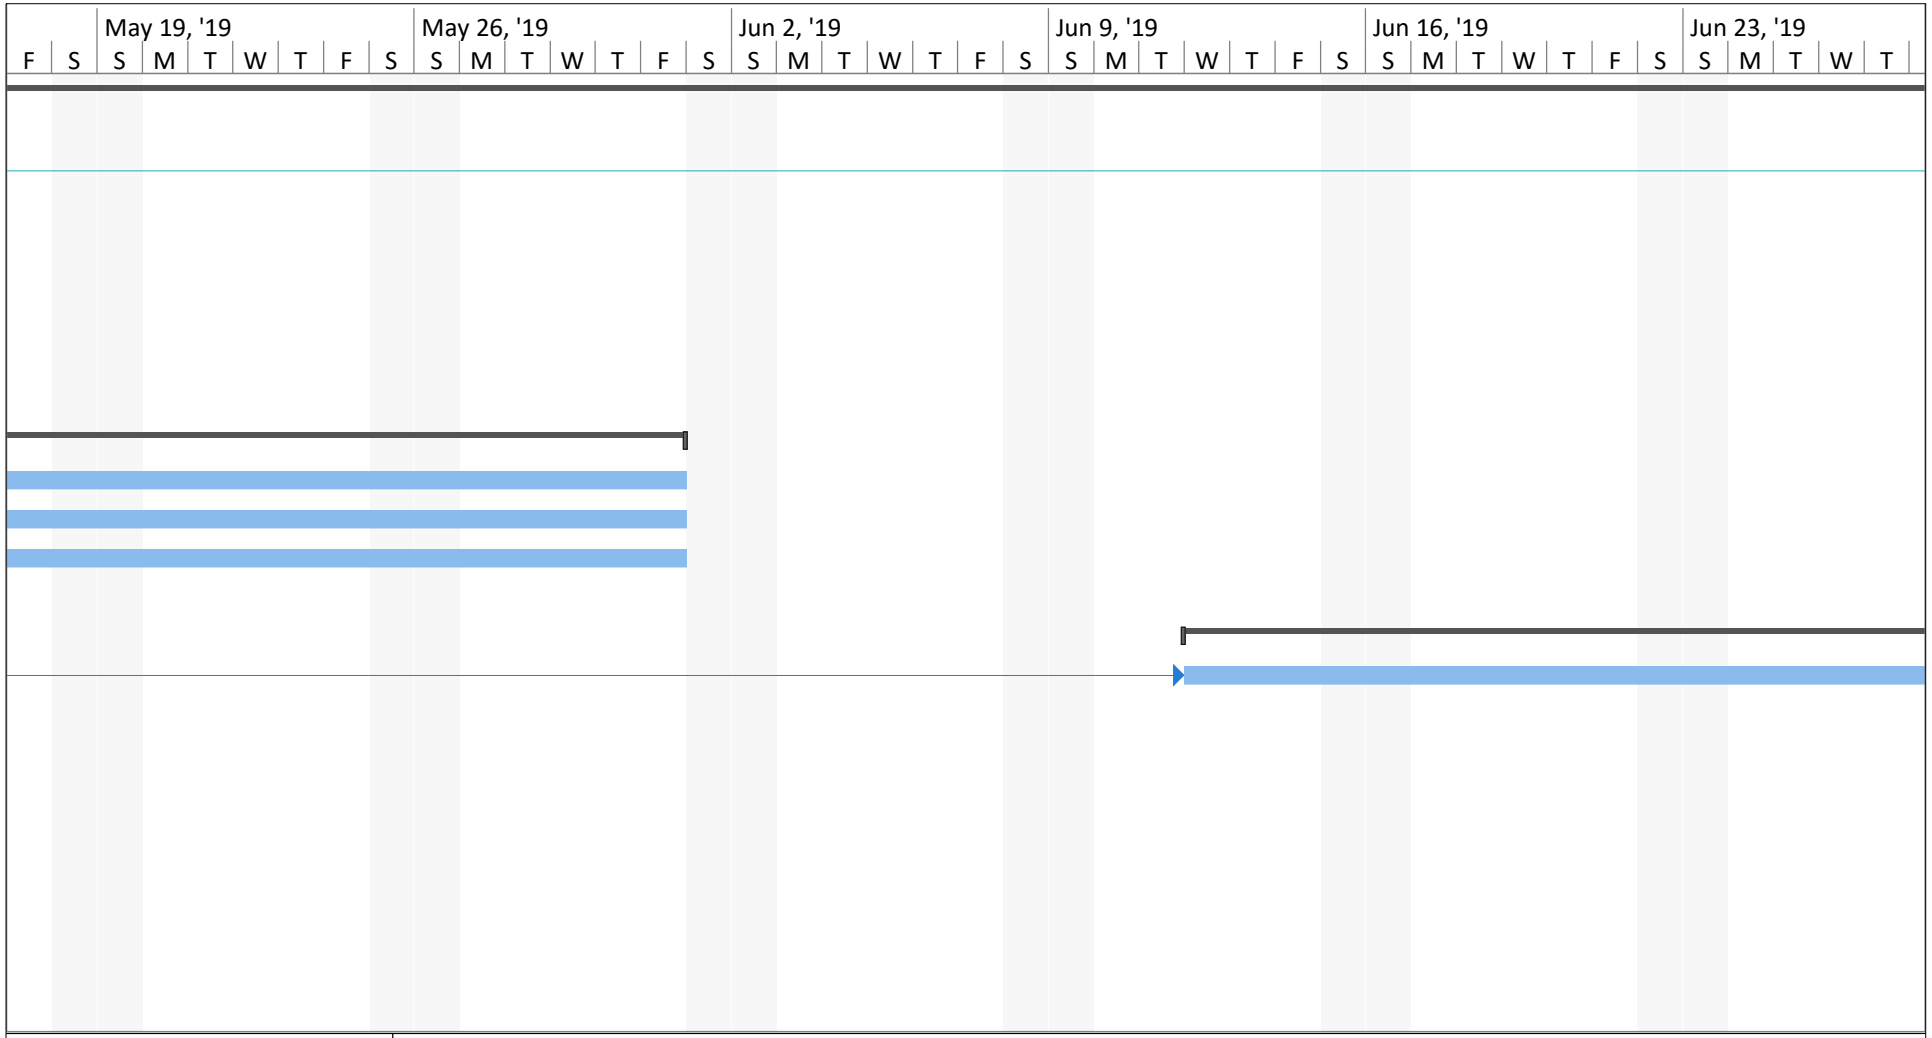


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

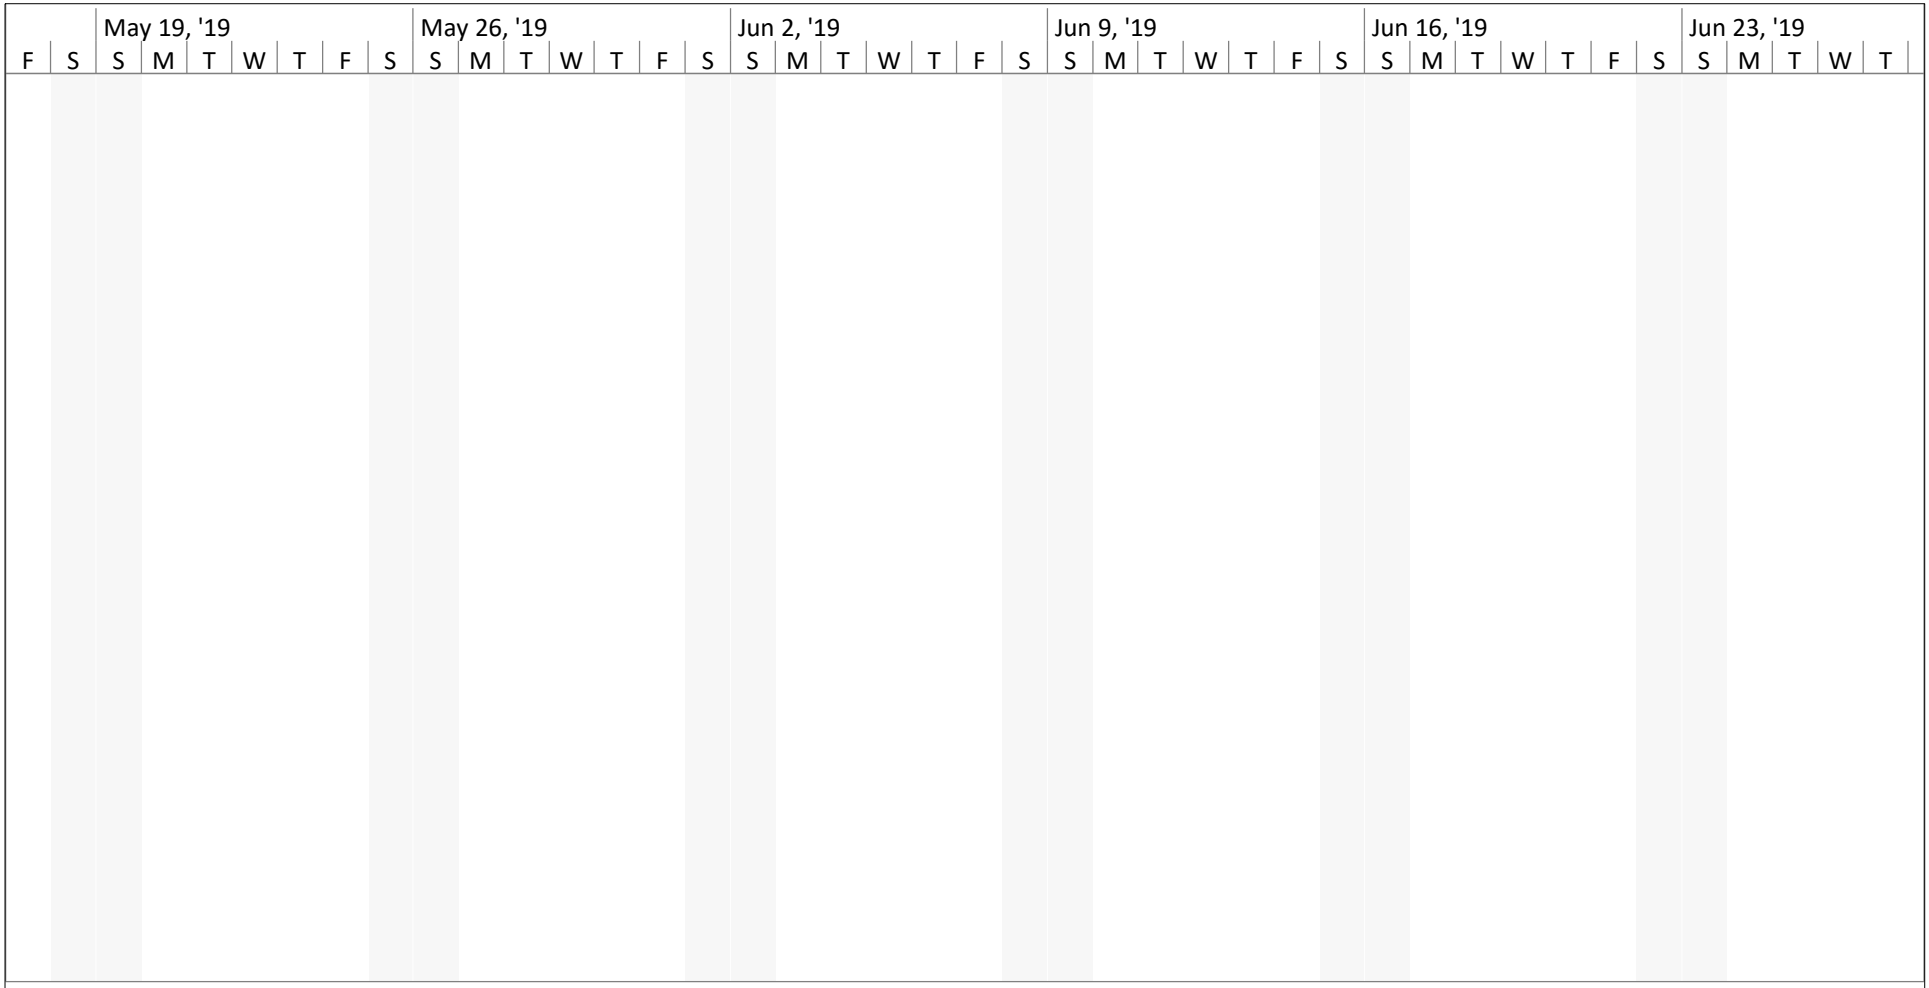


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

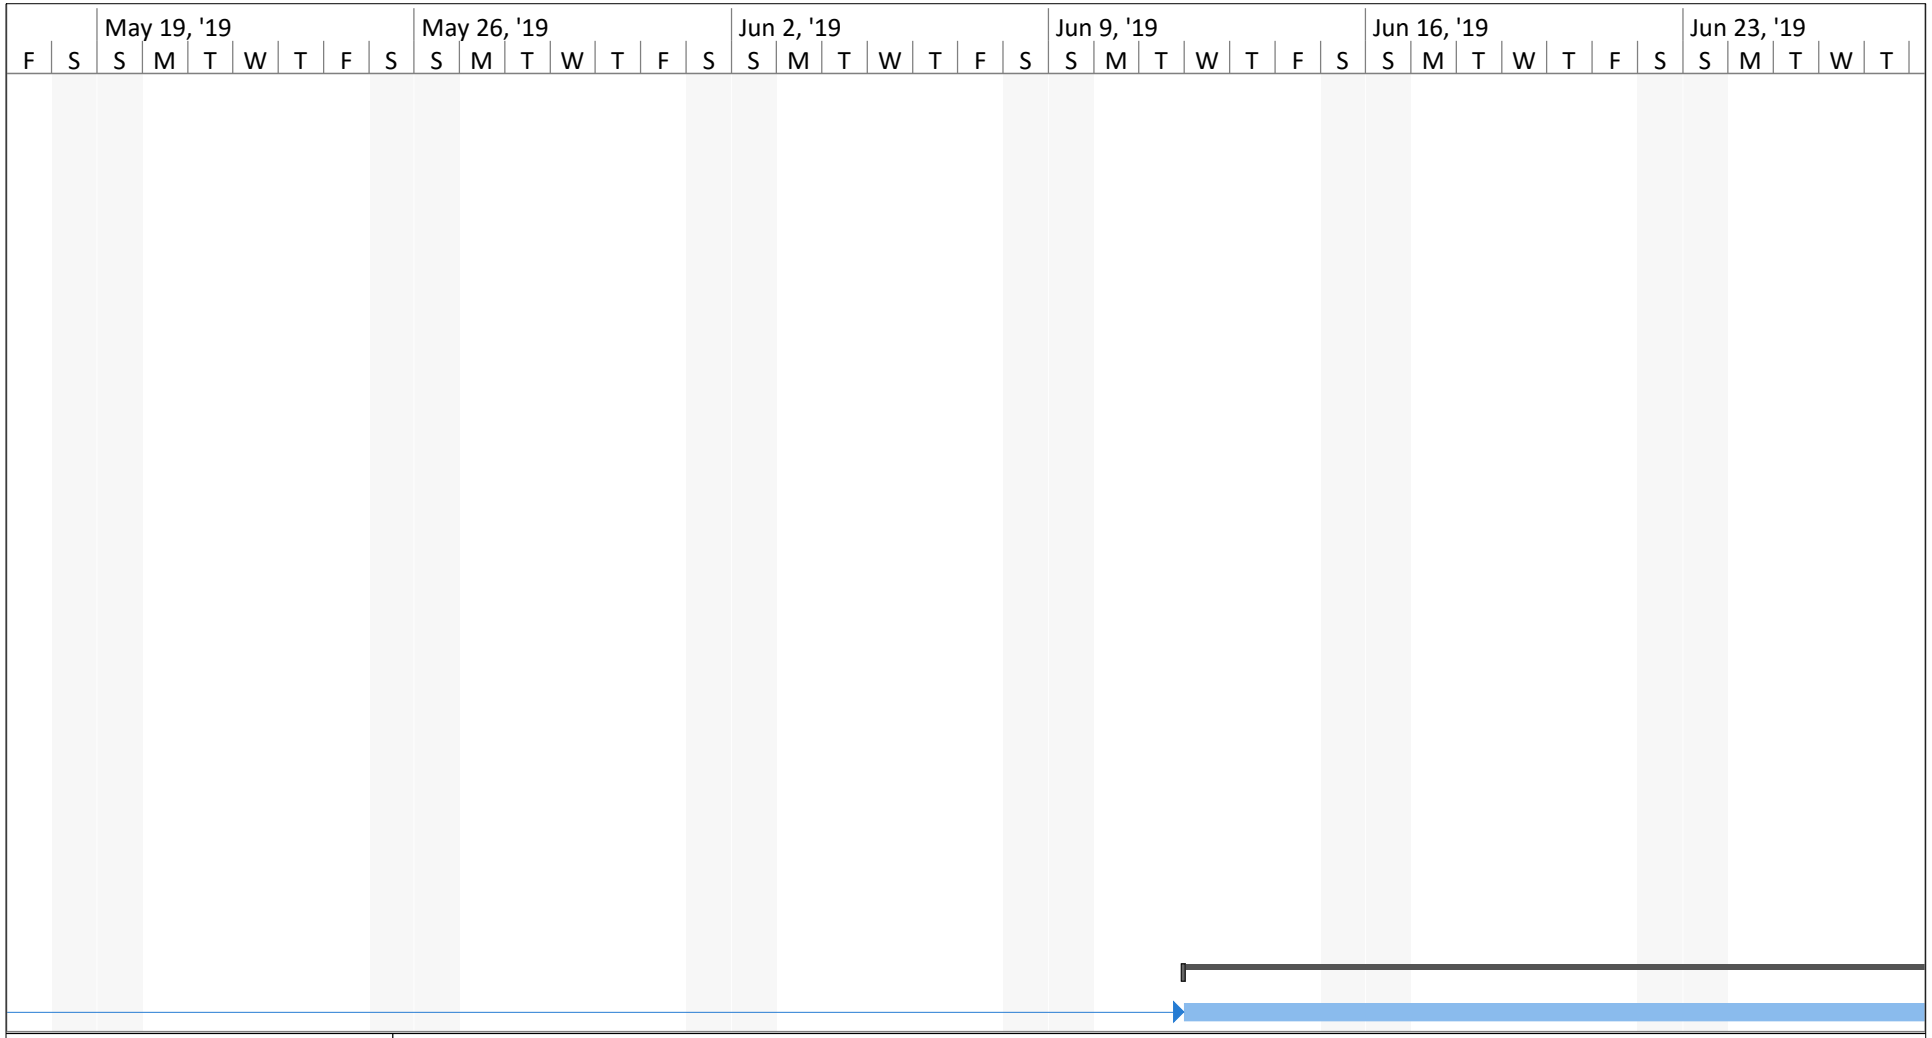


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

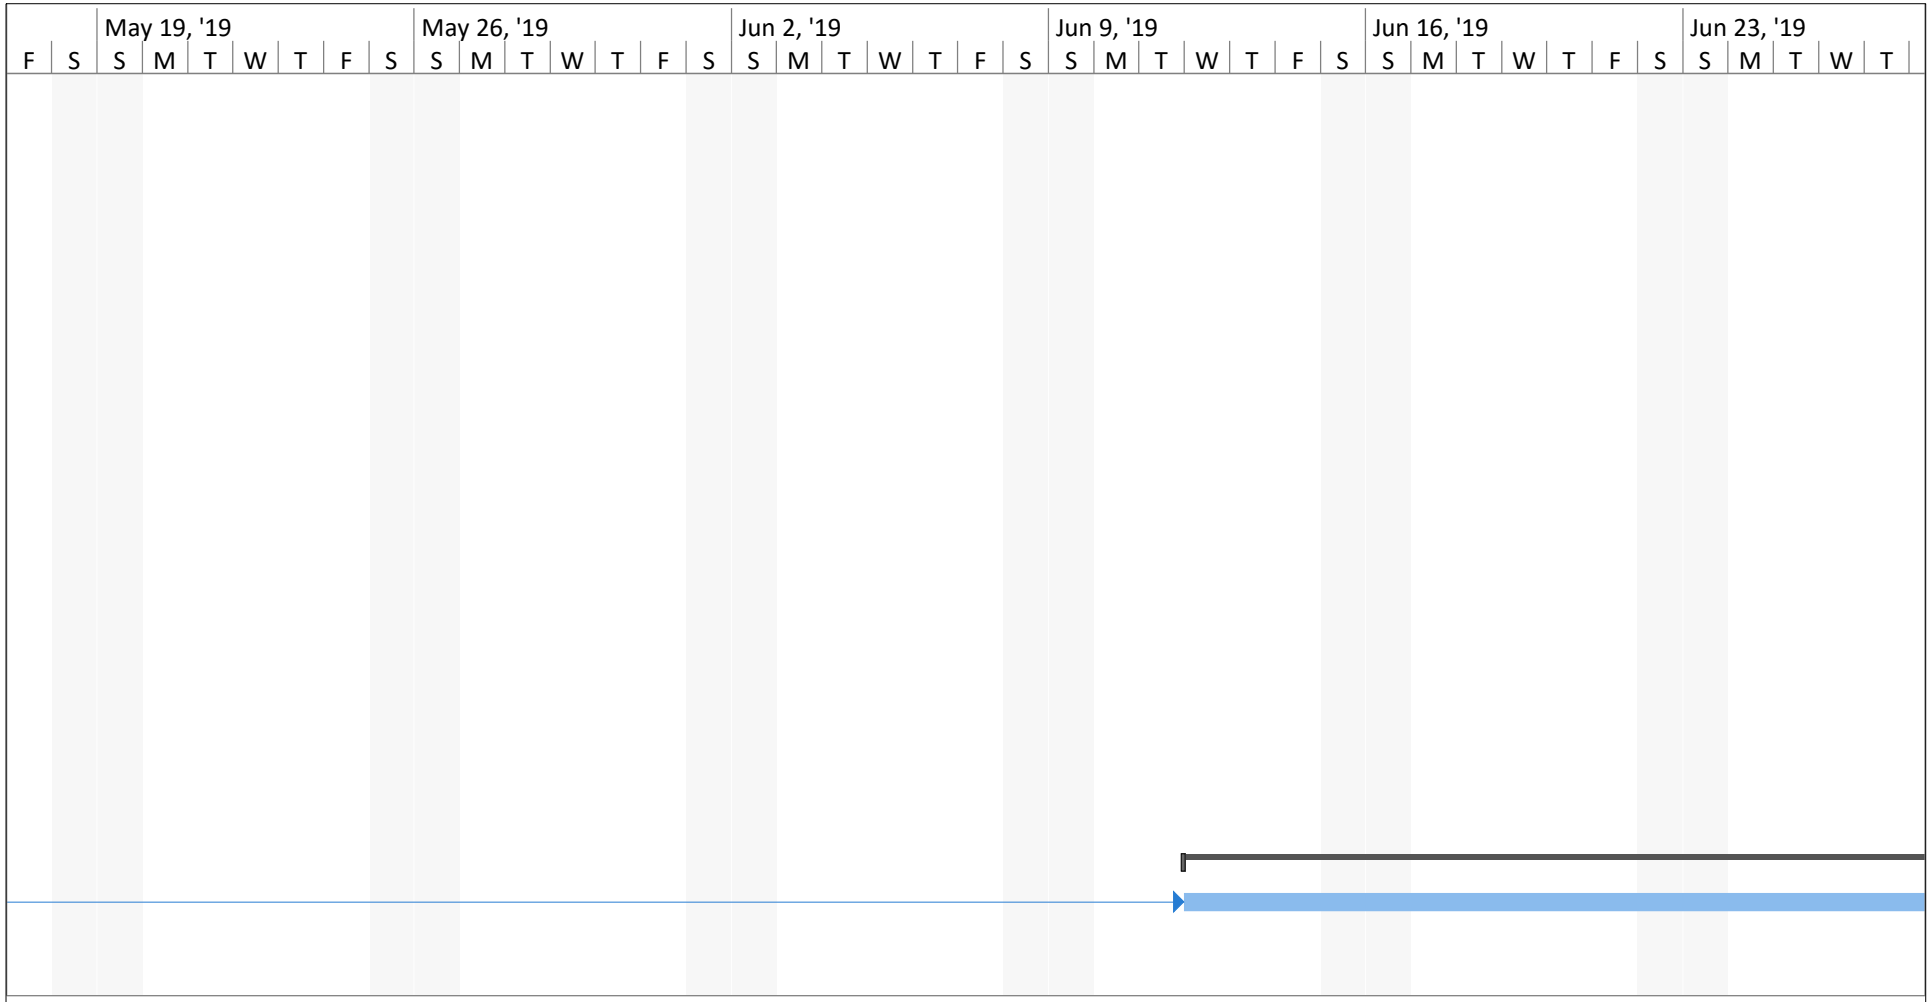


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

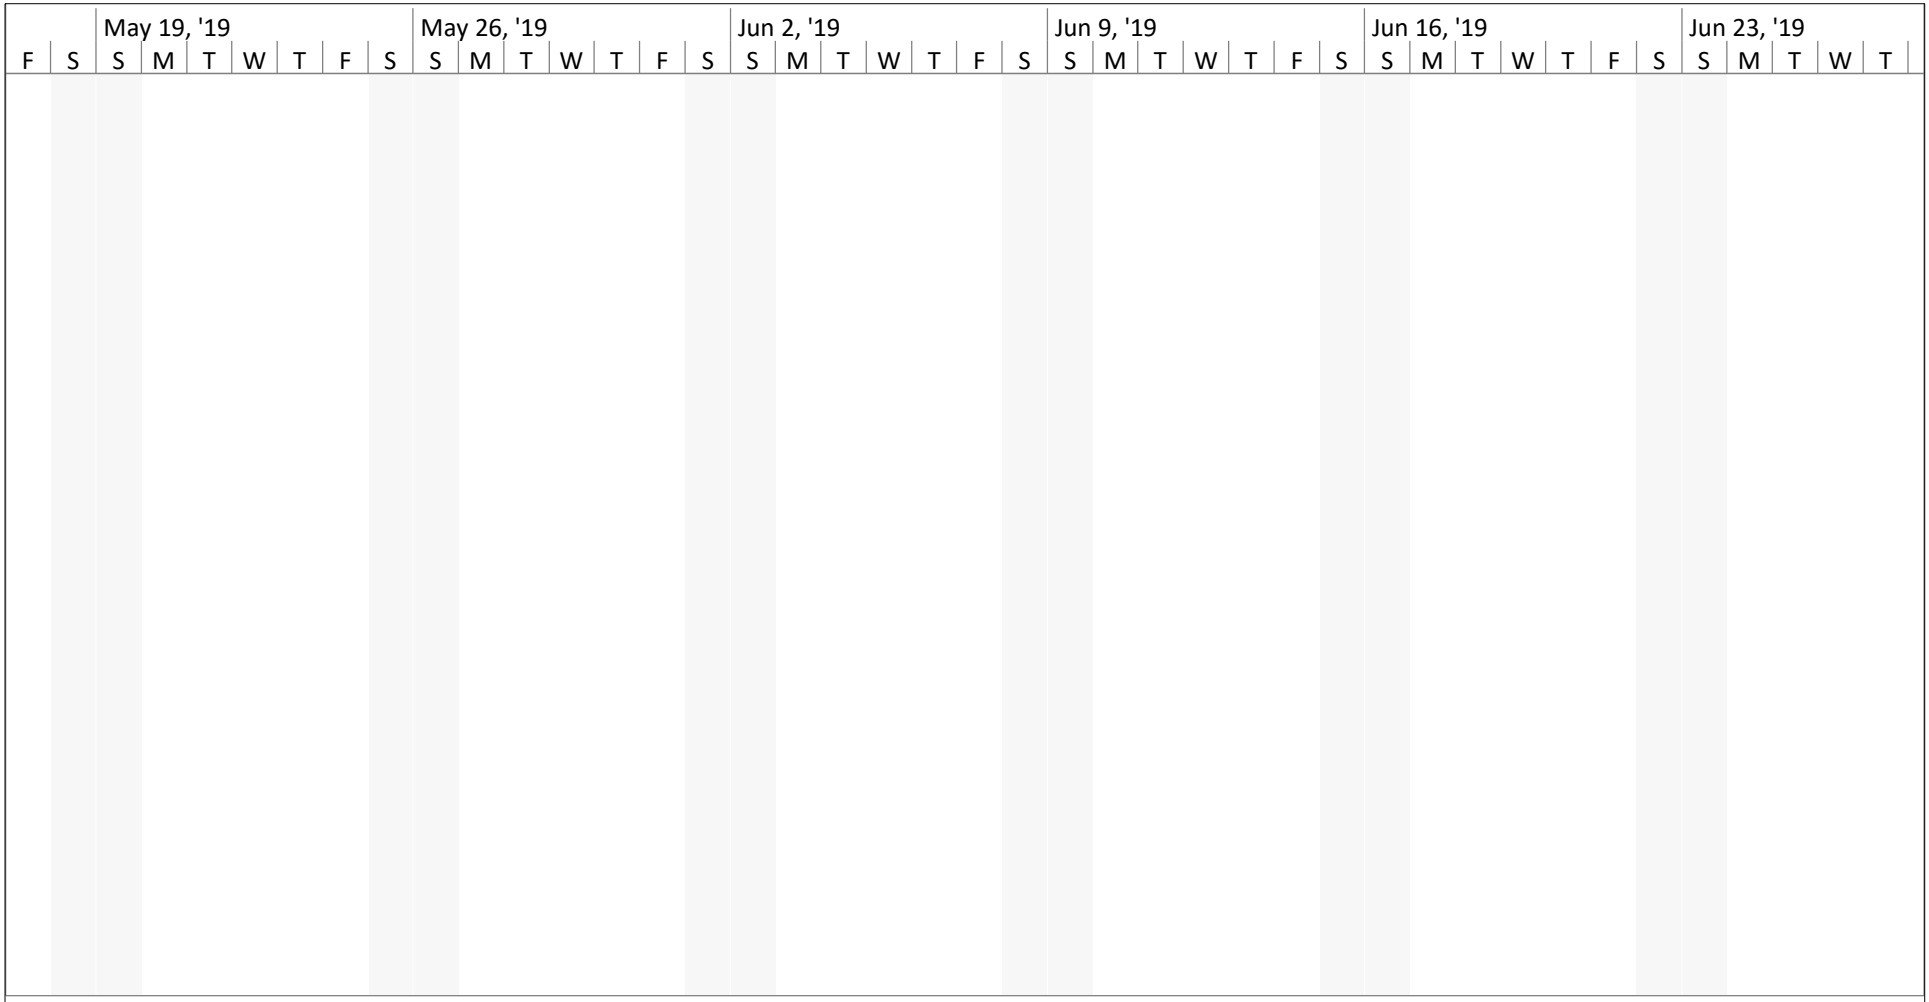


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

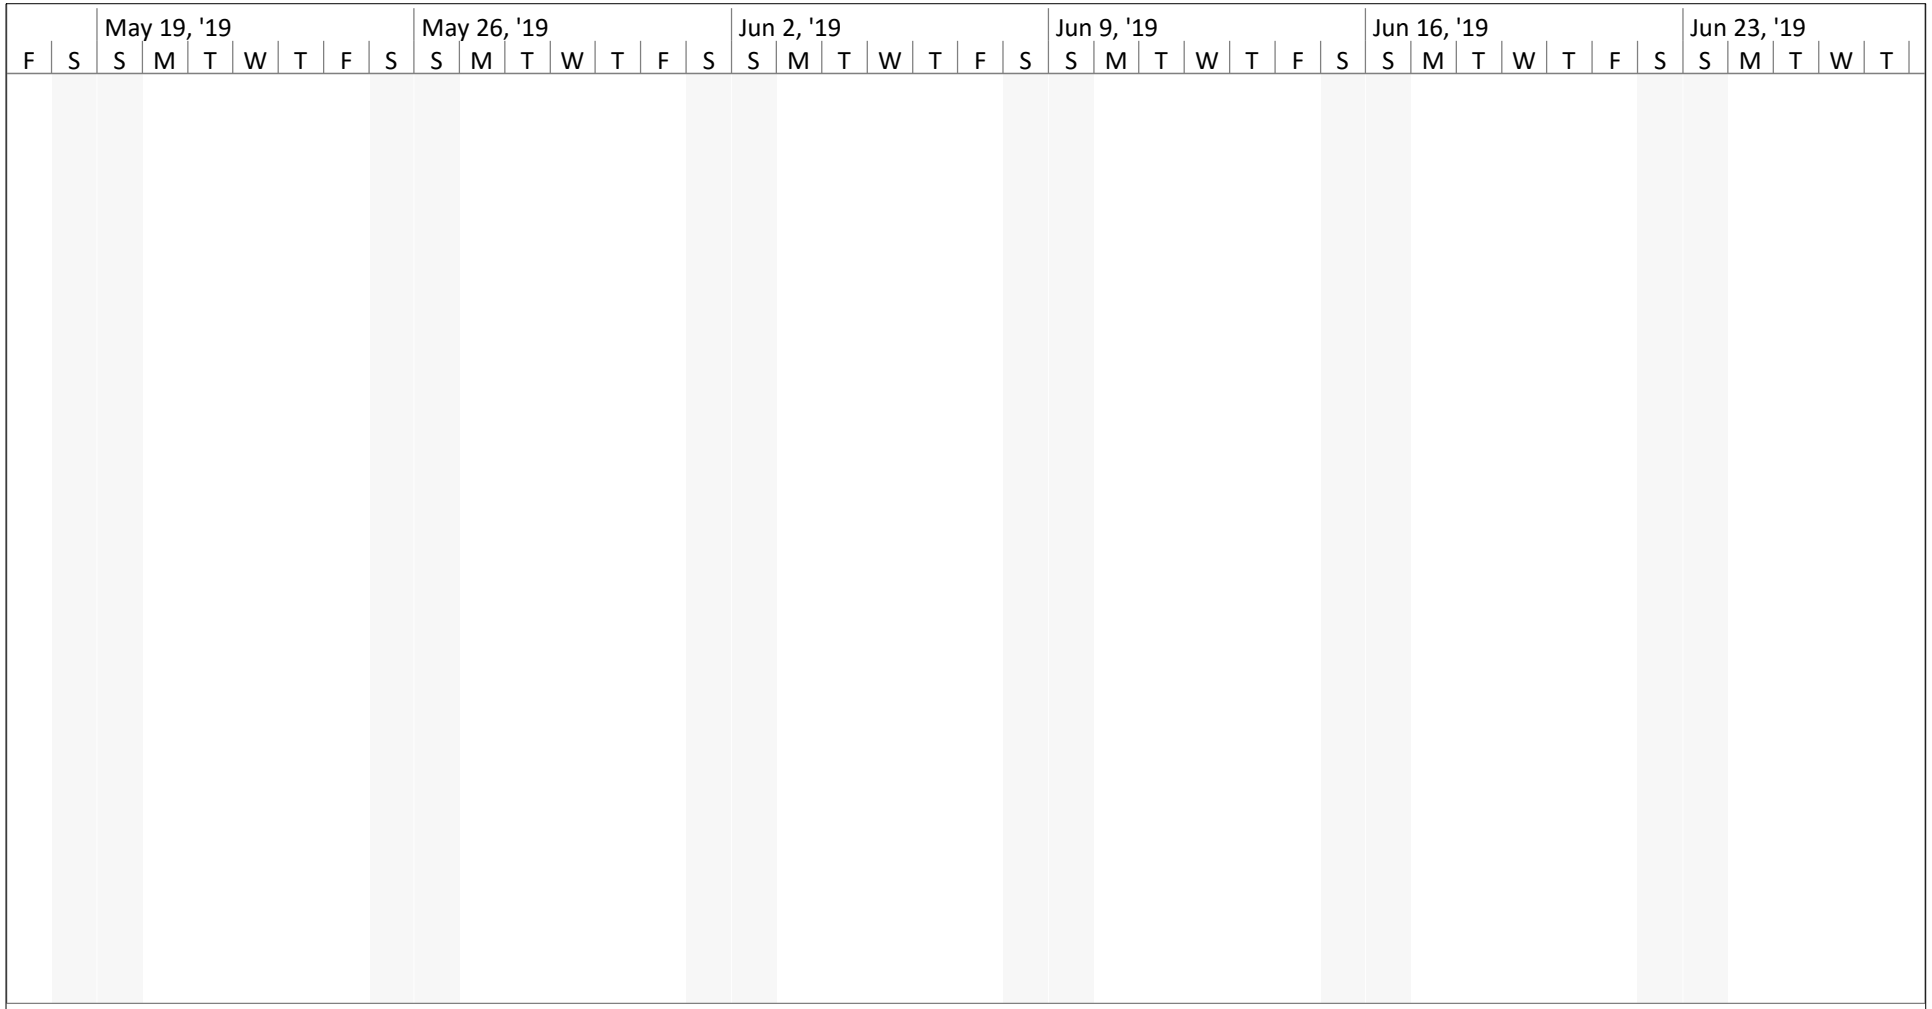


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

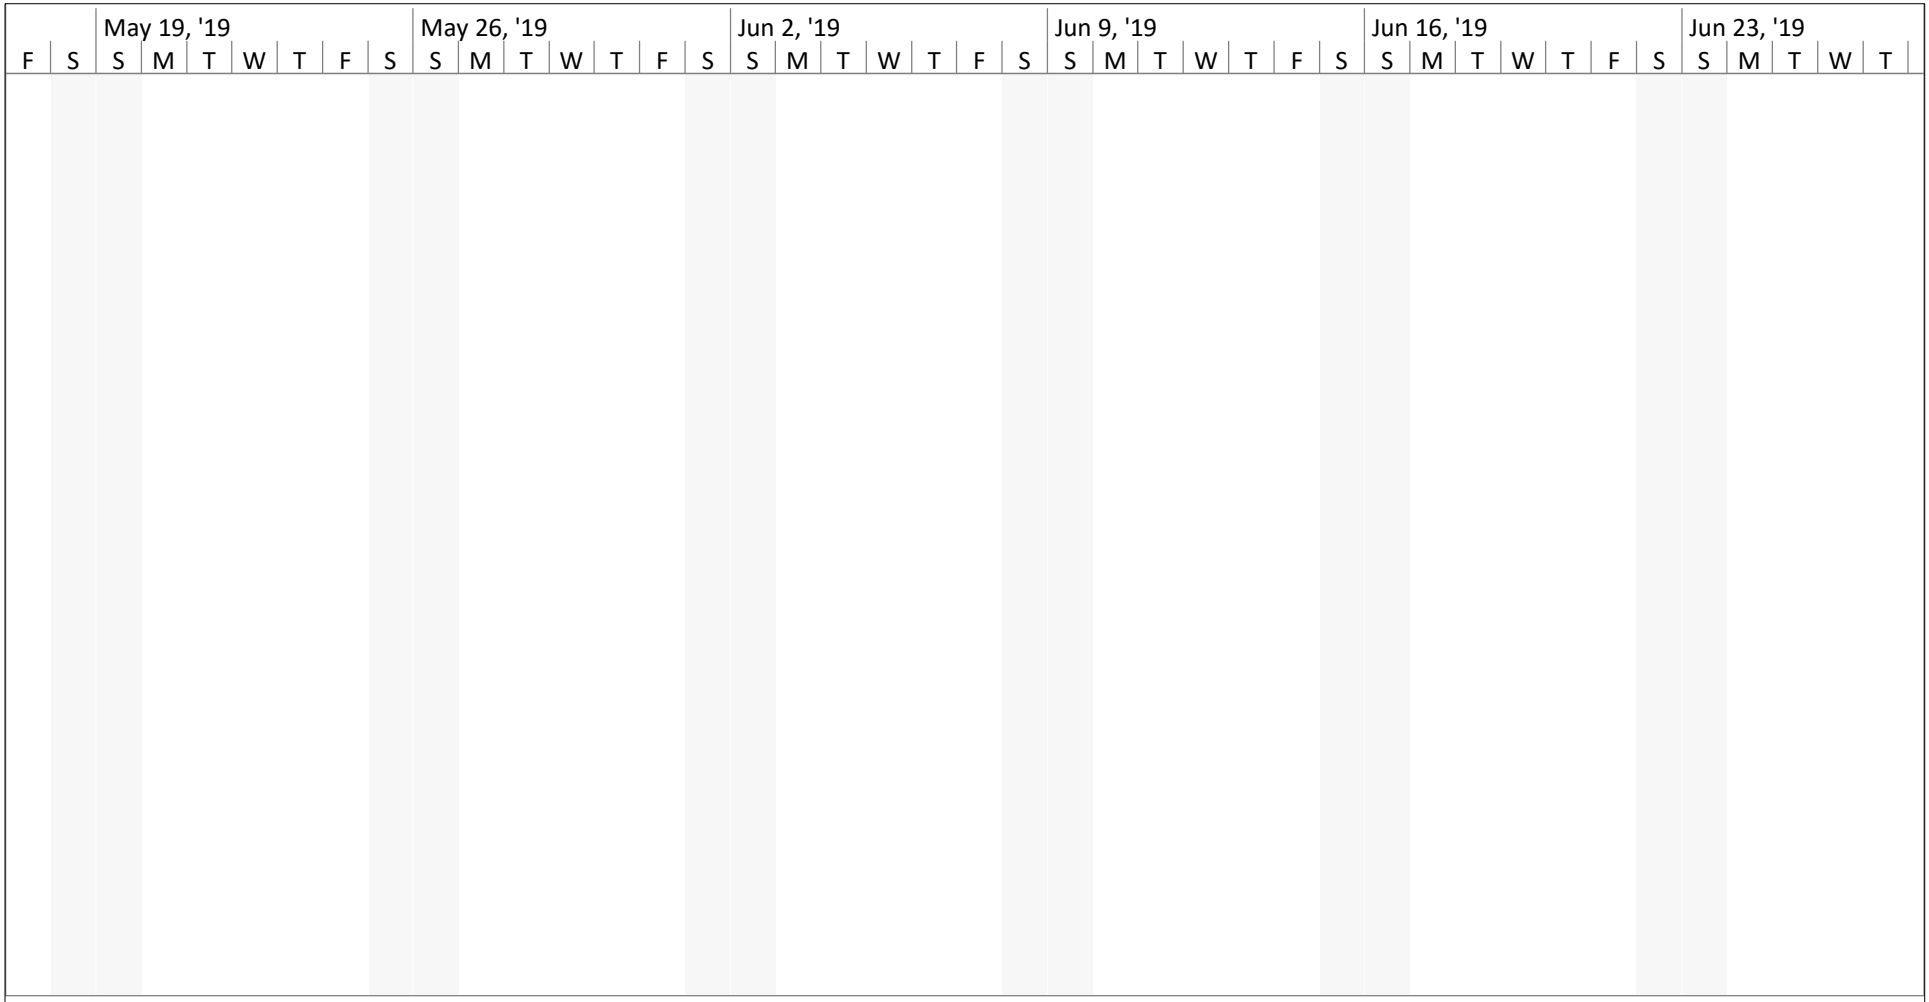


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |




Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | Inactive Task | Start-only |
| Split | Inactive Milestone | Finish-only |
| Milestone | Inactive Summary | Deadline |
| Summary | Manual Task | Progress |
| Project Summary | Duration-only | Manual Progress |
| External Tasks | Manual Summary Rollup | |
| External Milestone | Manual Summary | |

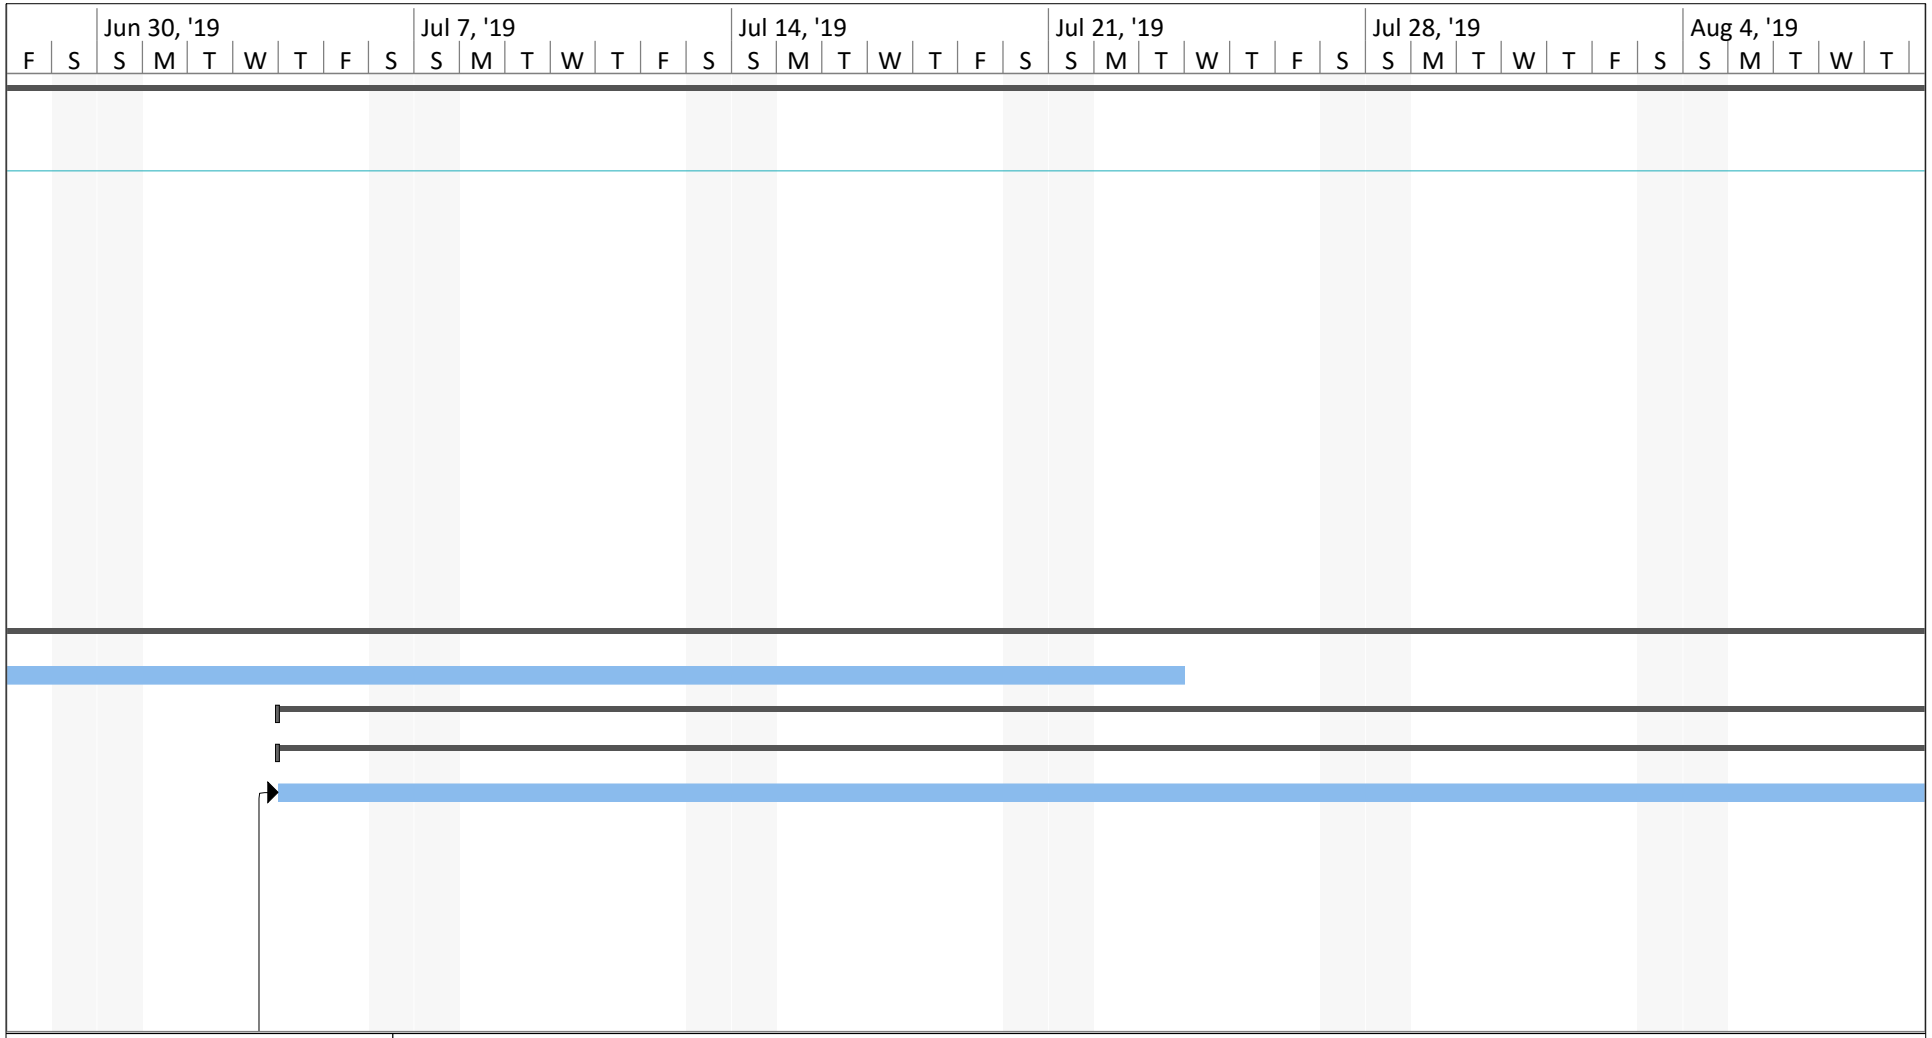


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

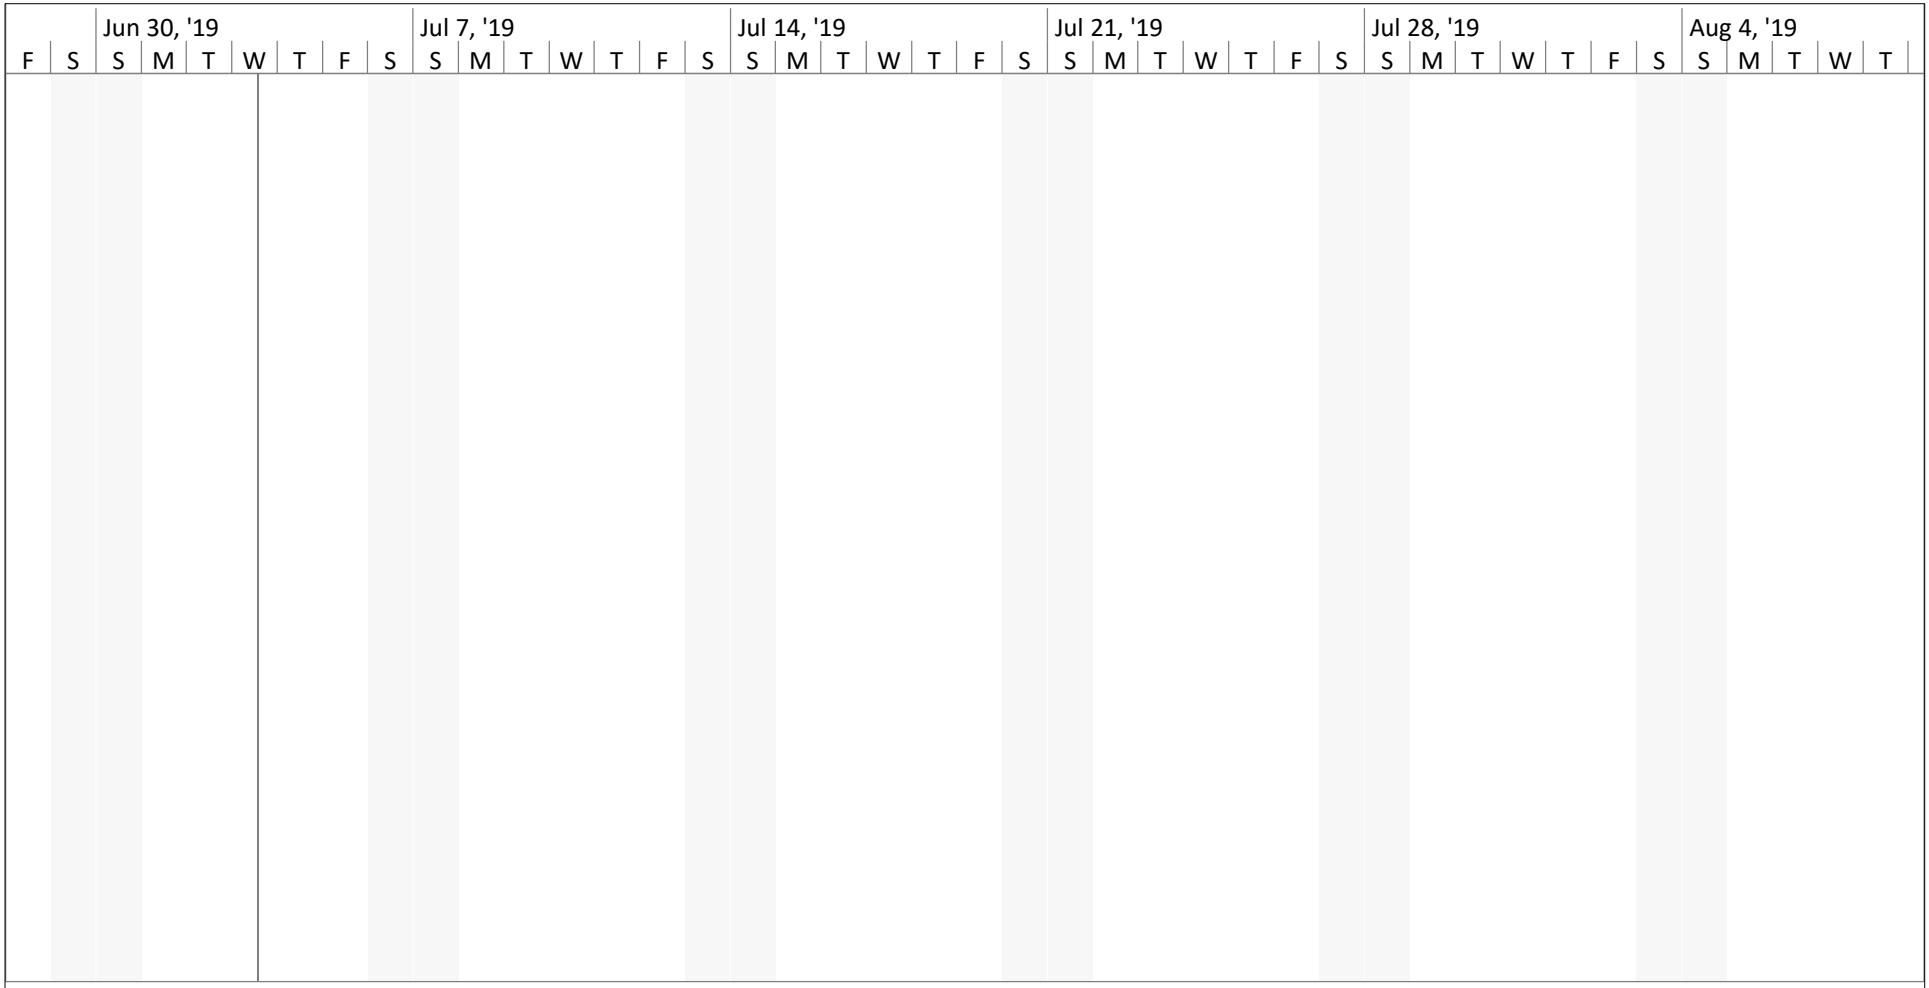


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

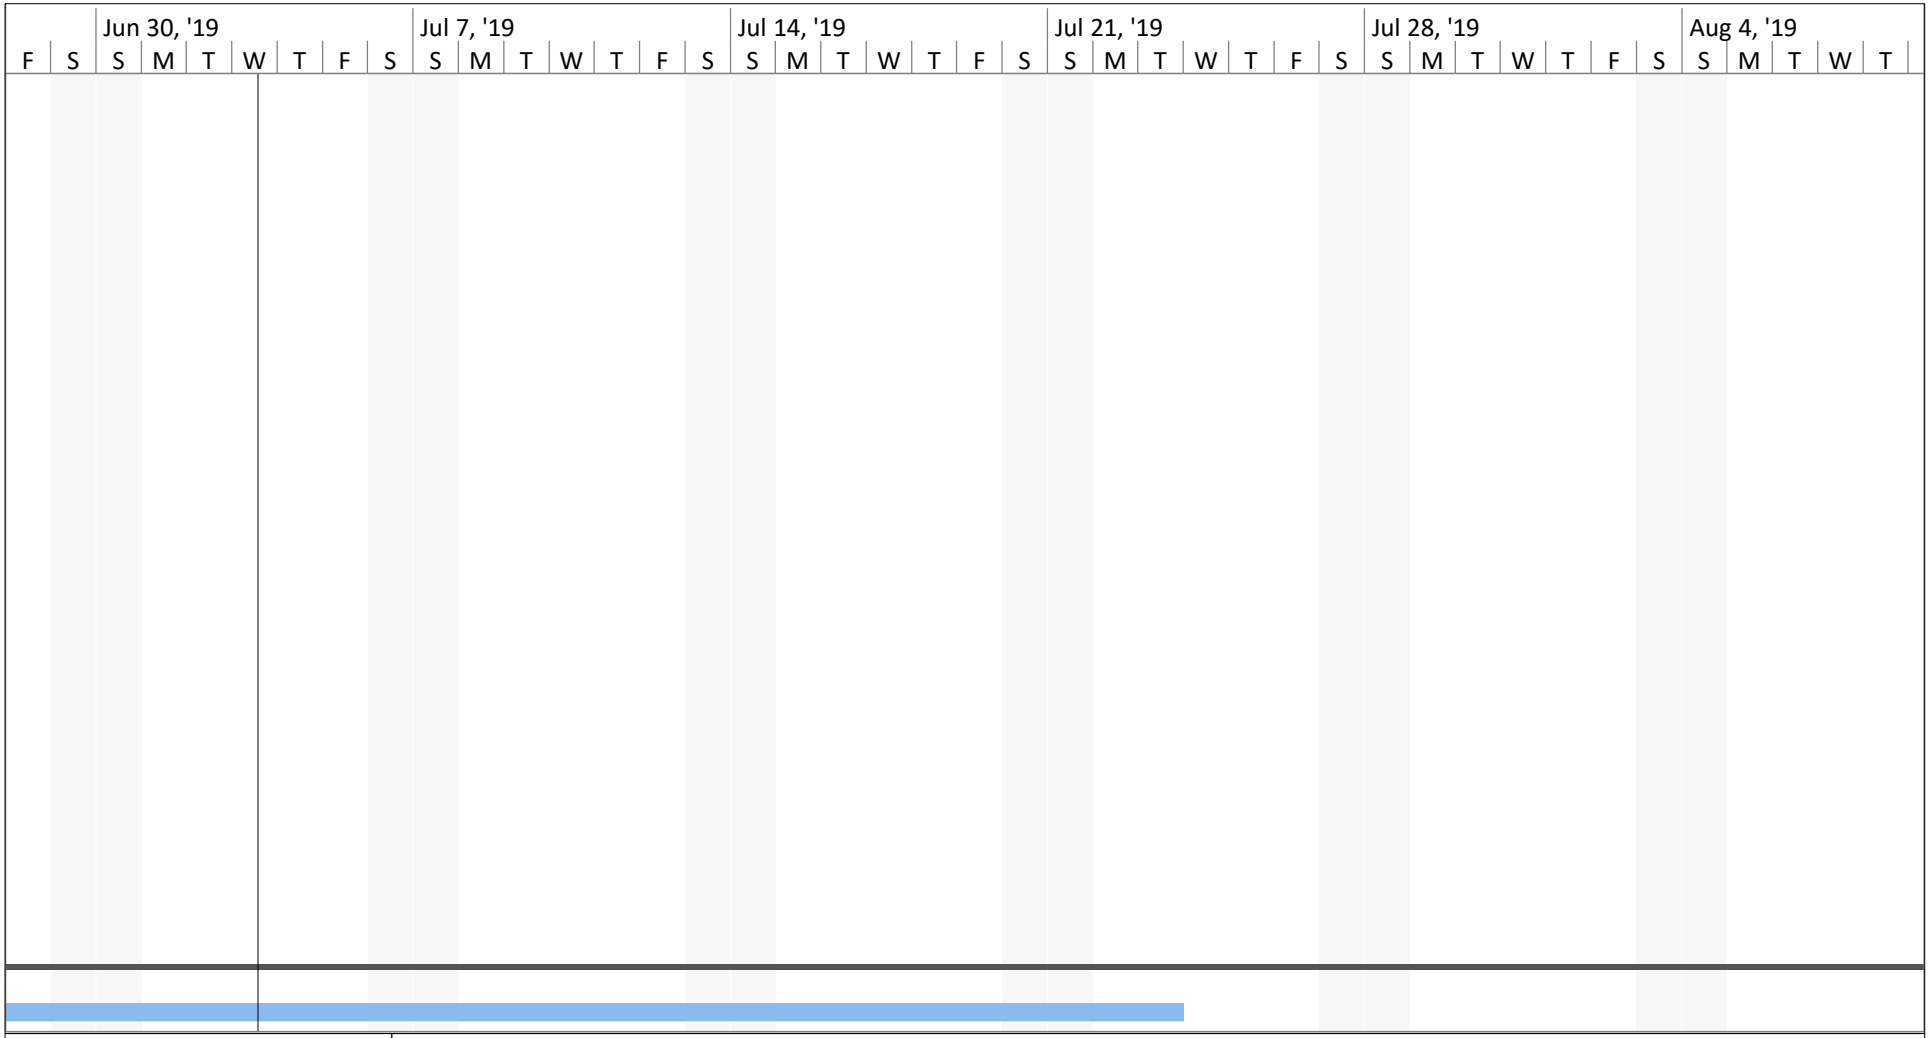


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

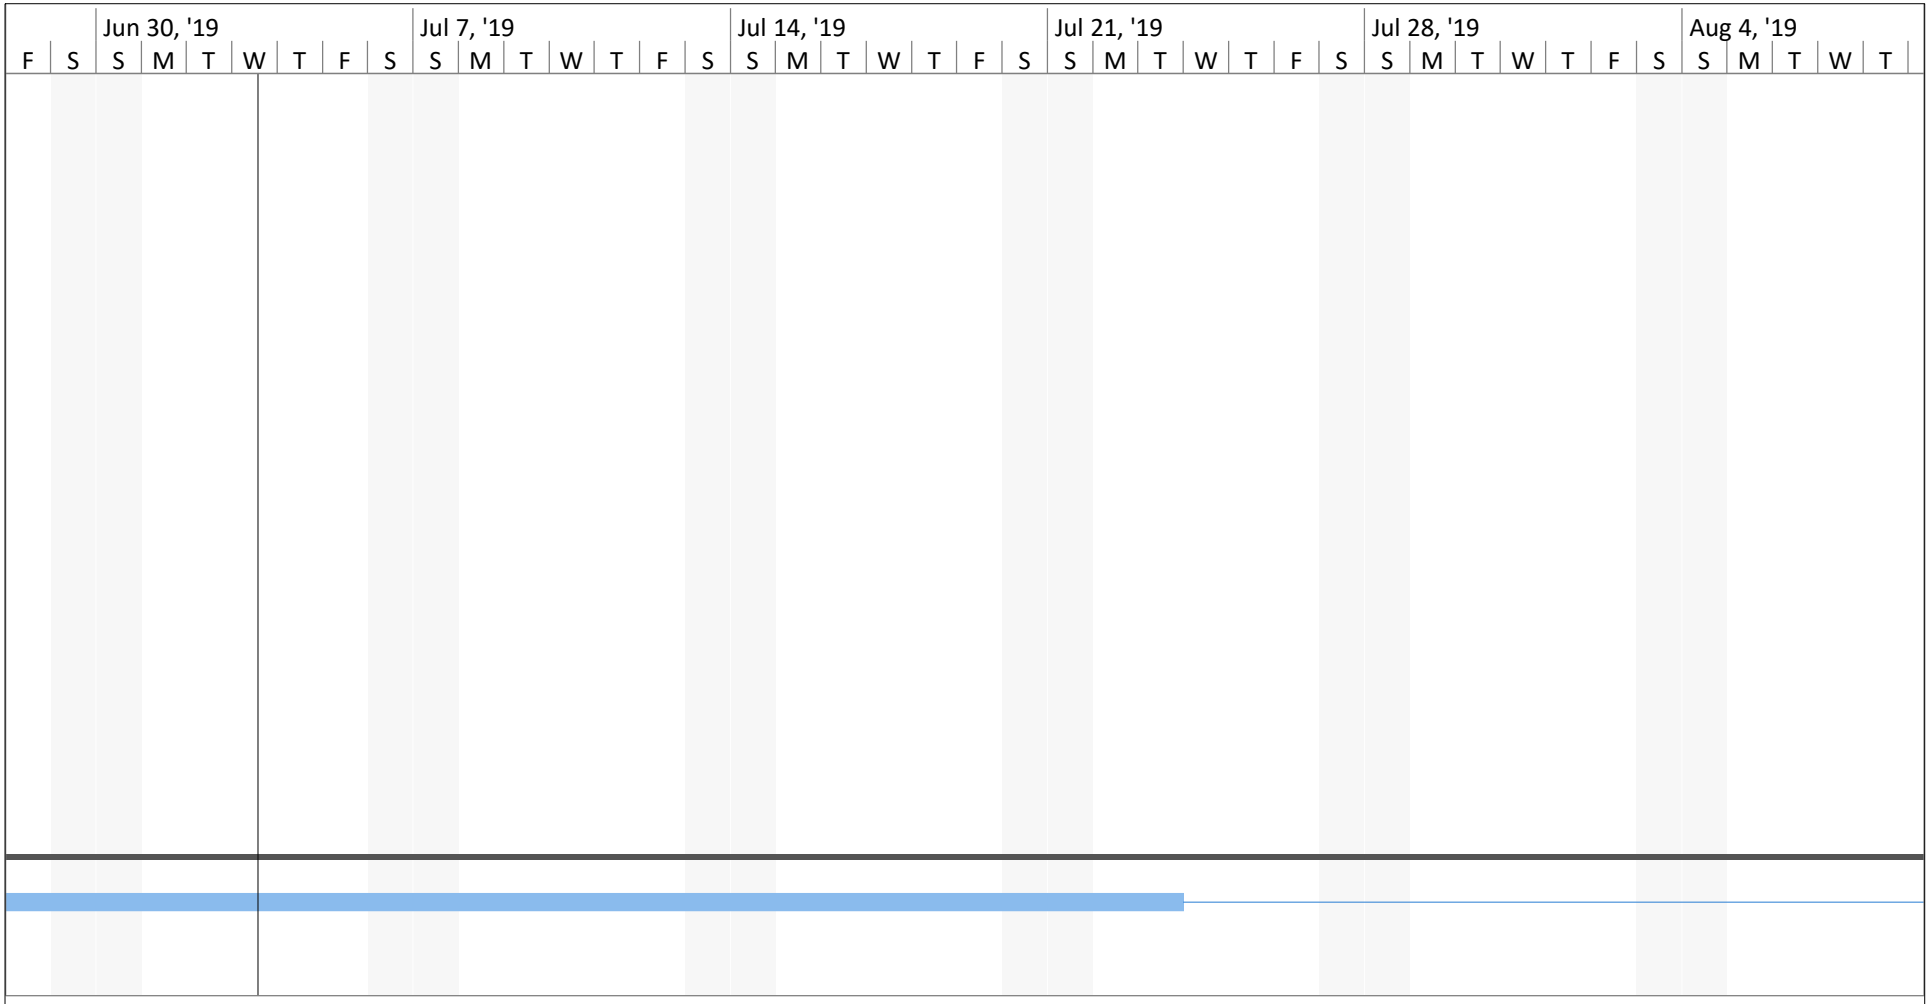


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

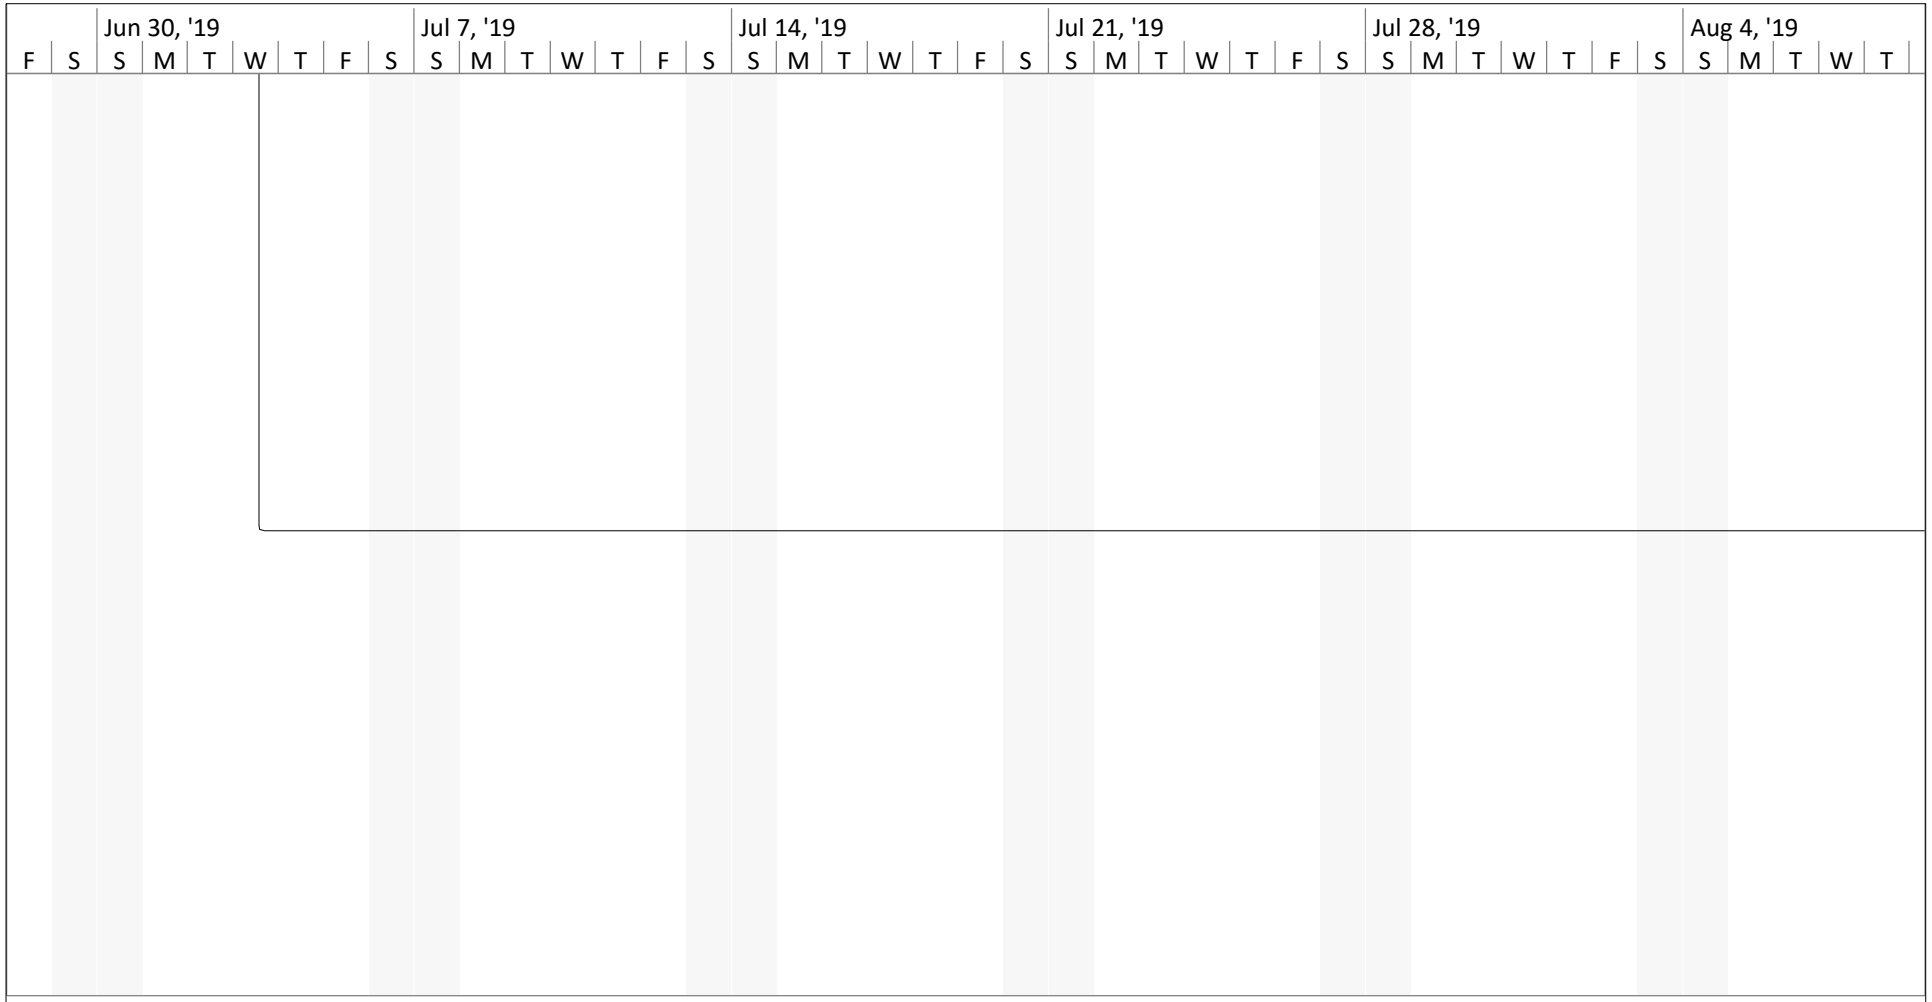


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

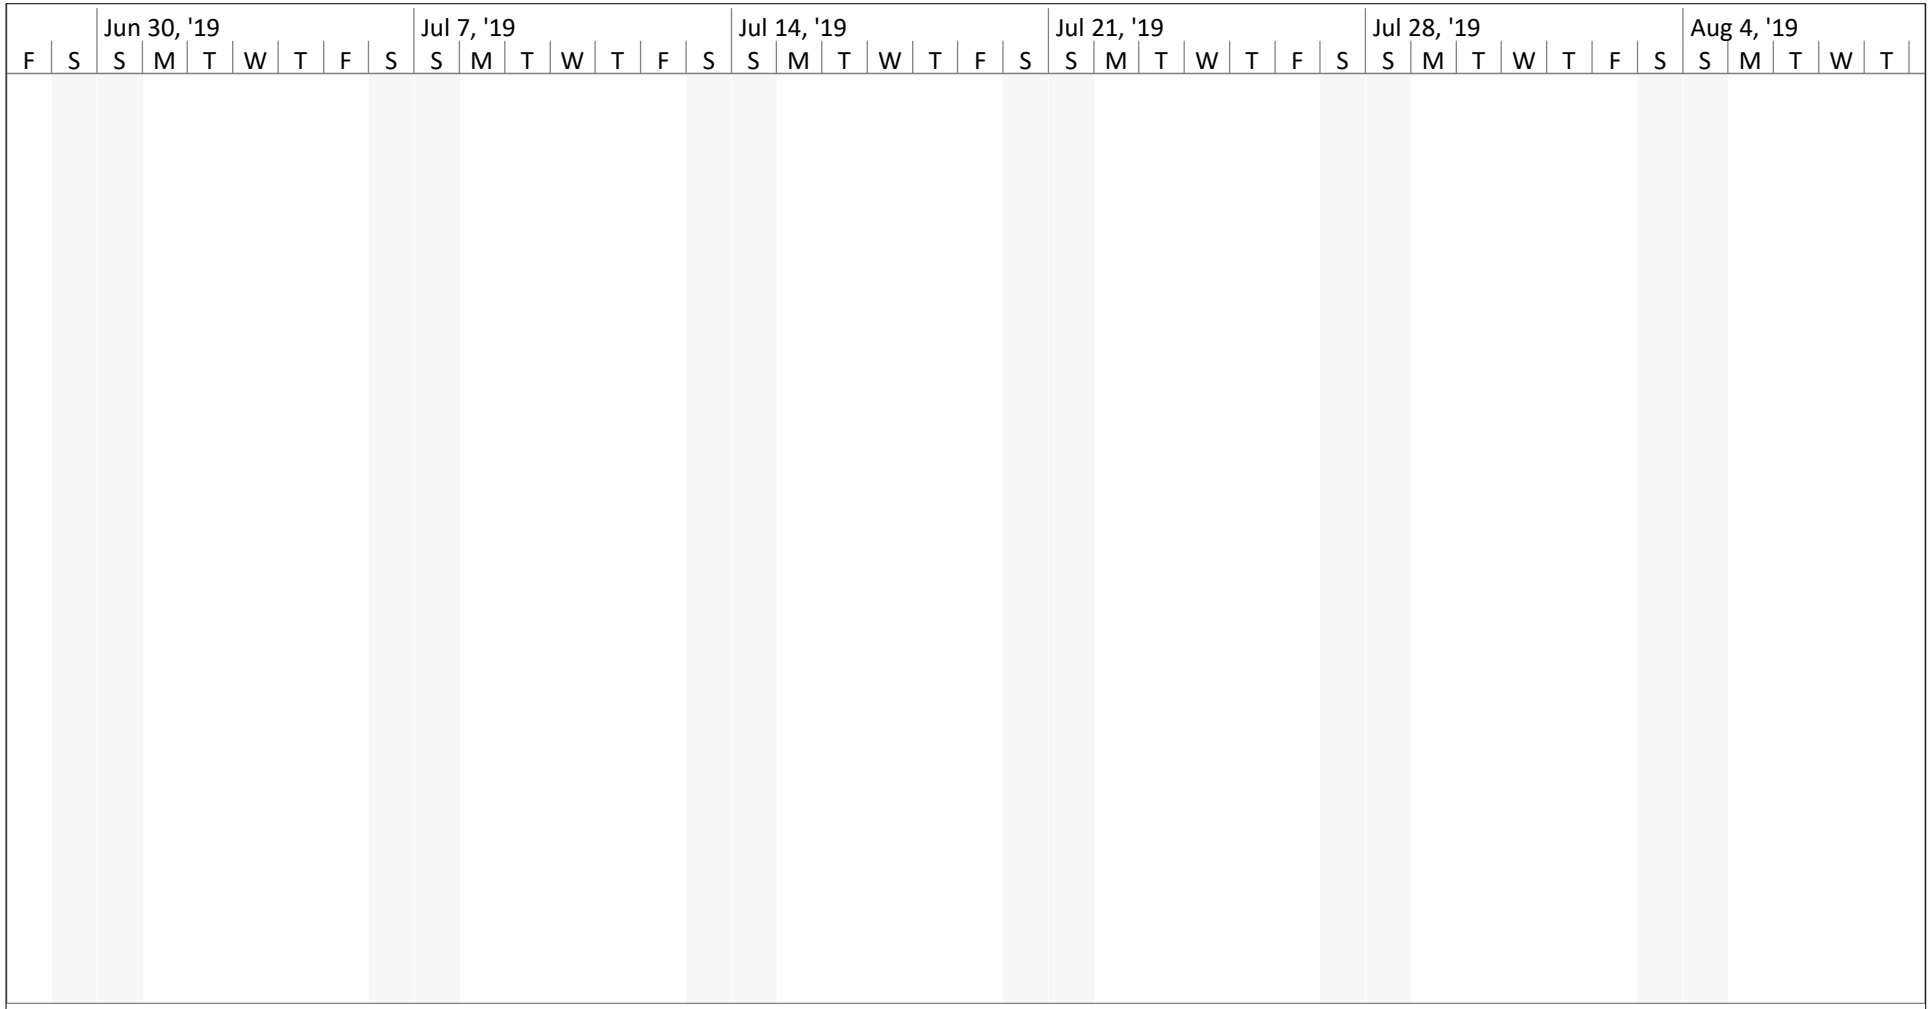


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

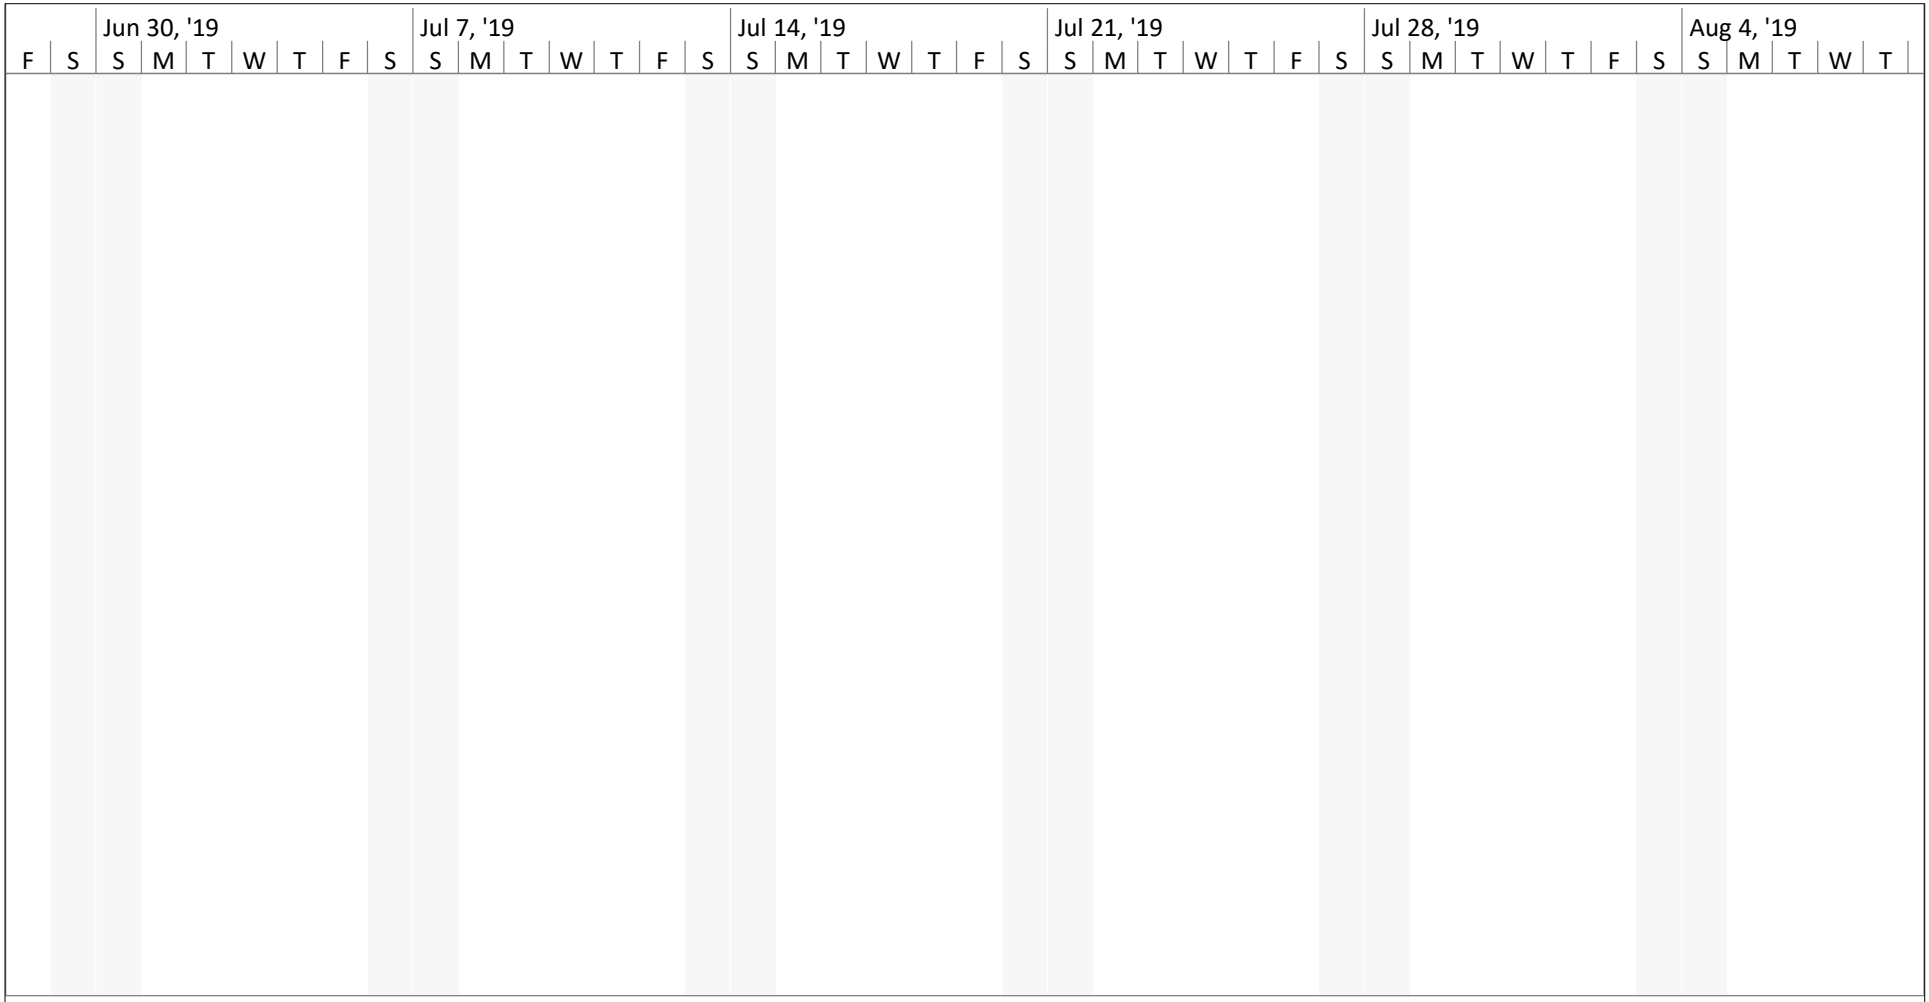


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |




Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

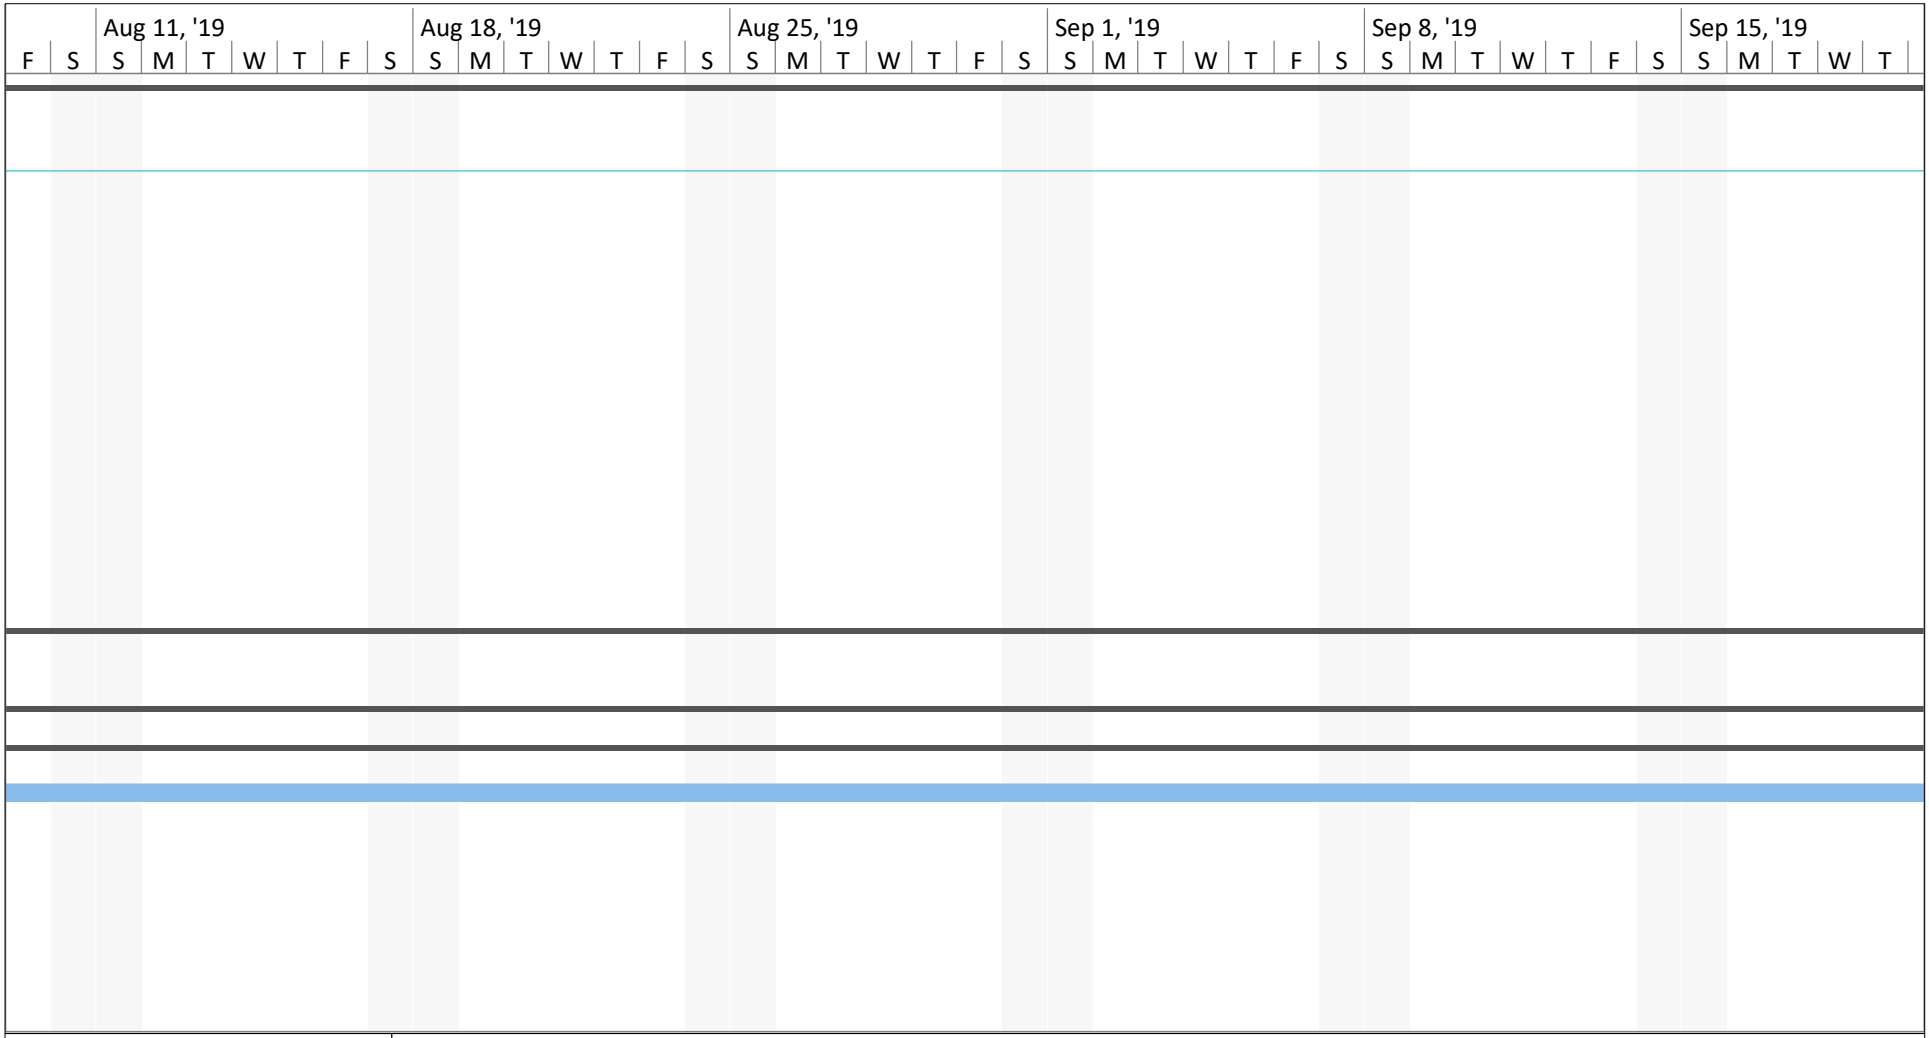


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

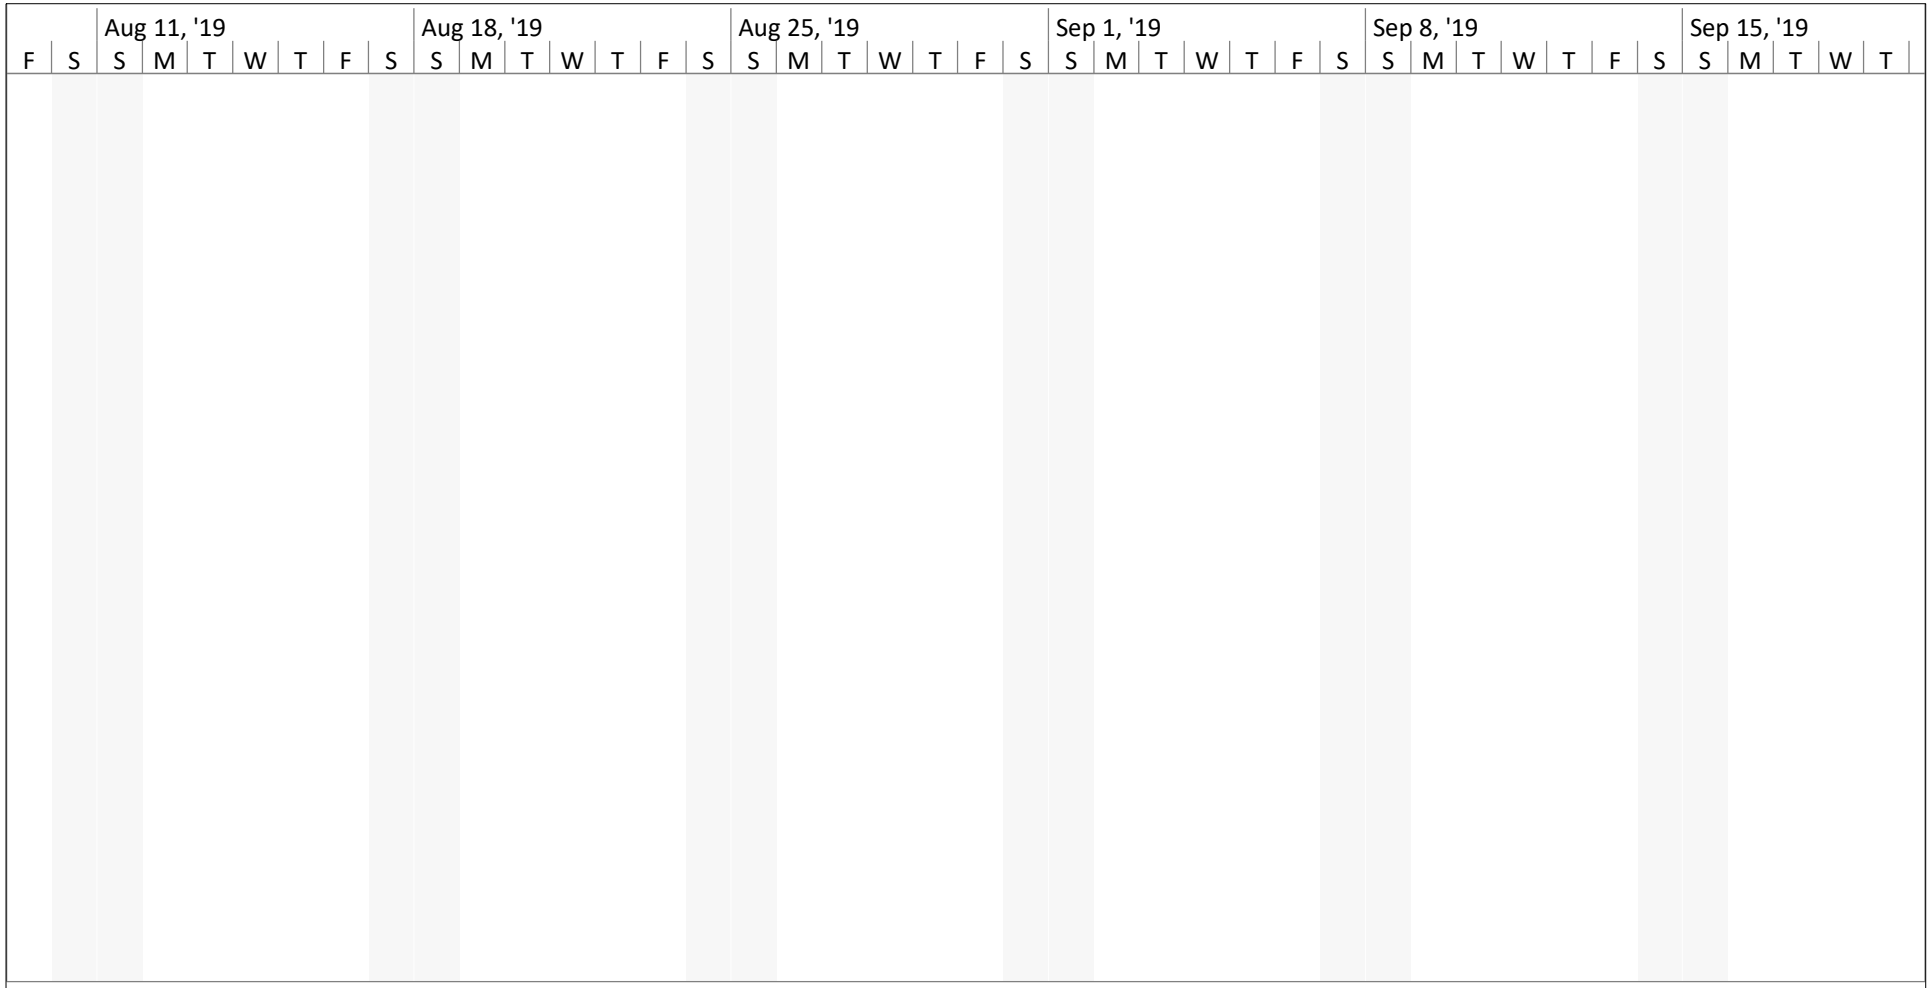


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

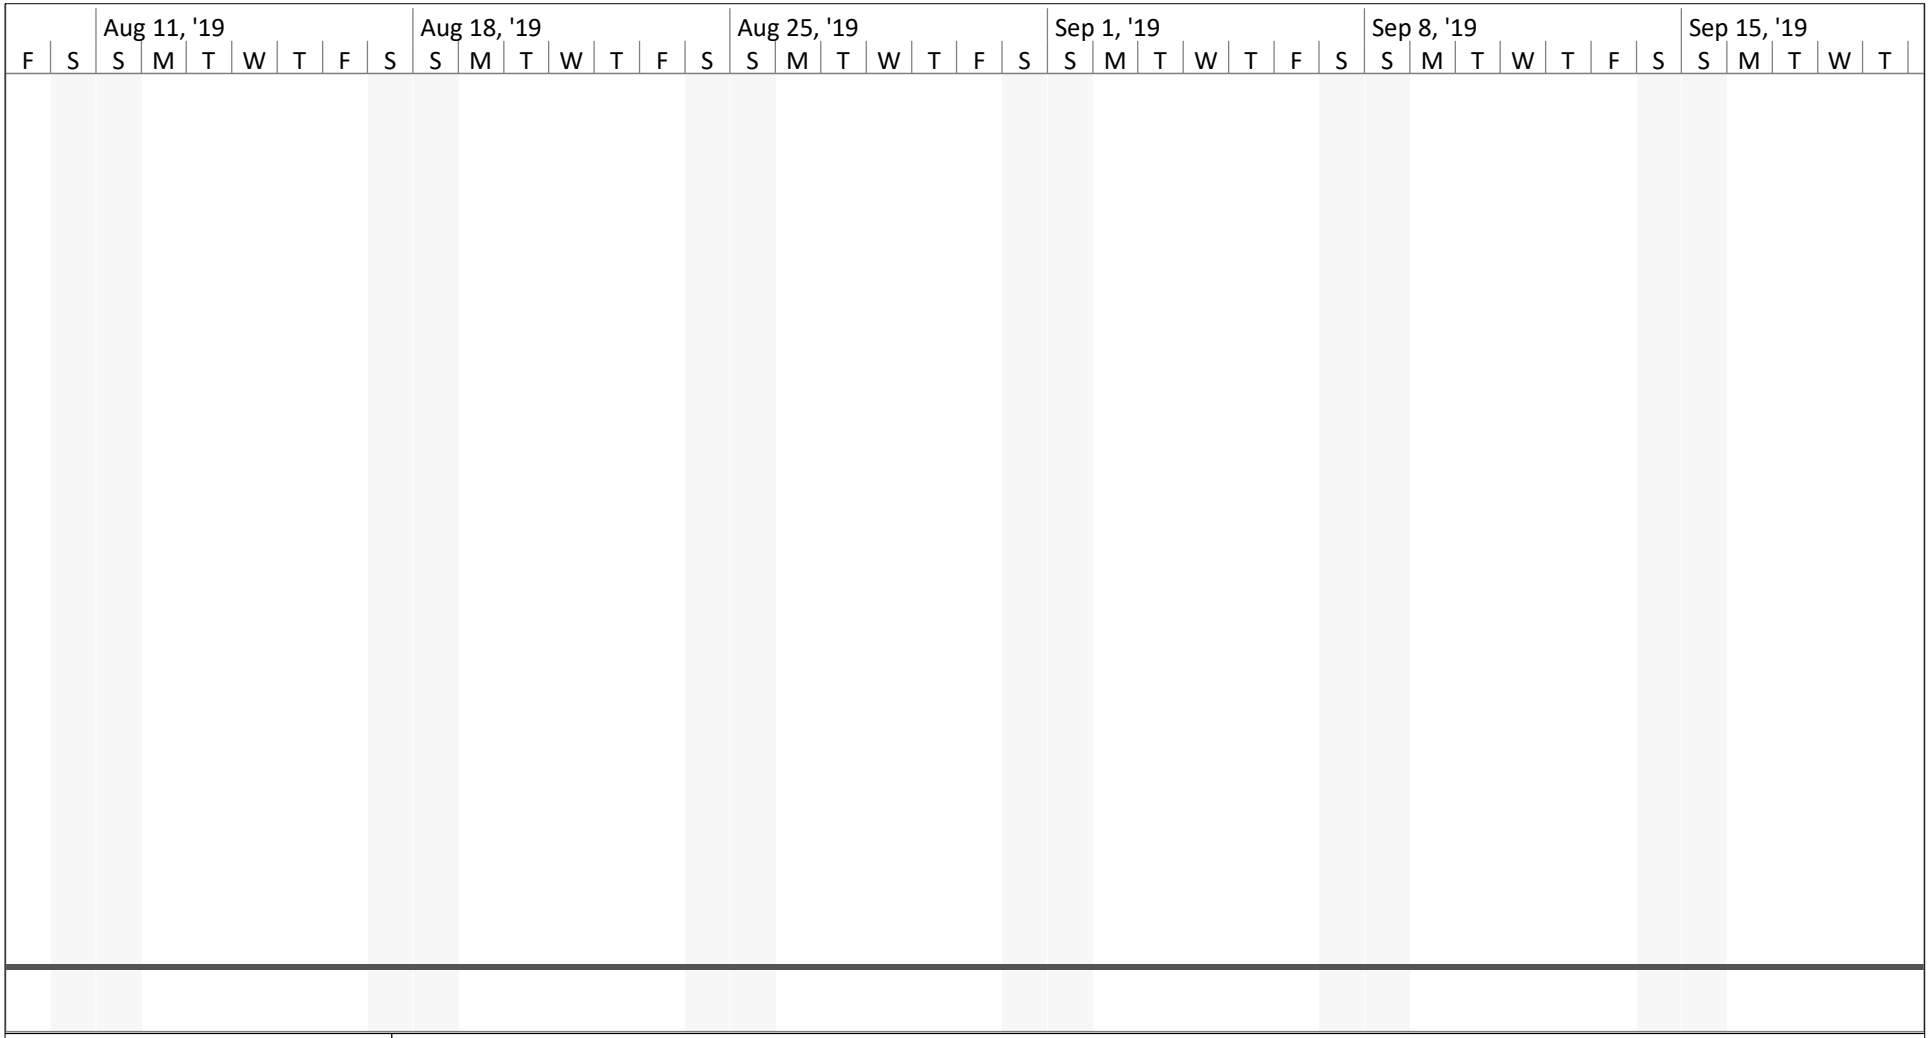


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

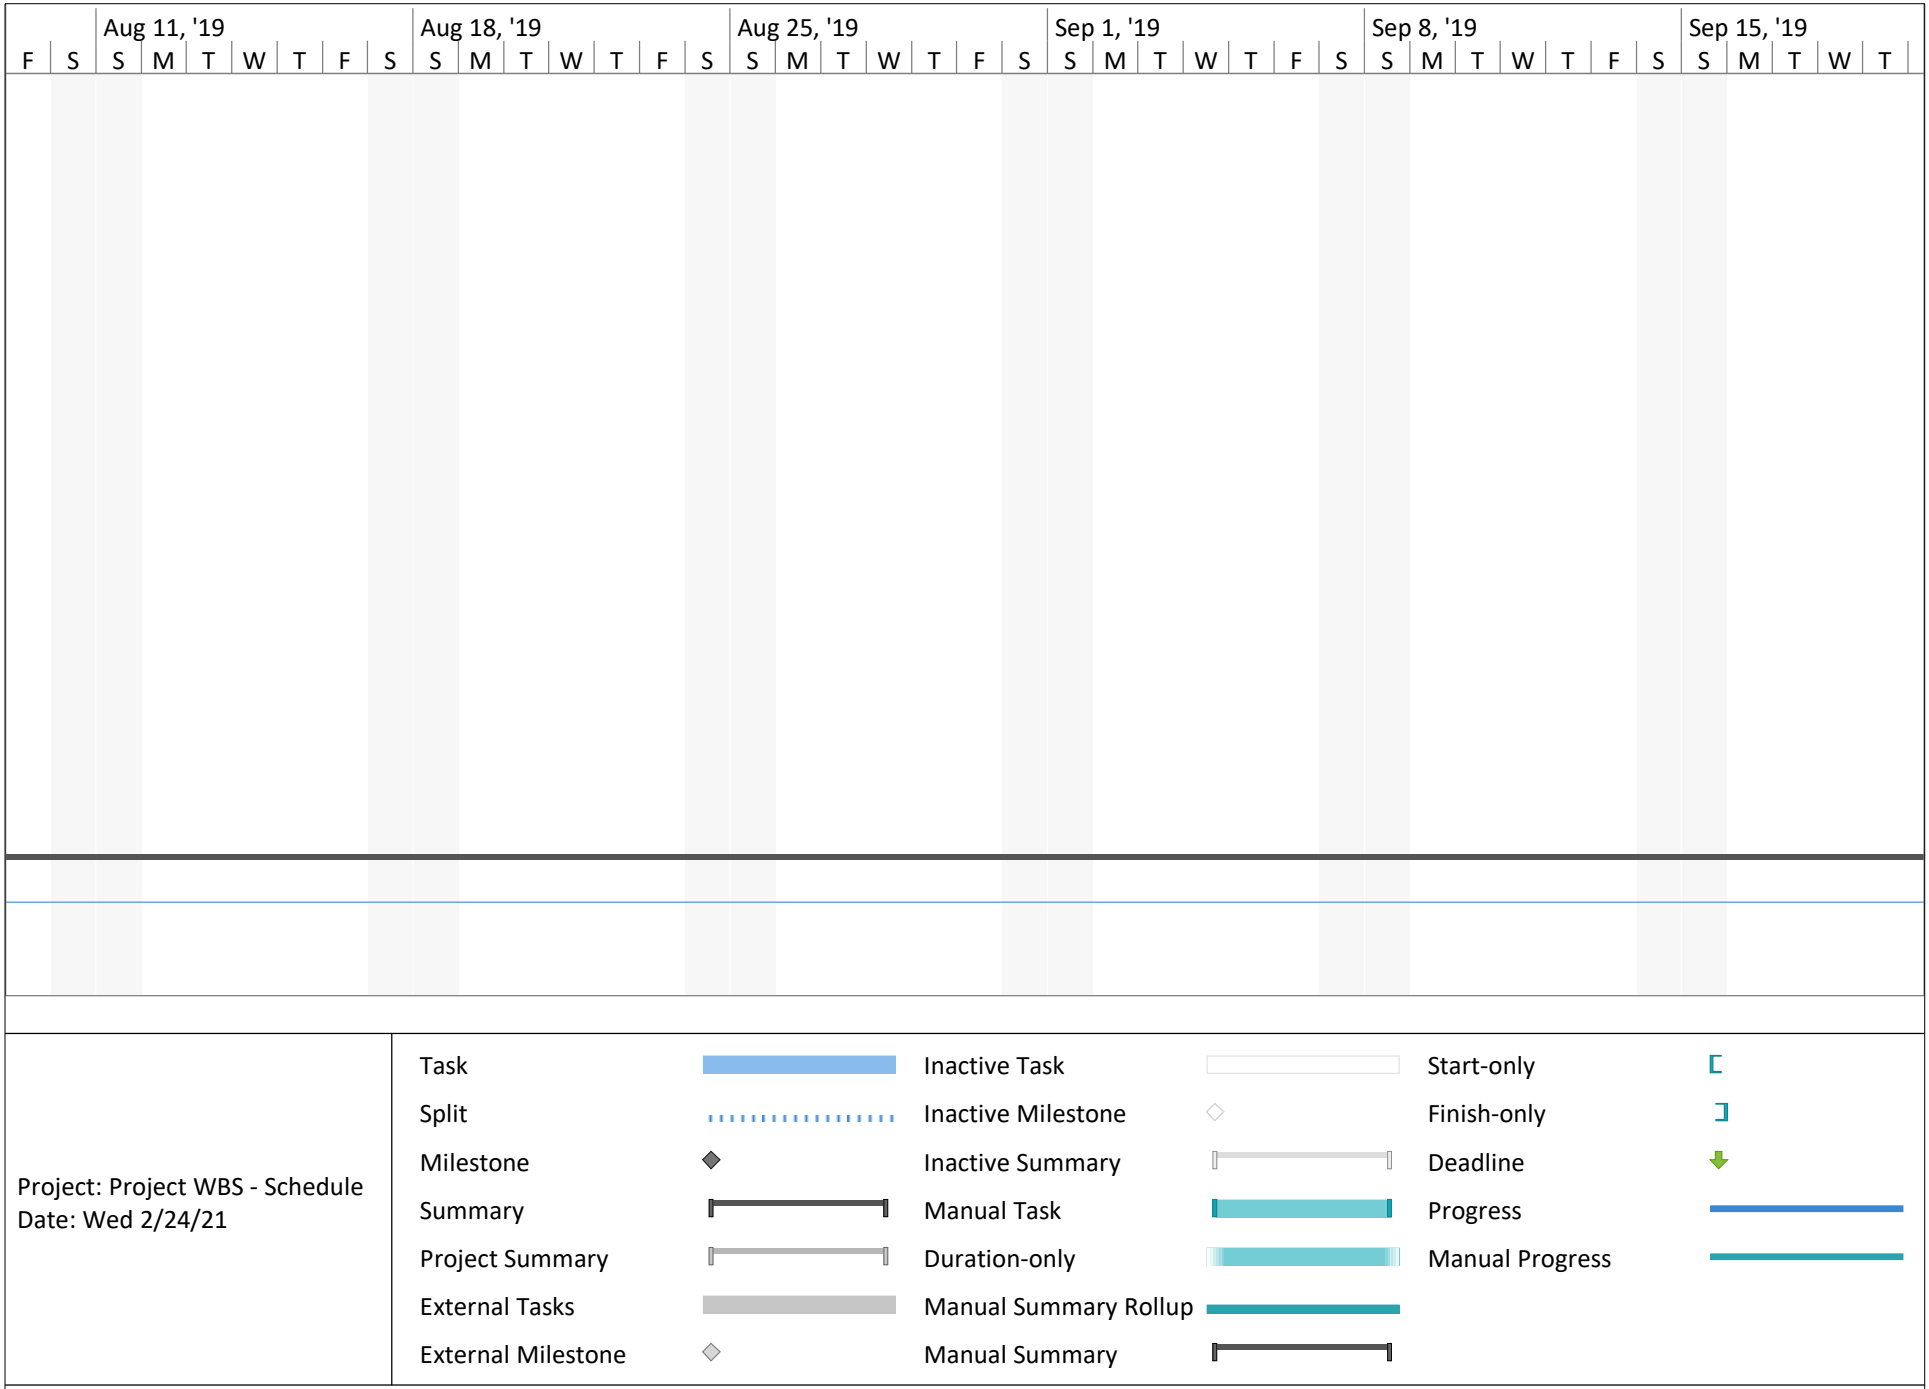


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

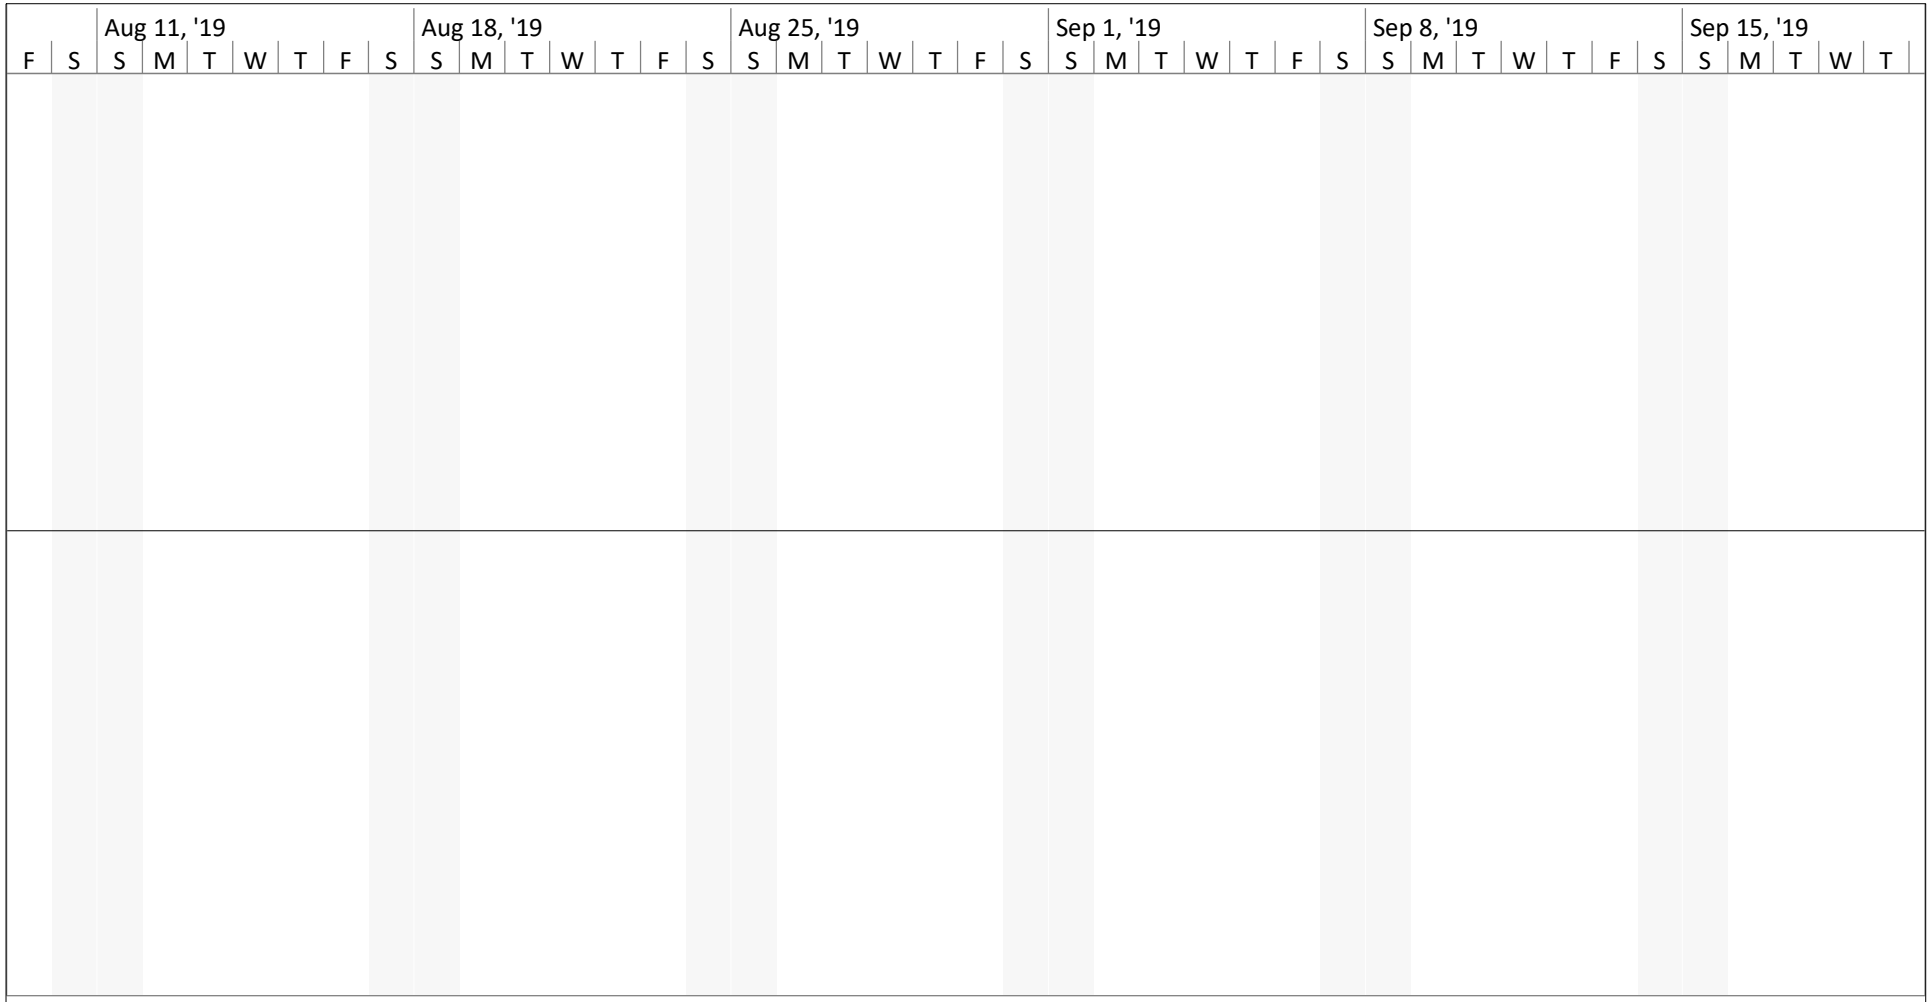


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

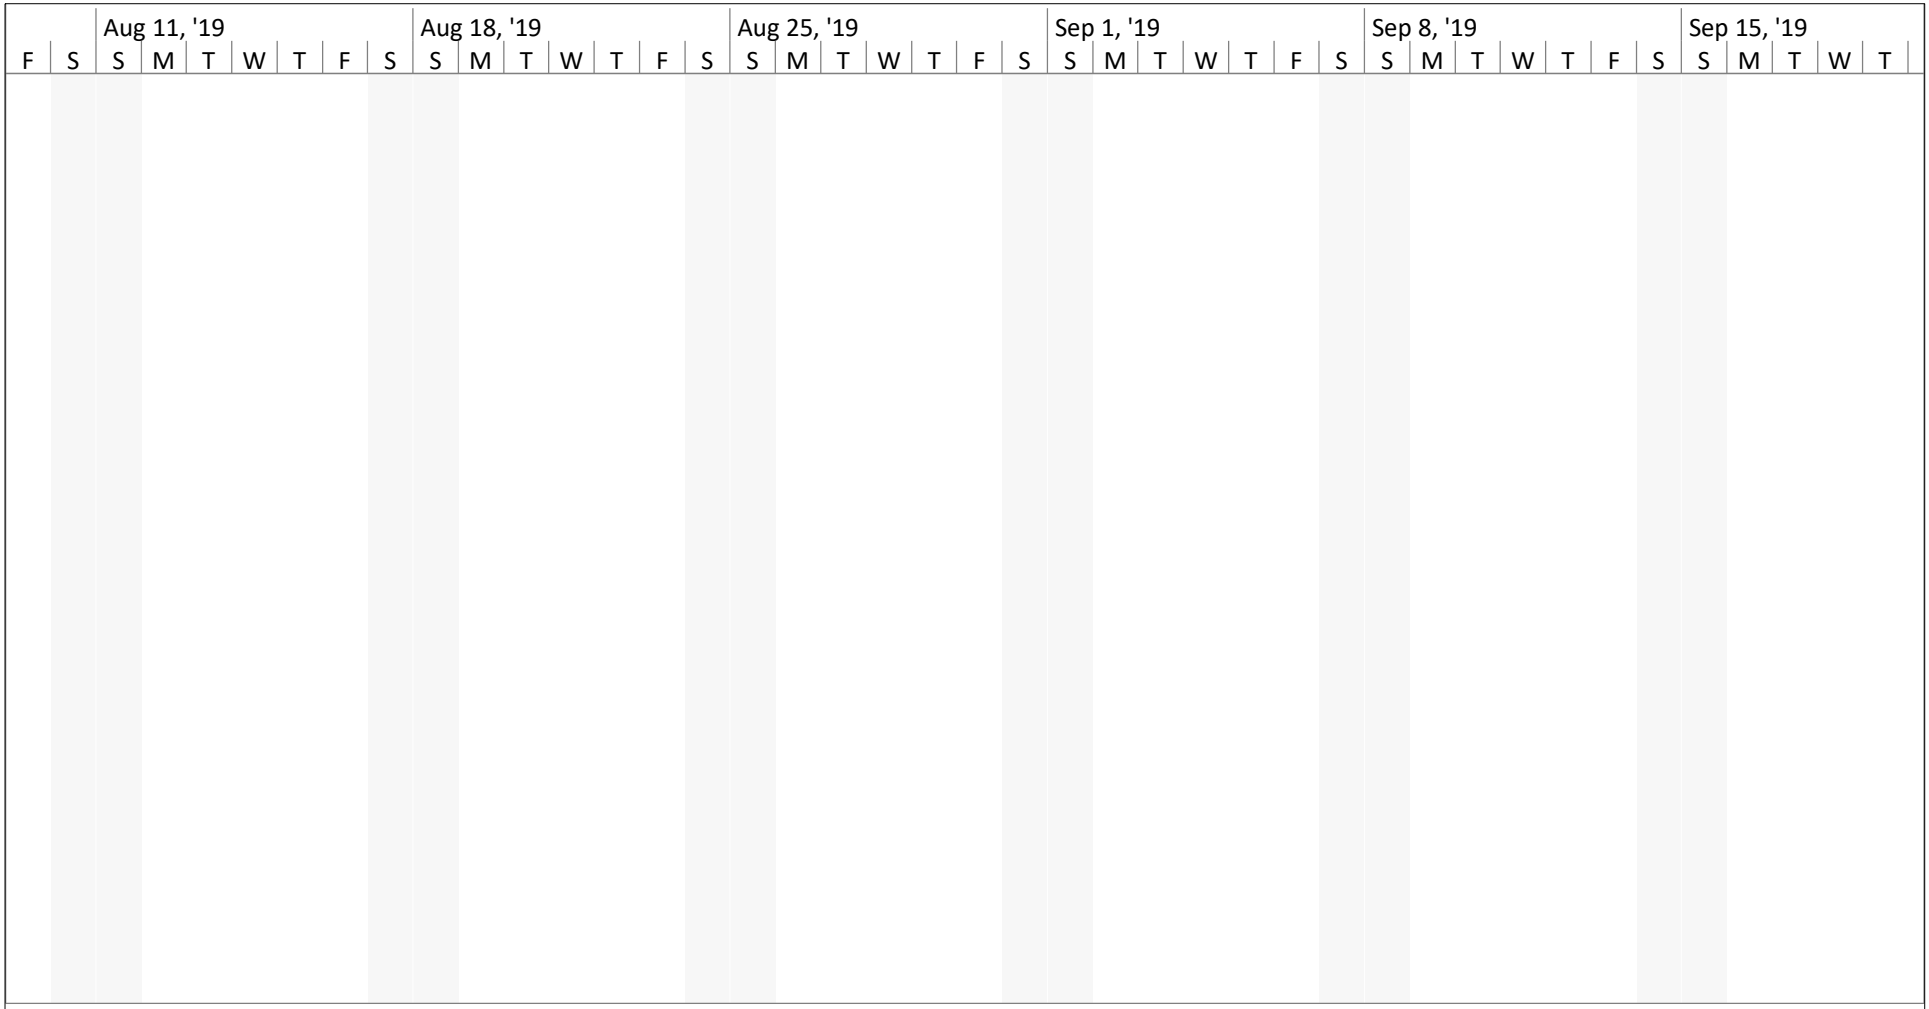


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

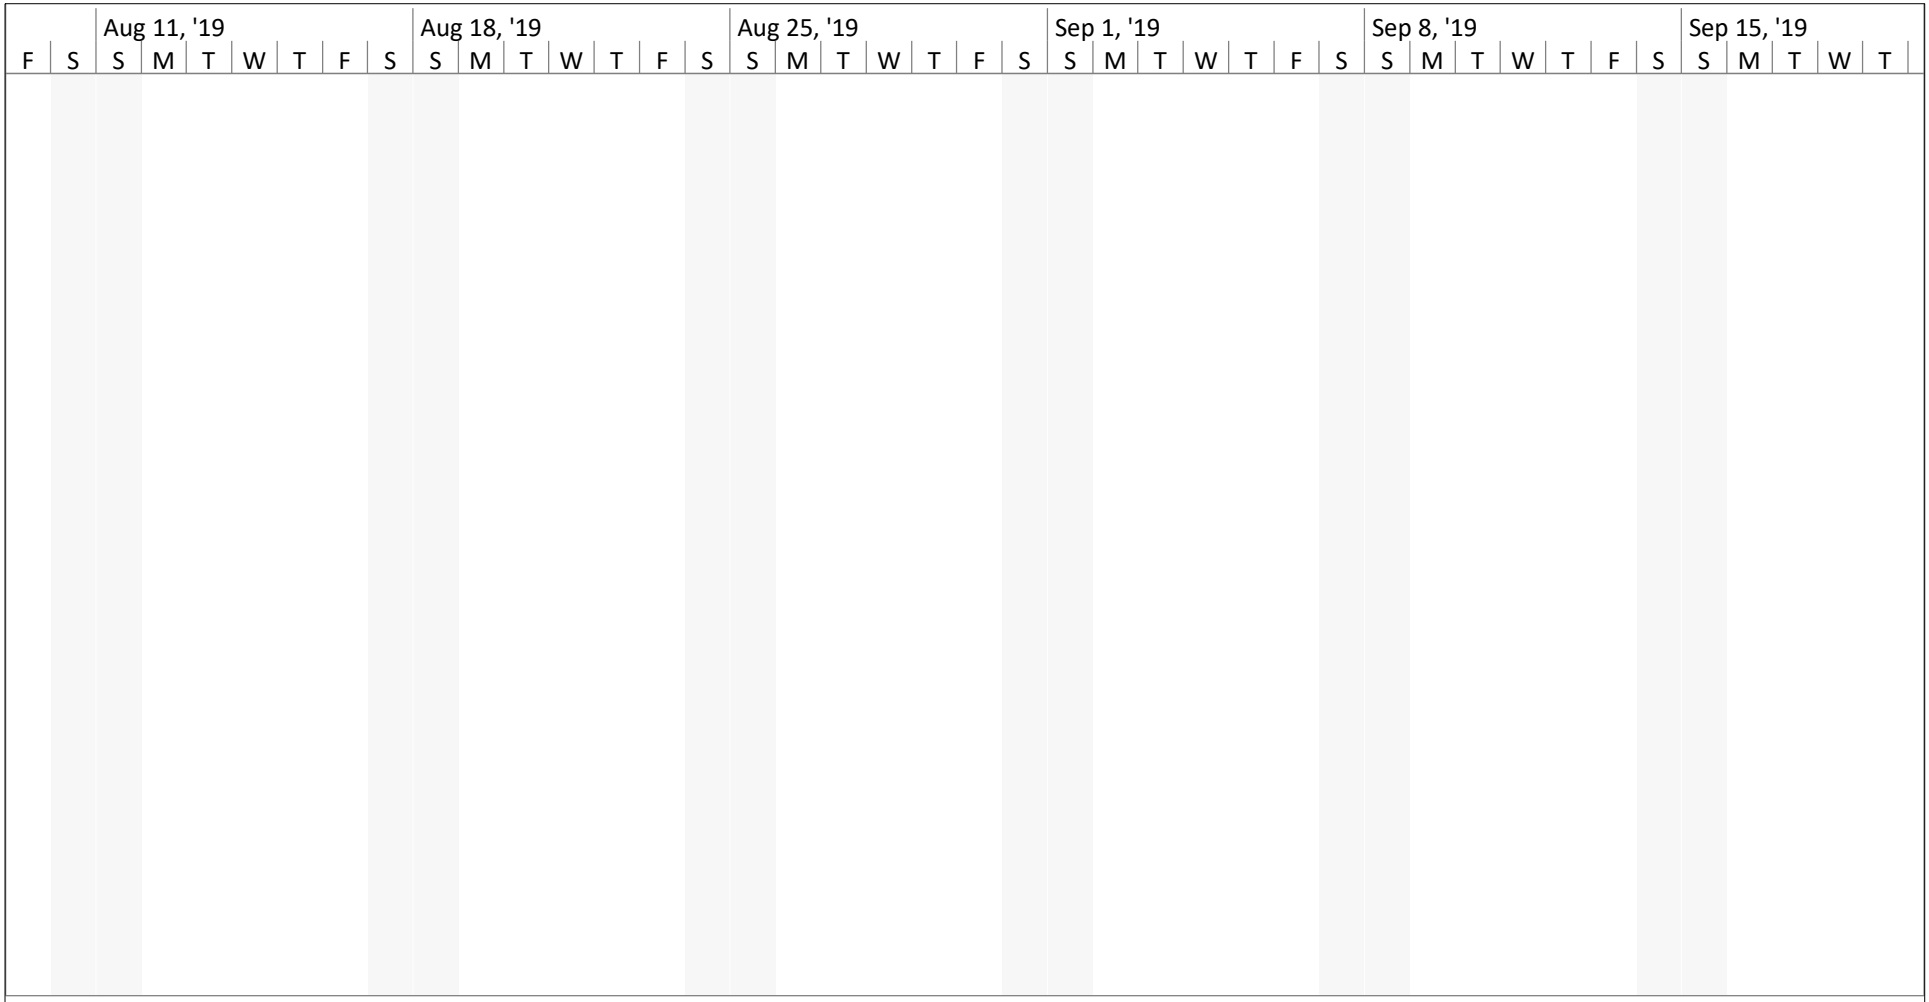


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |




Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

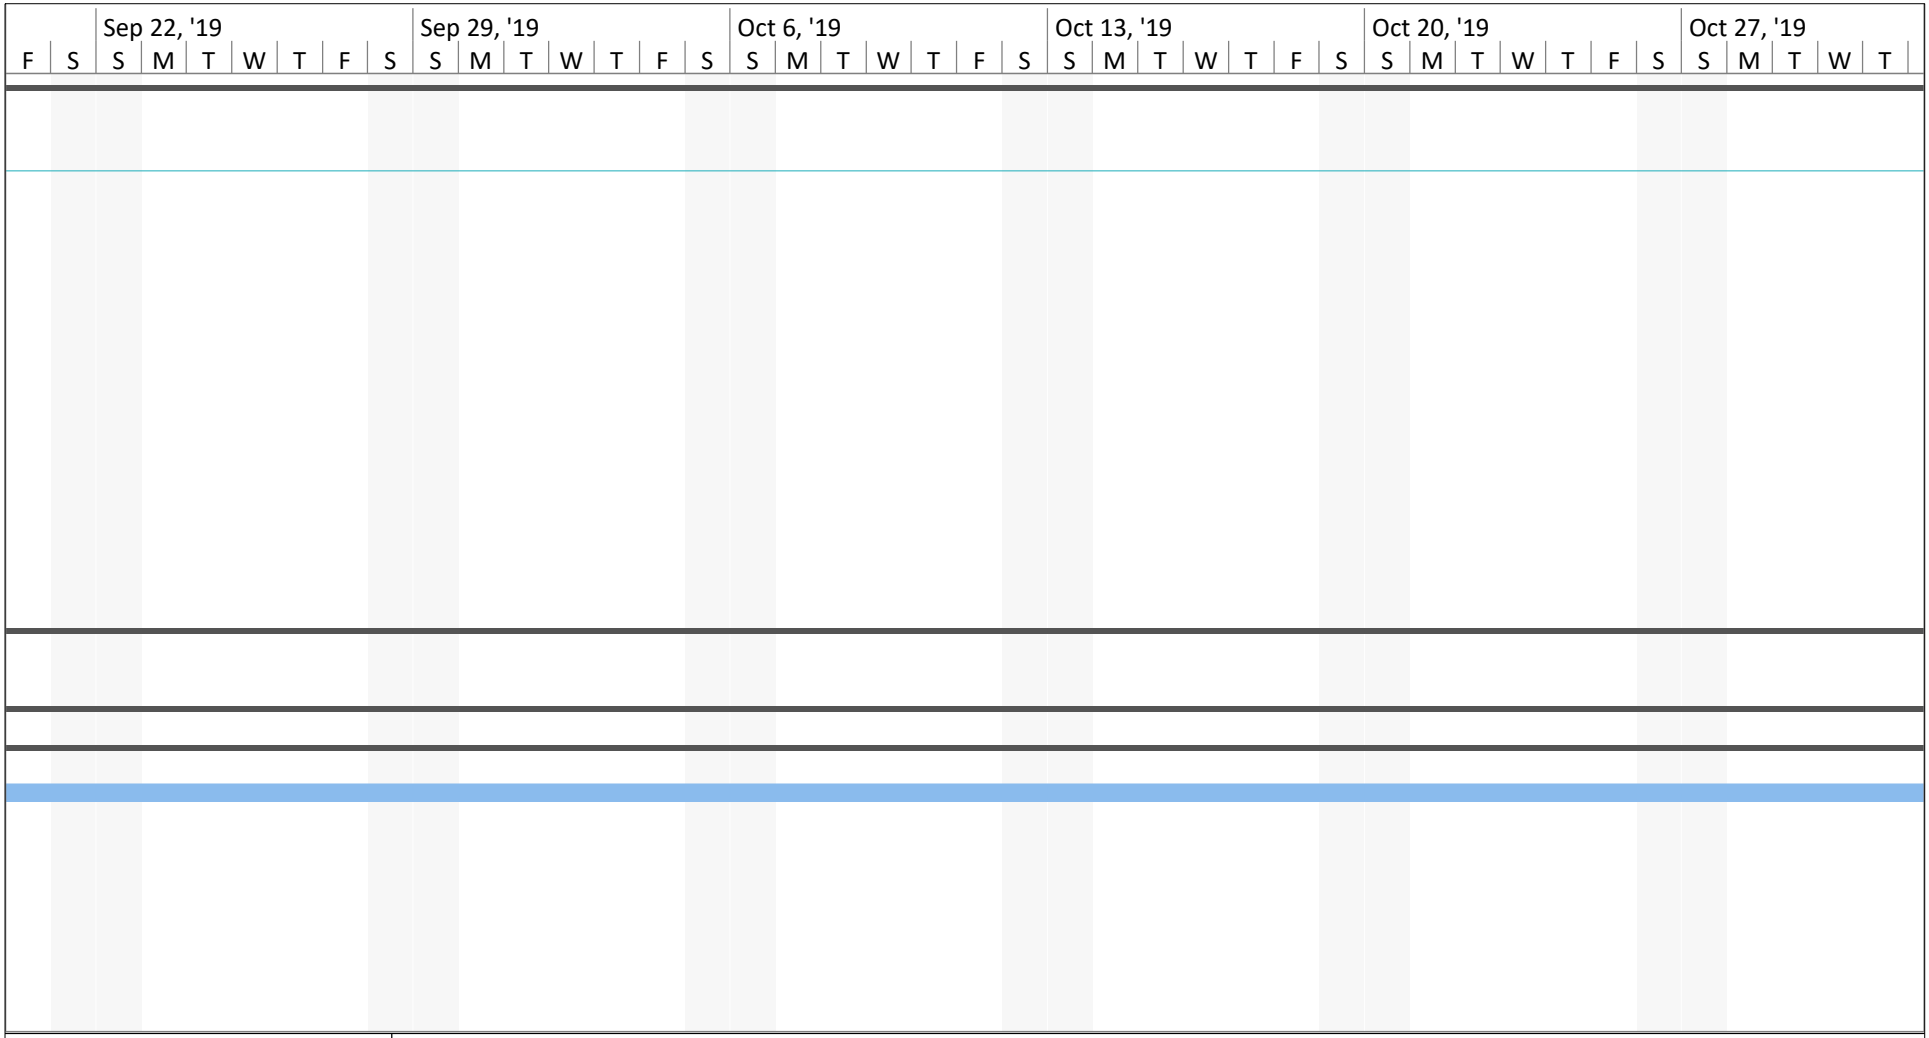


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

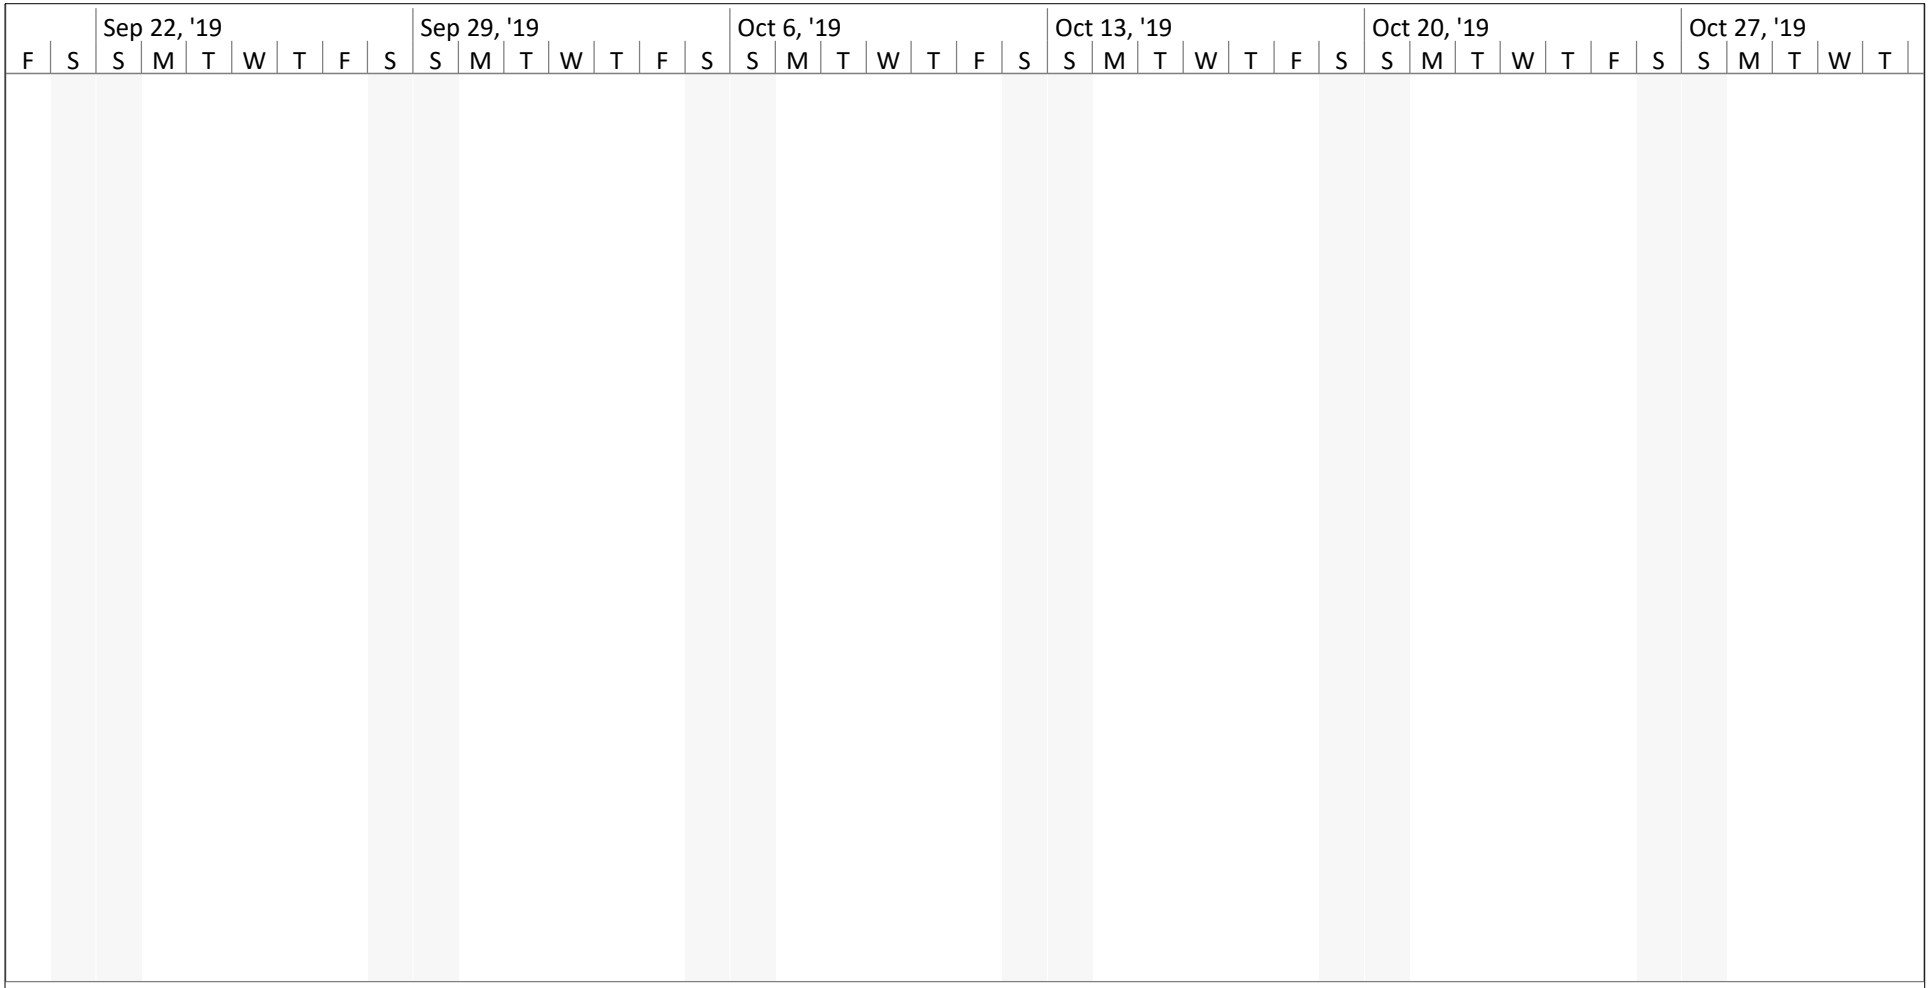


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

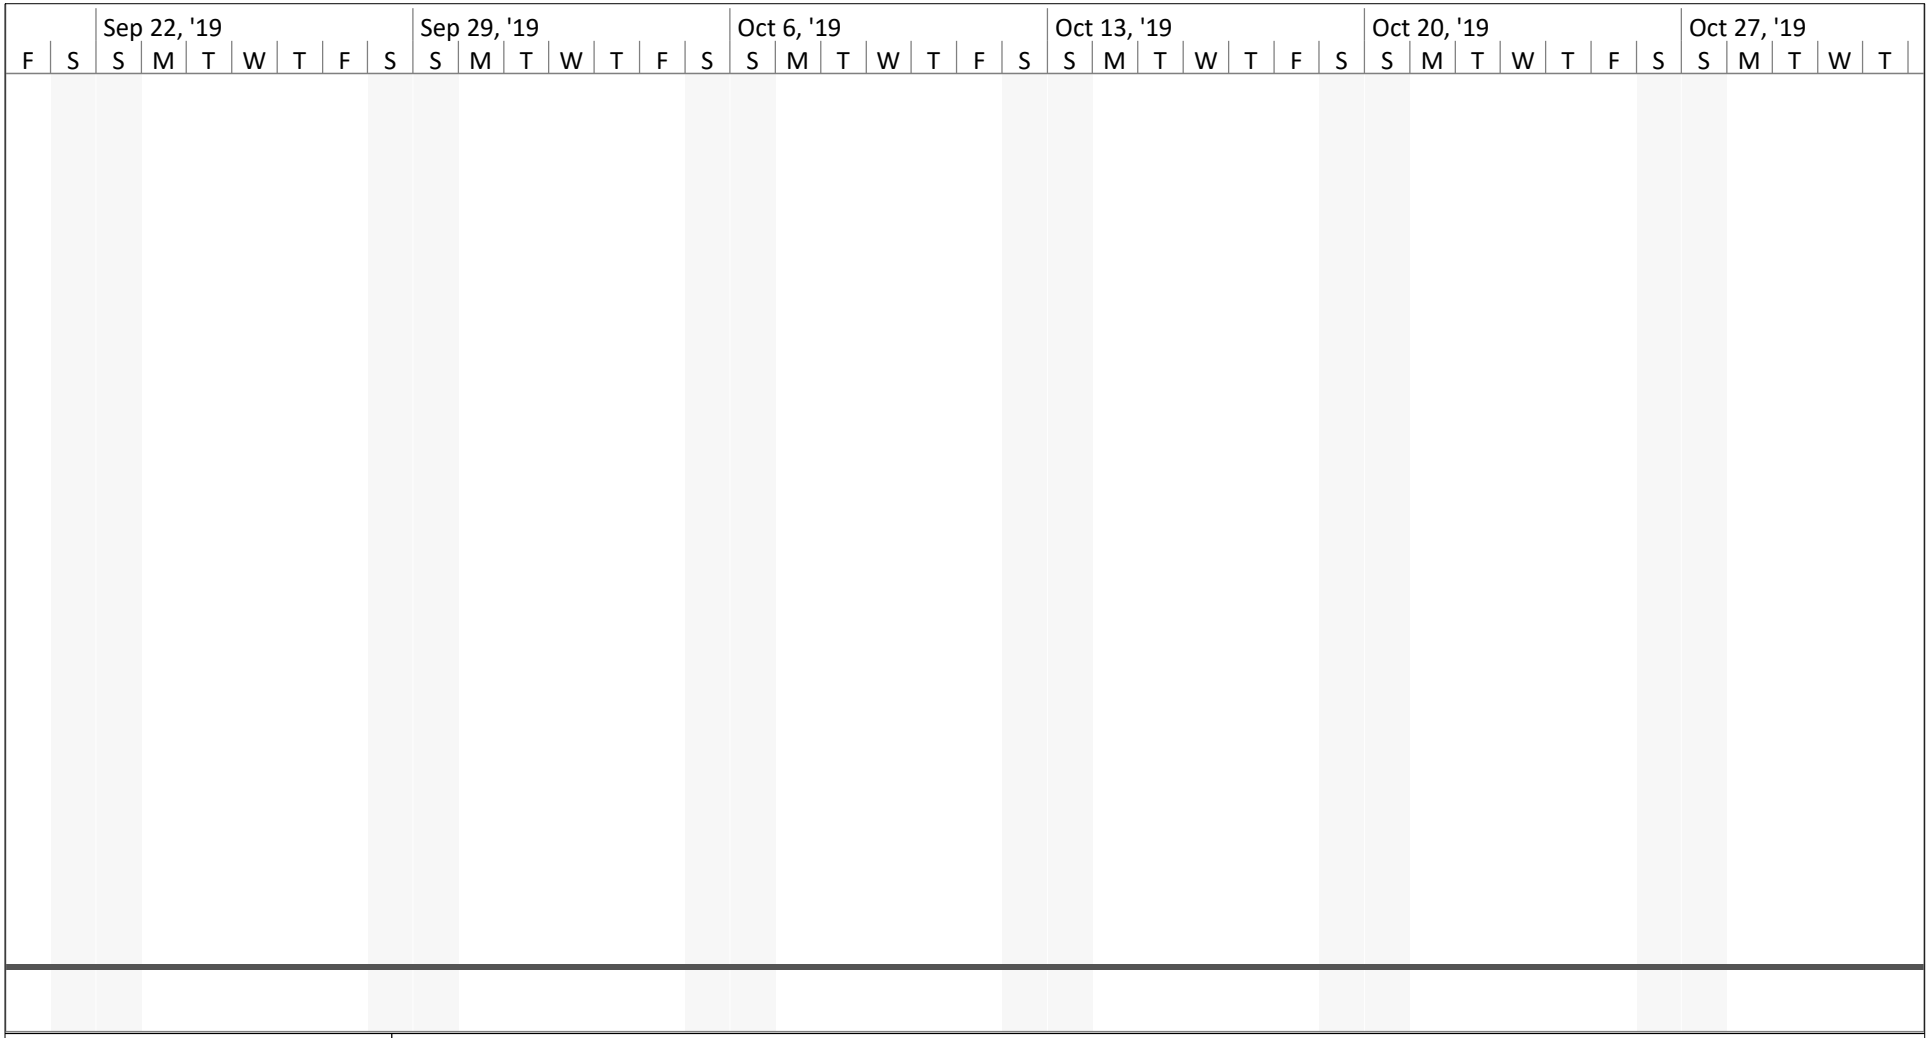


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

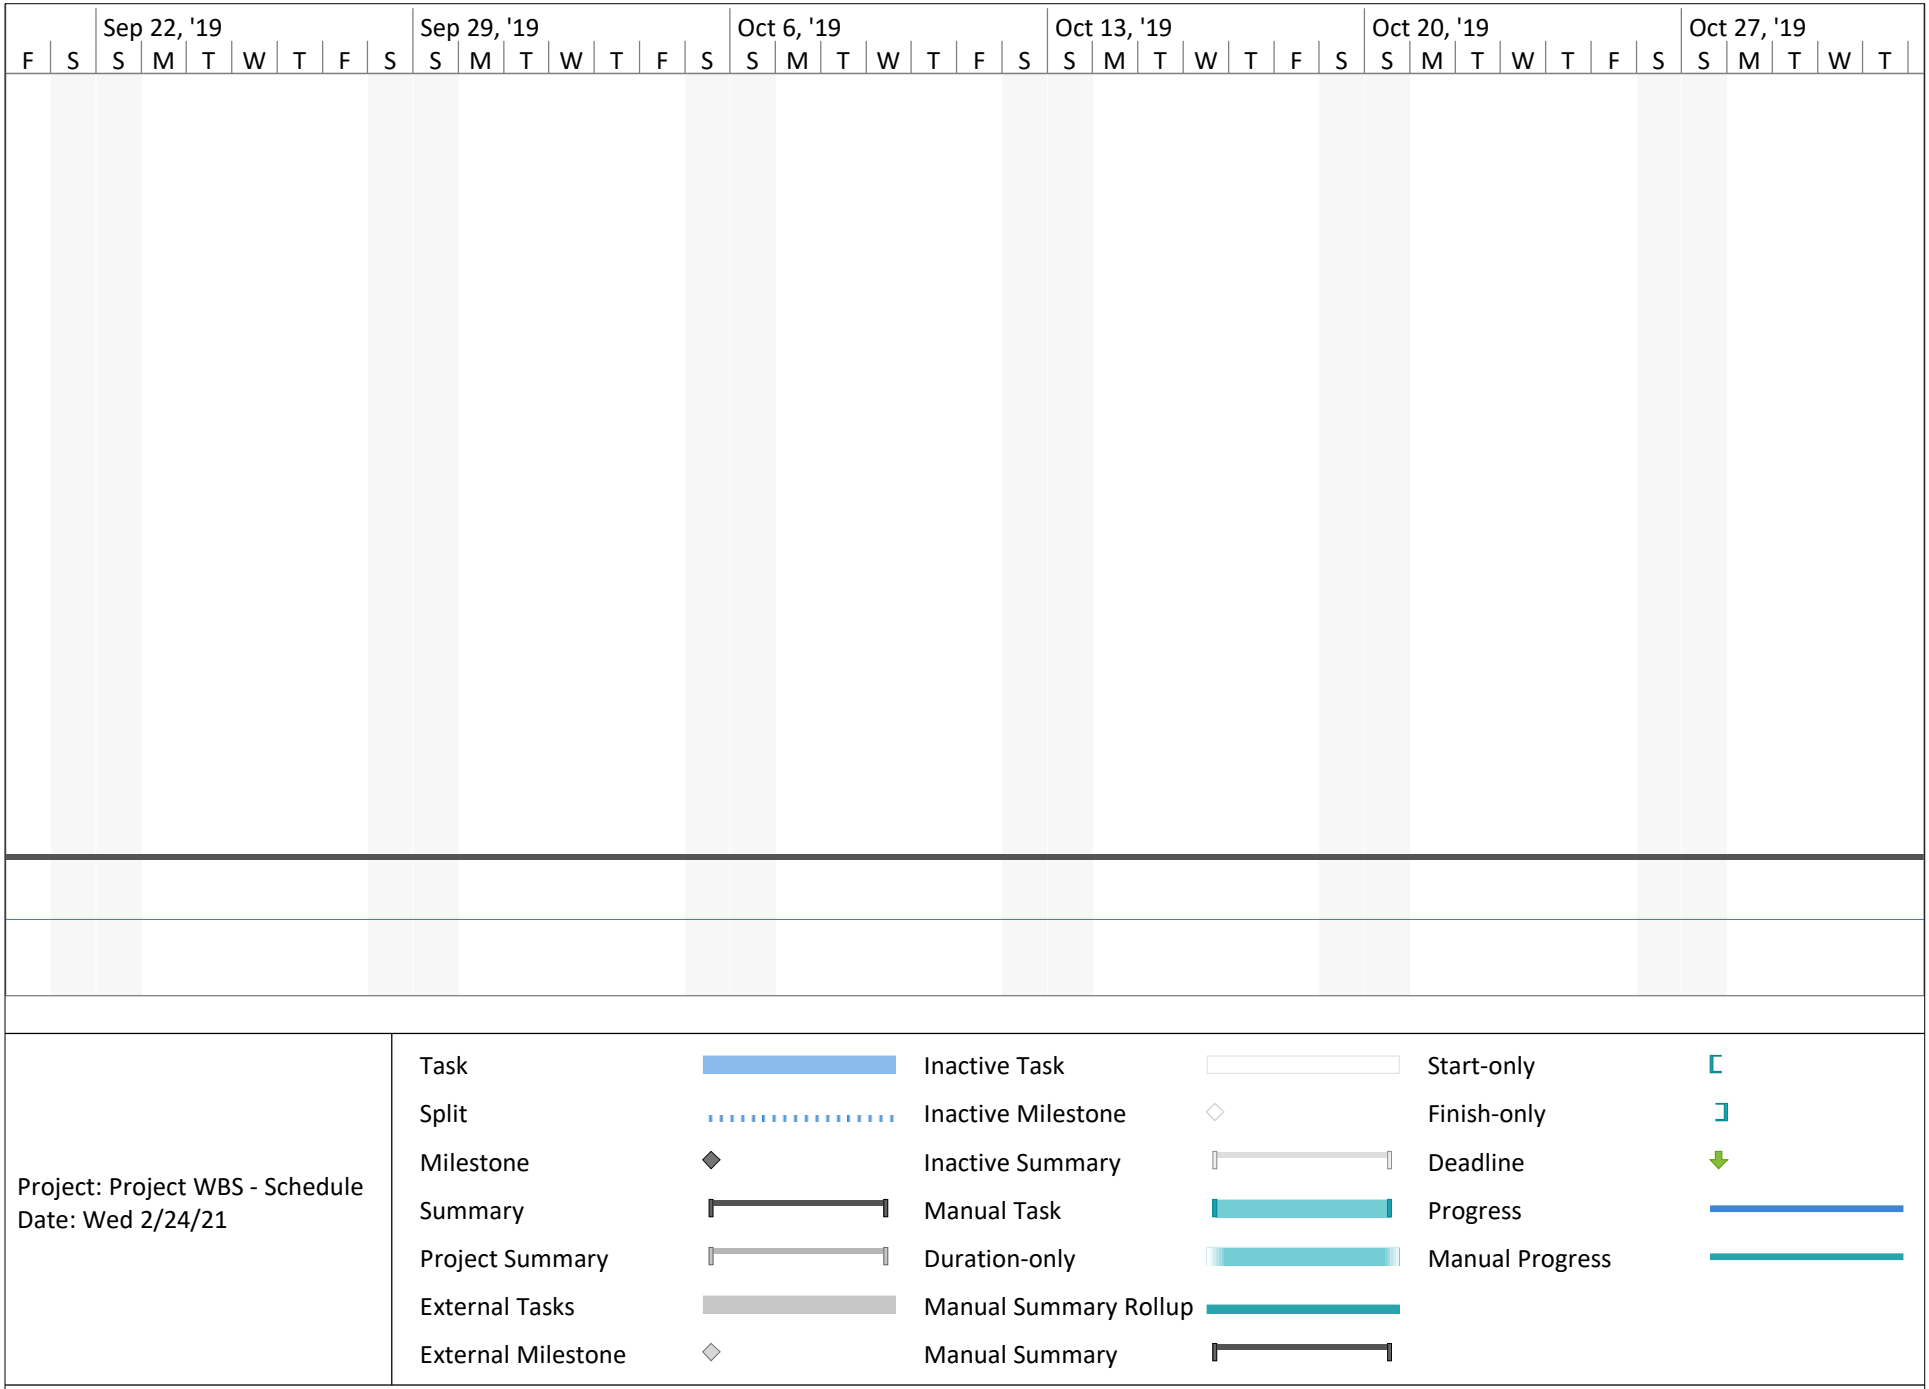
Sep 22, '19
Sep 29, '19
Oct 6, '19
Oct 13, '19
Oct 20, '19
Oct 27, '19
F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T
Project: Project WBS - Schedule
Date: Wed 2/24/21
Task
Split
Milestone
Summary
Project Summary
External Tasks
External Milestone
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
Deadline
Progress
Manual Progress

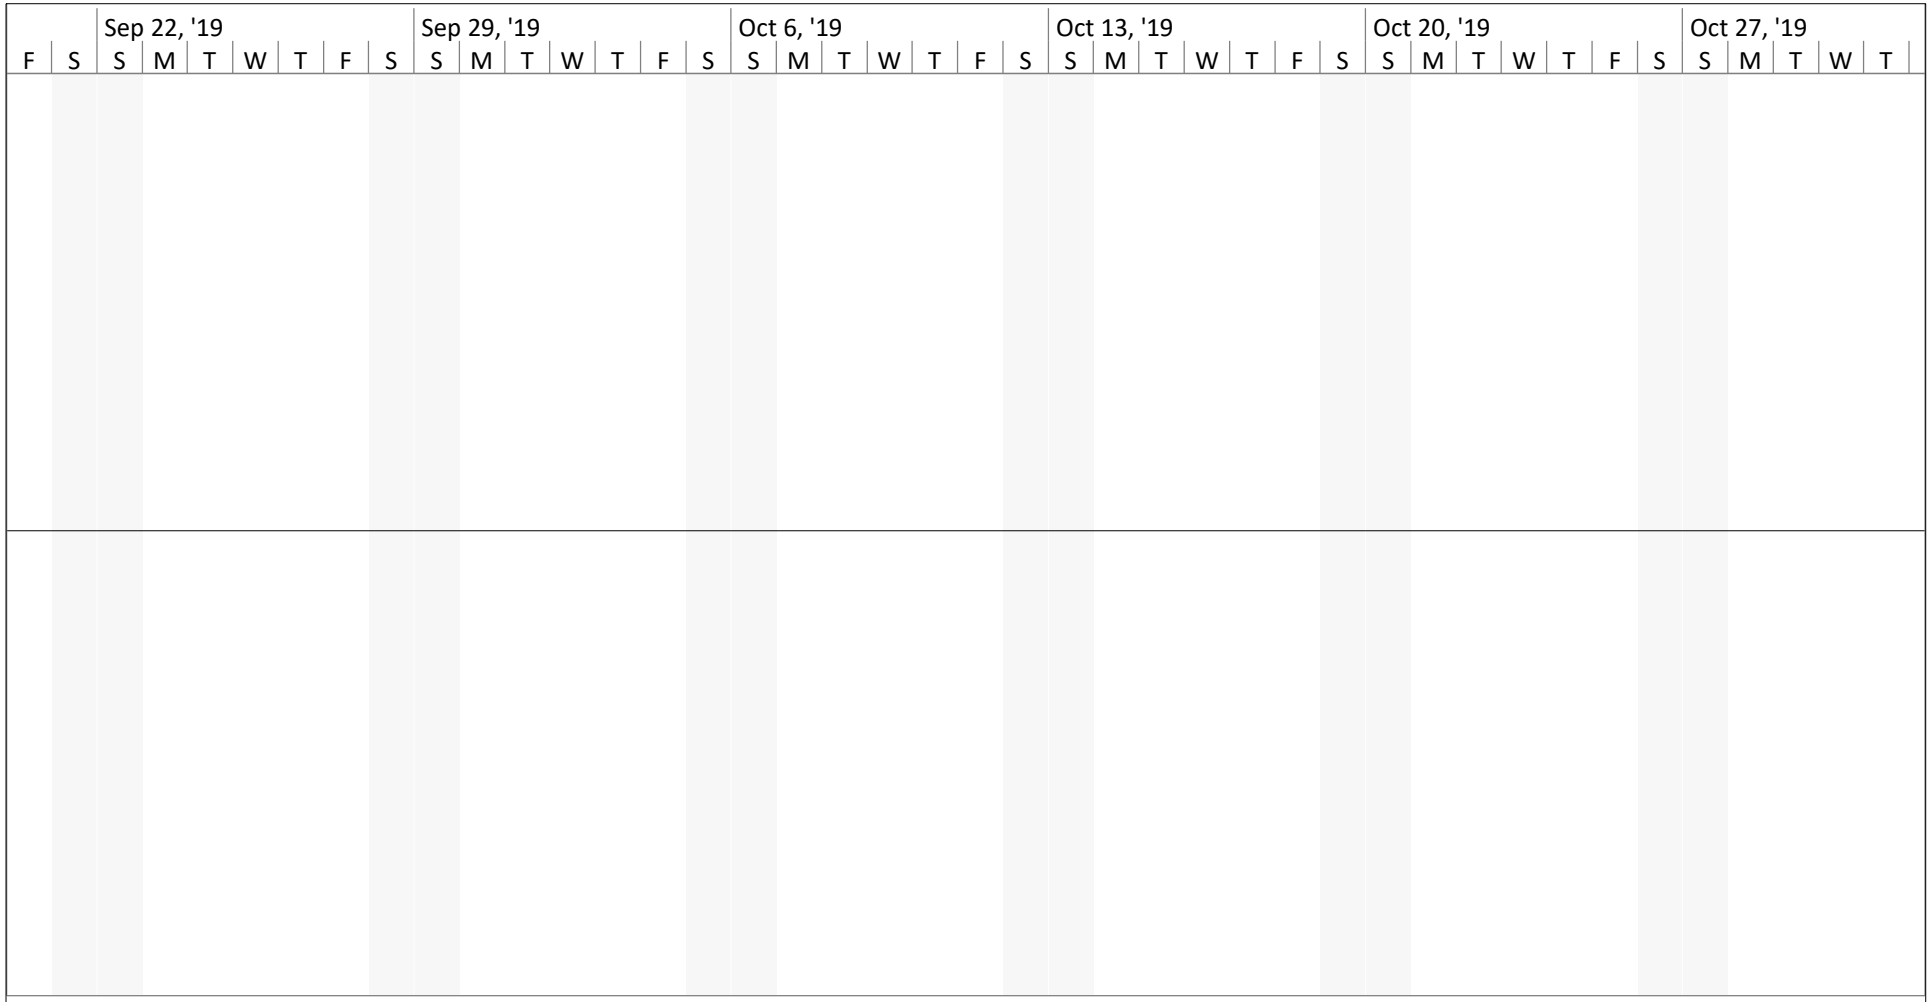


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

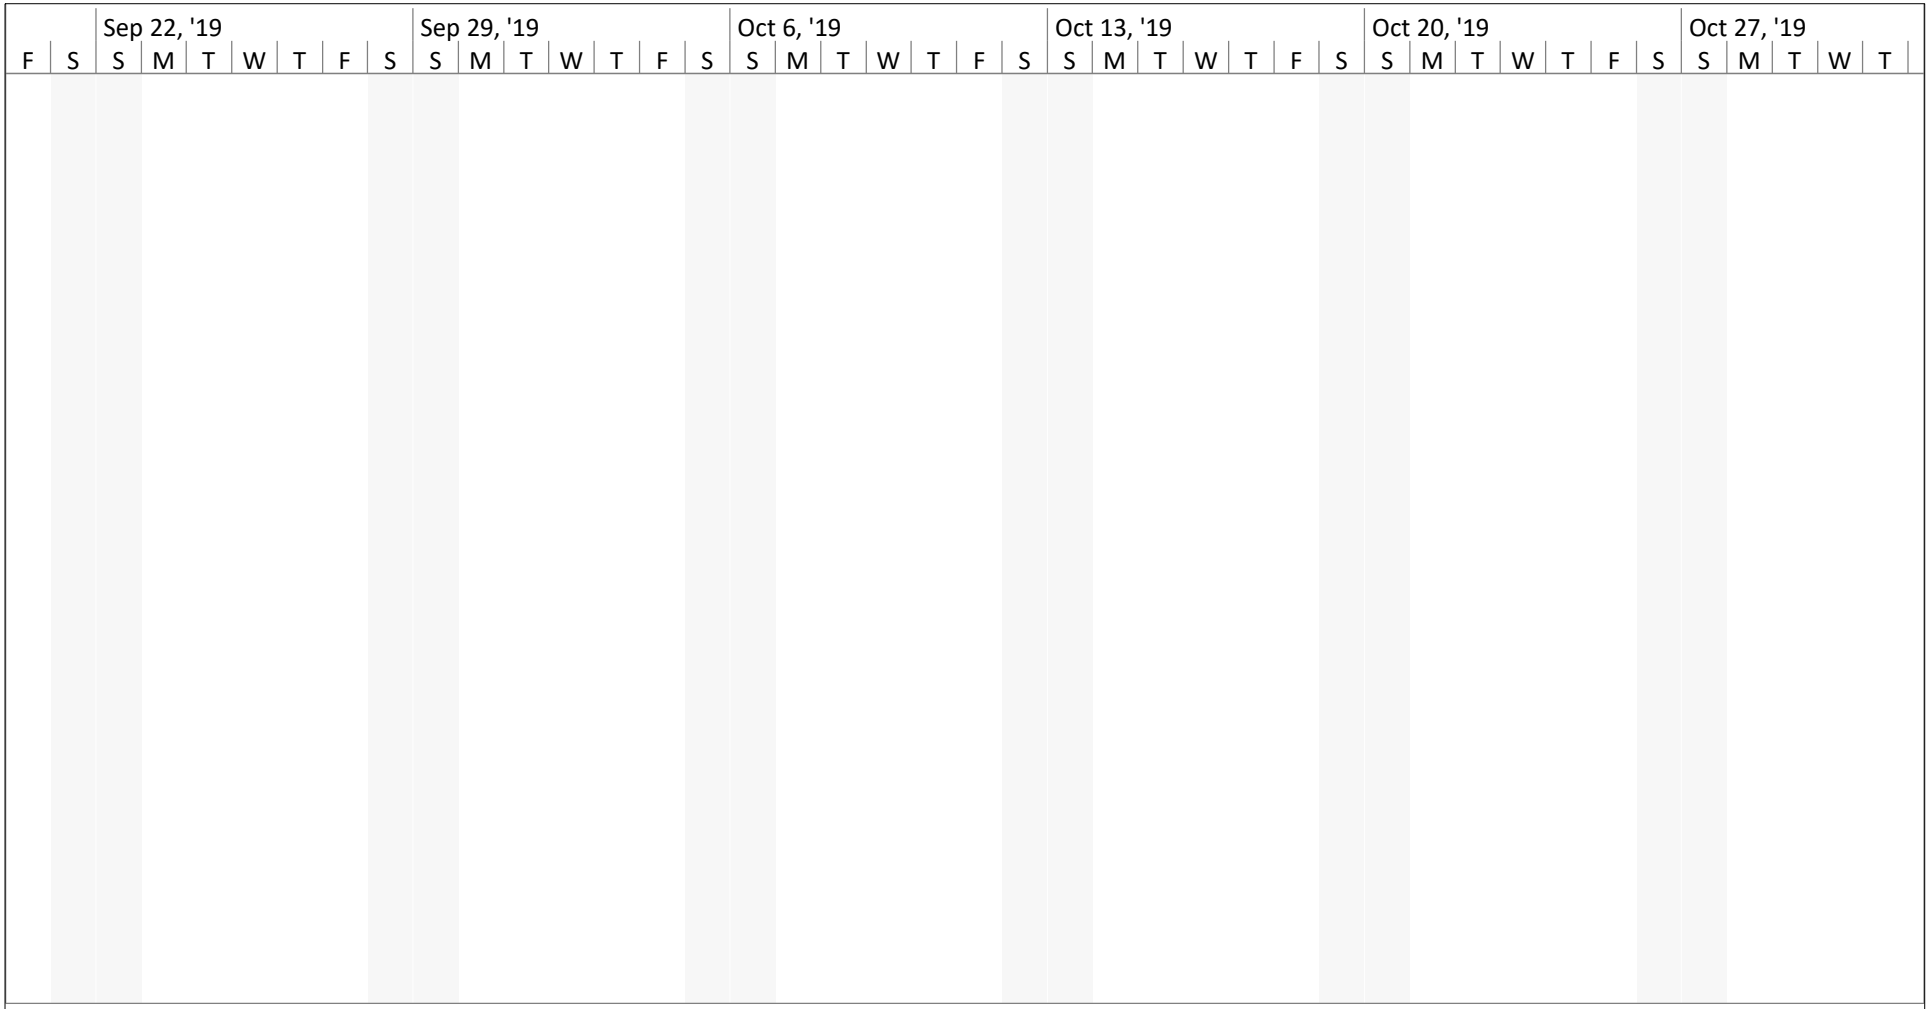


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

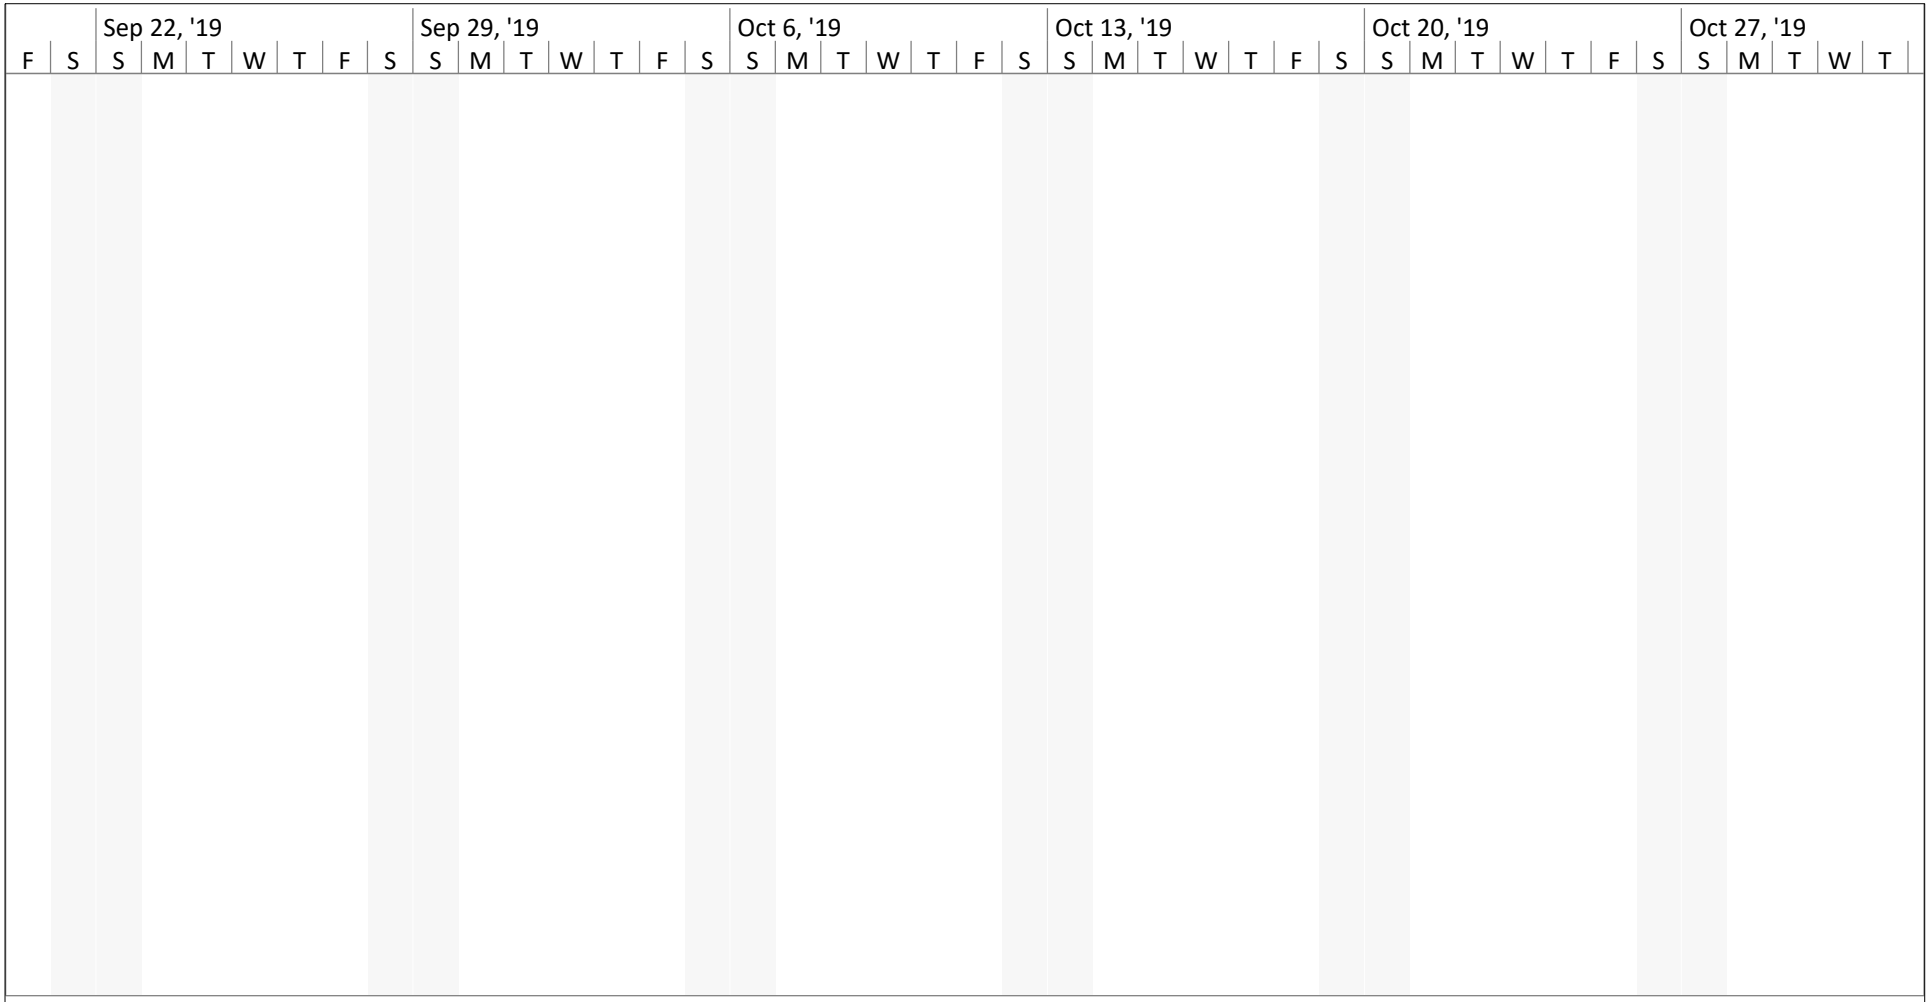


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |




Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

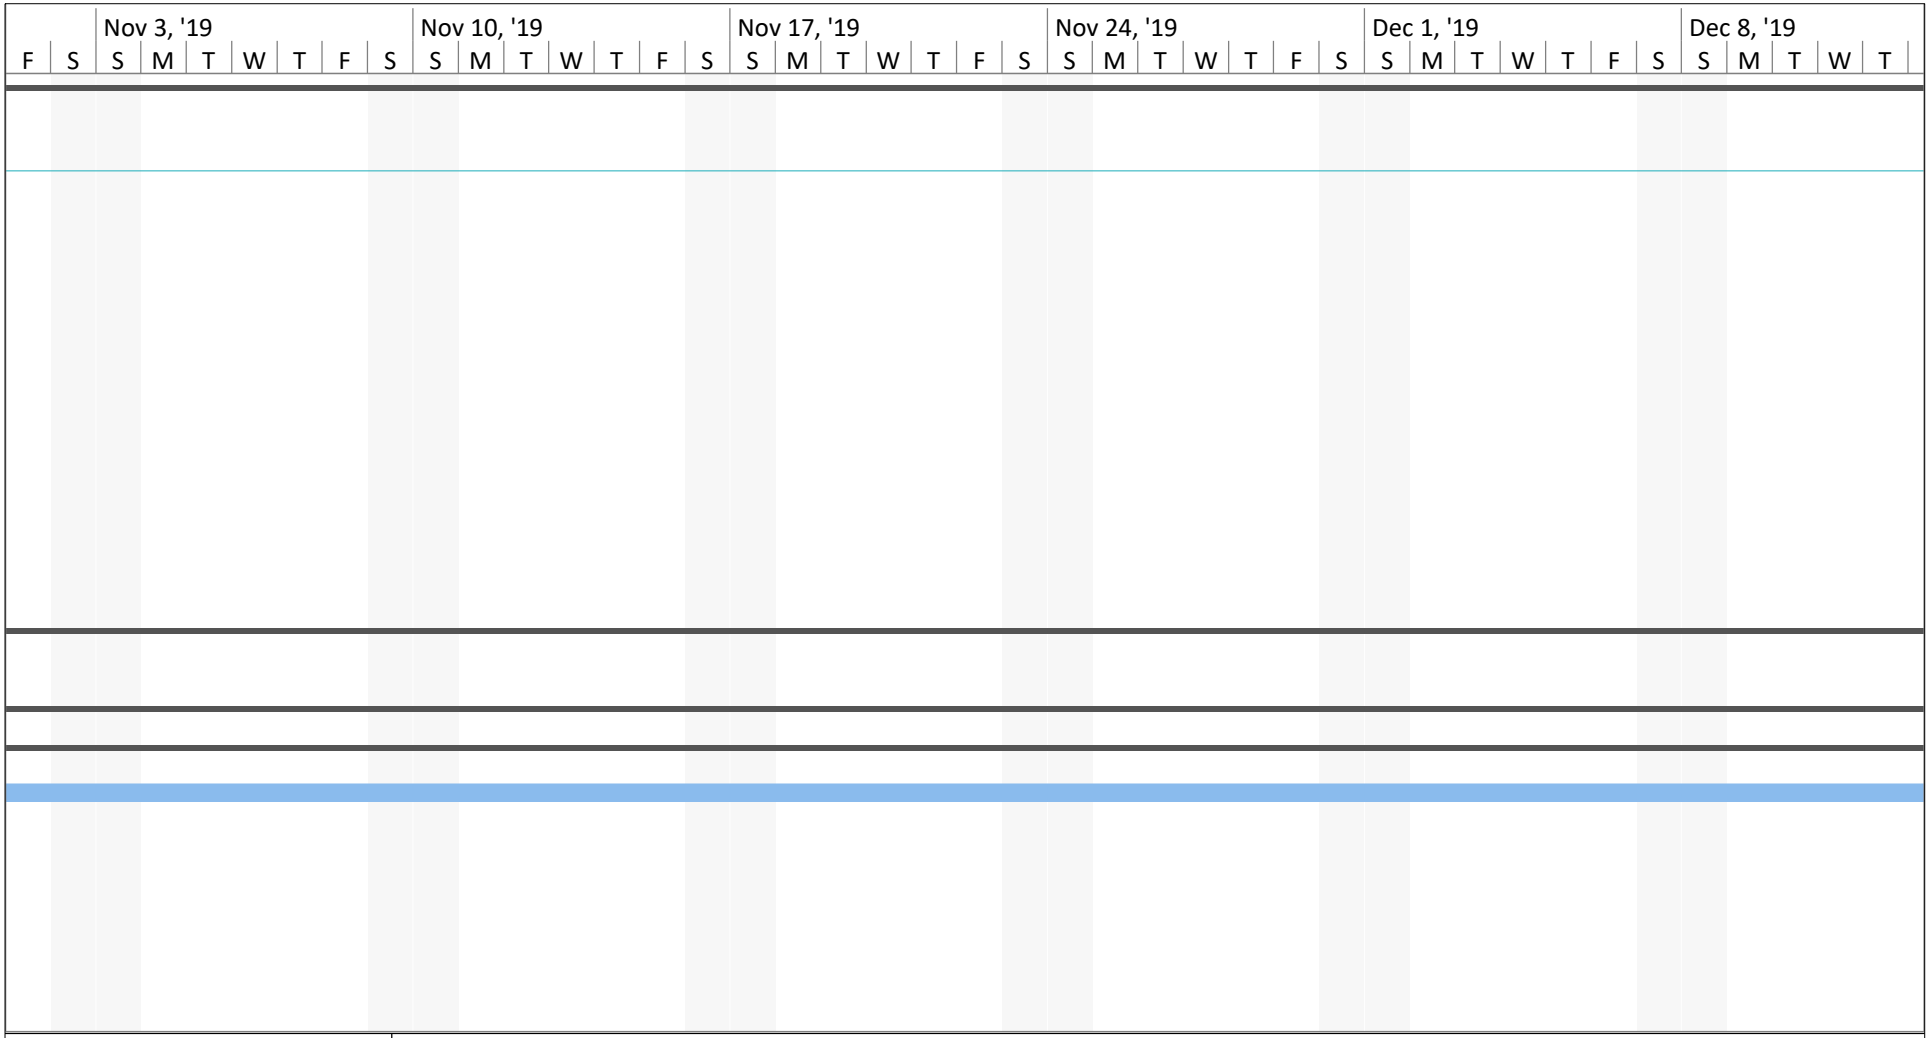


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

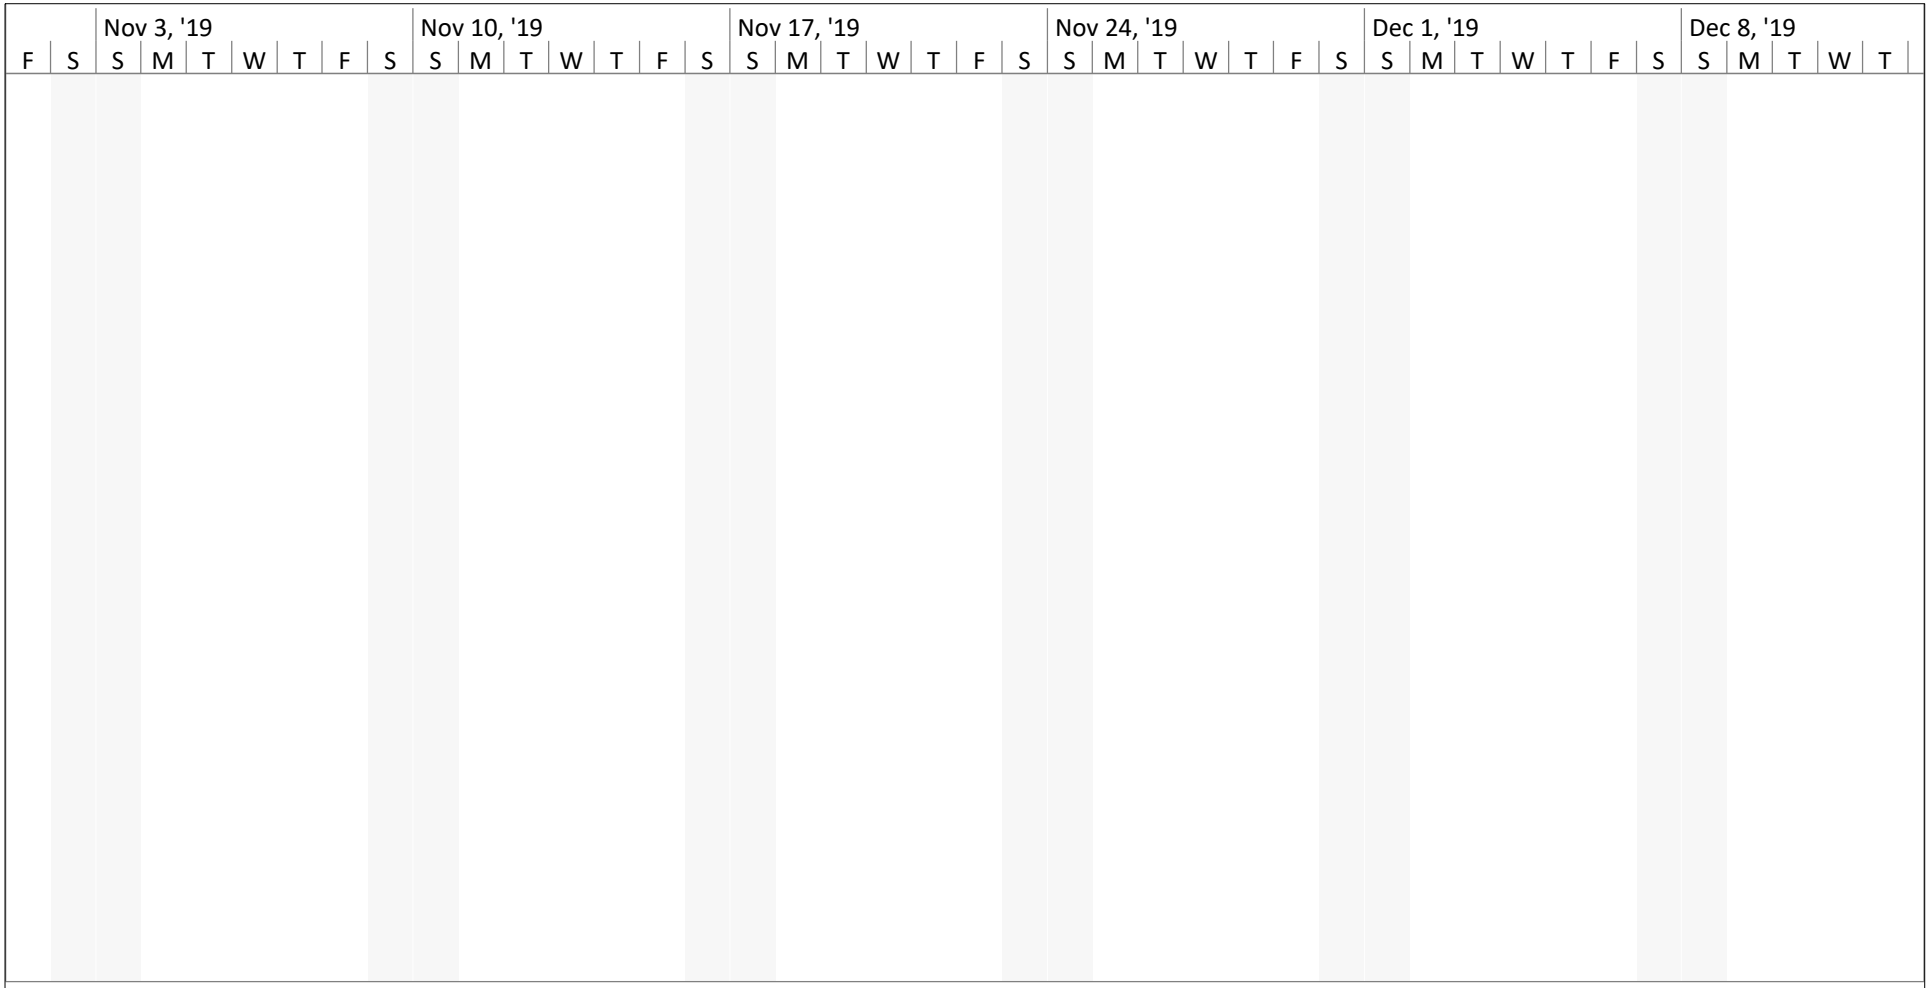


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

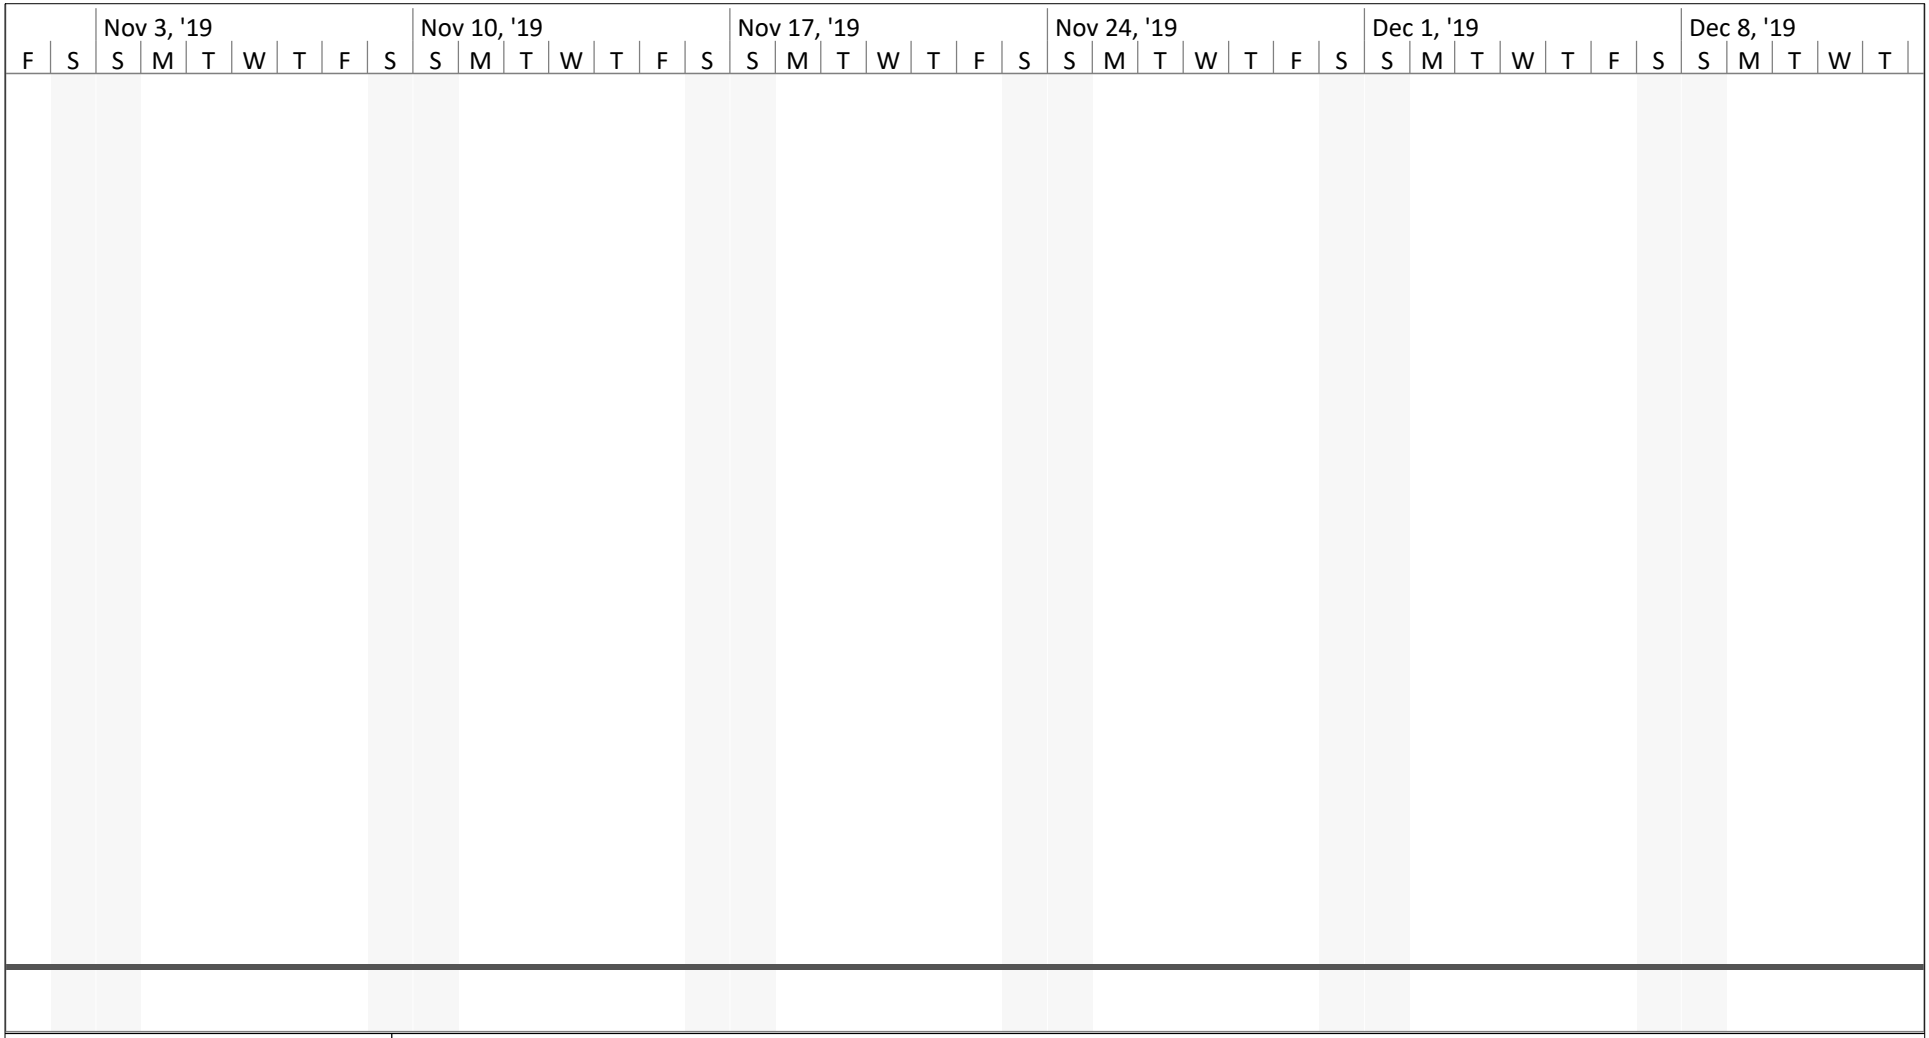


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

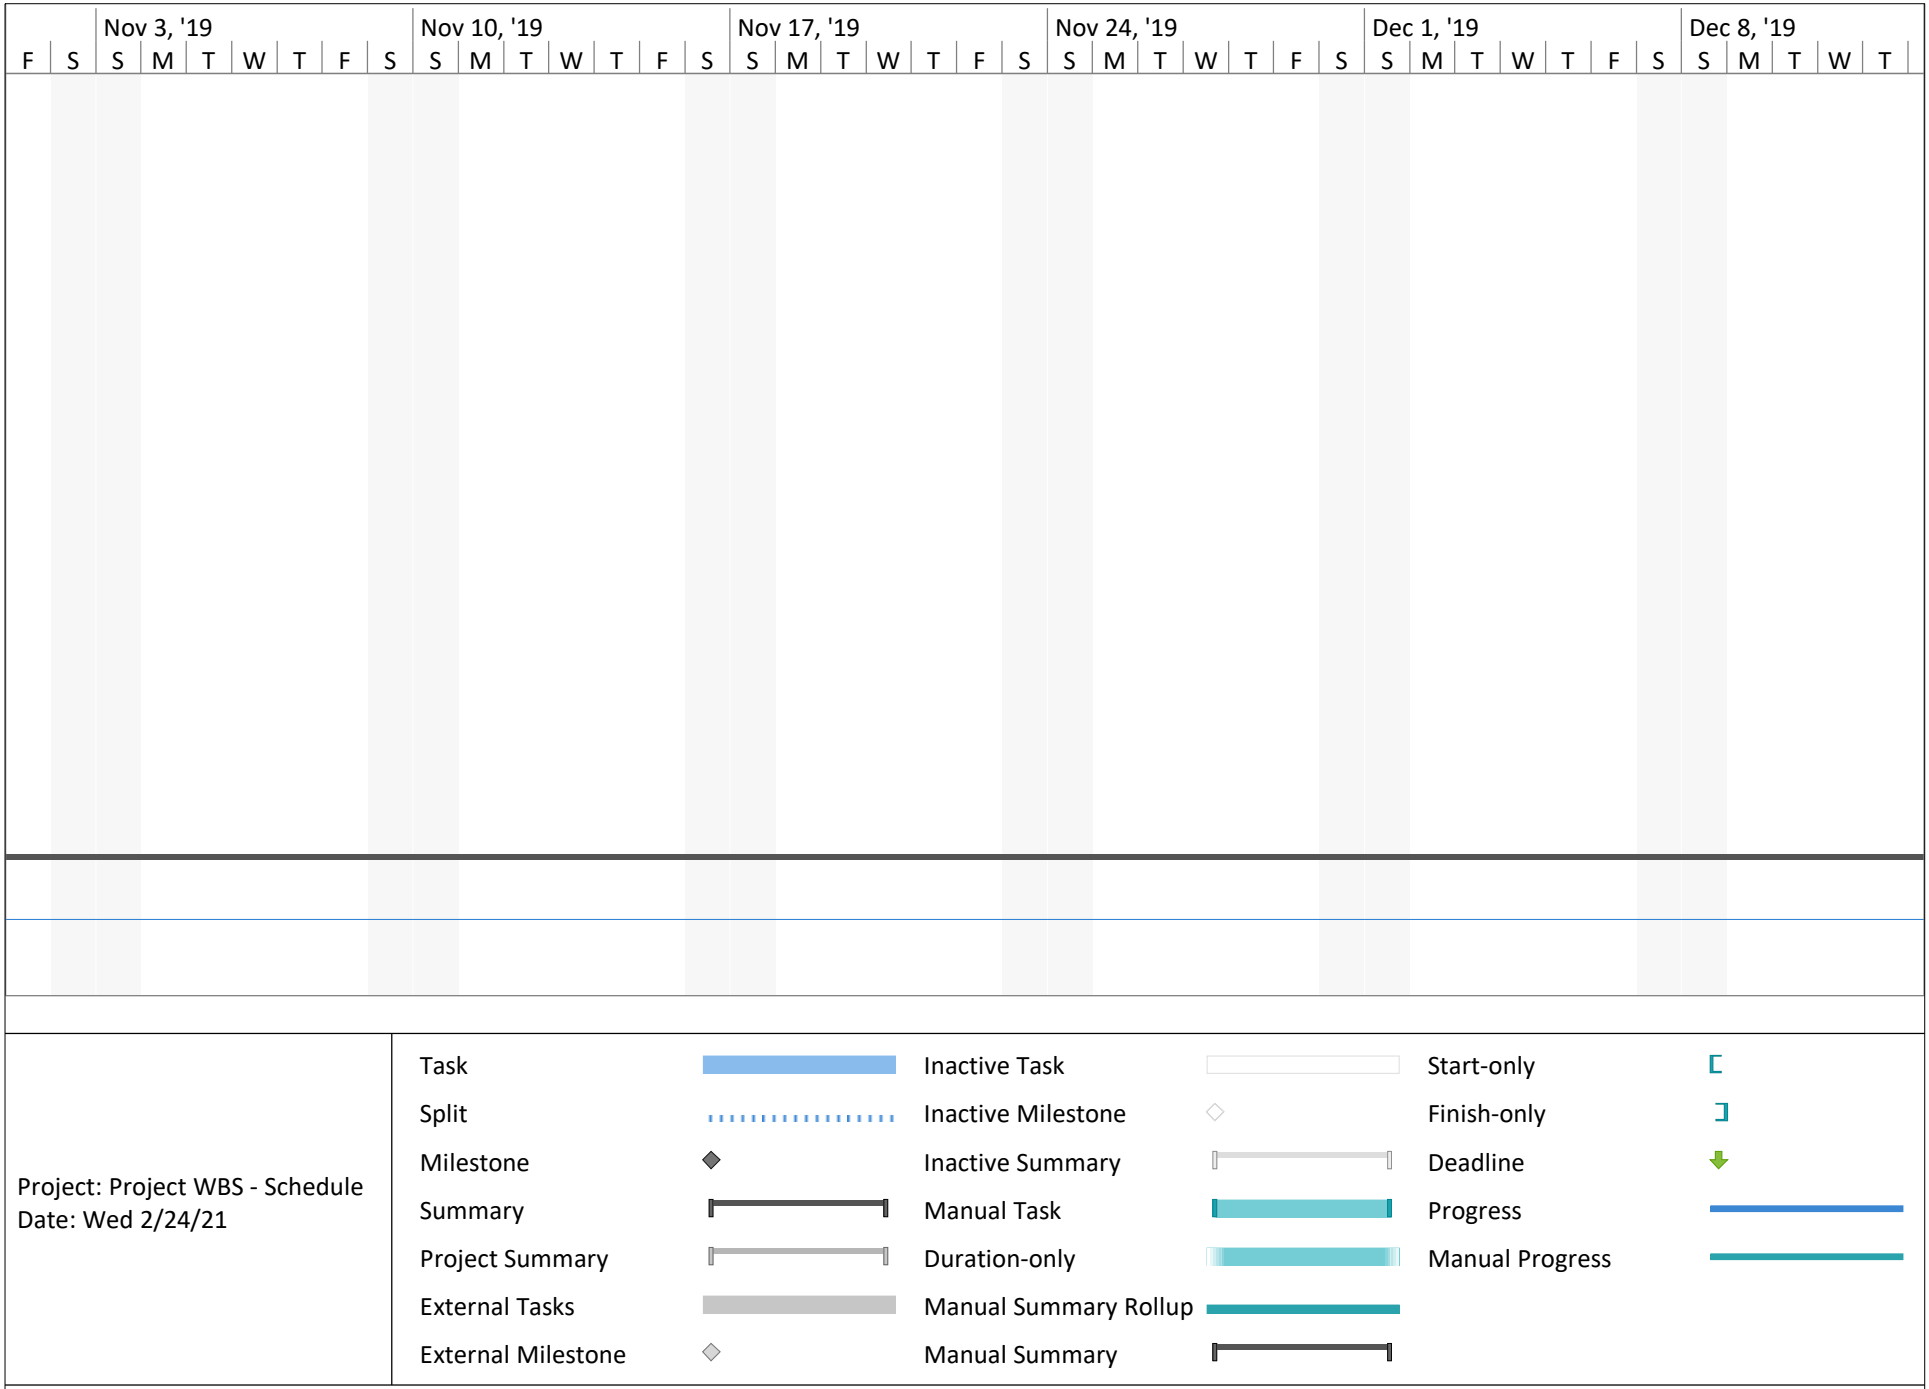
Nov 3, '19
Nov 10, '19
Nov 17, '19
Nov 24, '19
Dec 1, '19
Dec 8, '19
F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T
Project: Project WBS - Schedule
Date: Wed 2/24/21
Task
Split
Milestone
Summary
Project Summary
External Tasks
External Milestone
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
Deadline
Progress
Manual Progress

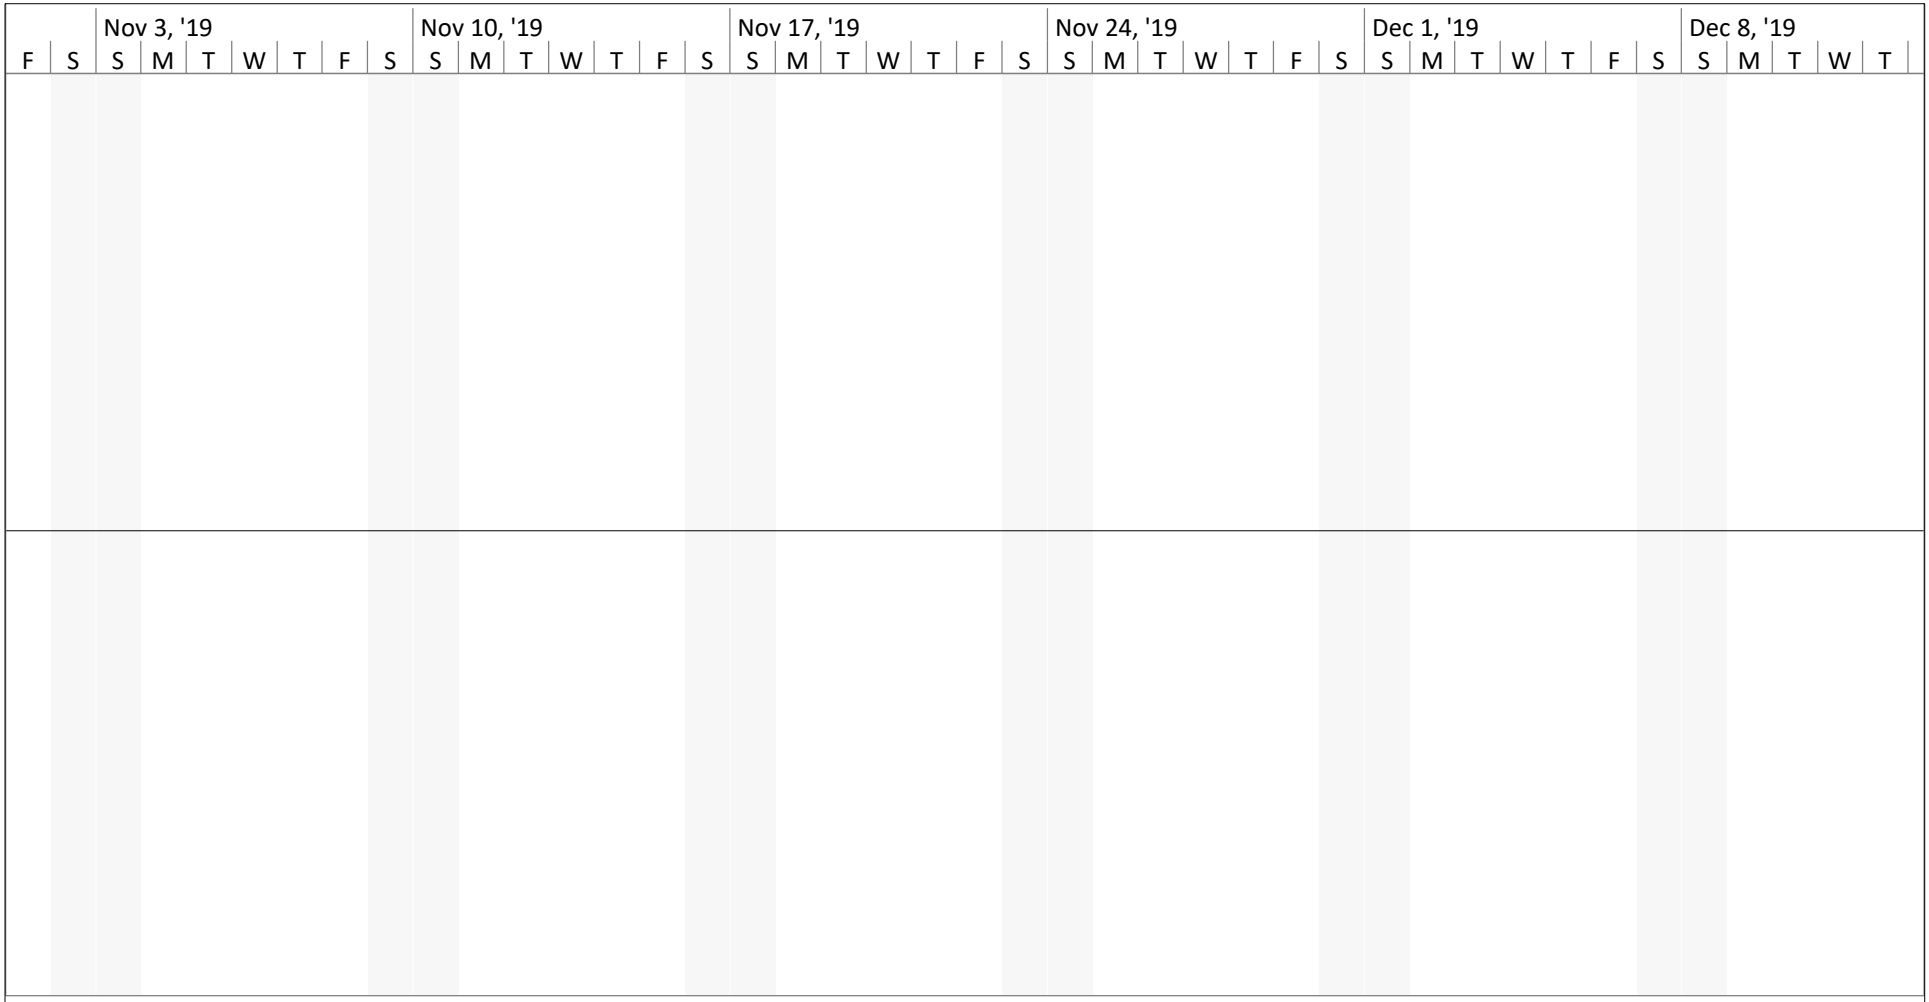


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

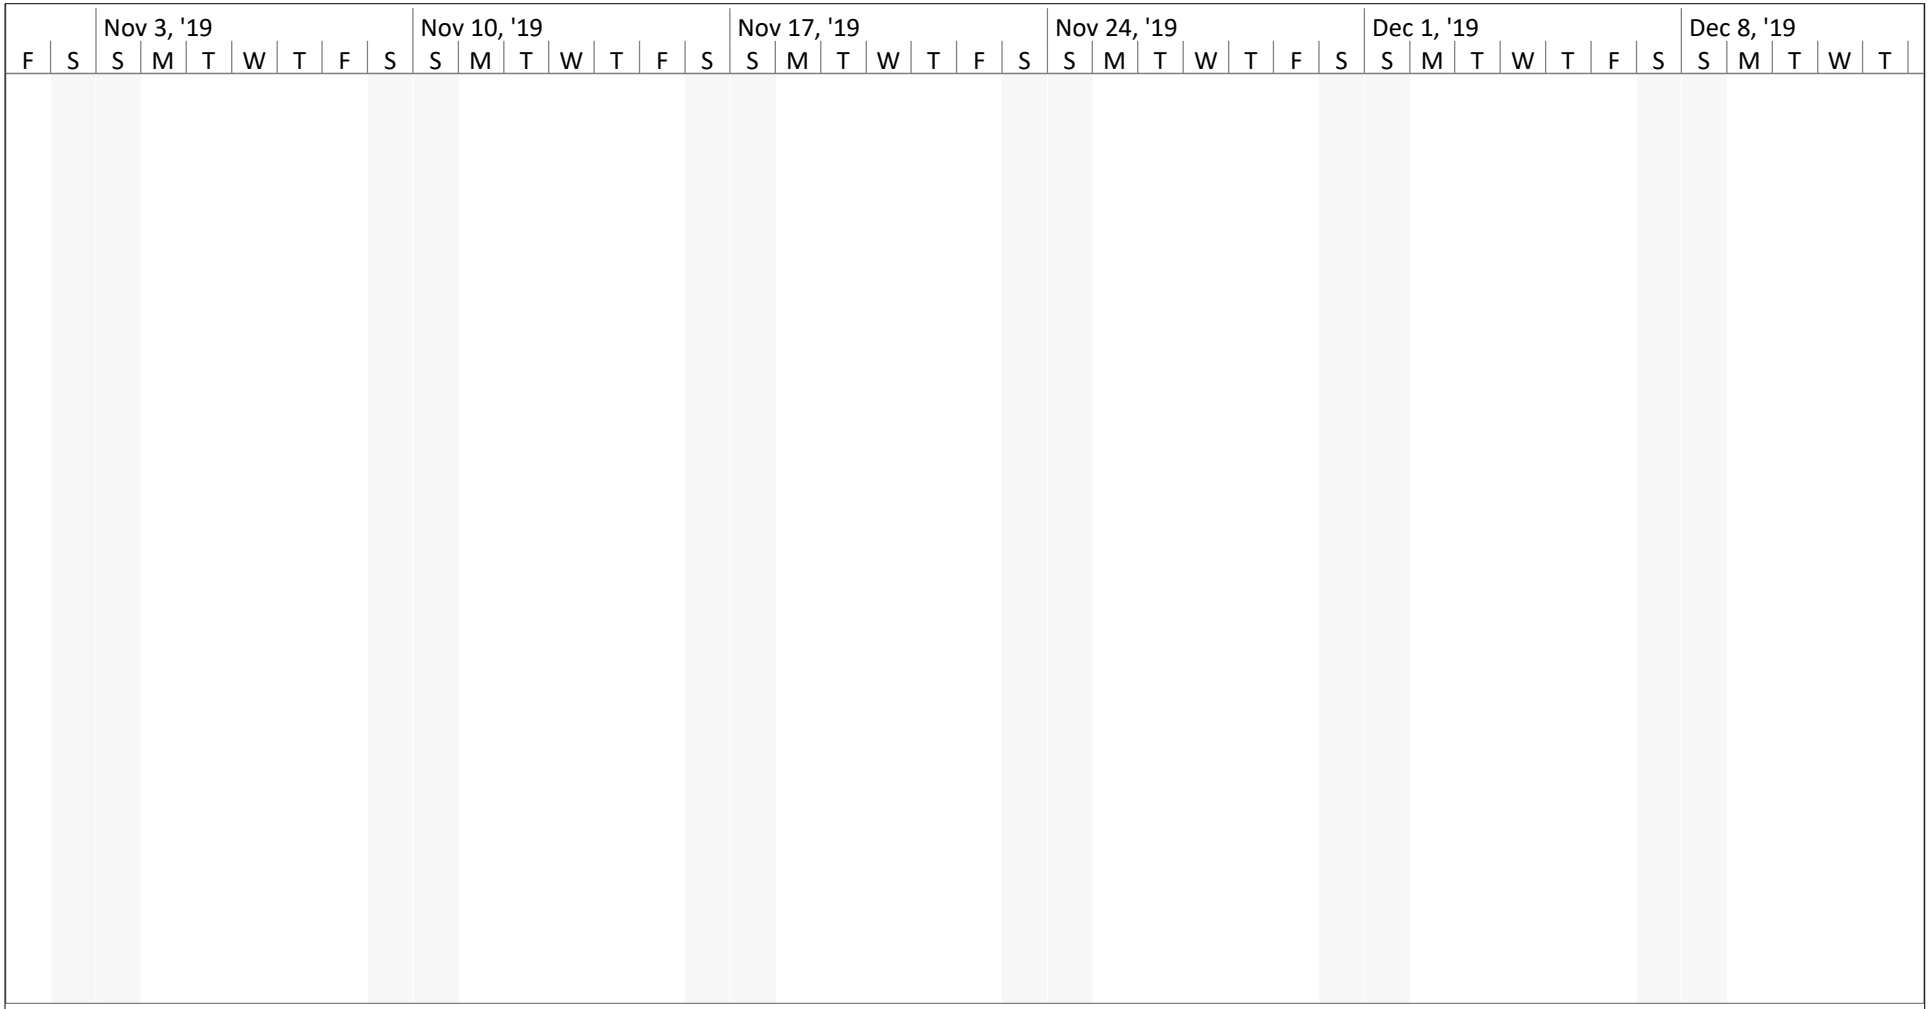


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

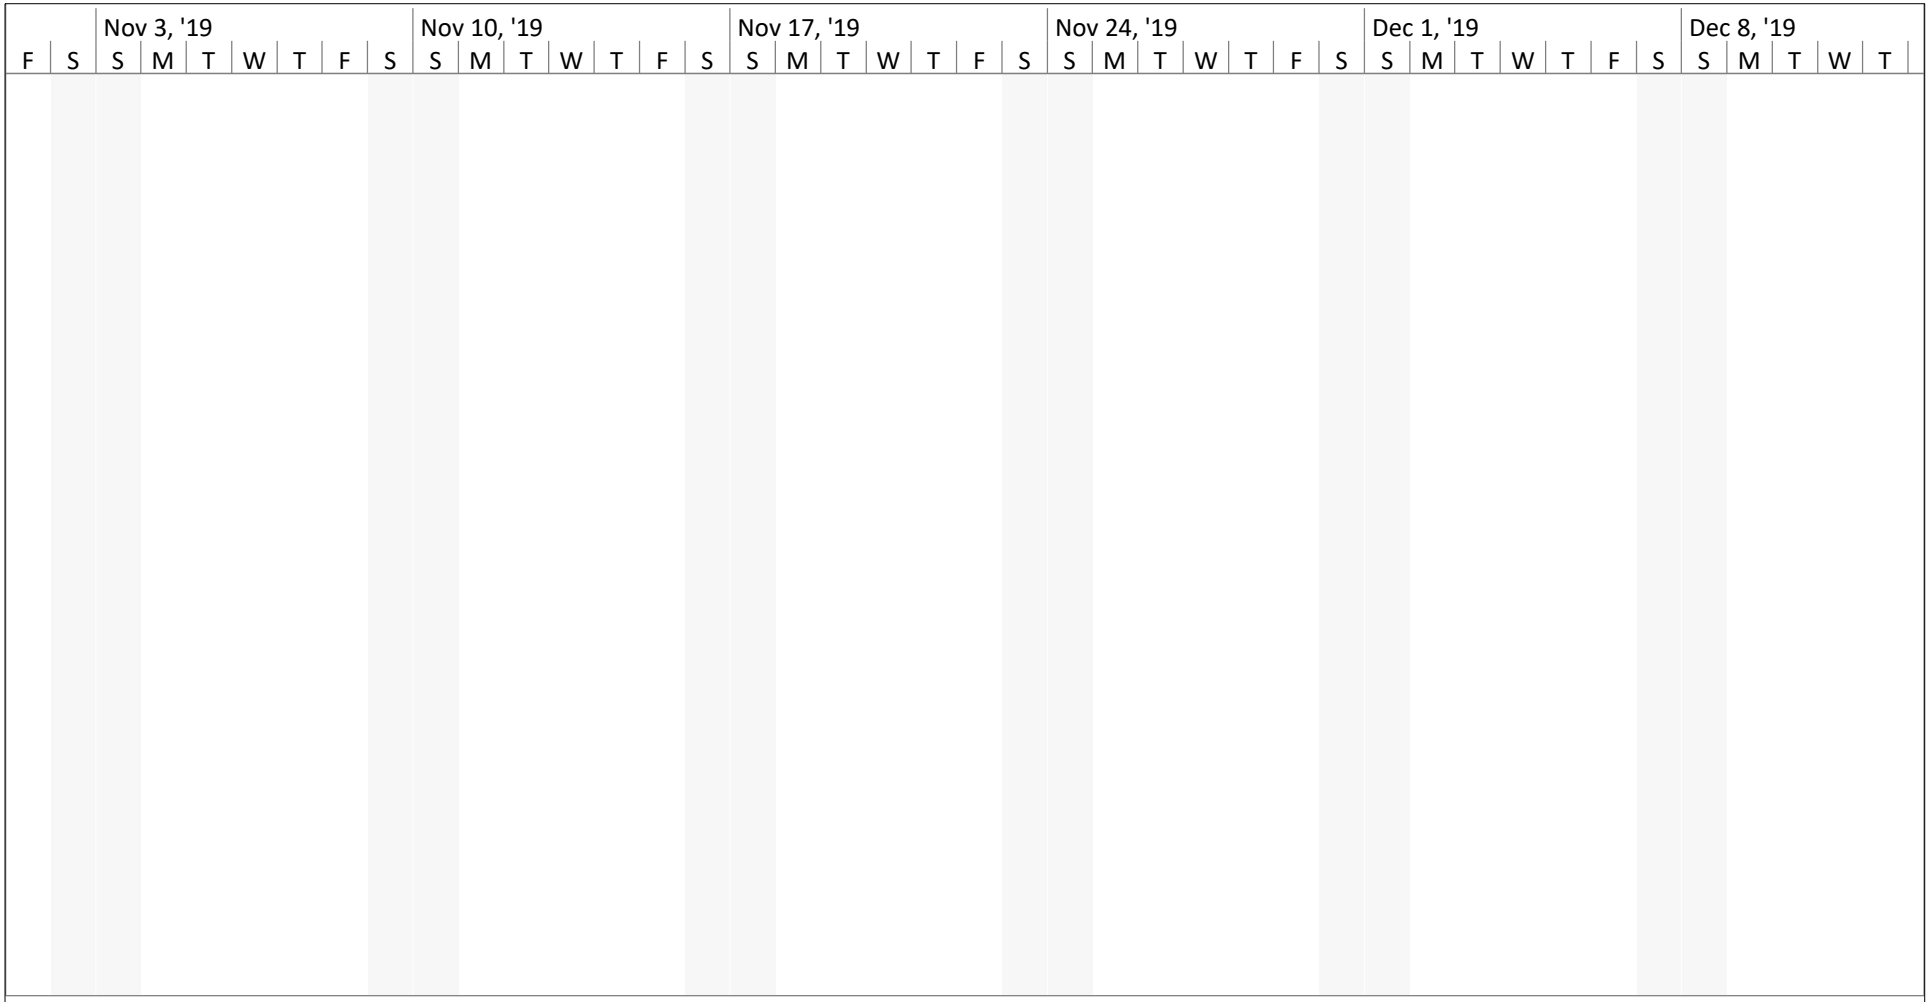


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |




Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

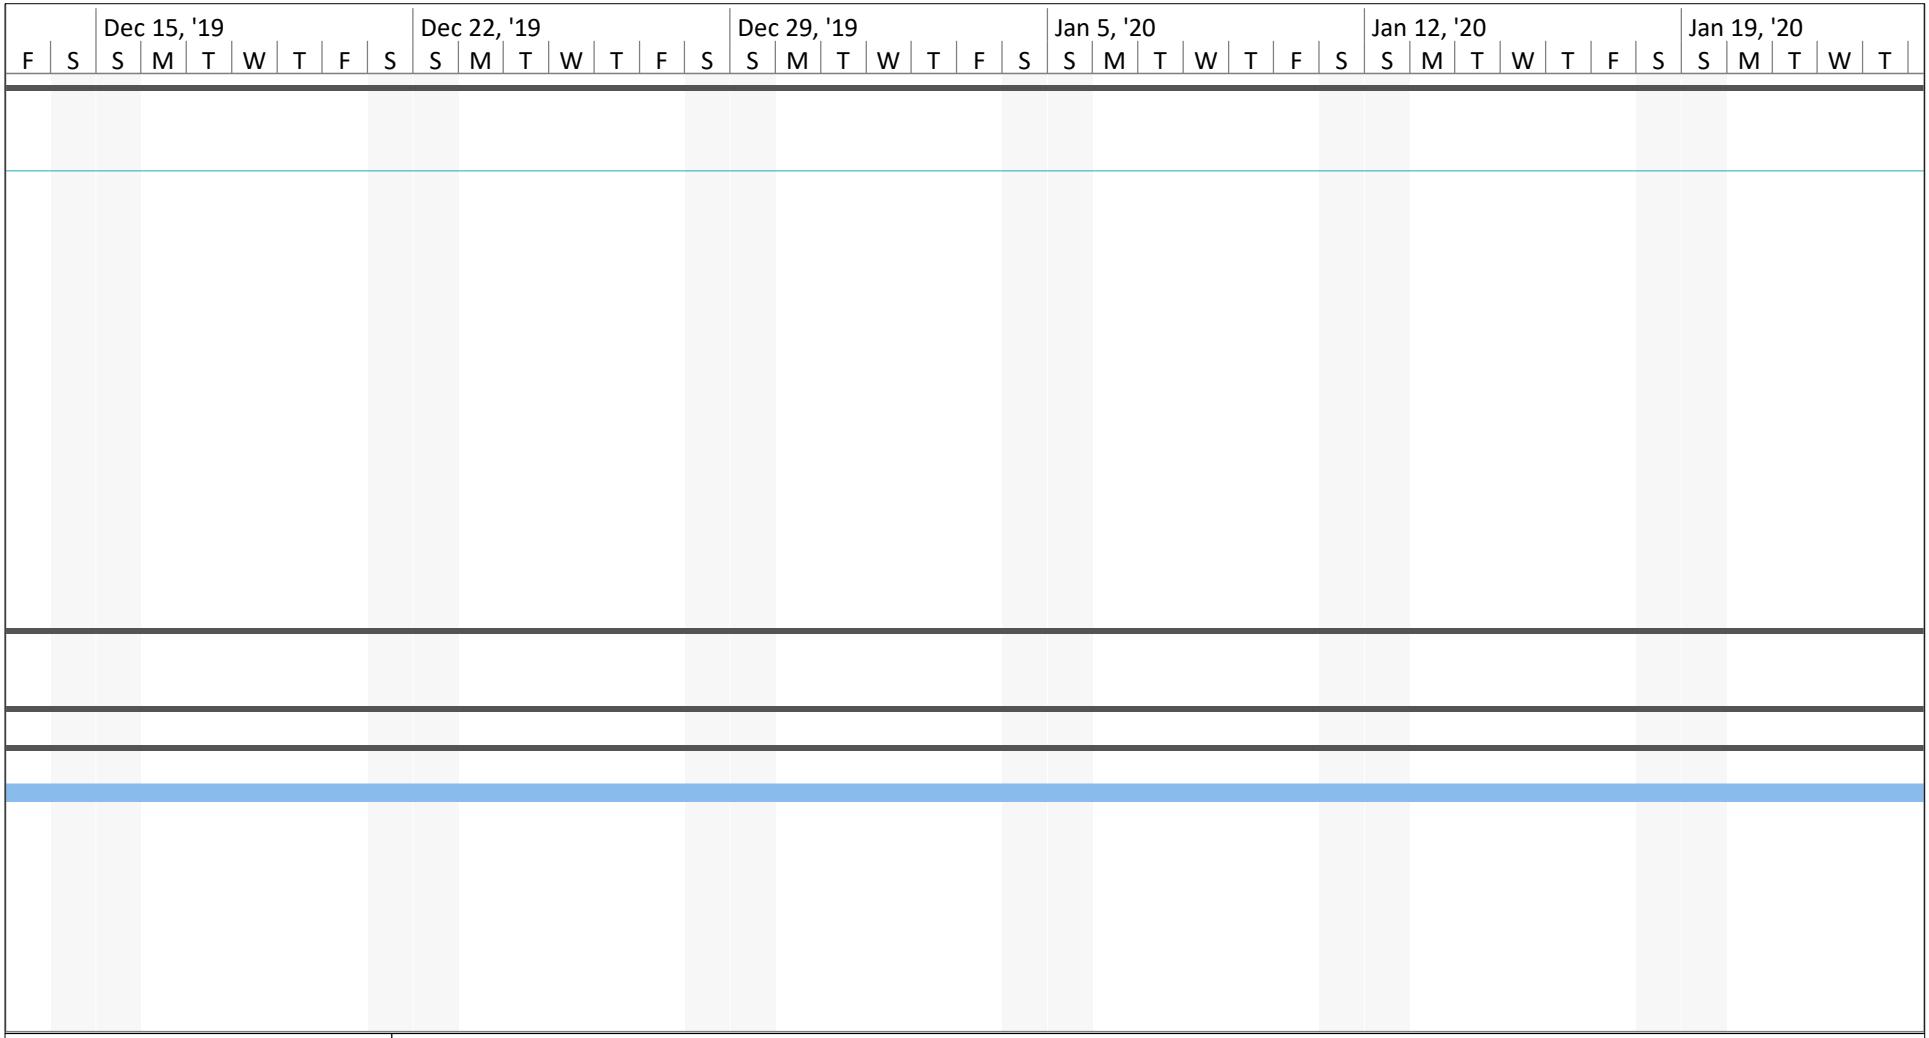


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

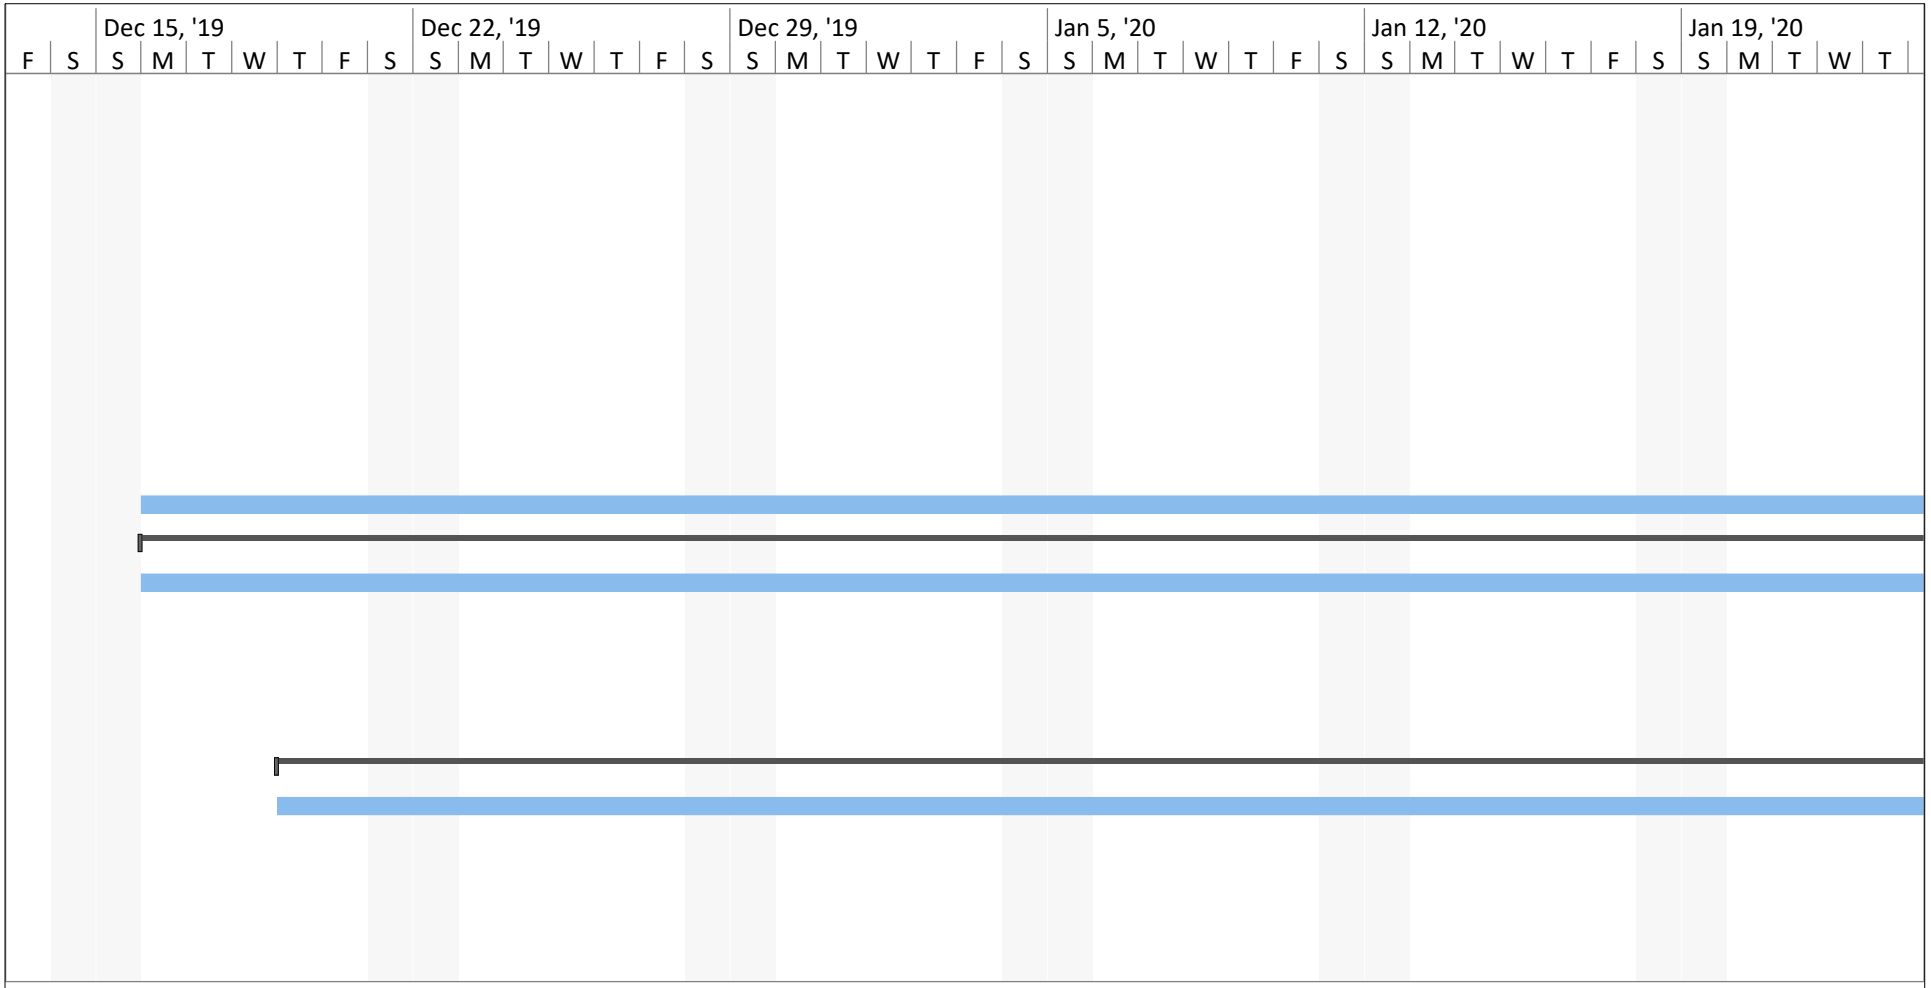


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

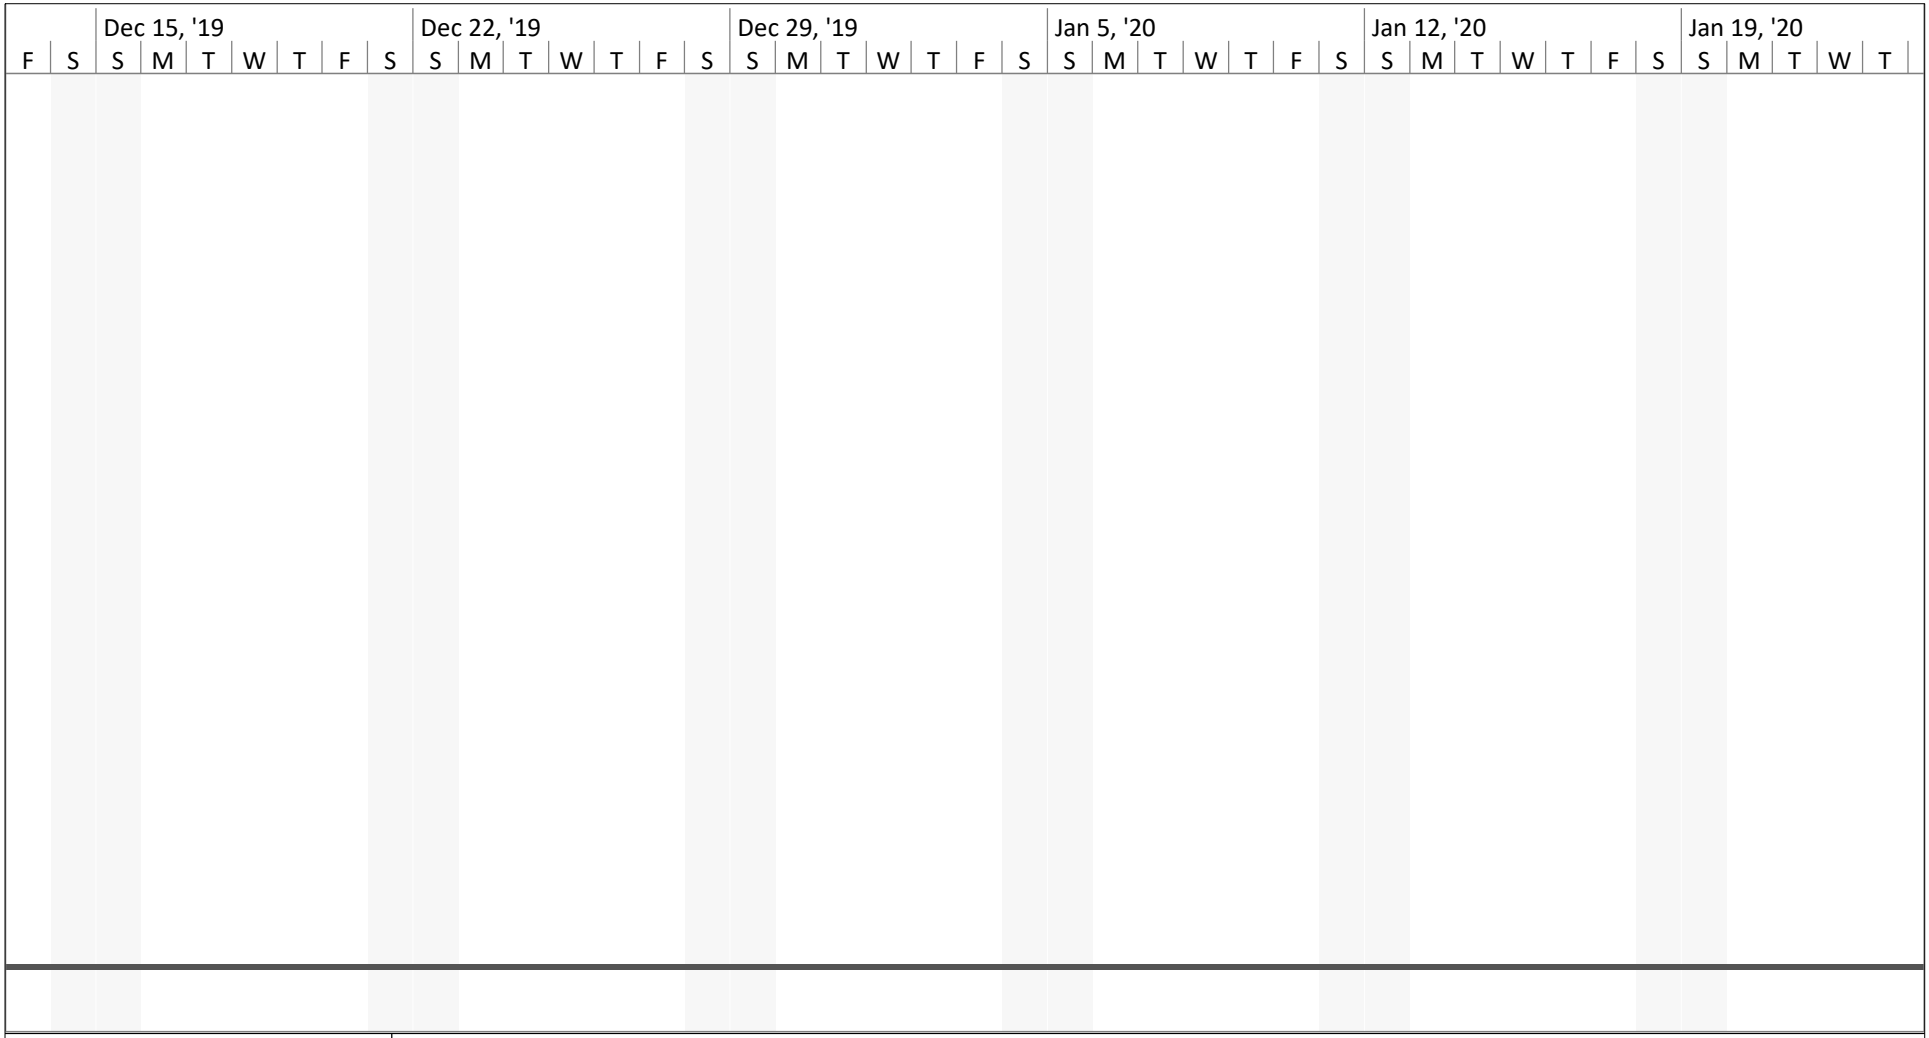


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

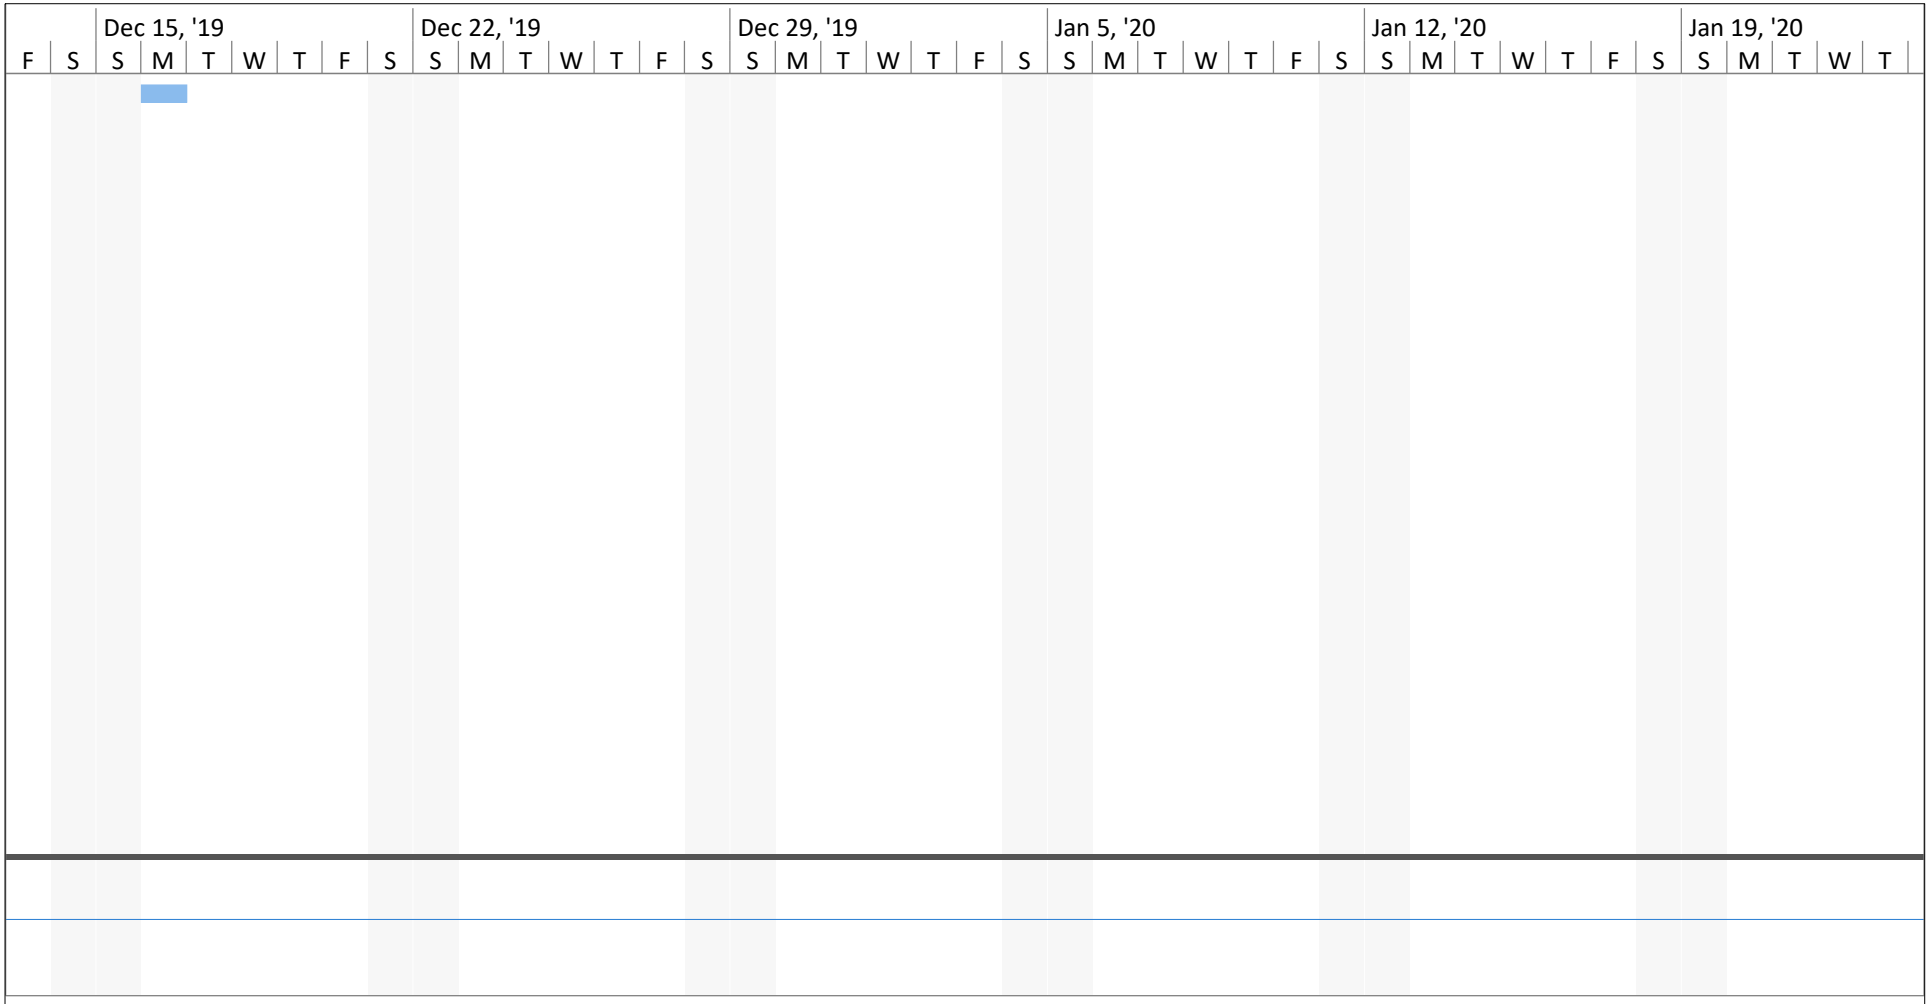


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

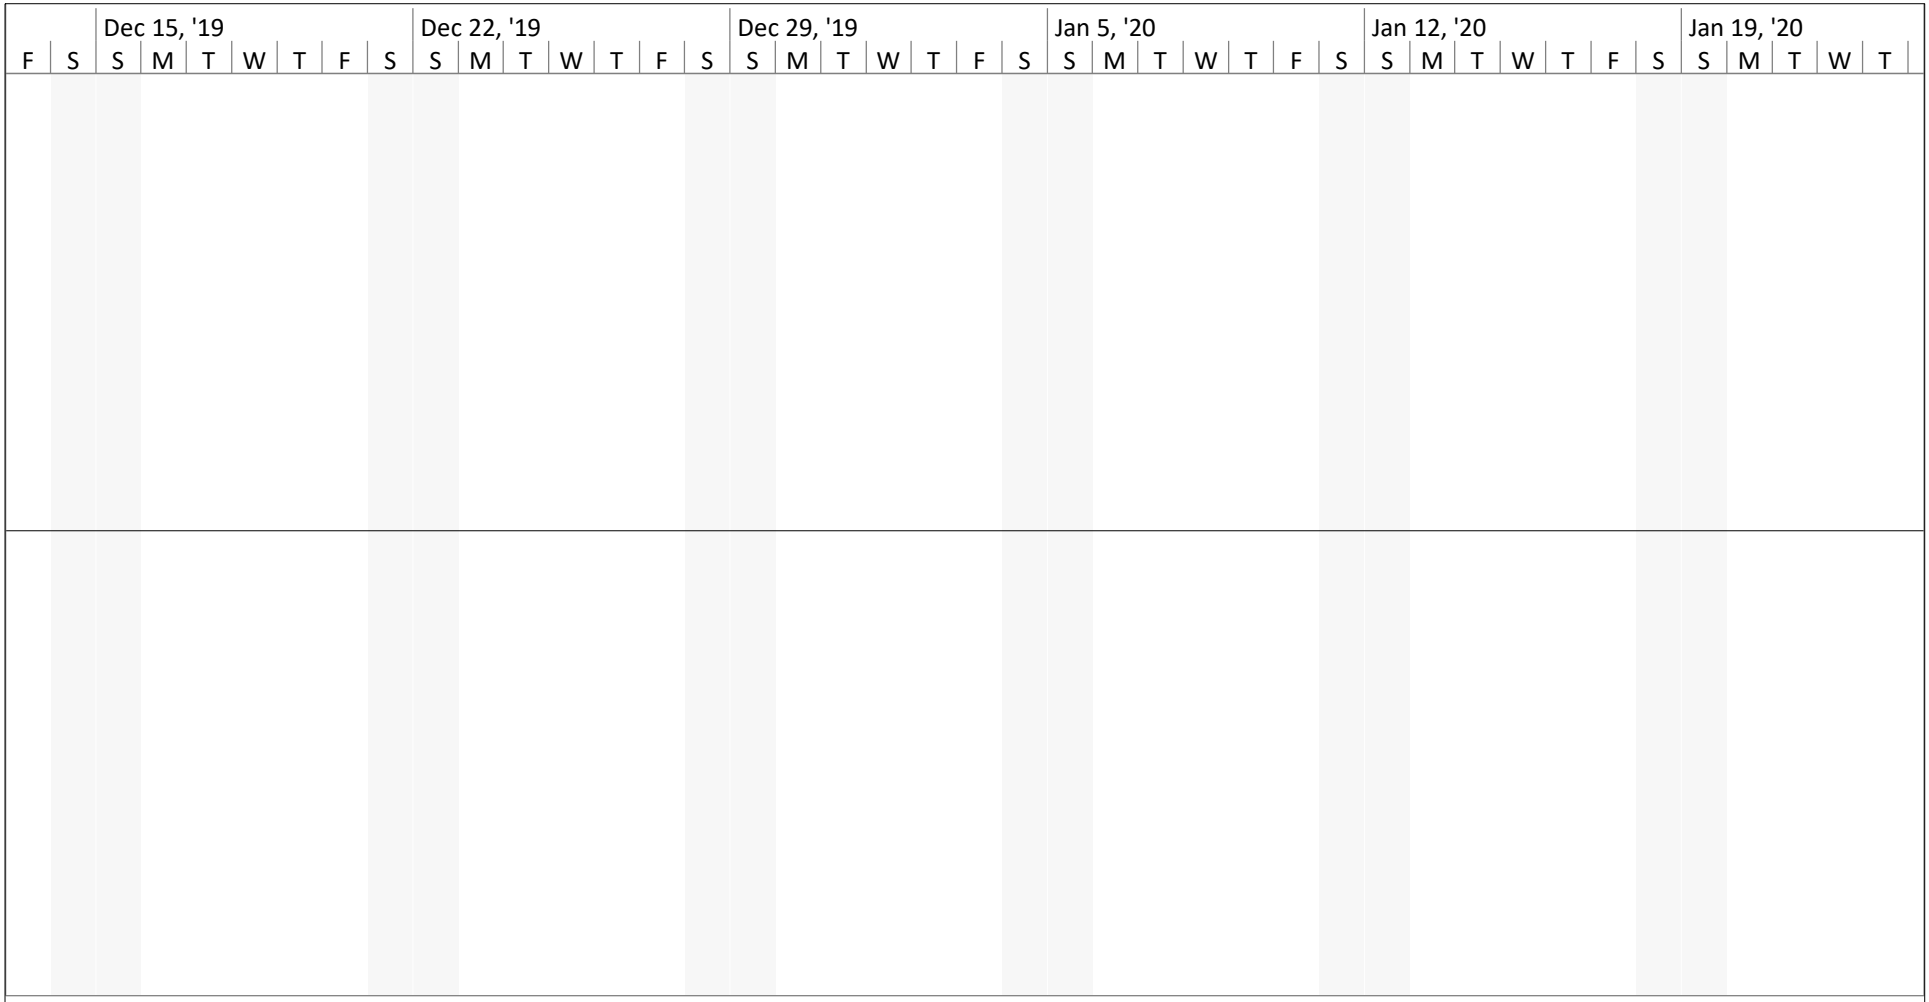


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

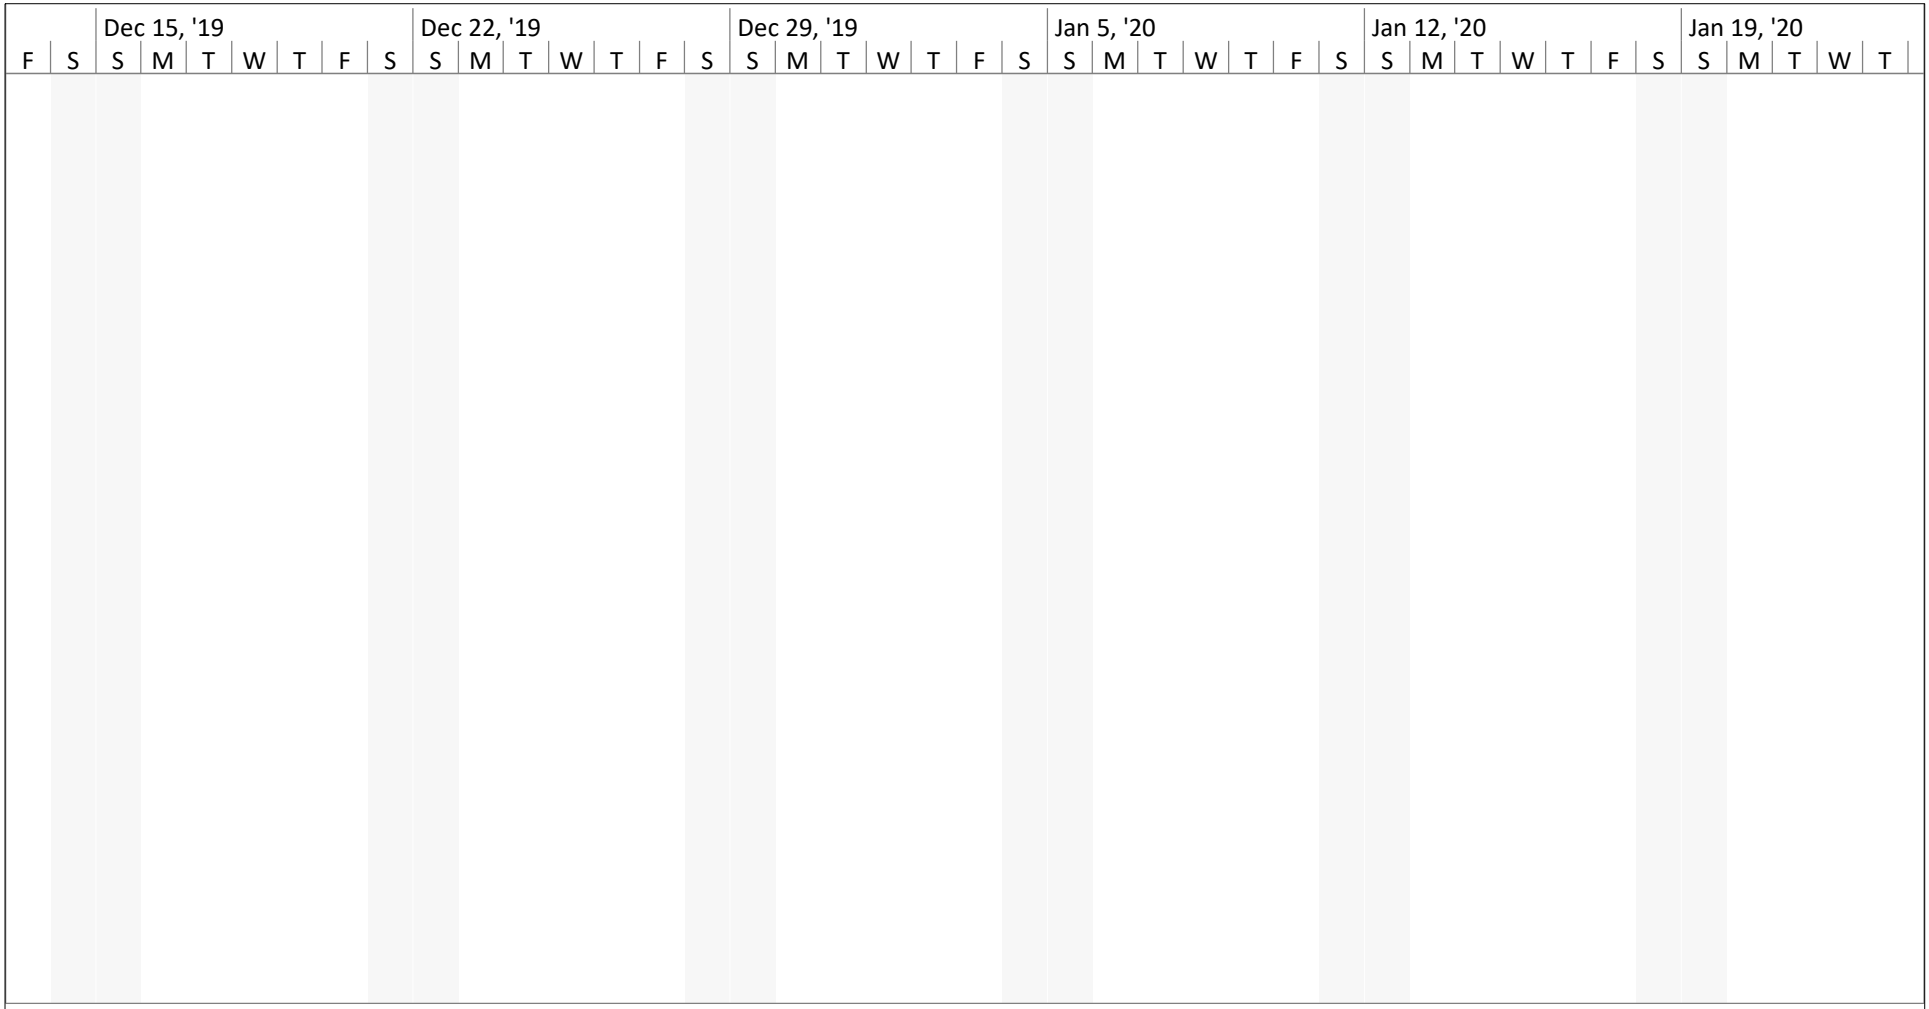


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

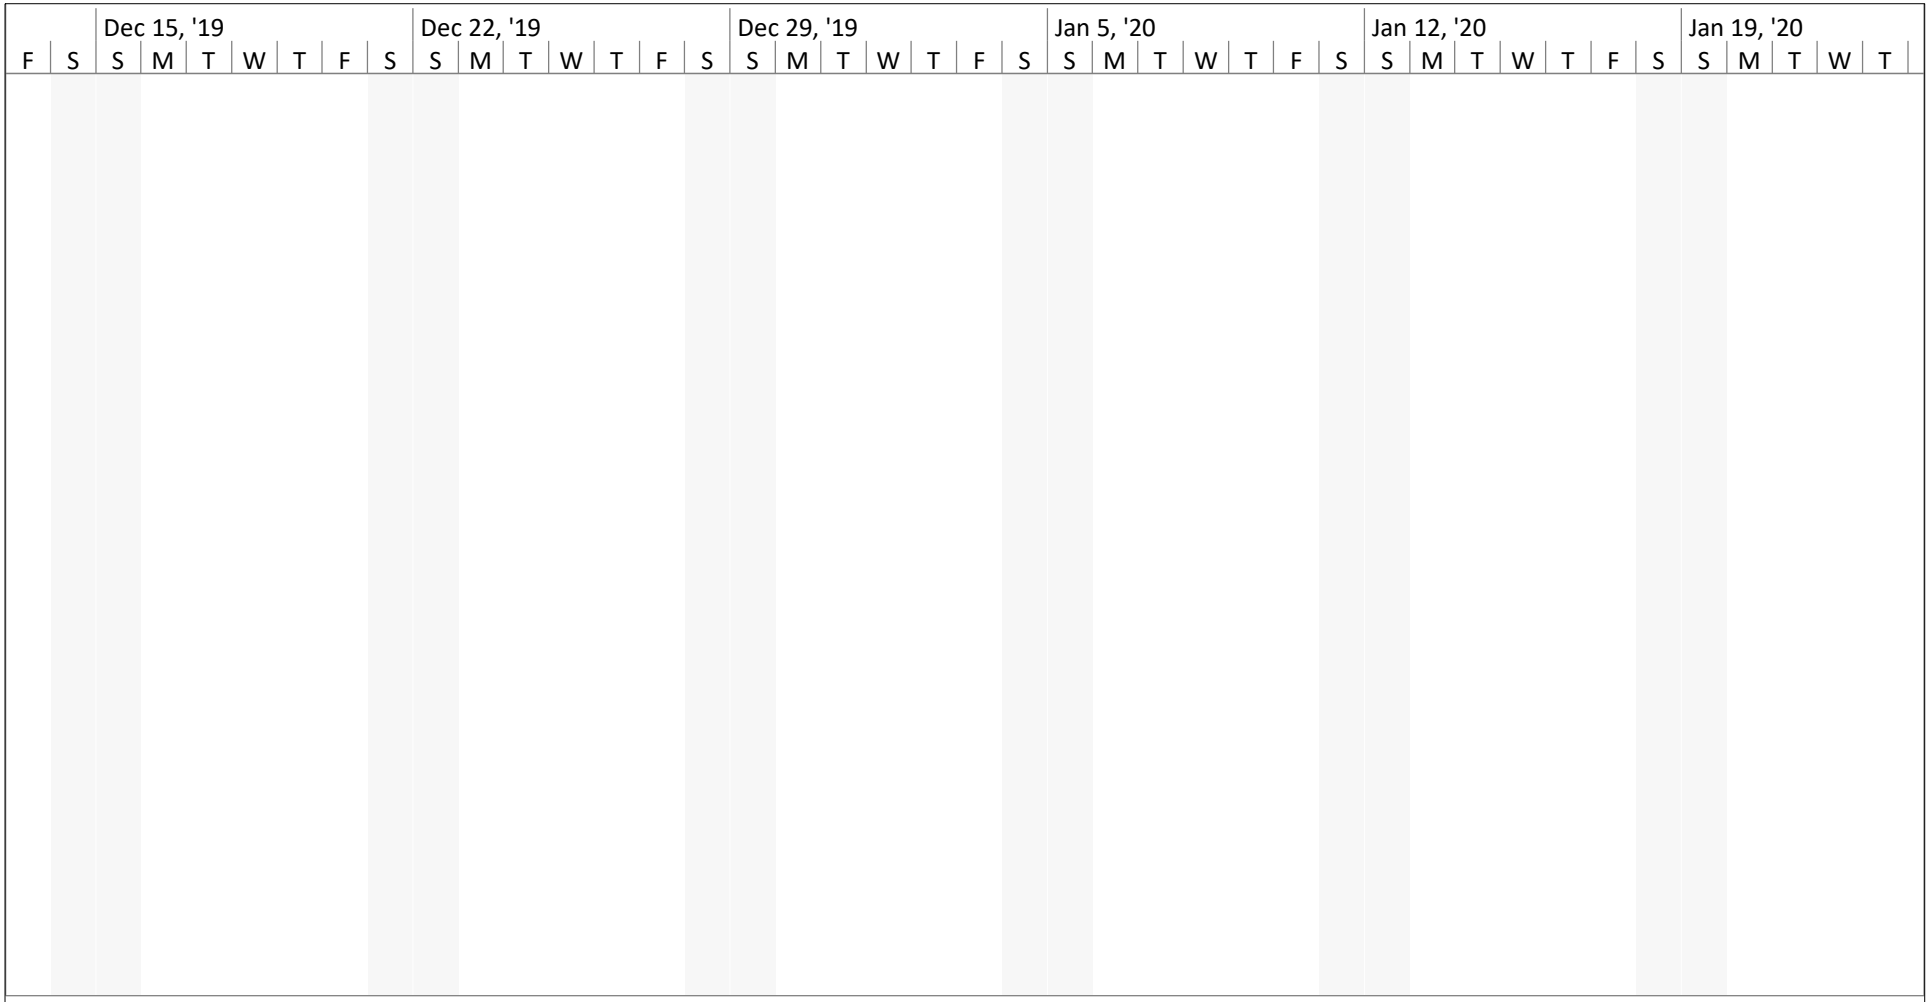


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |




Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

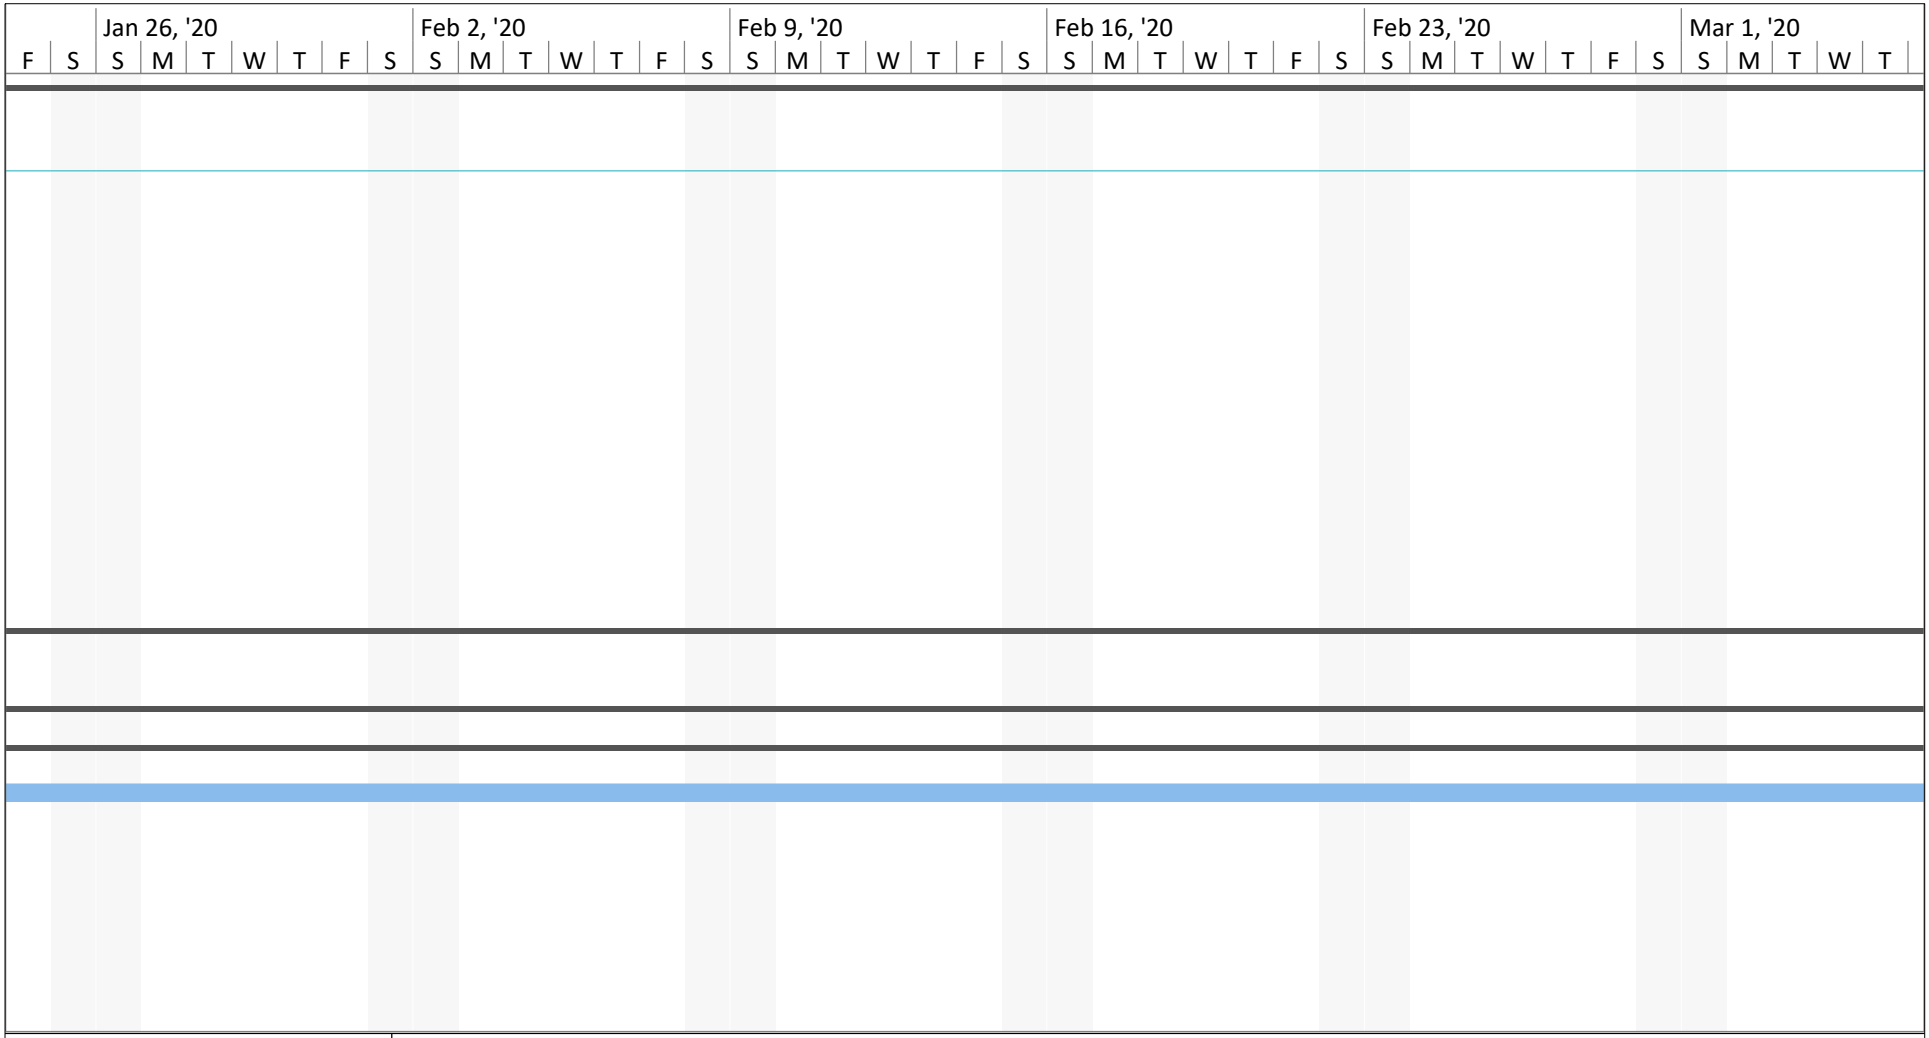


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

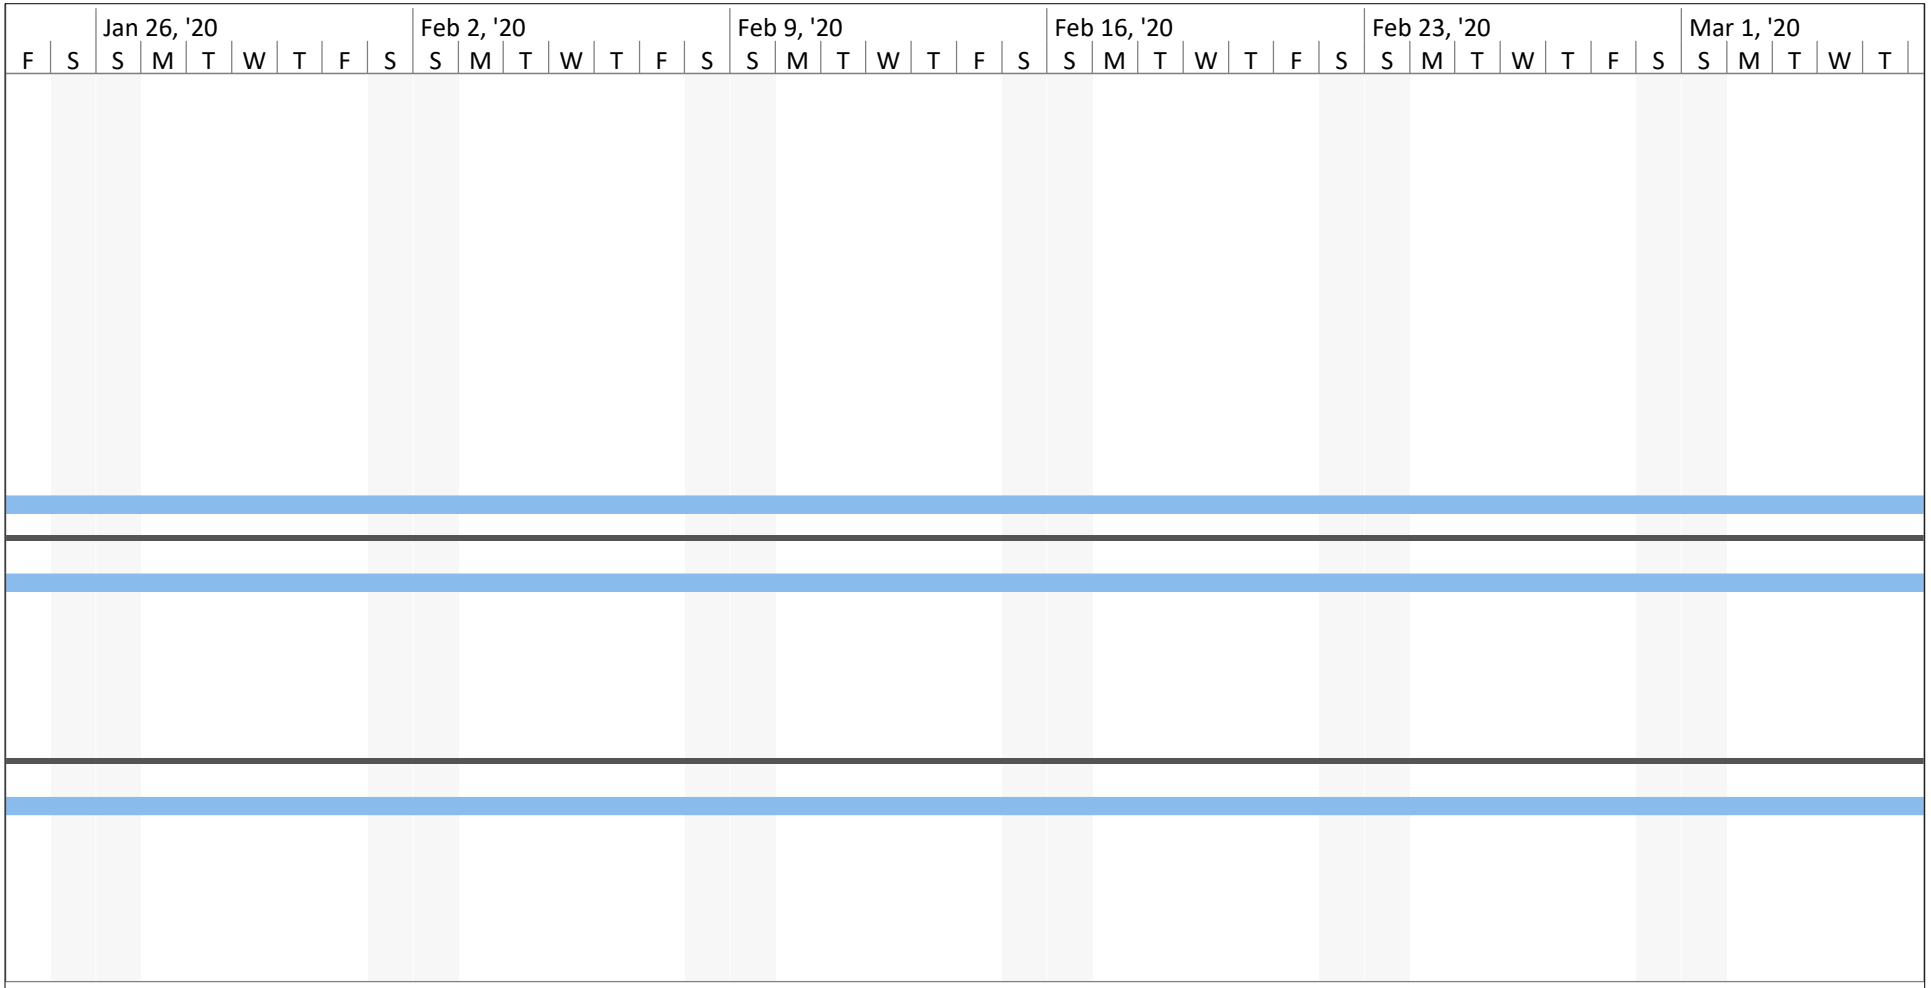


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

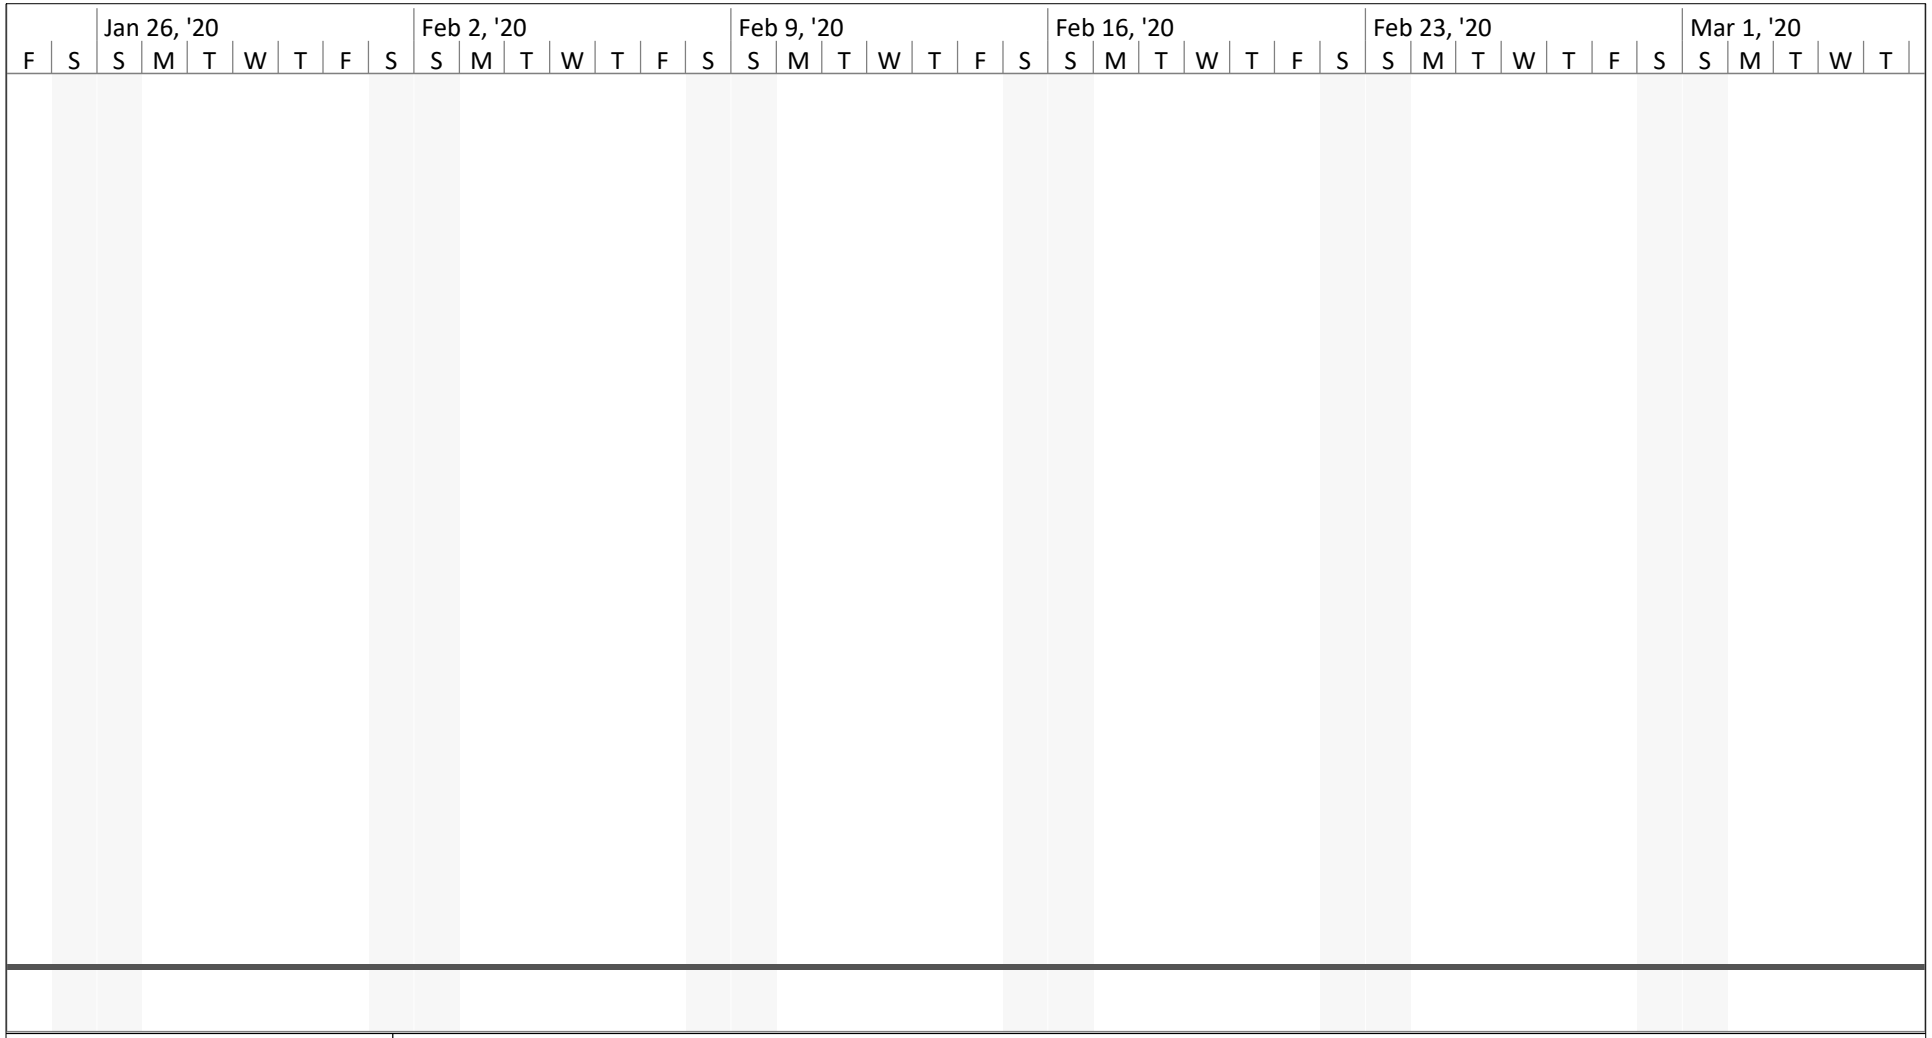


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

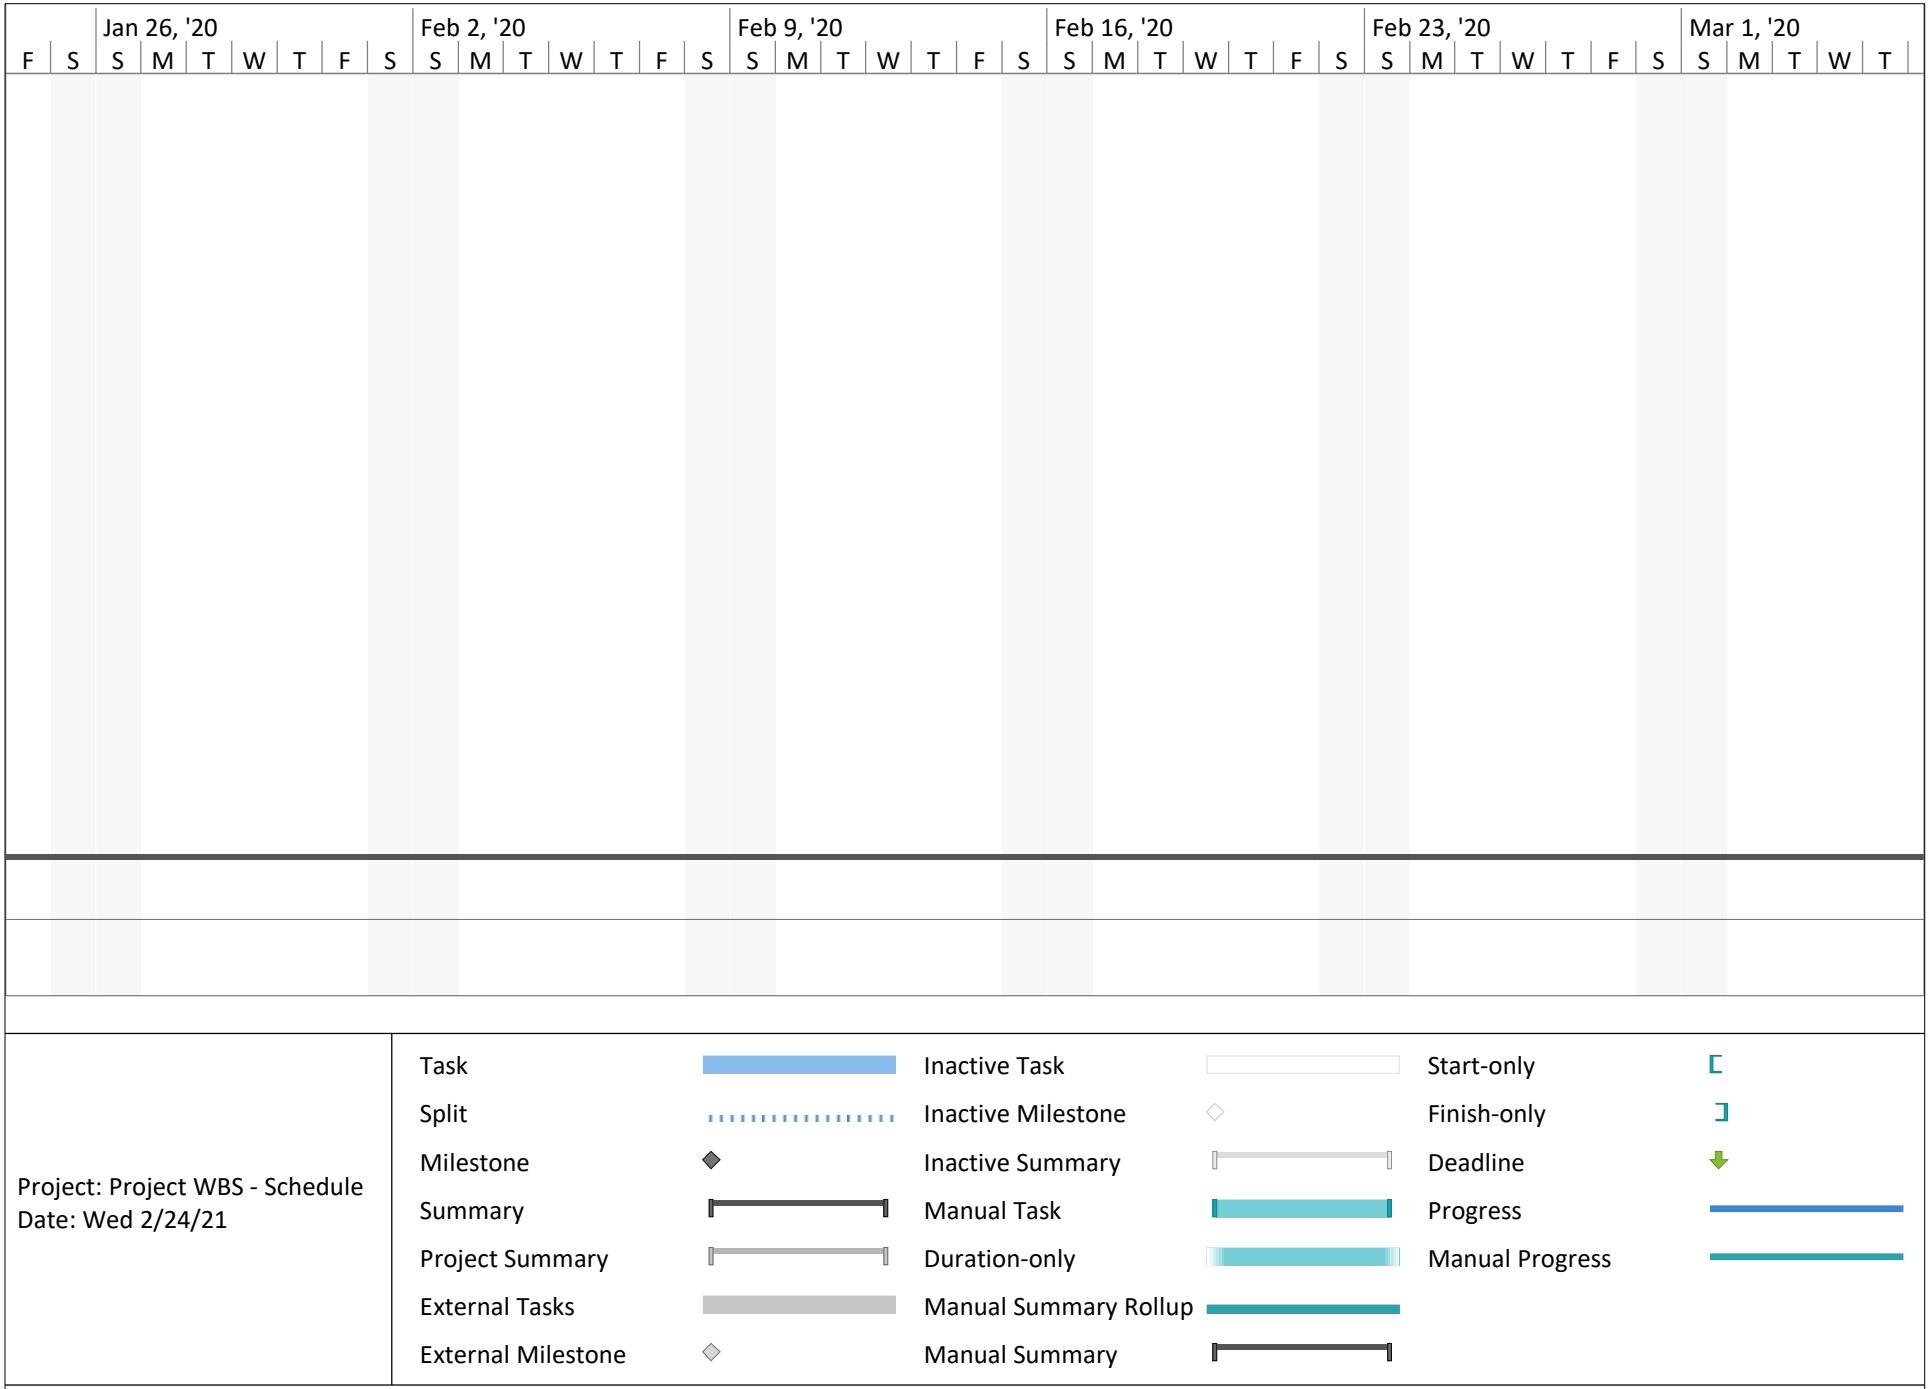
Jan 26, '20
Feb 2, '20
Feb 9, '20
Feb 16, '20
Feb 23, '20
Mar 1, '20
F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S
Project: Project WBS - Schedule
Date: Wed 2/24/21
Task
Split
Milestone
Summary
Project Summary
External Tasks
External Milestone
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
Deadline
Progress
Manual Progress

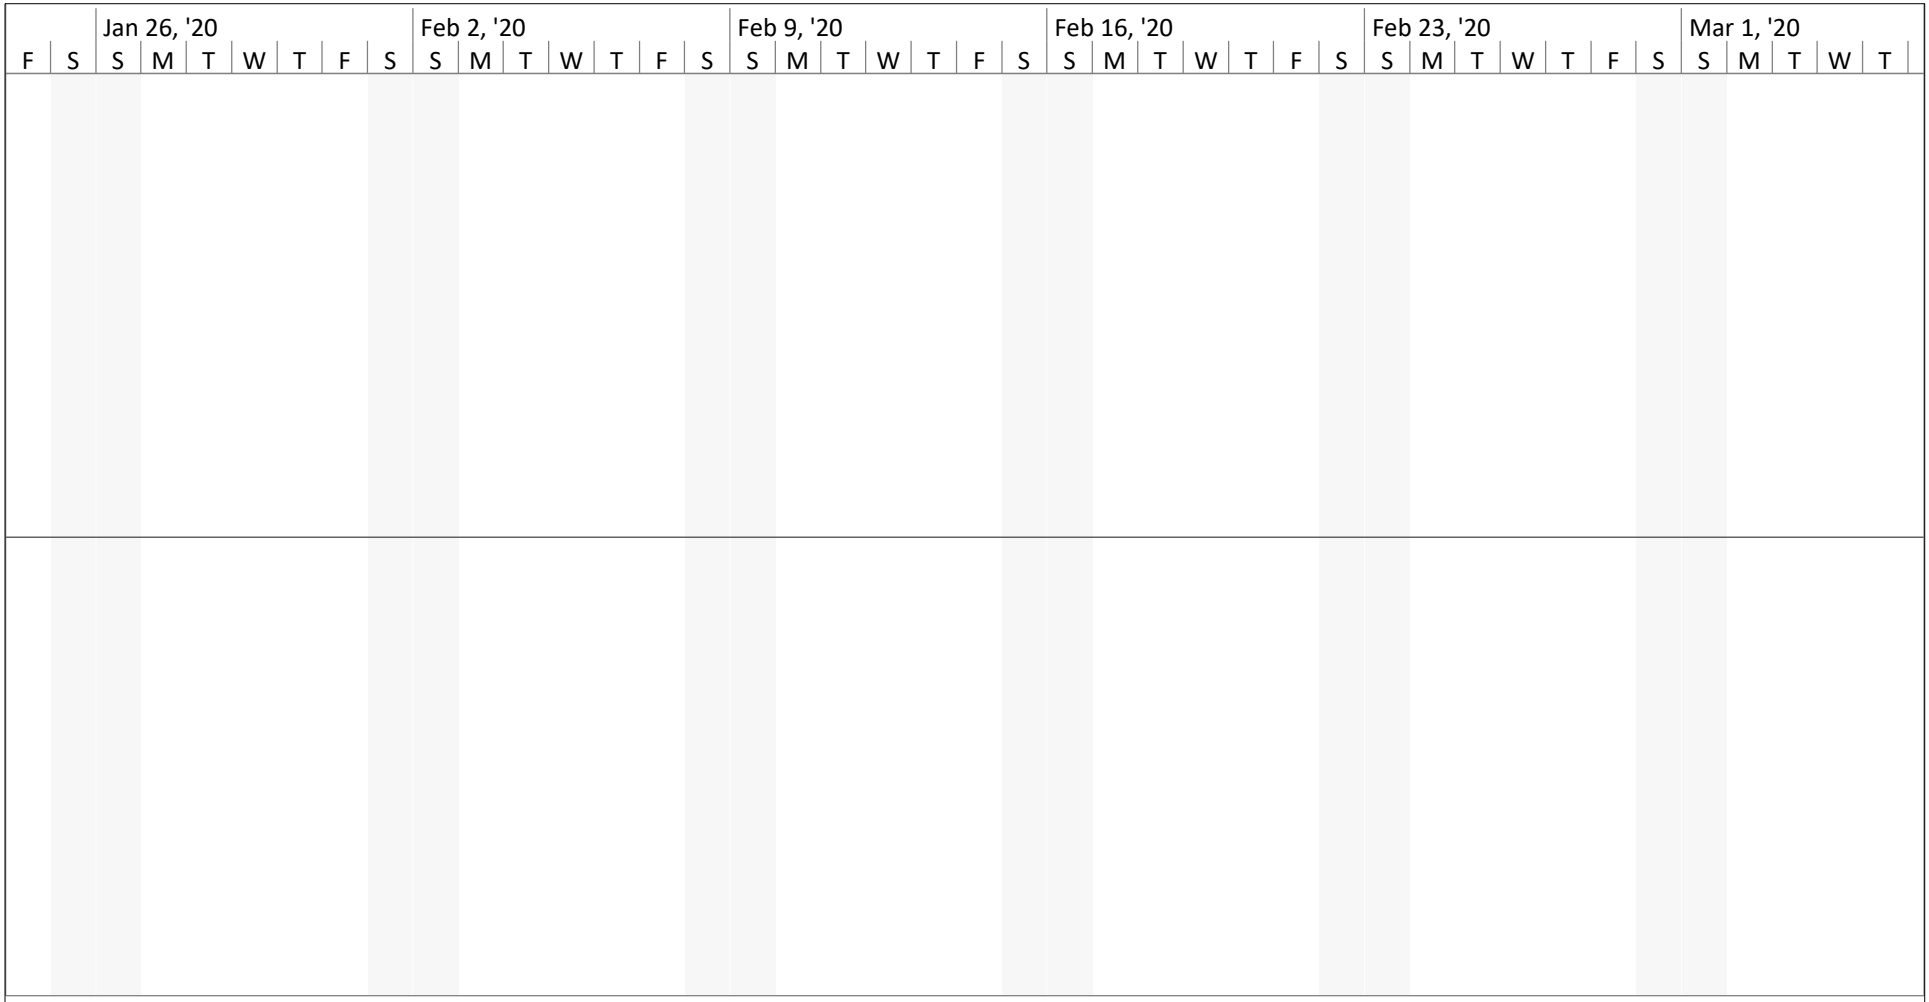


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

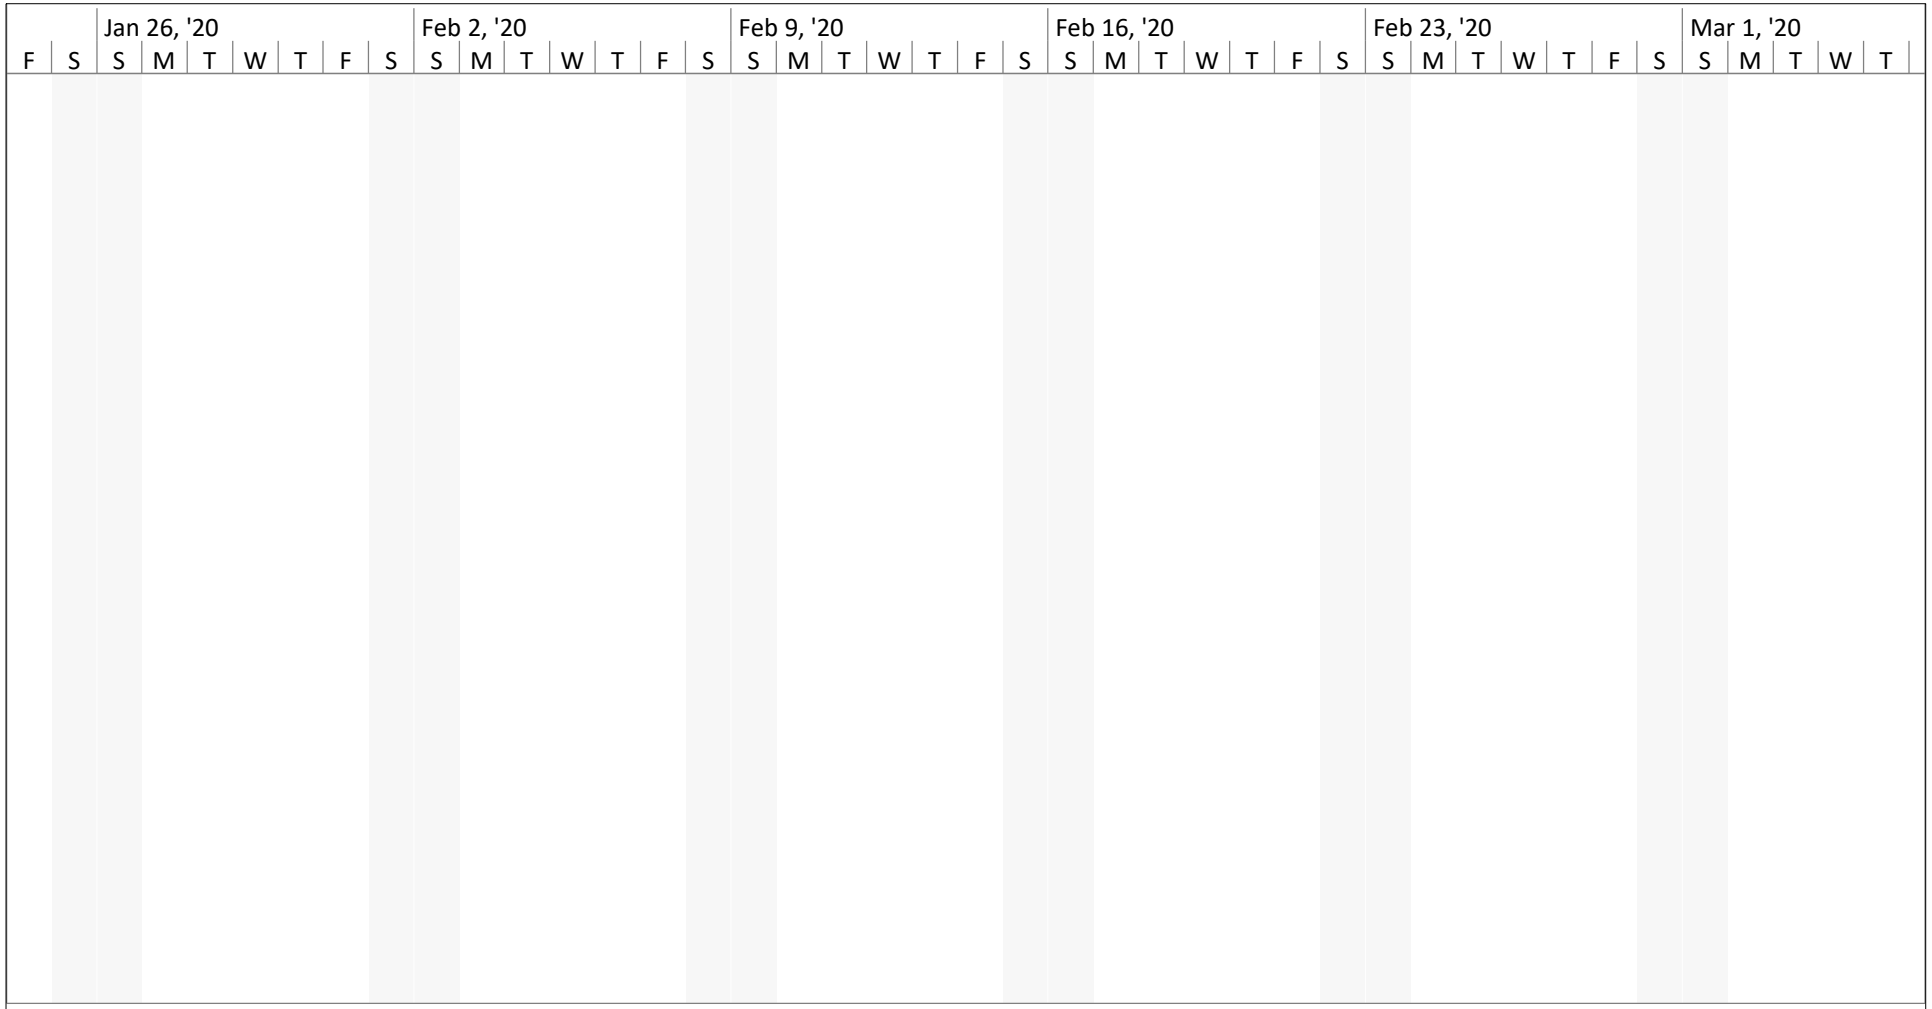


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

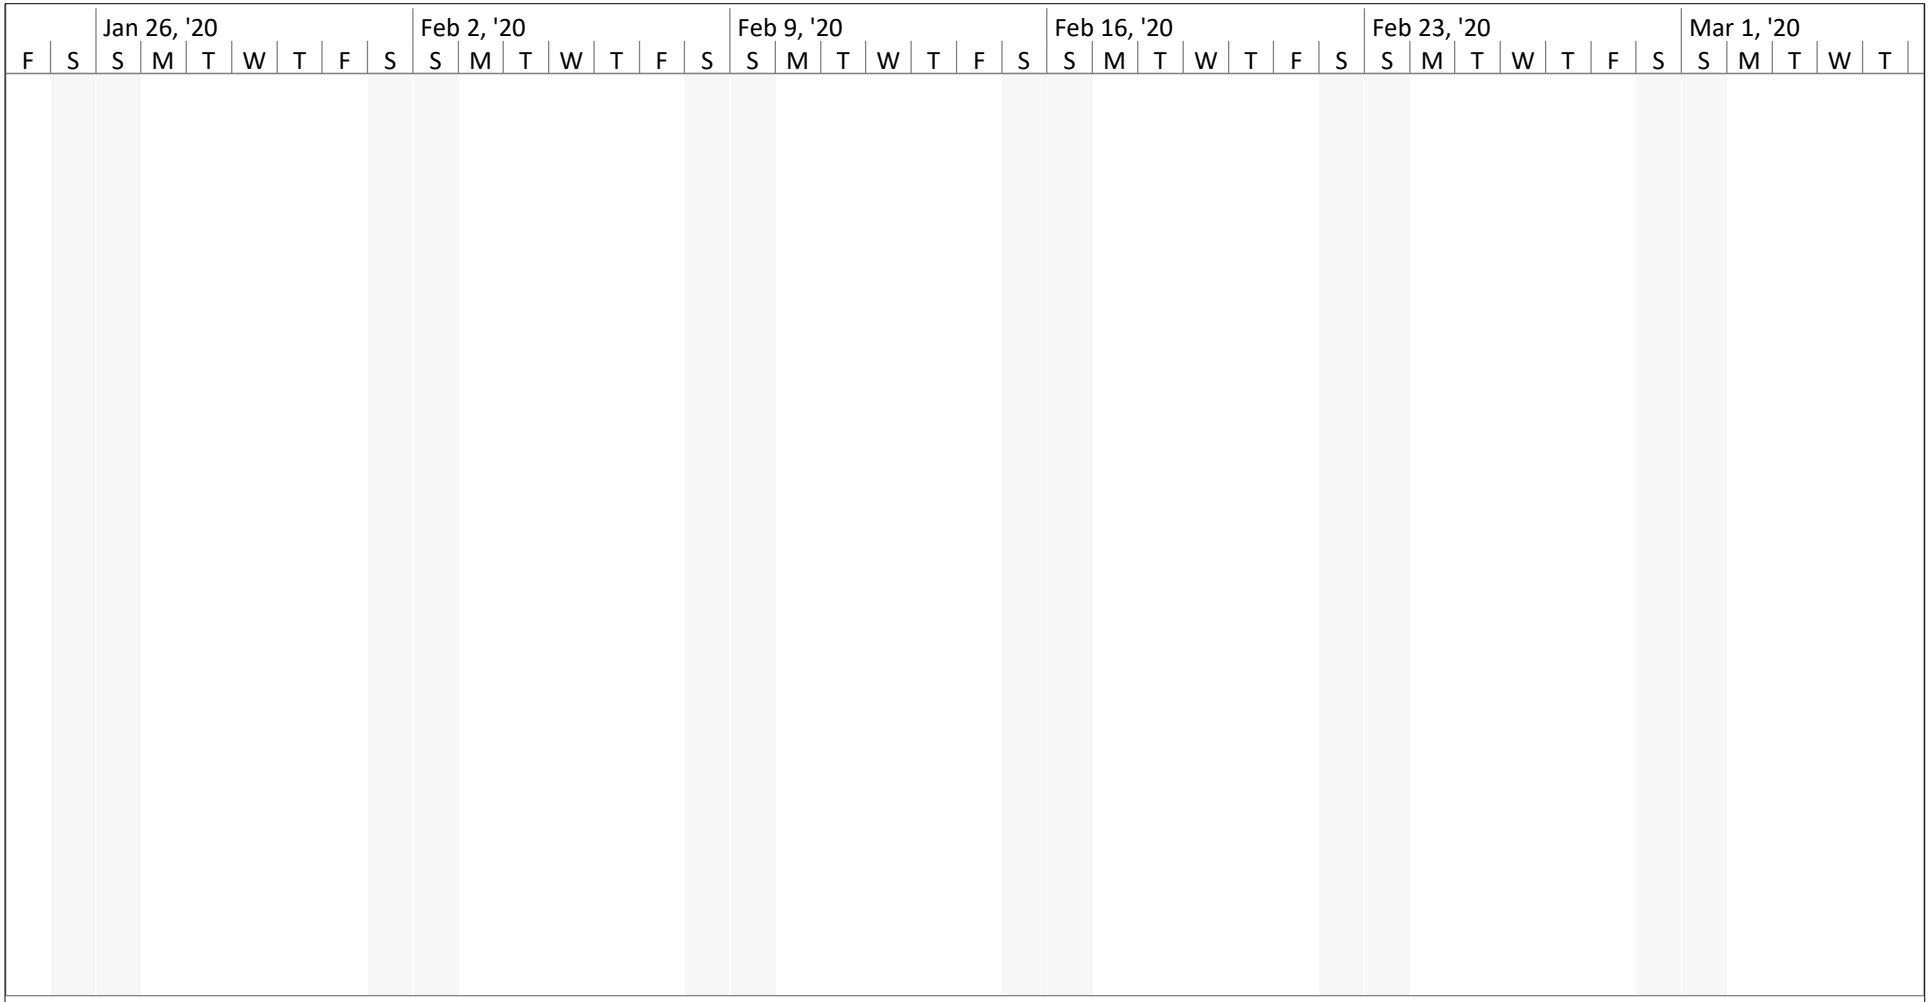


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |




Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

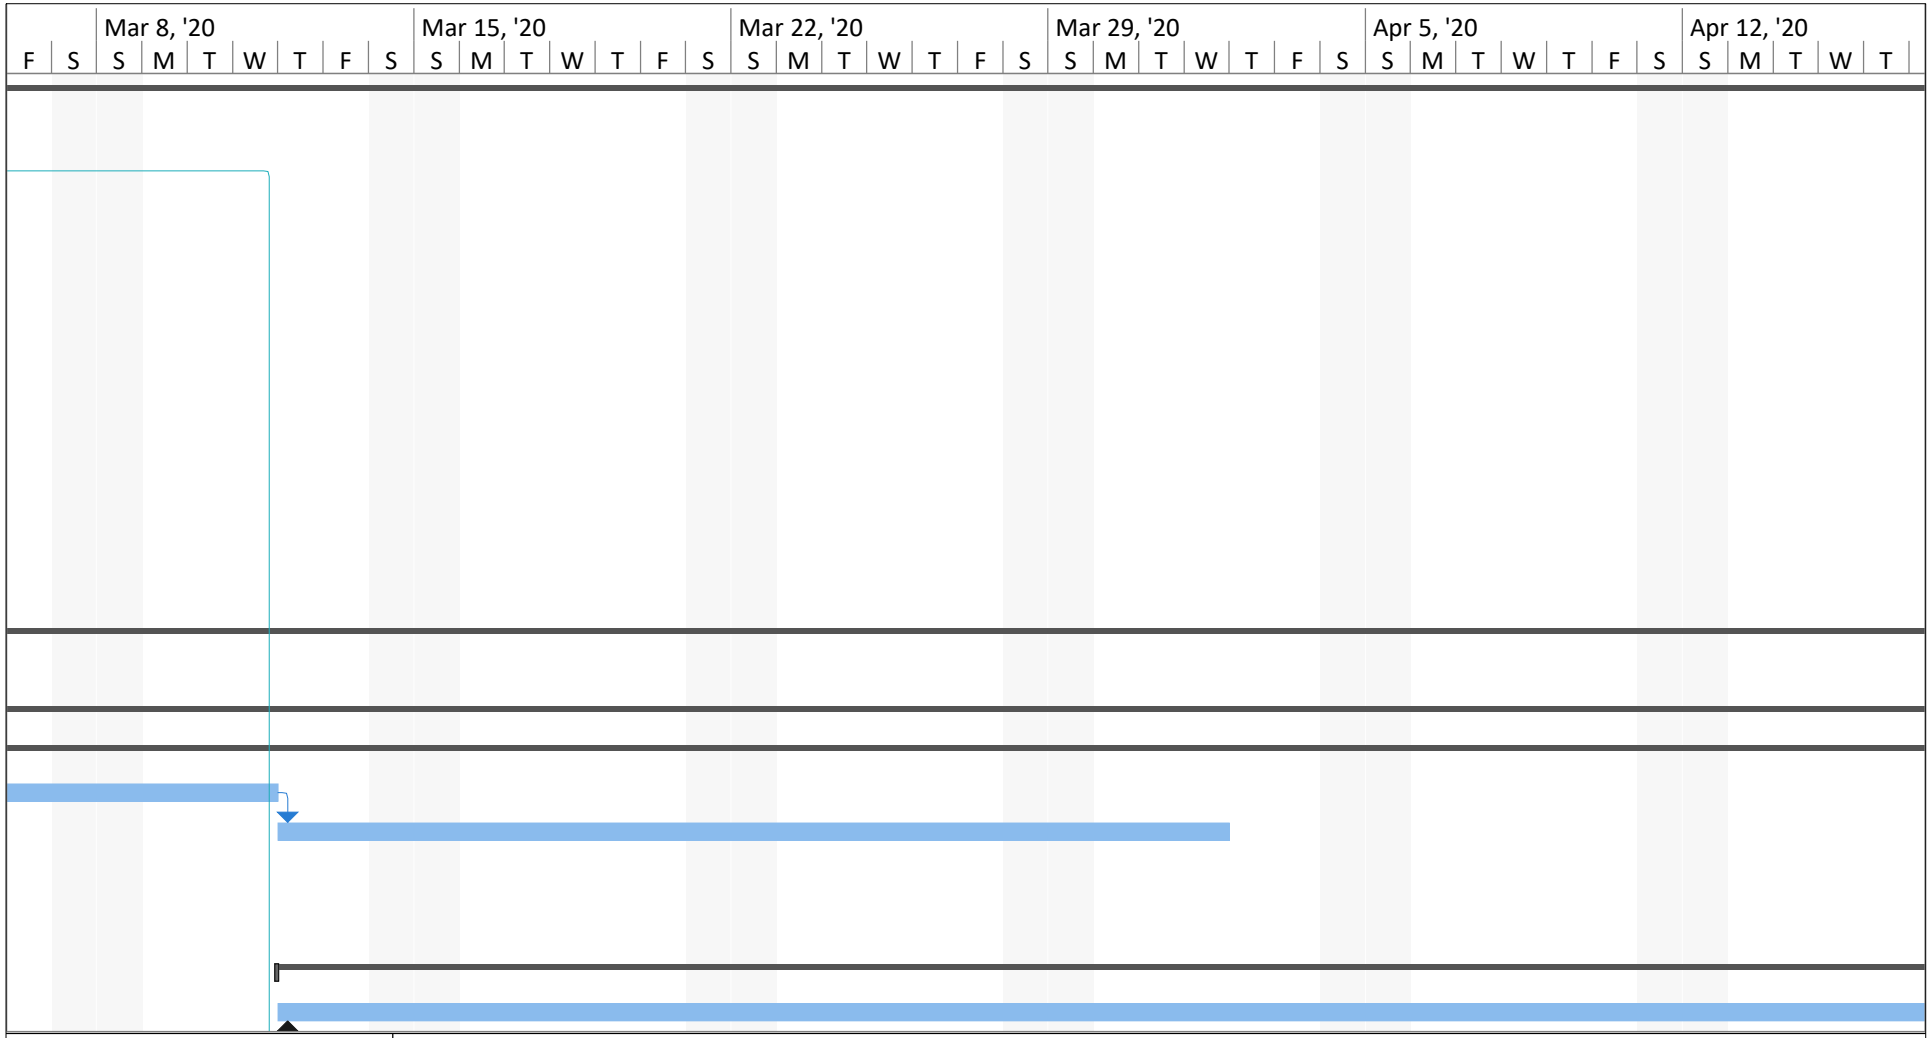


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

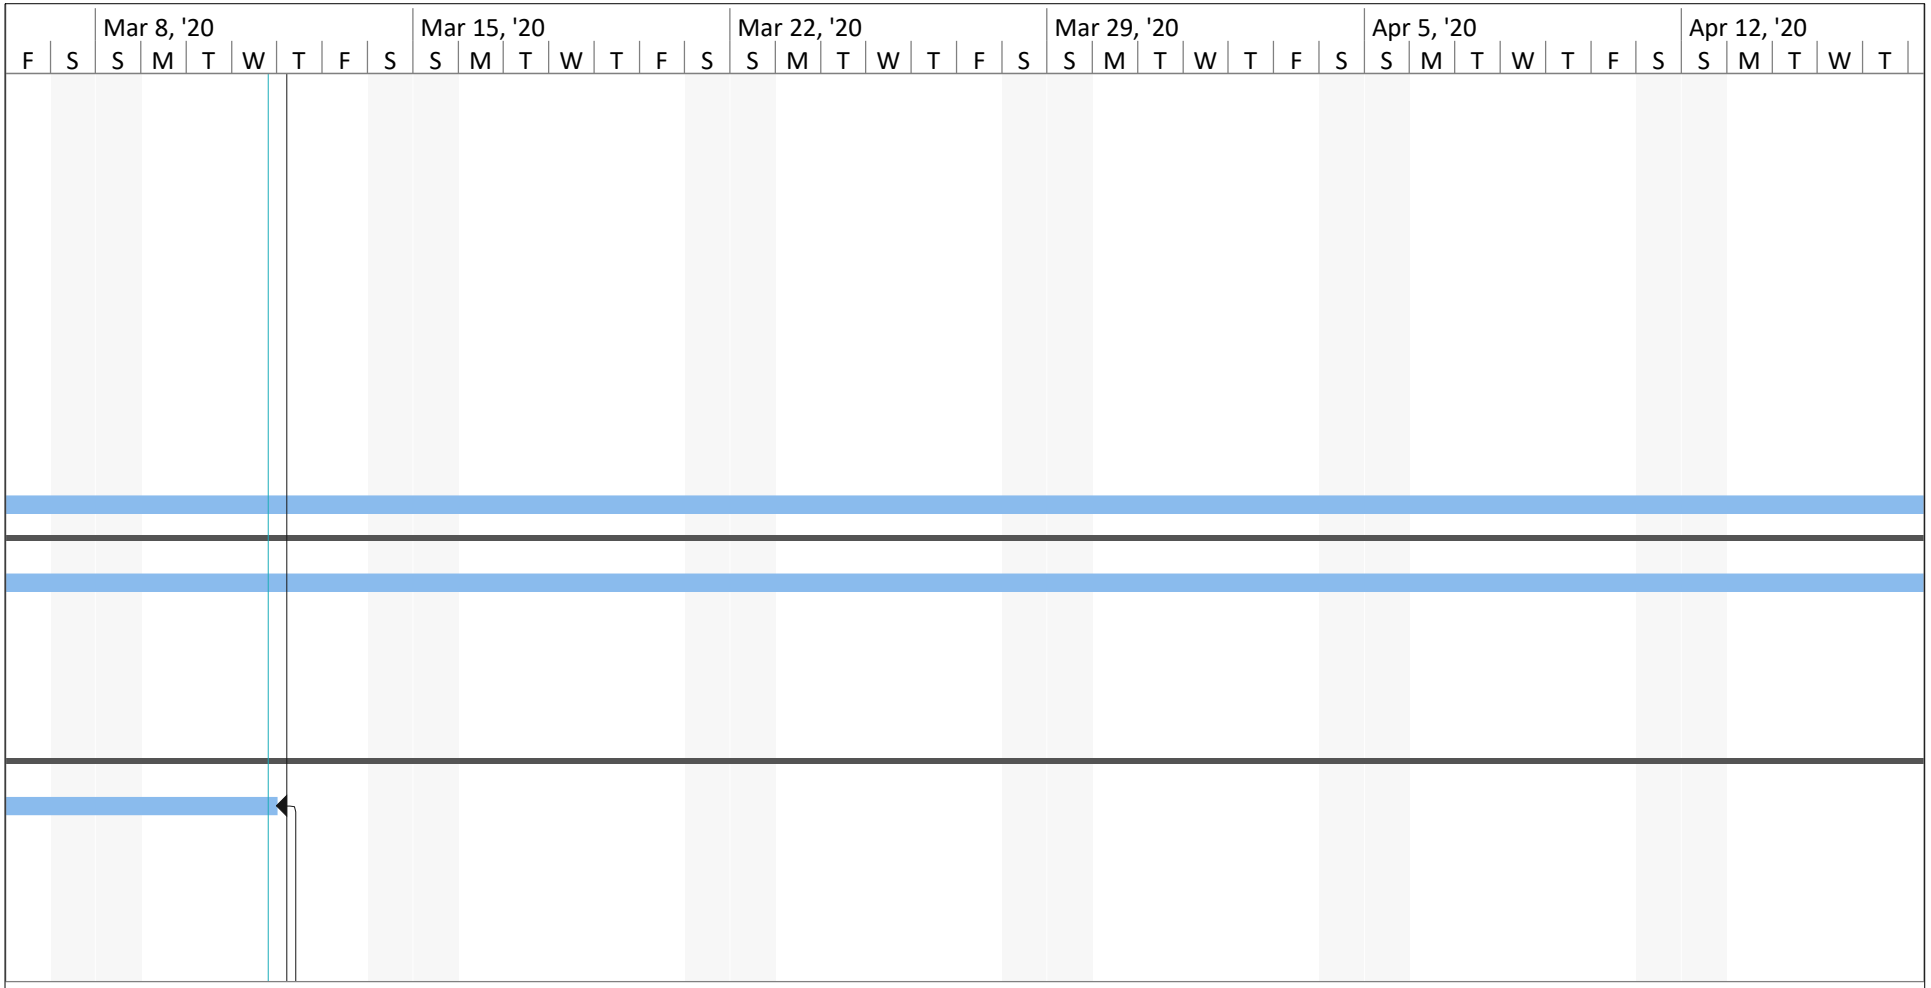


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

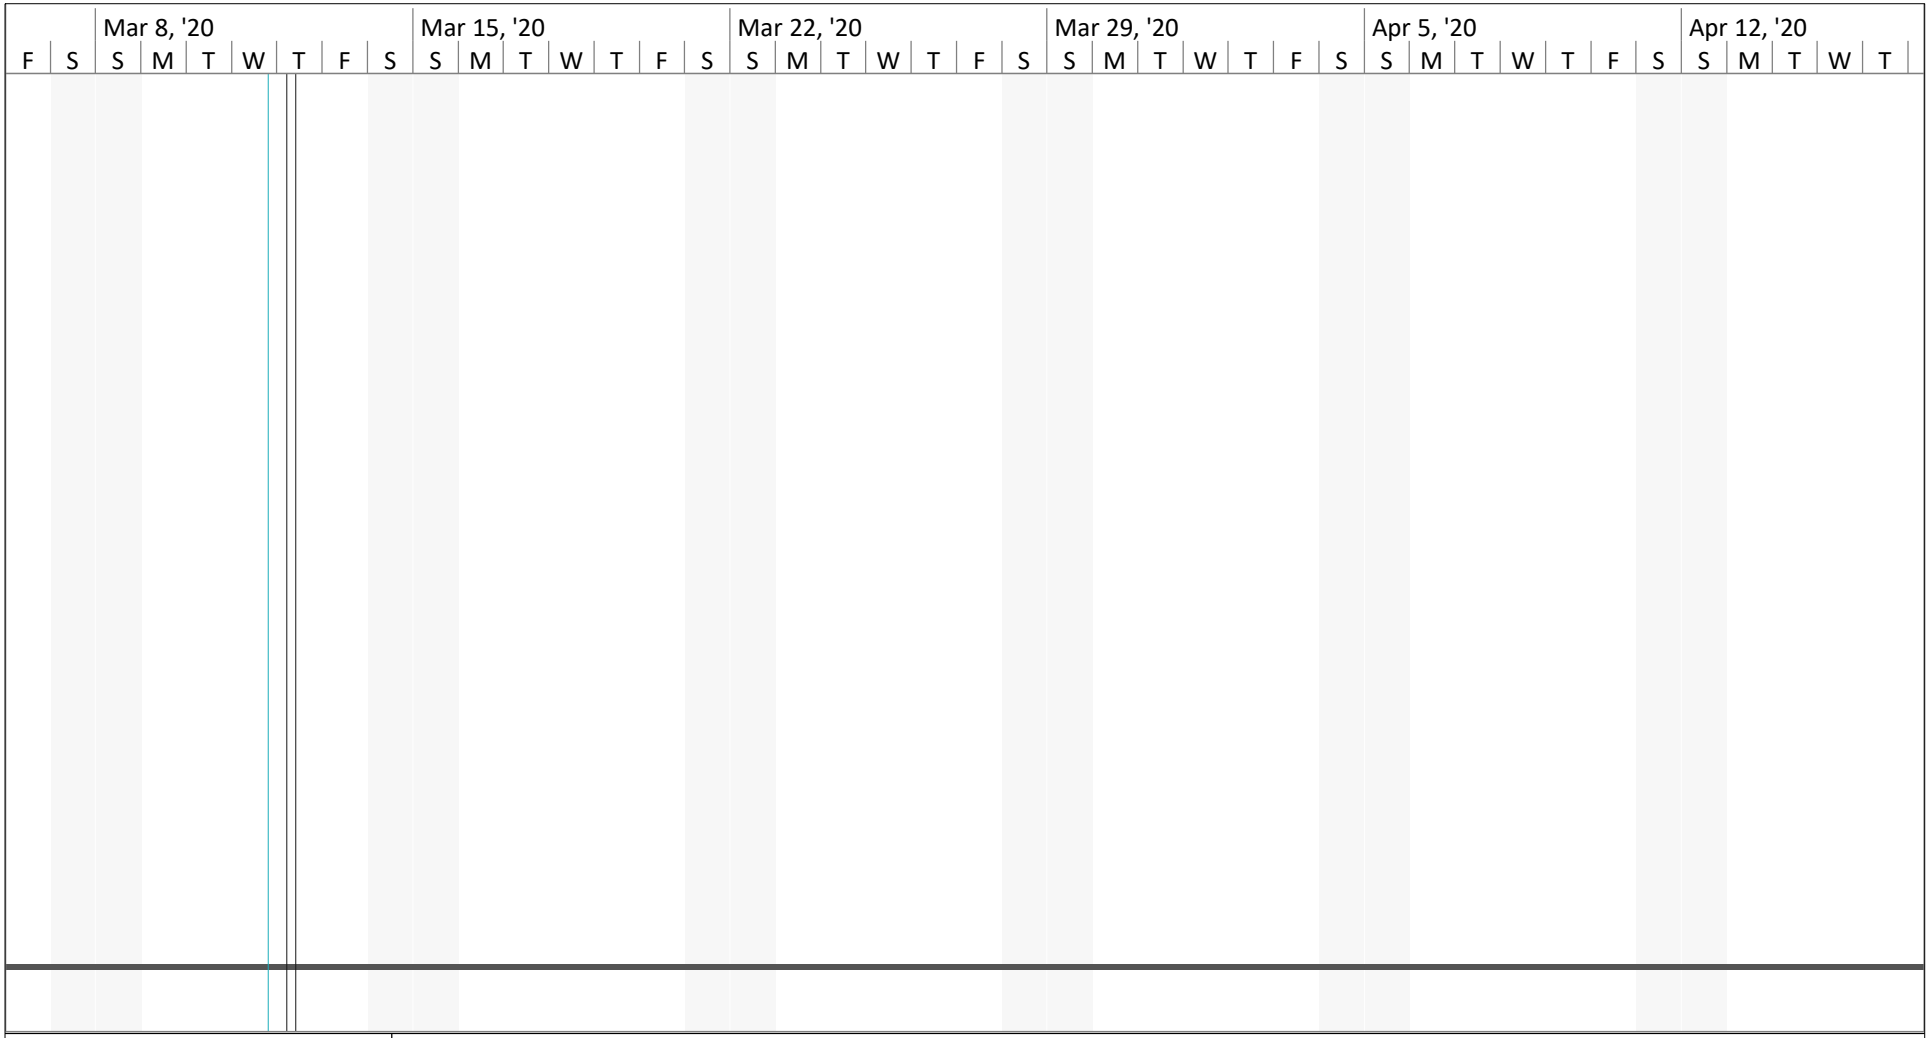


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

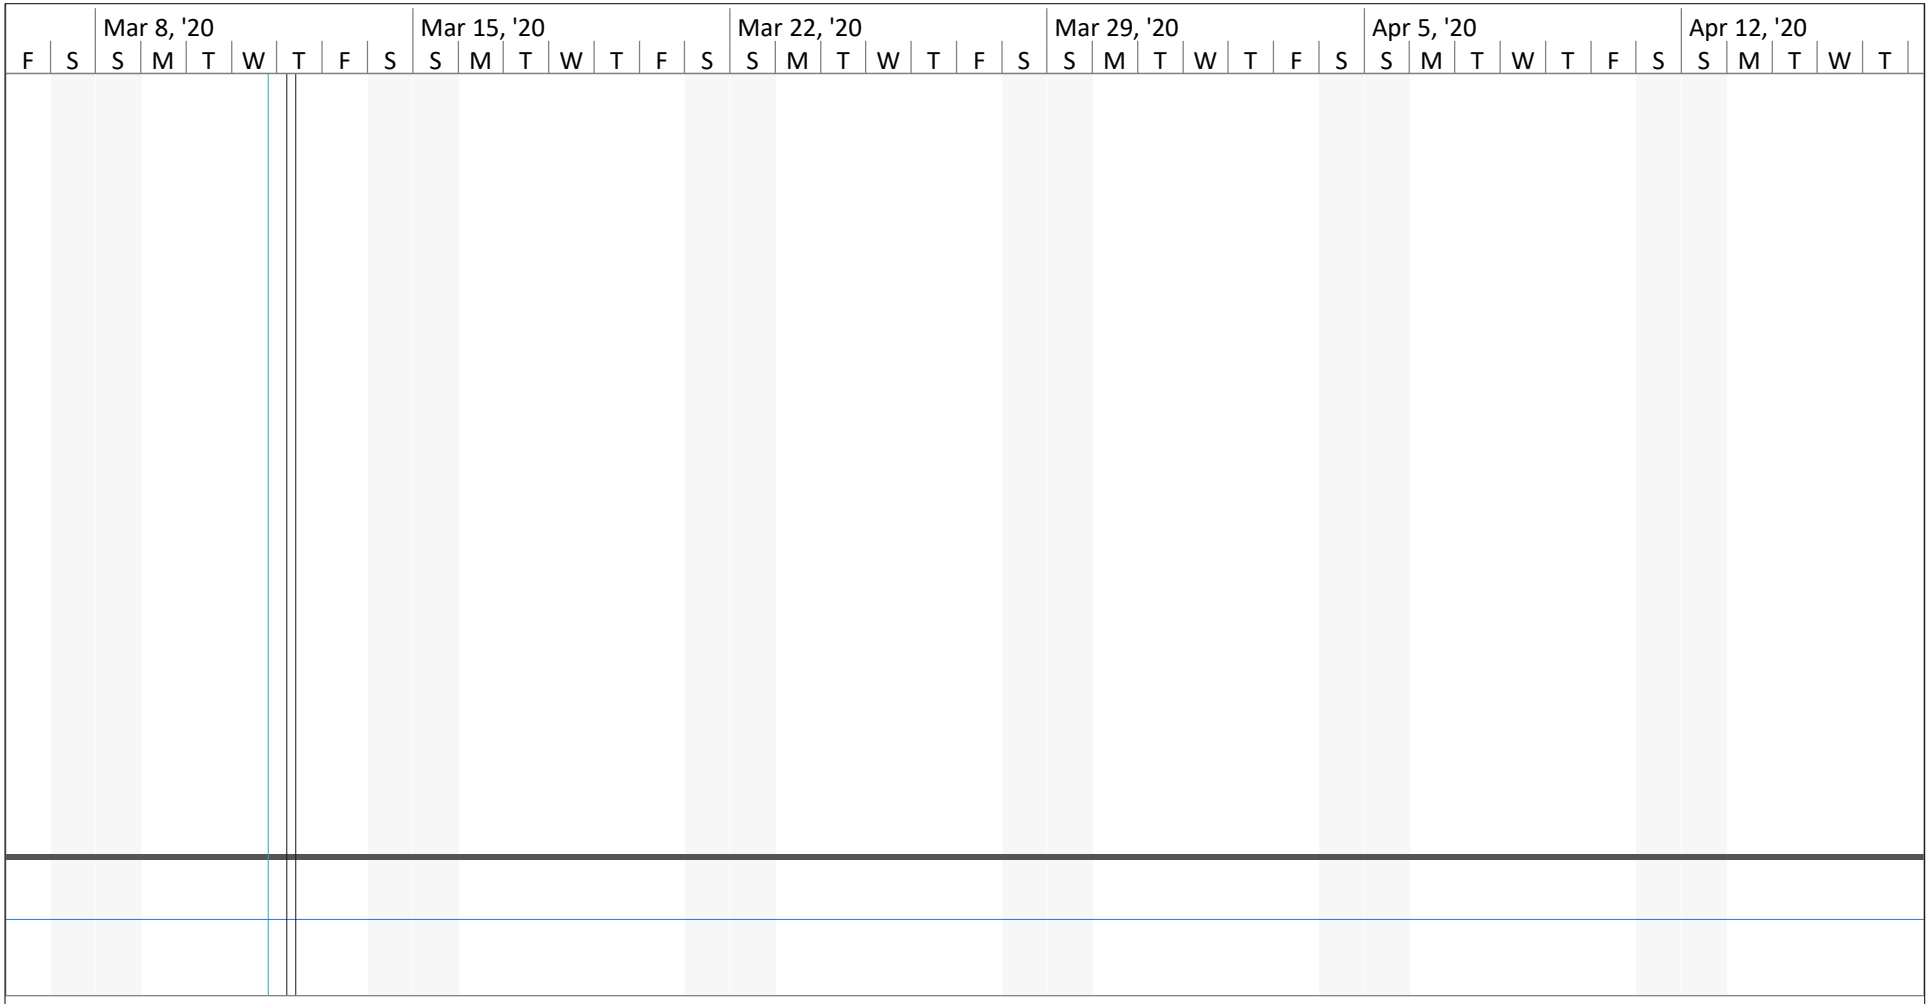


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

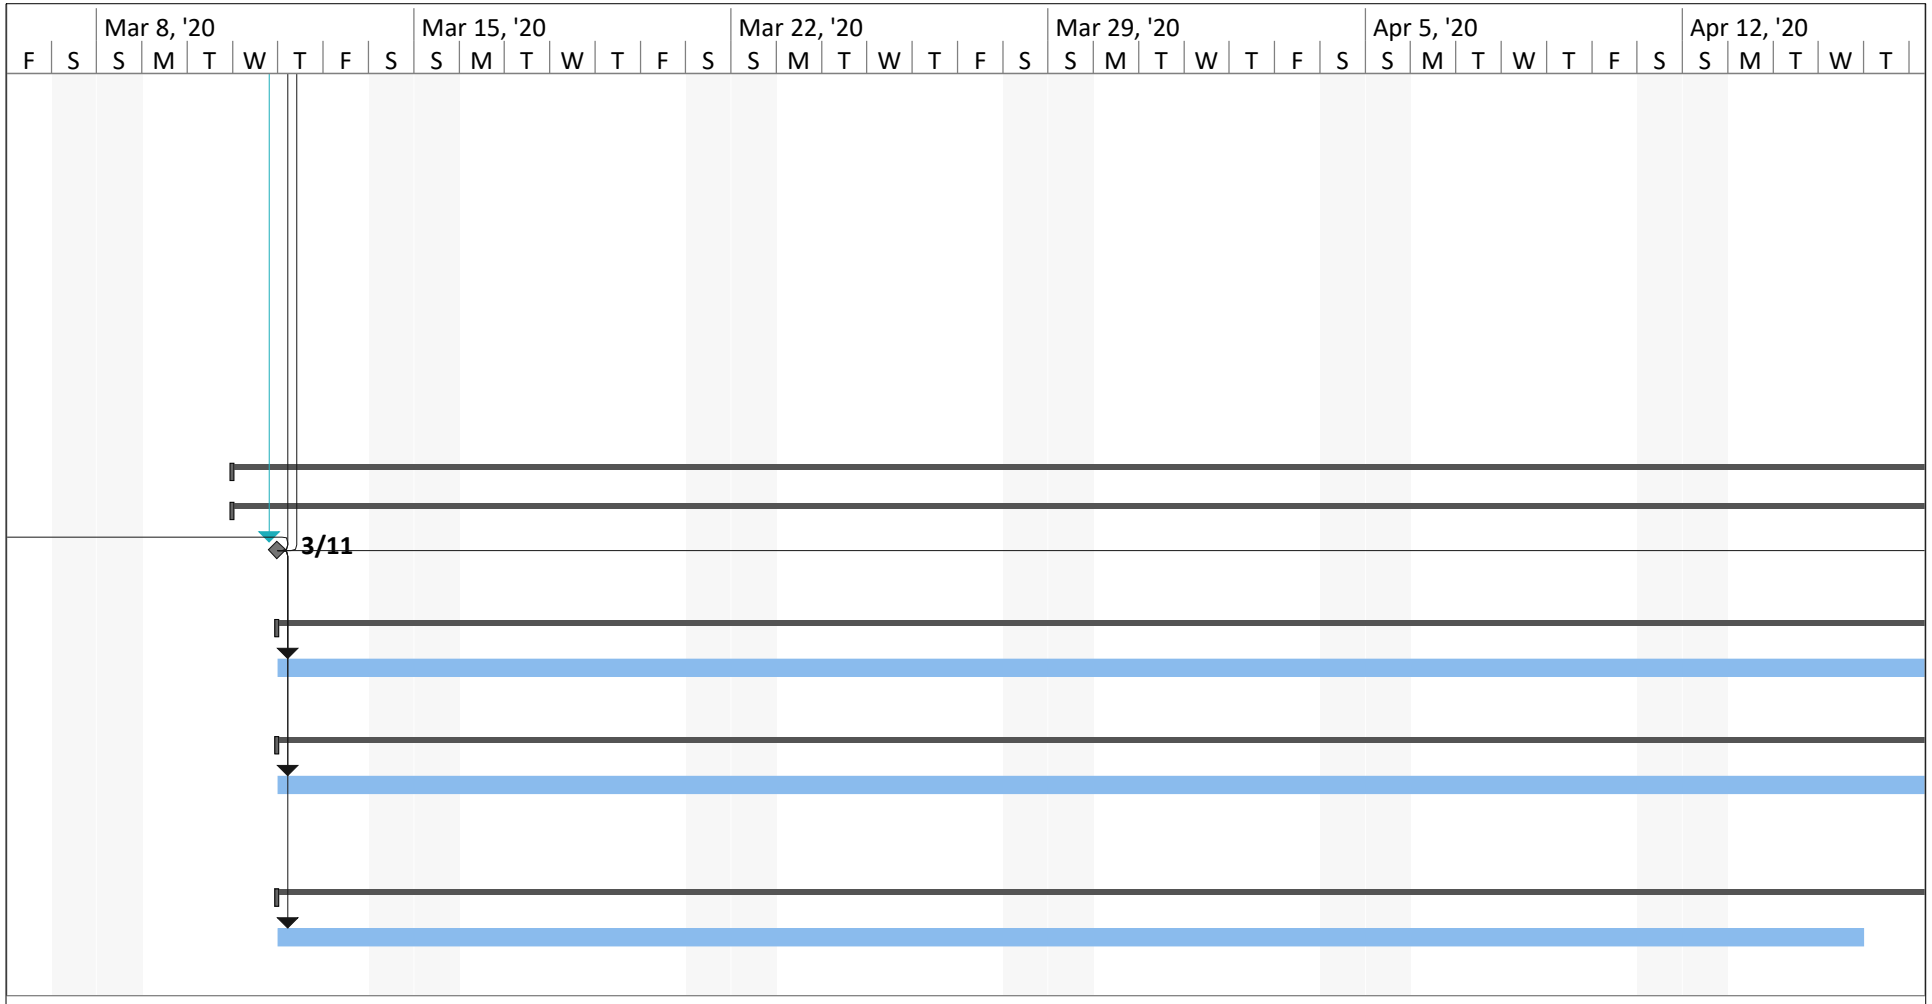


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

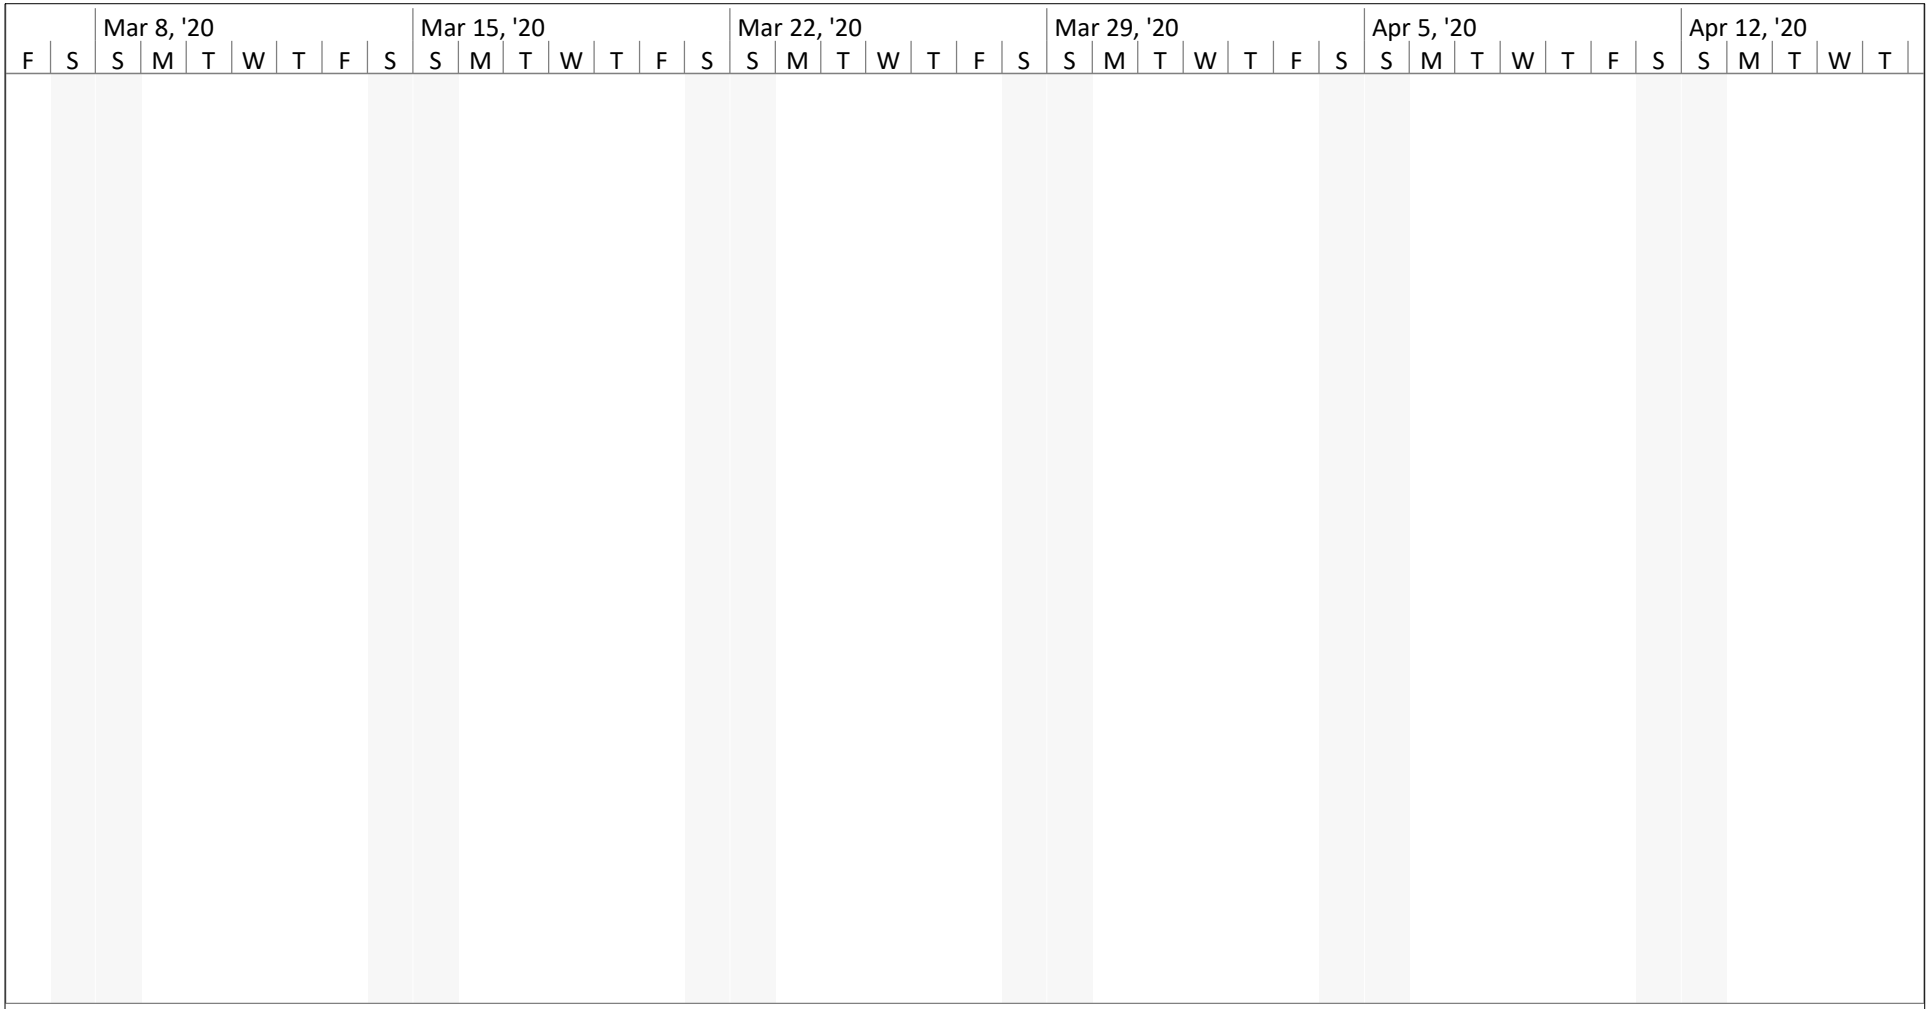


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

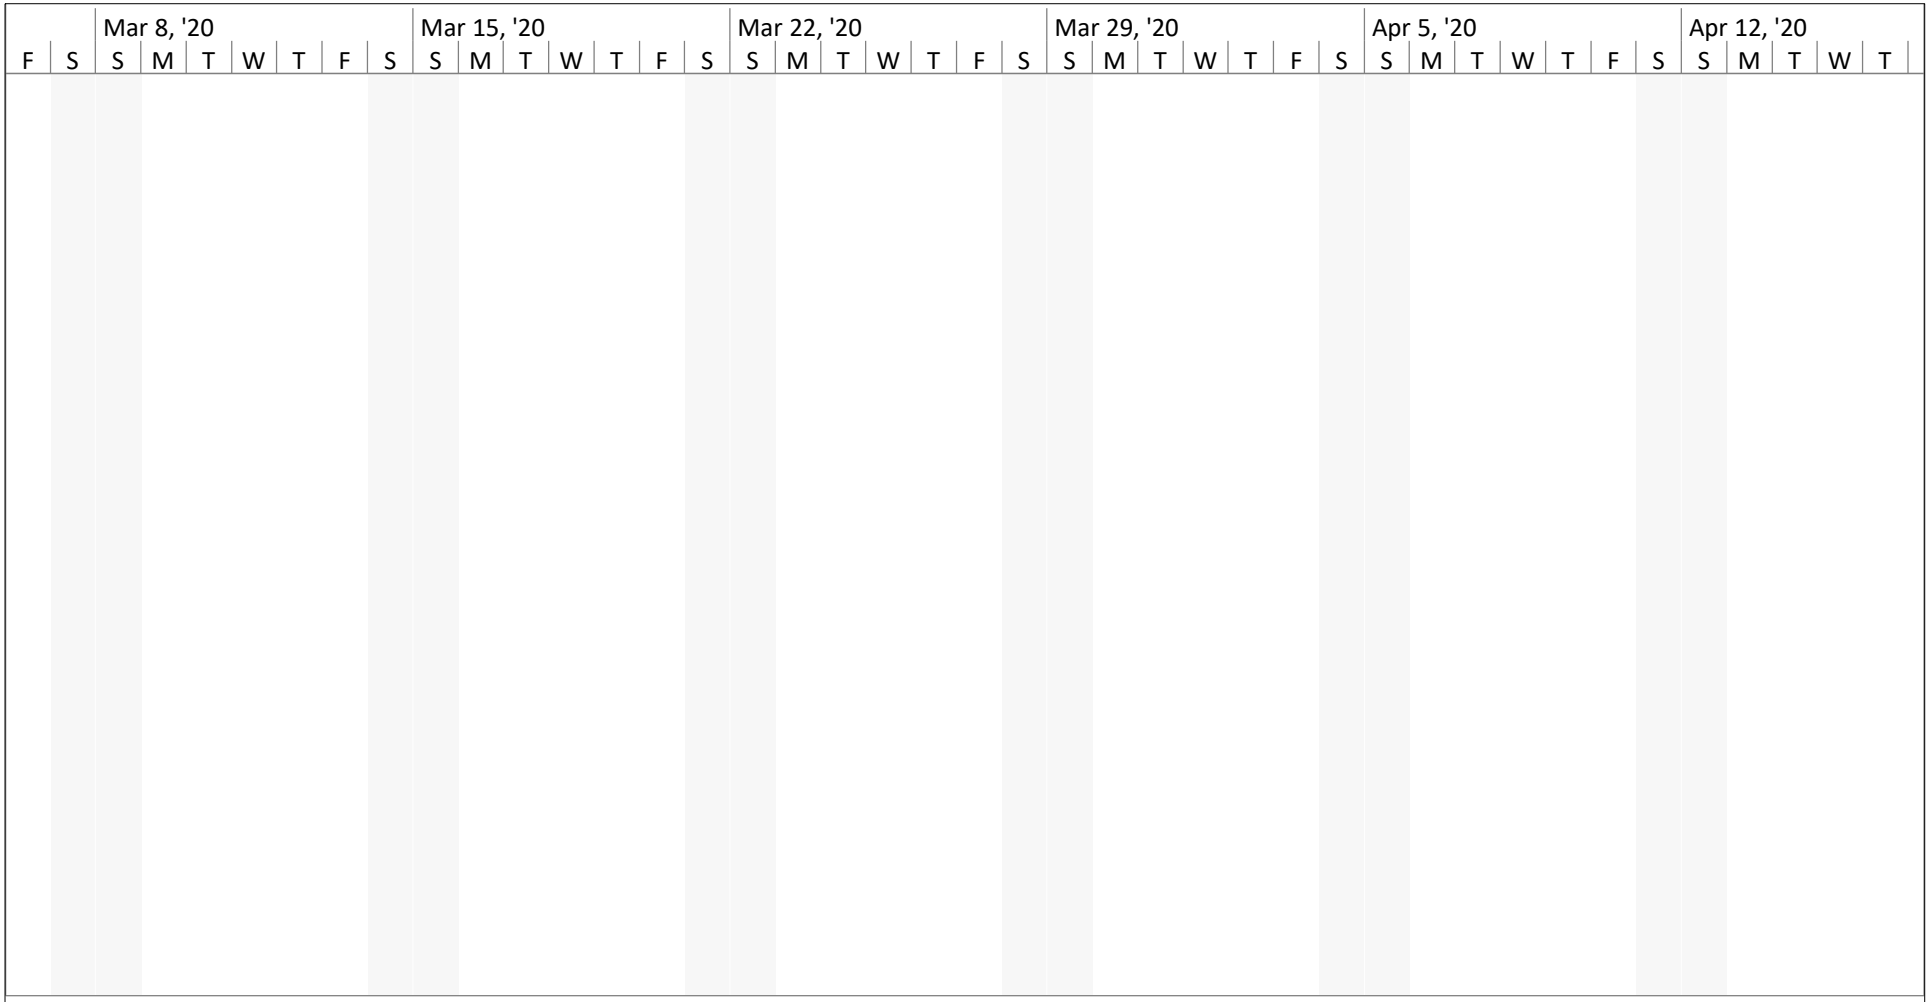


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |




Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

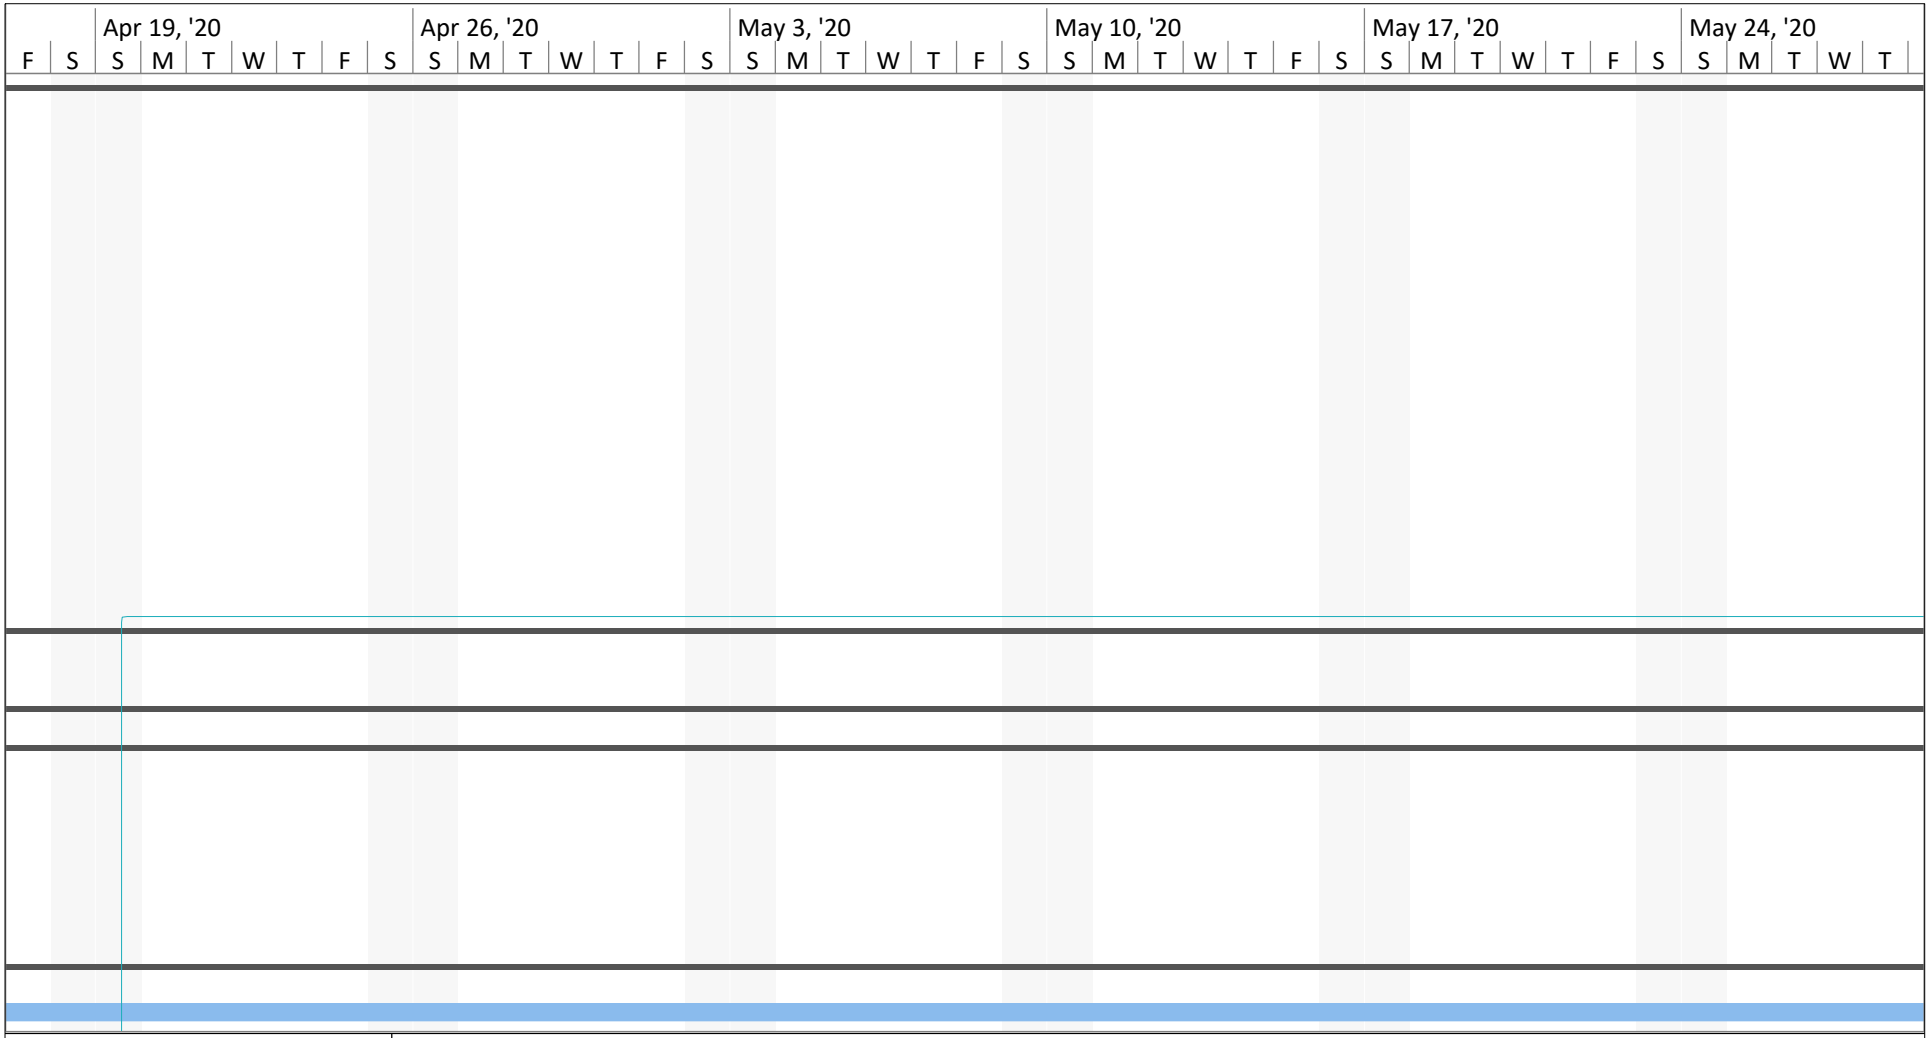


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

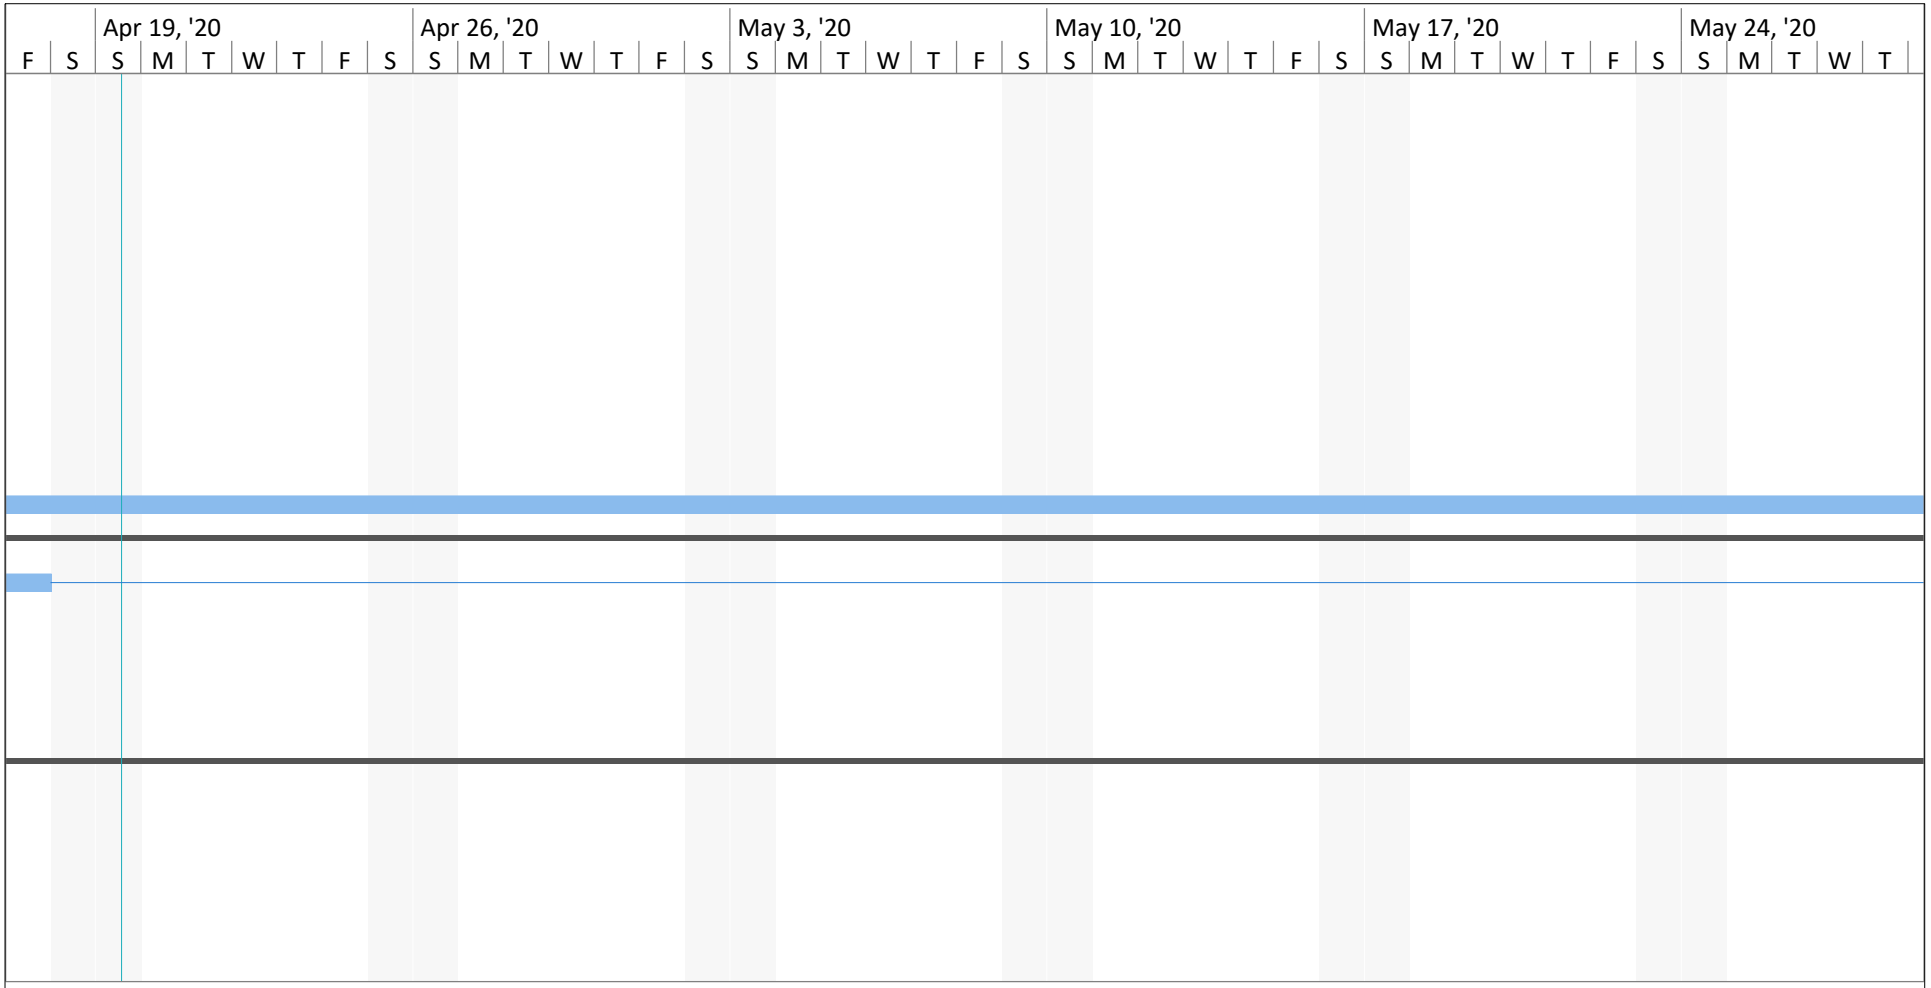


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

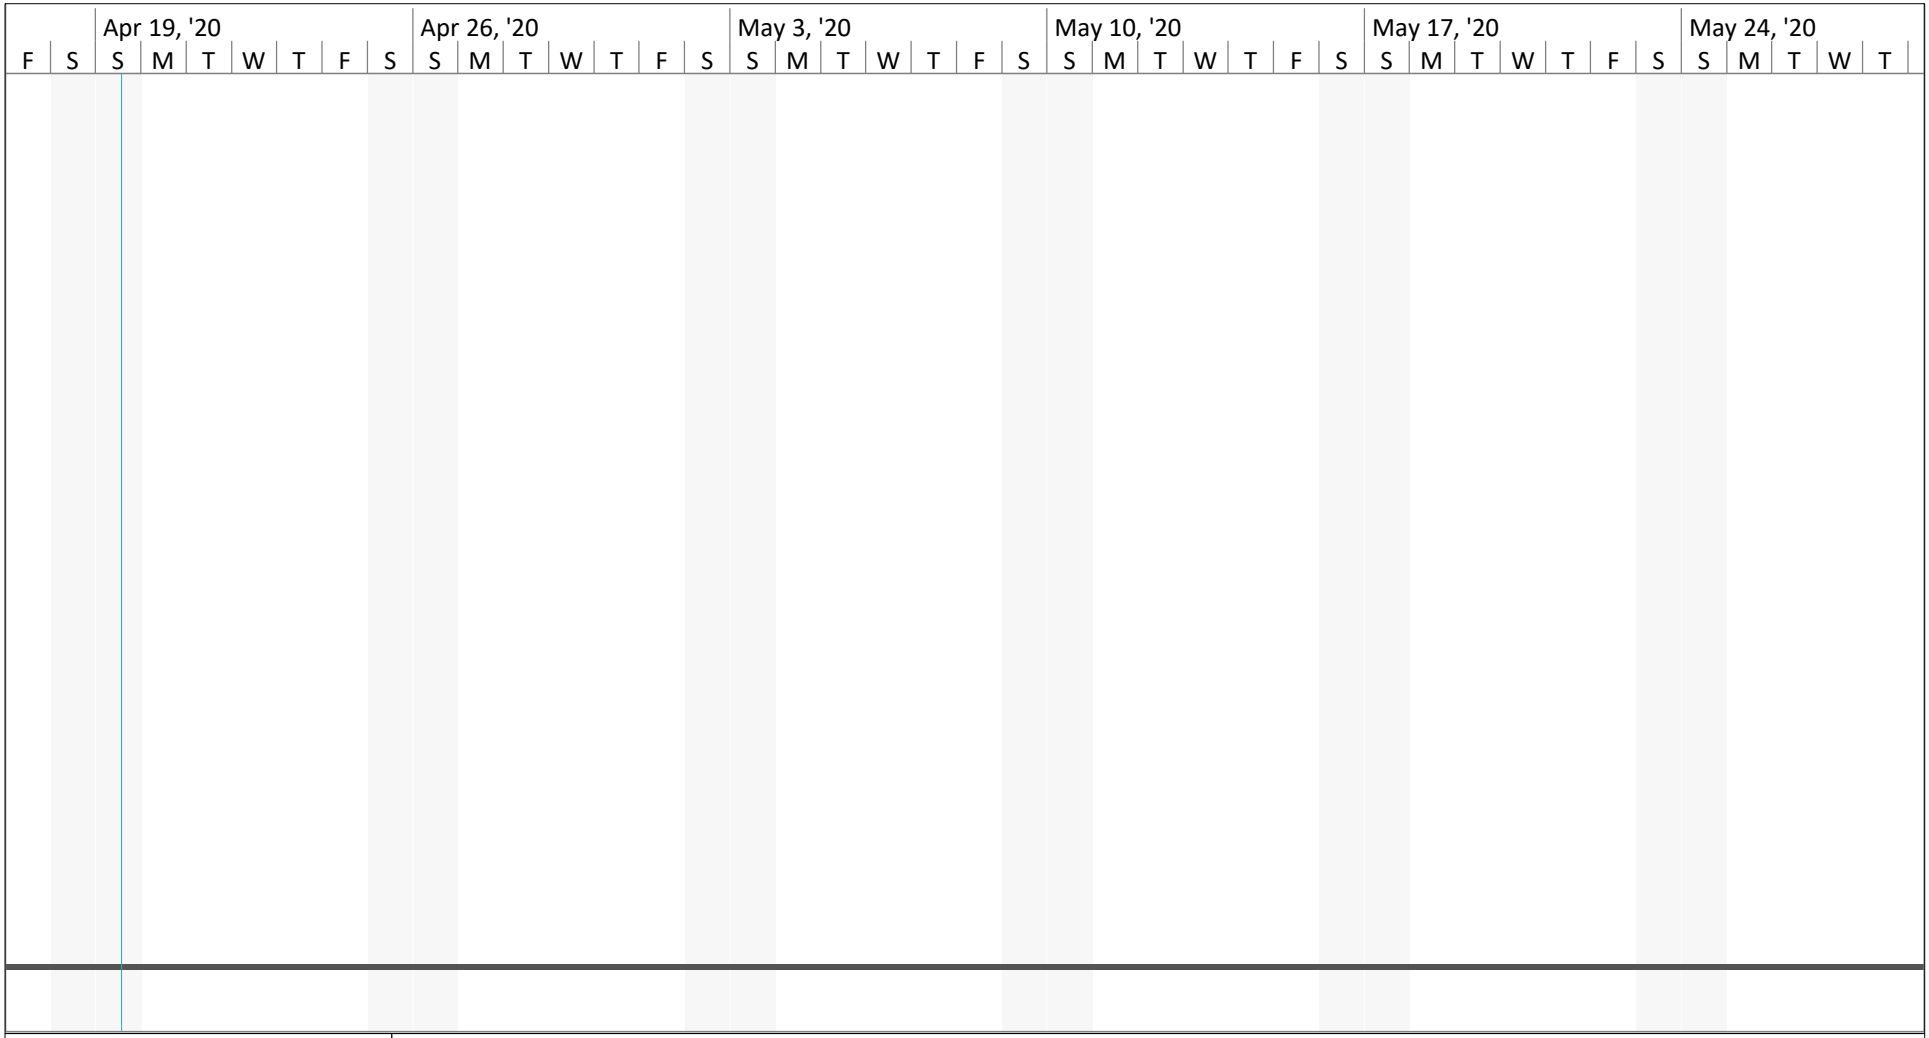


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

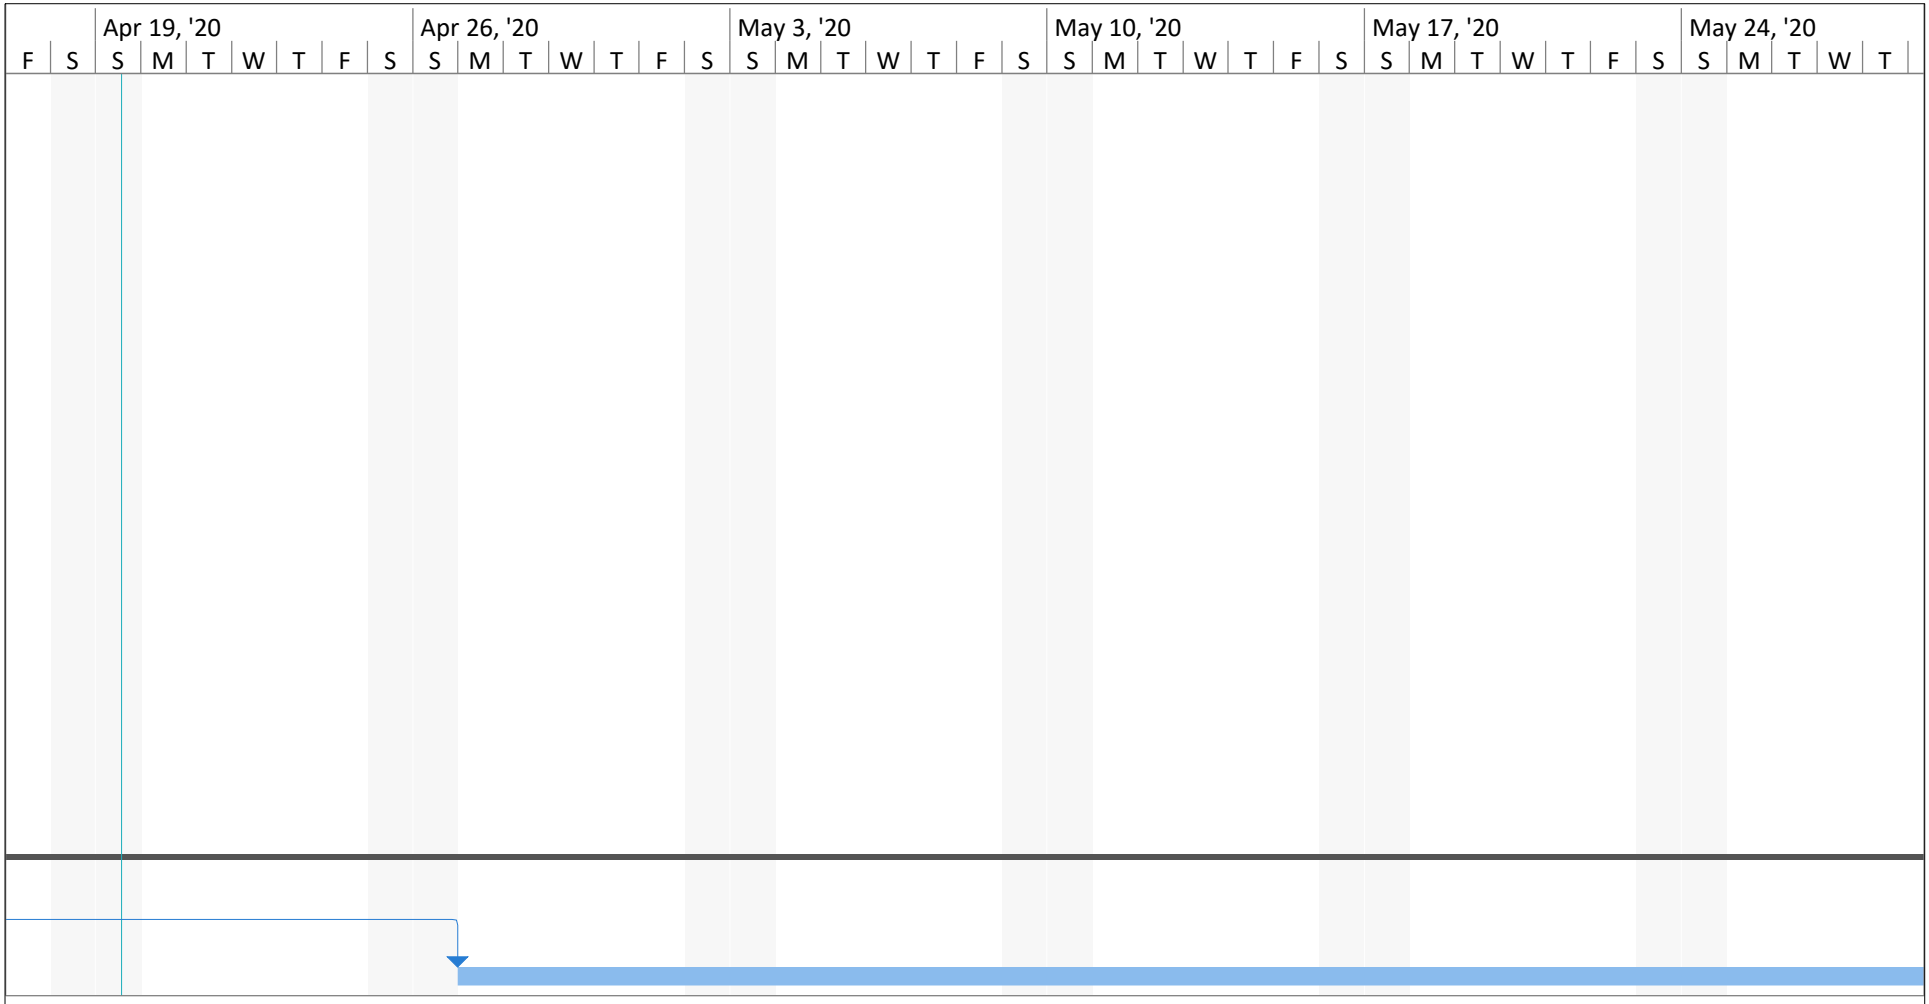


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

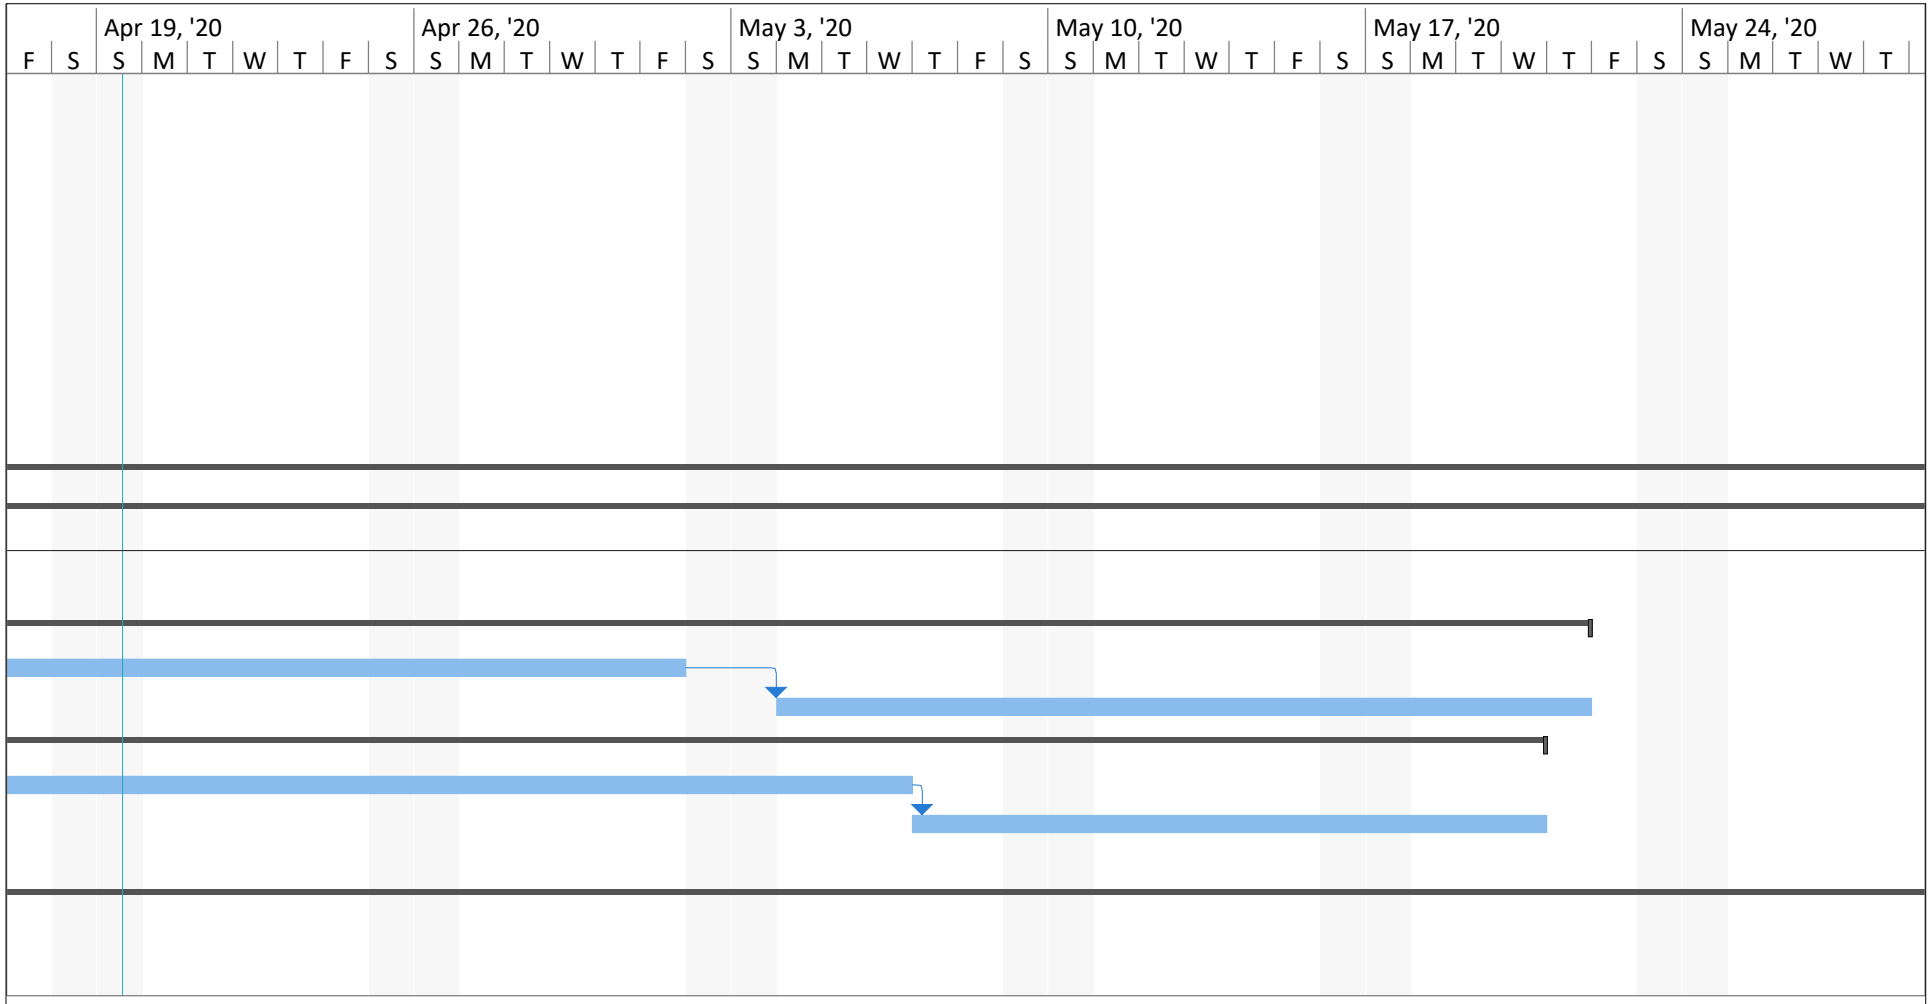


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

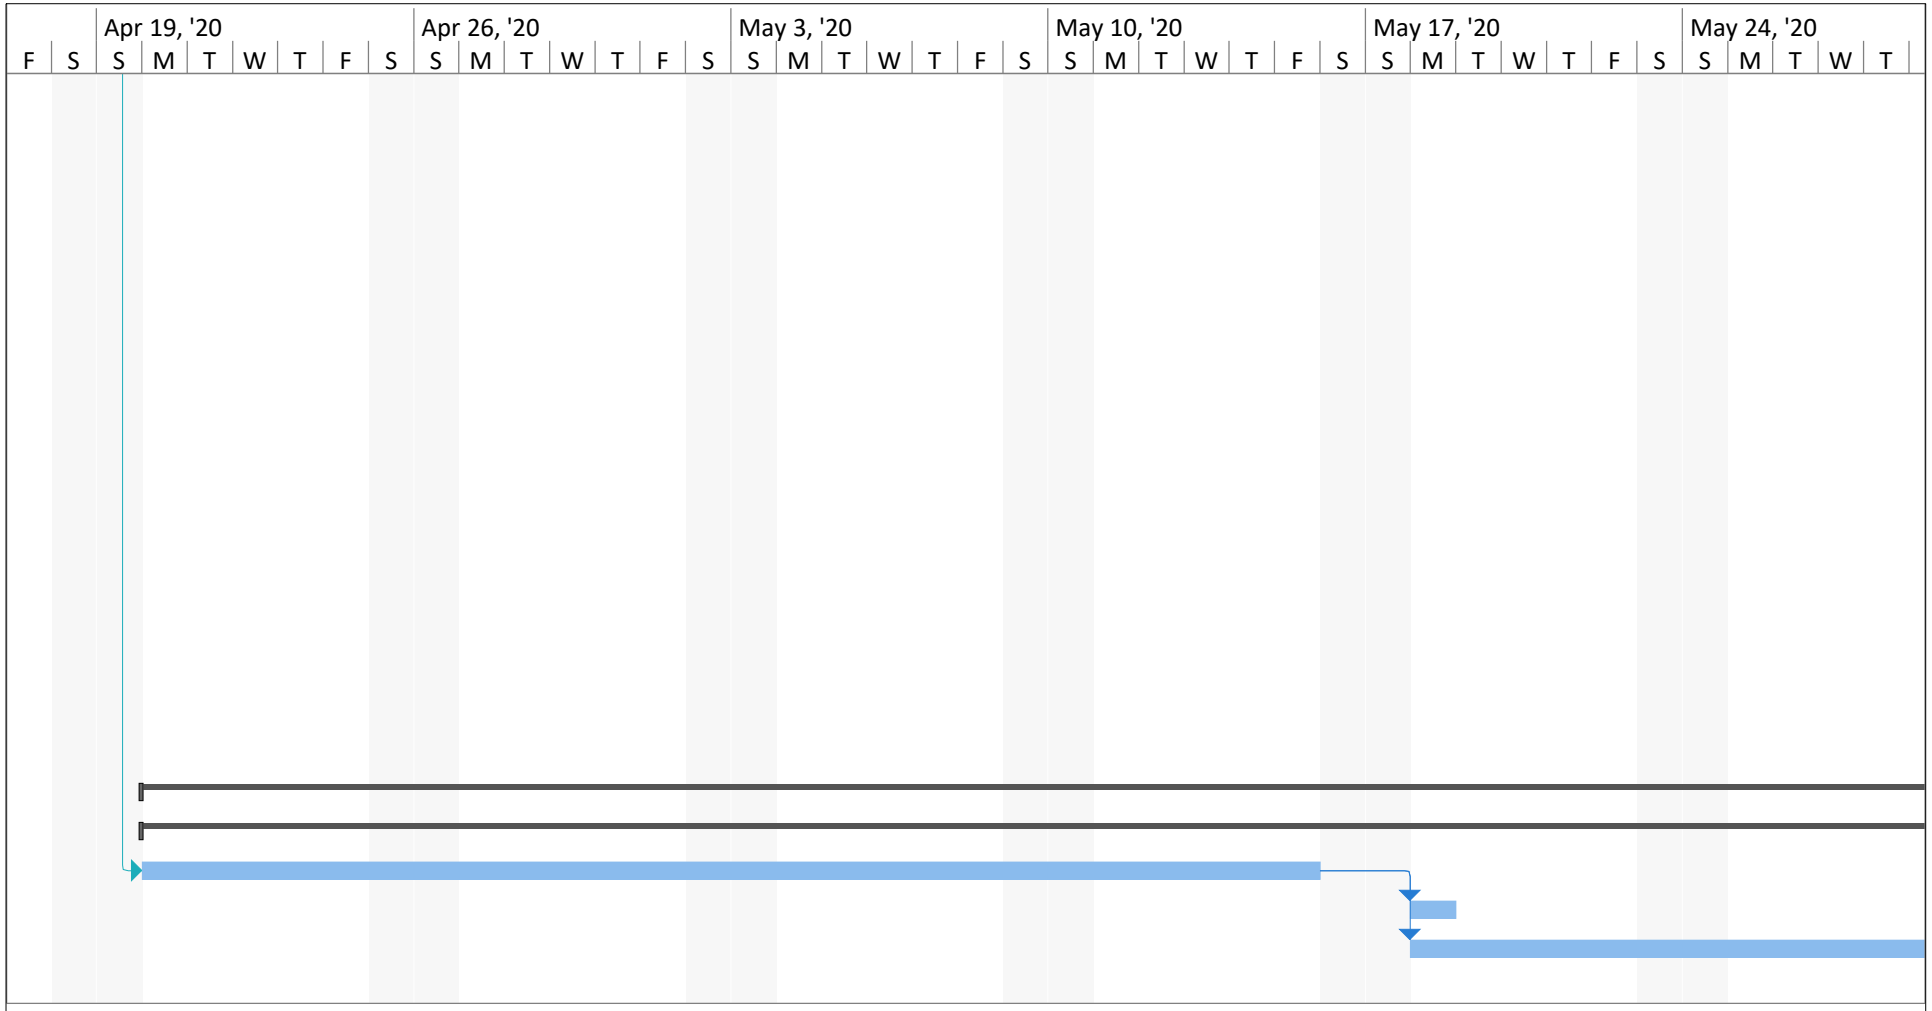


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

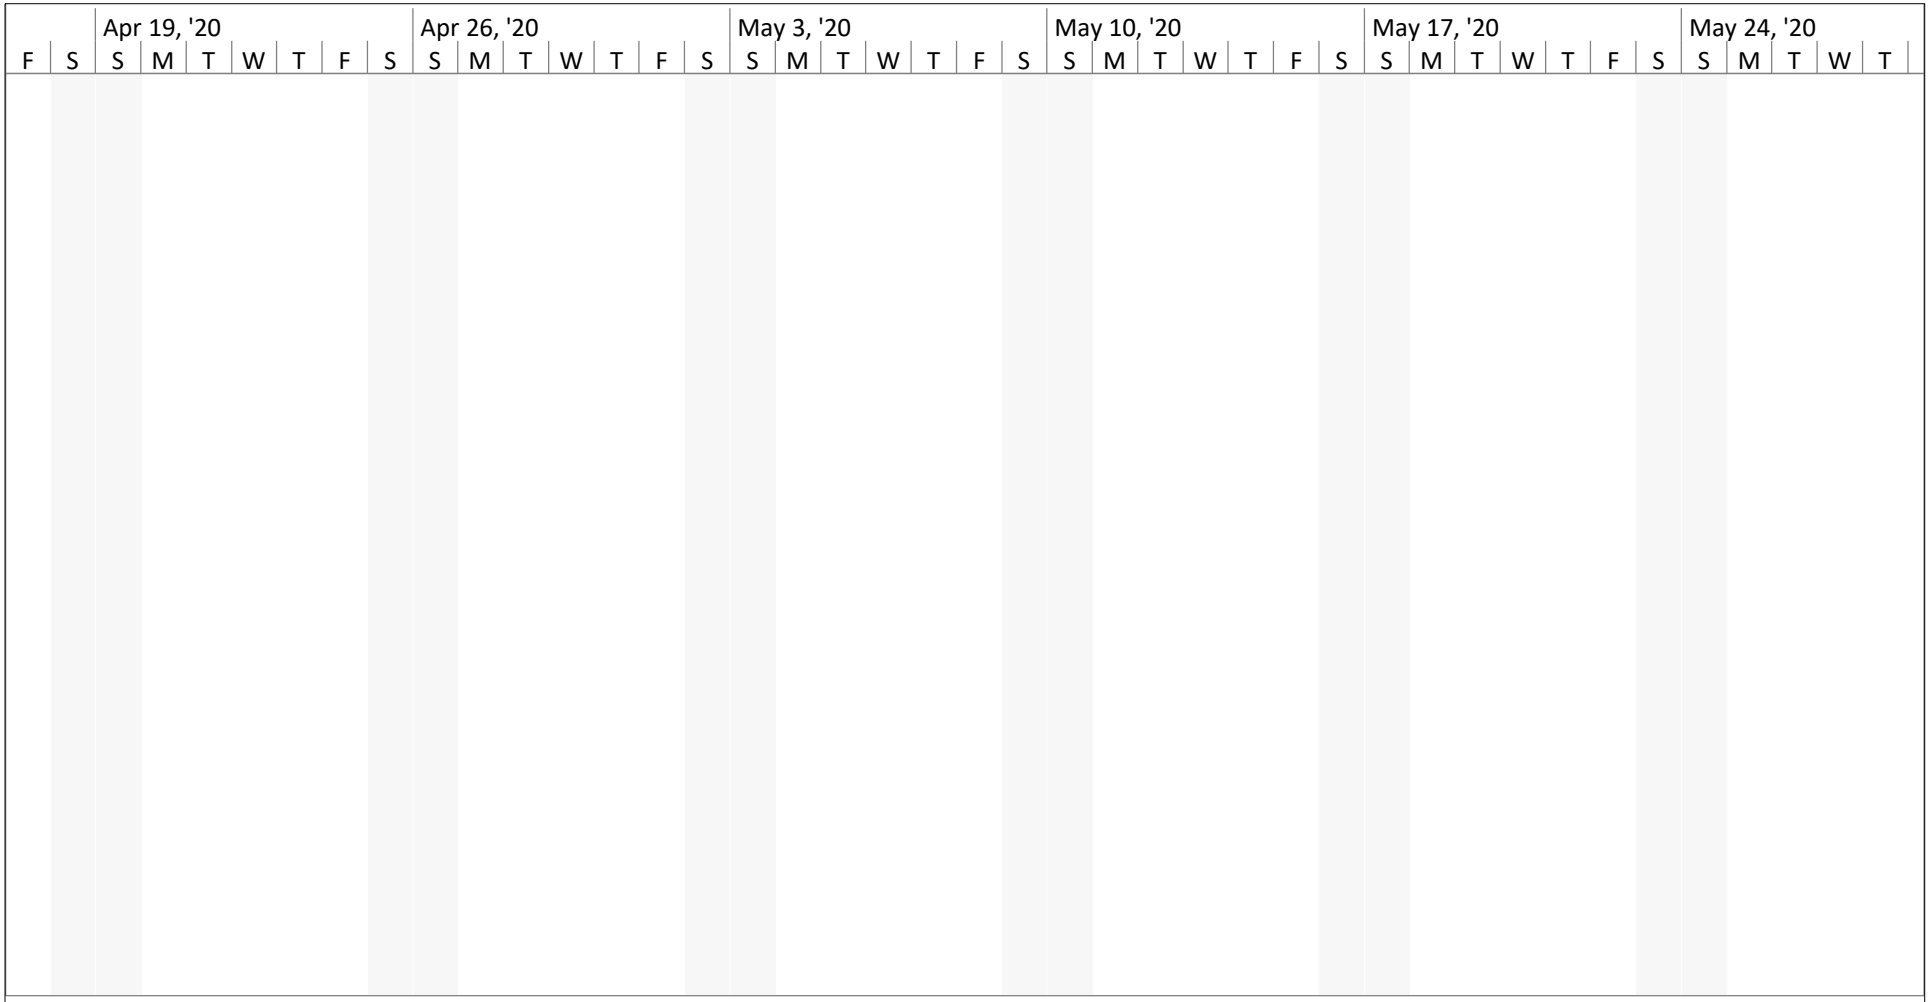


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |




Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

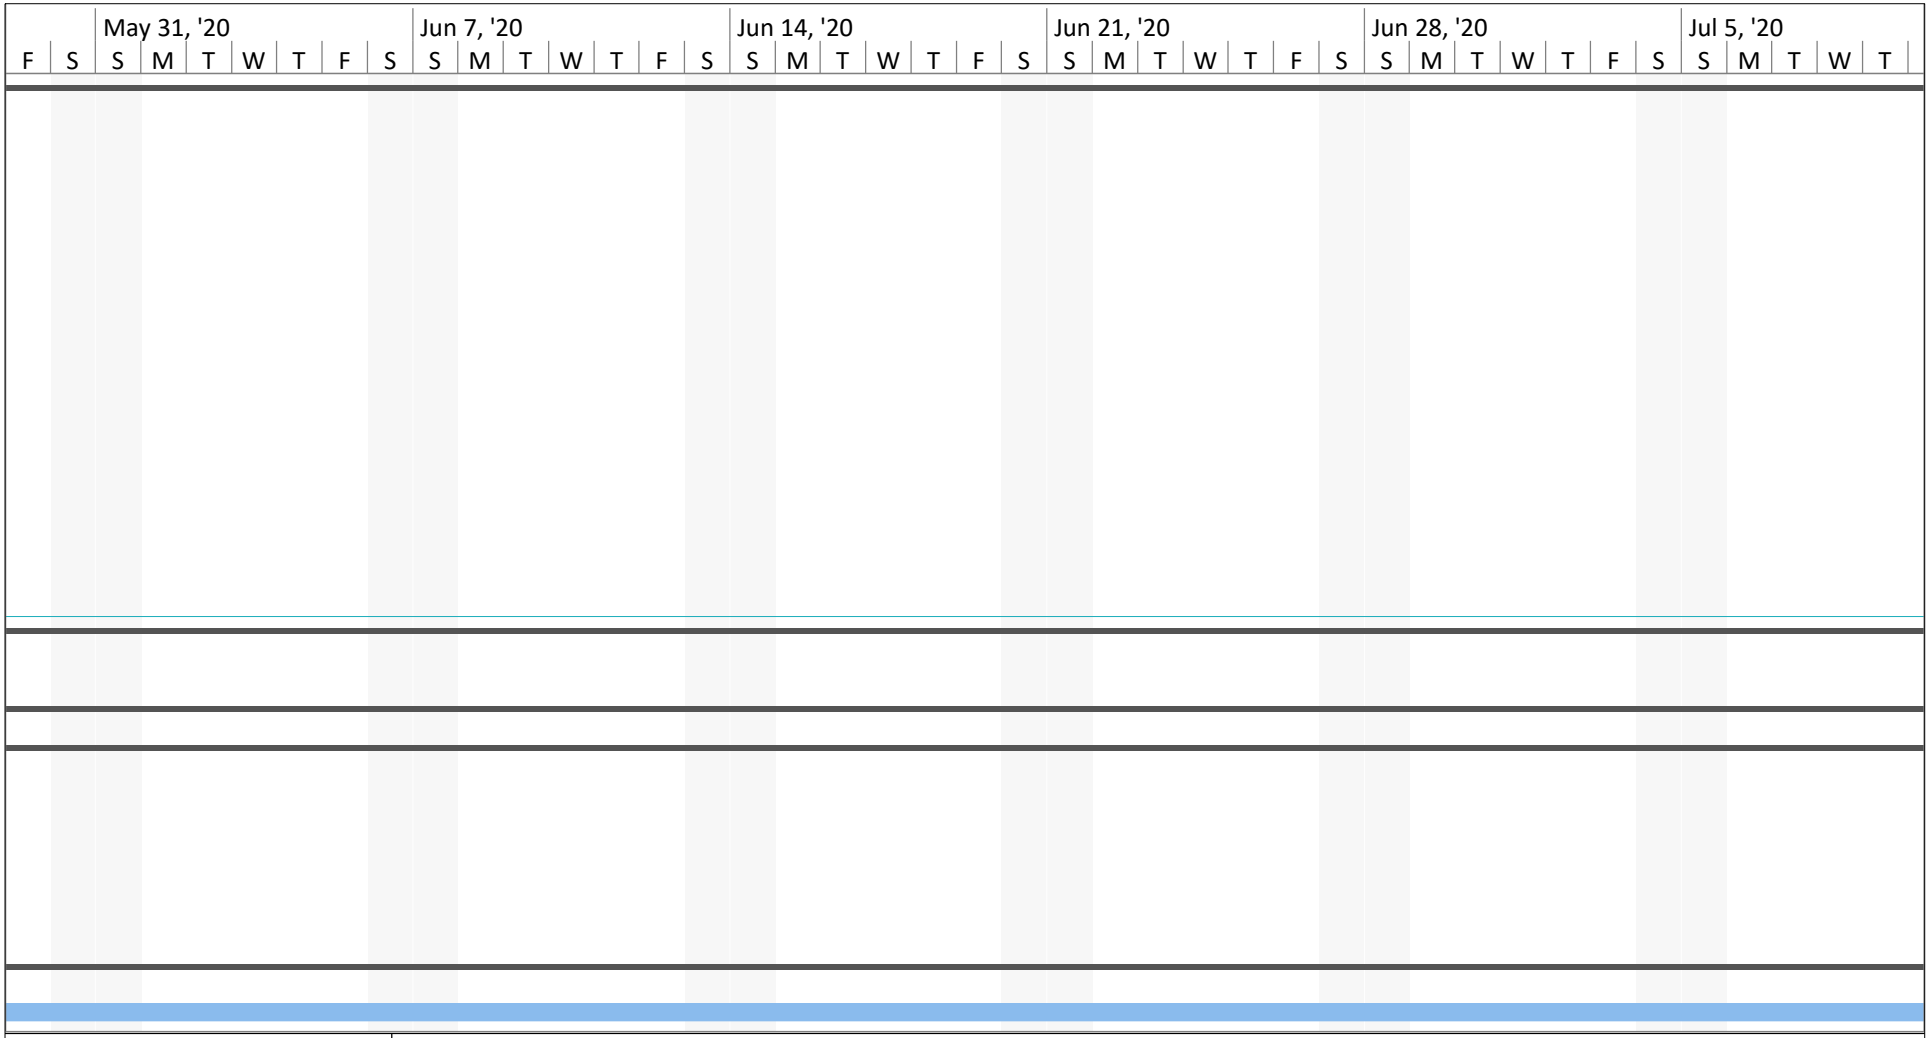


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

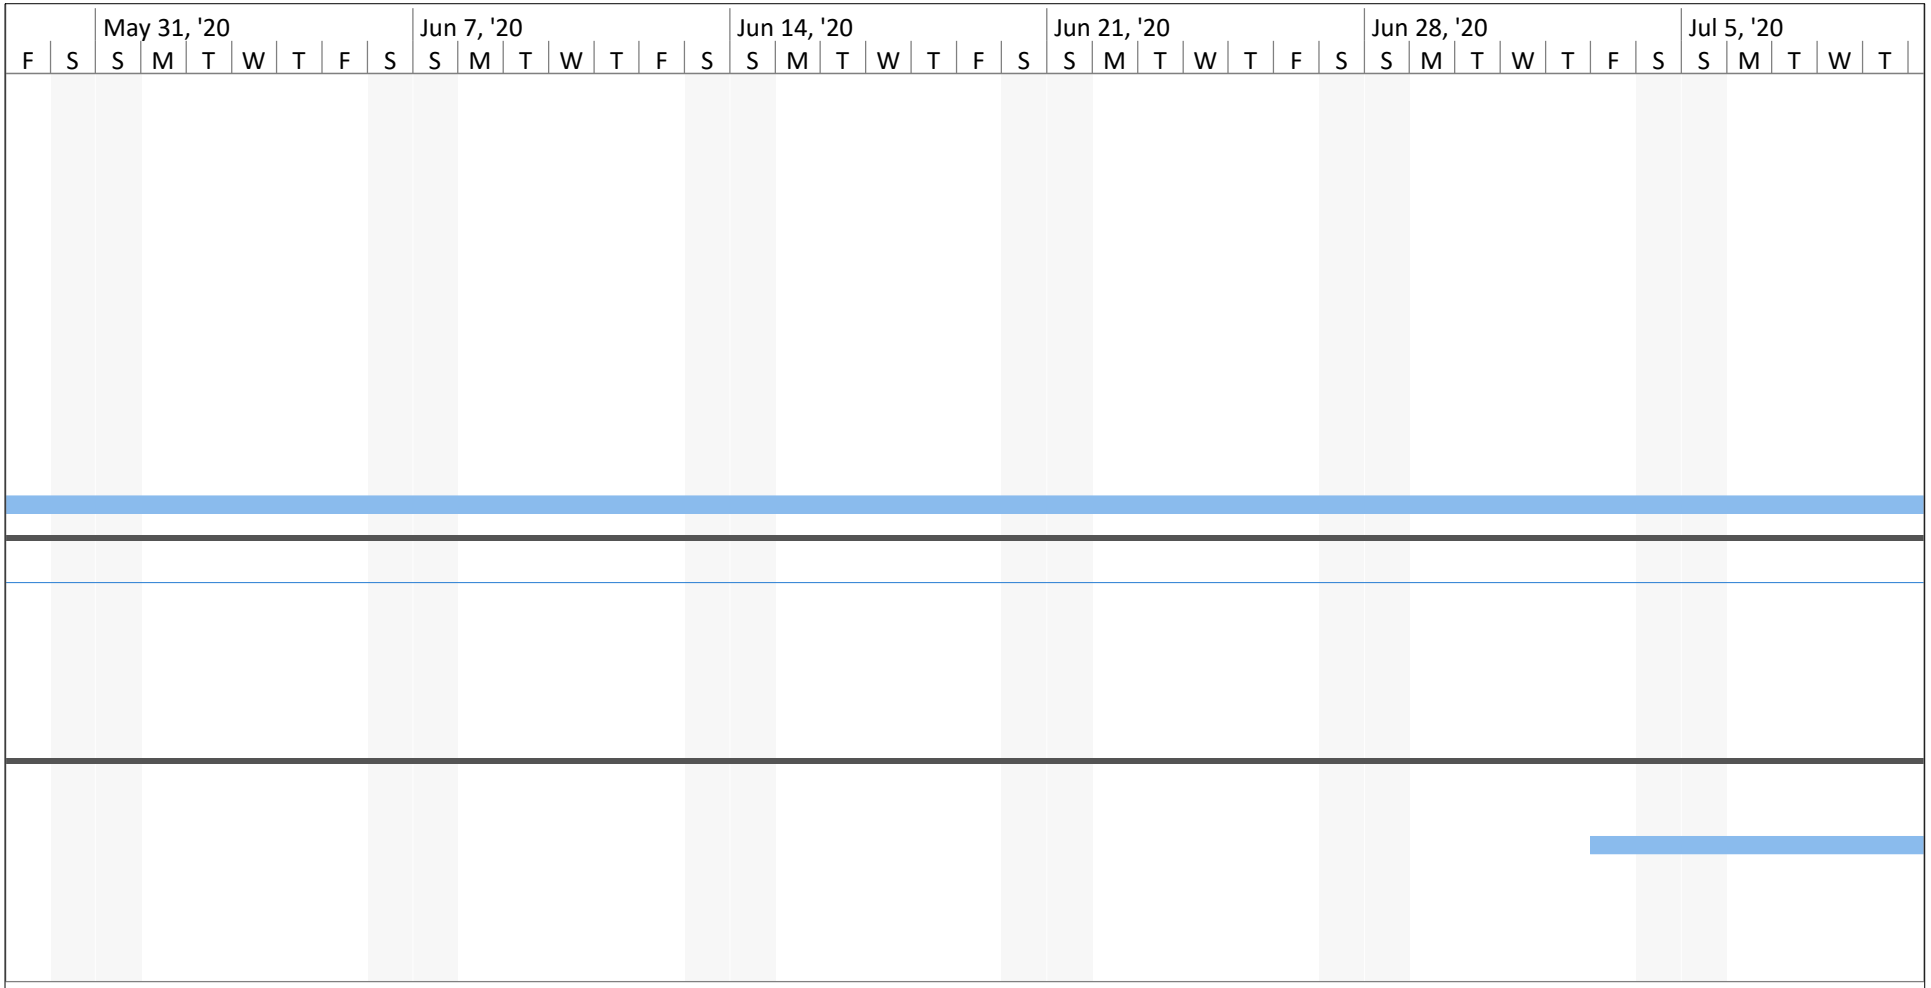


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

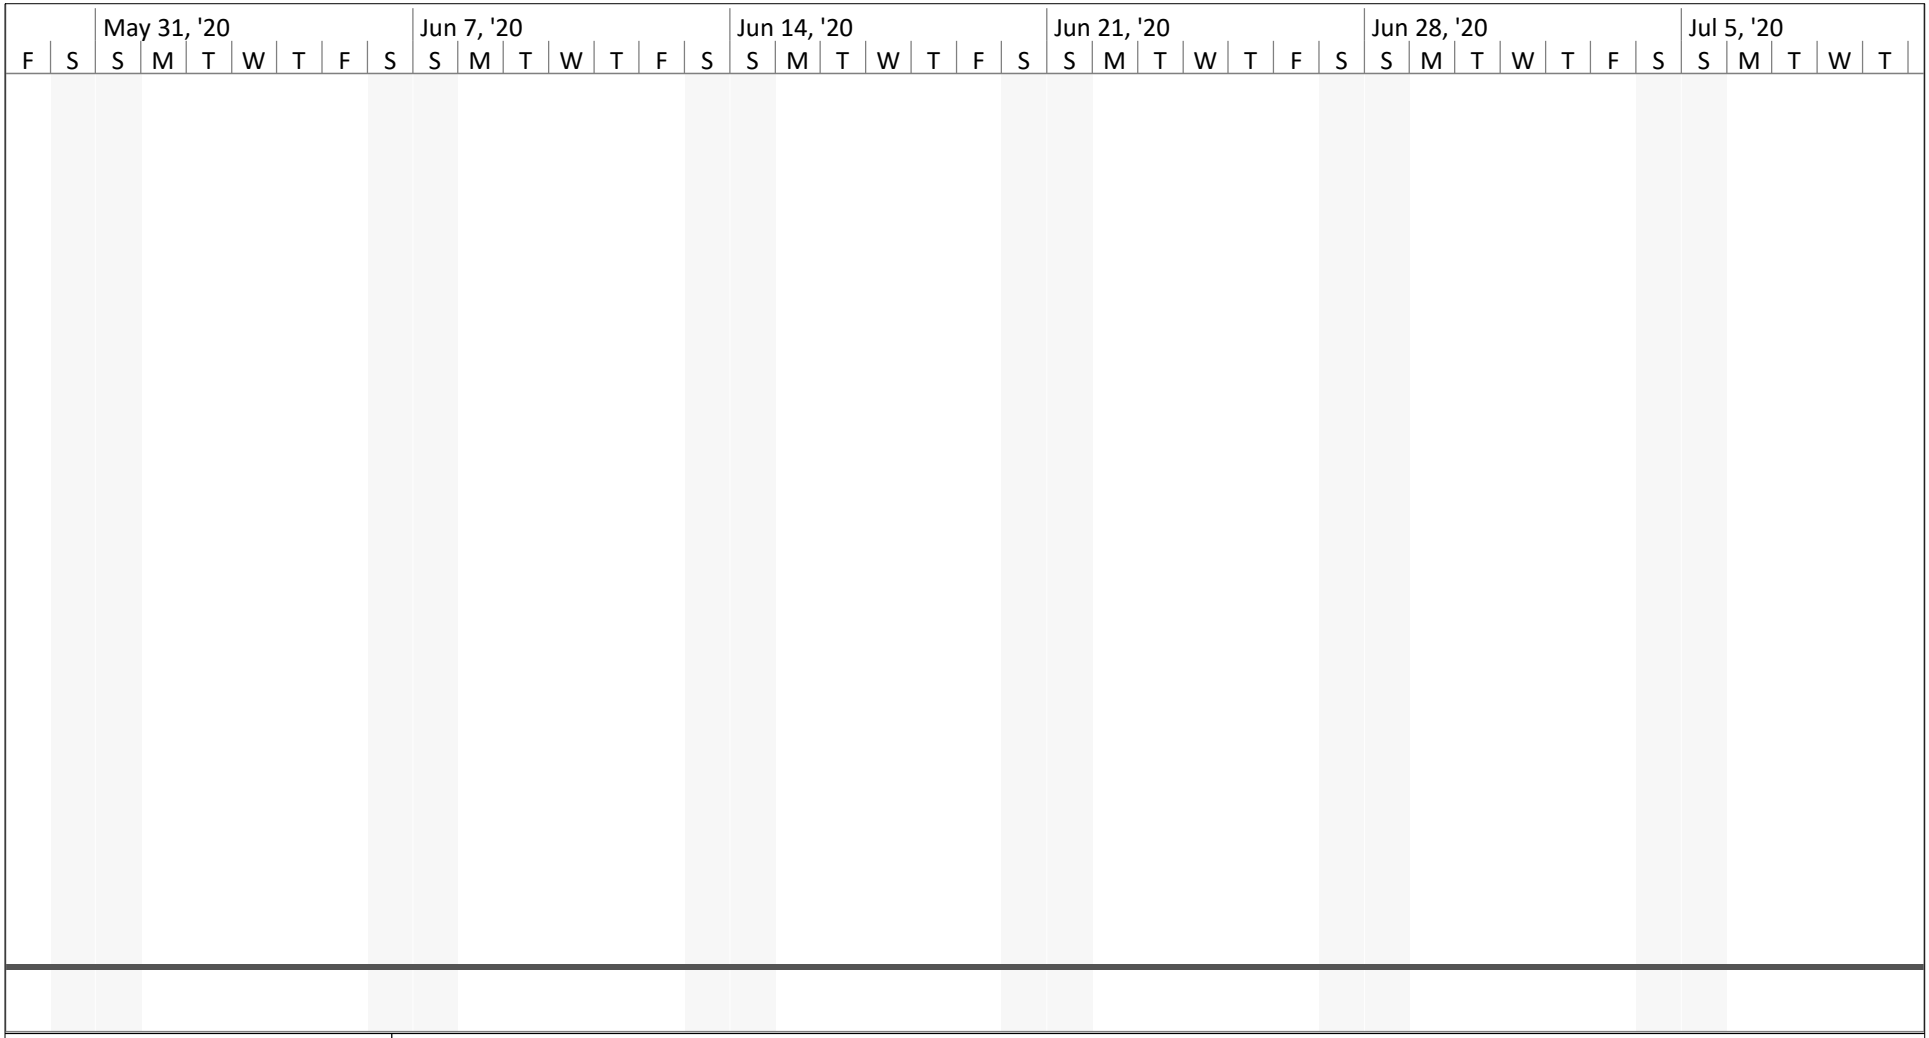


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

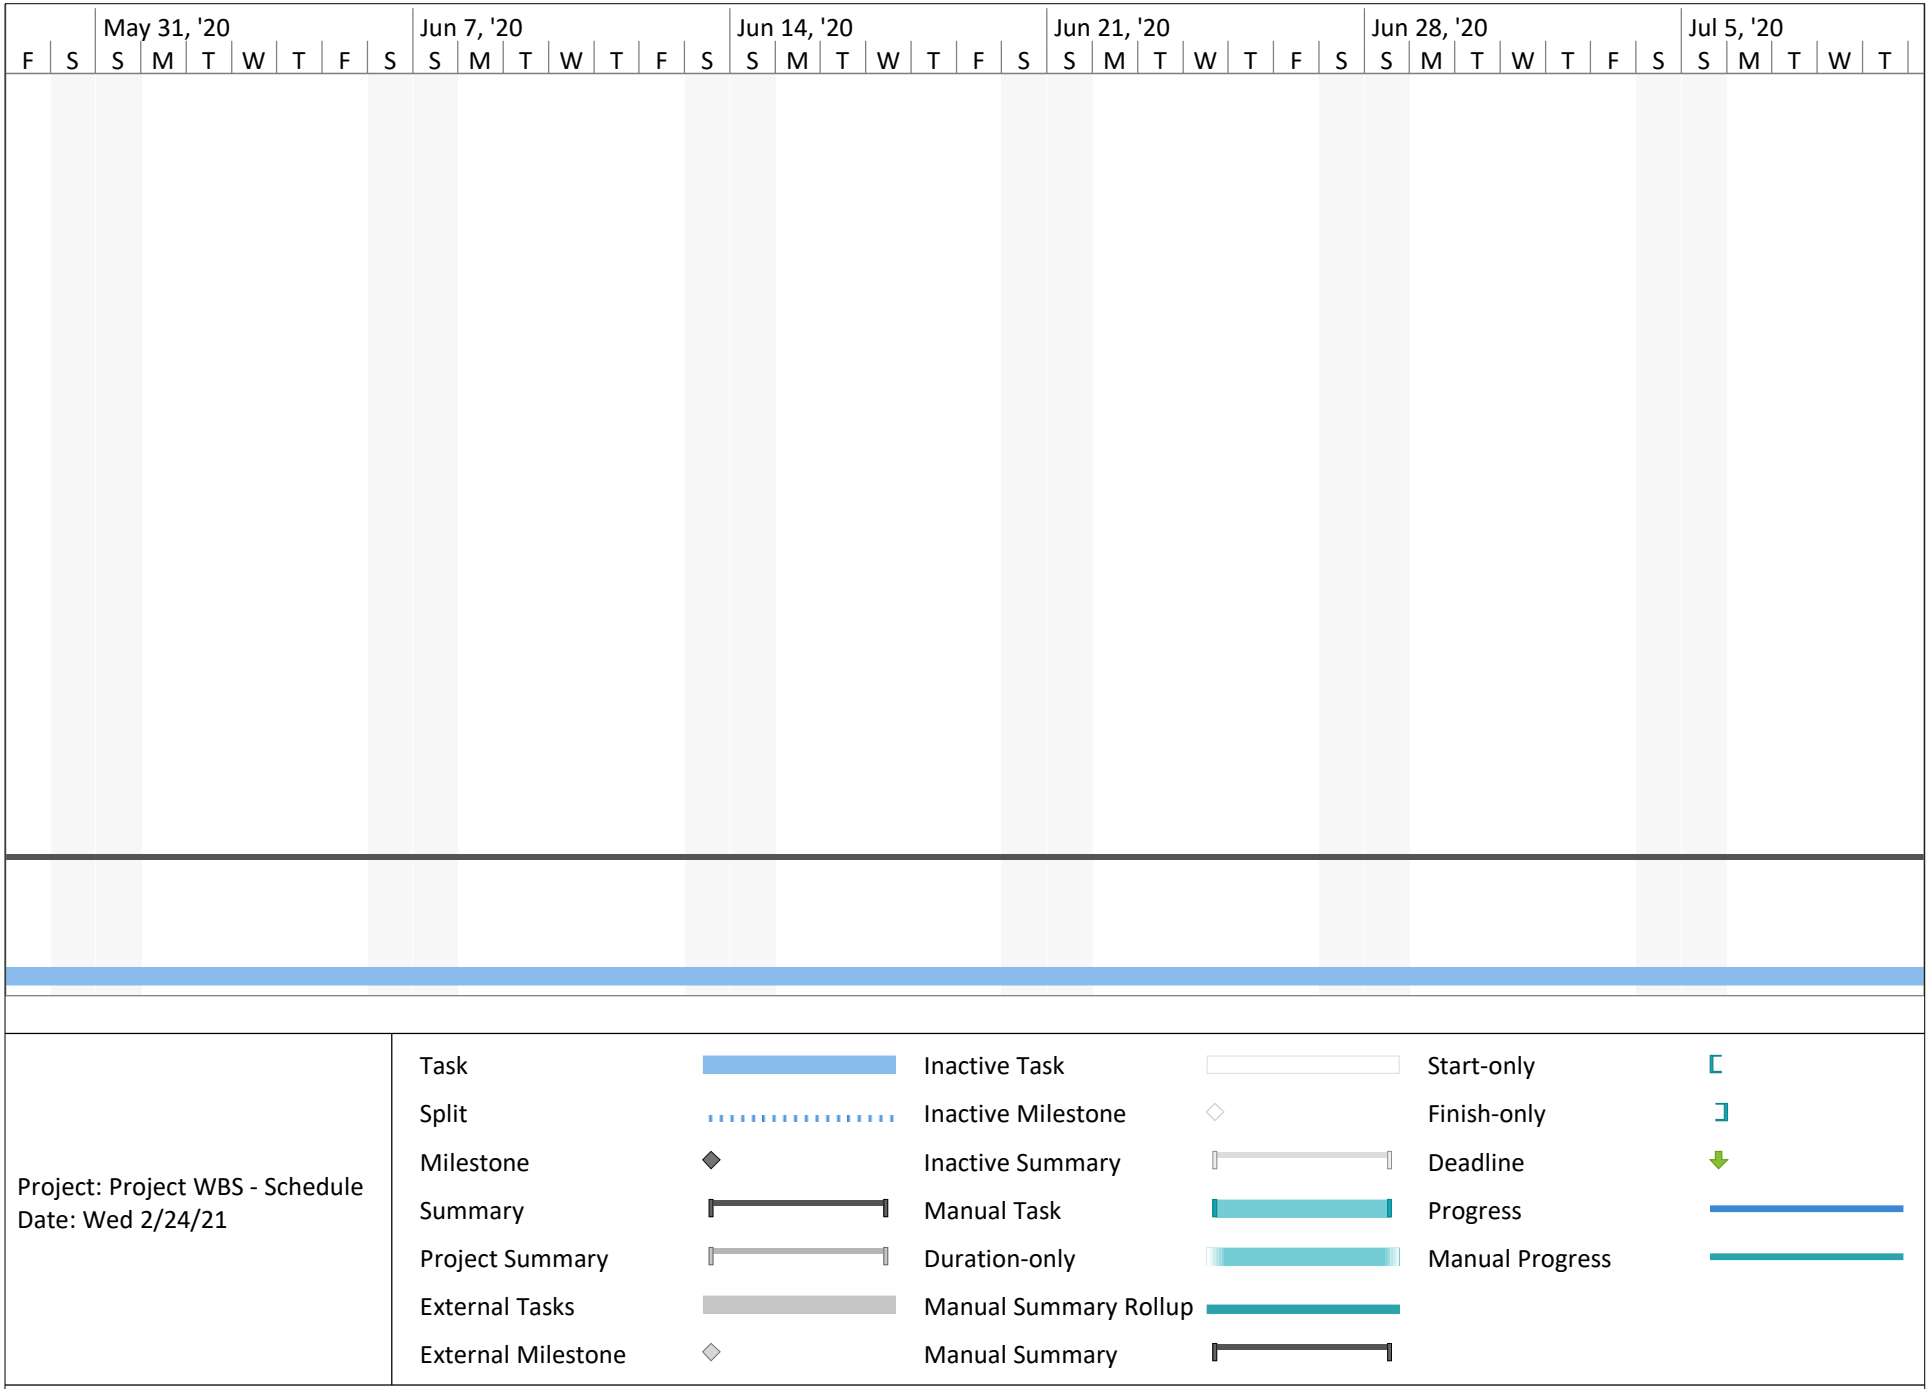


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

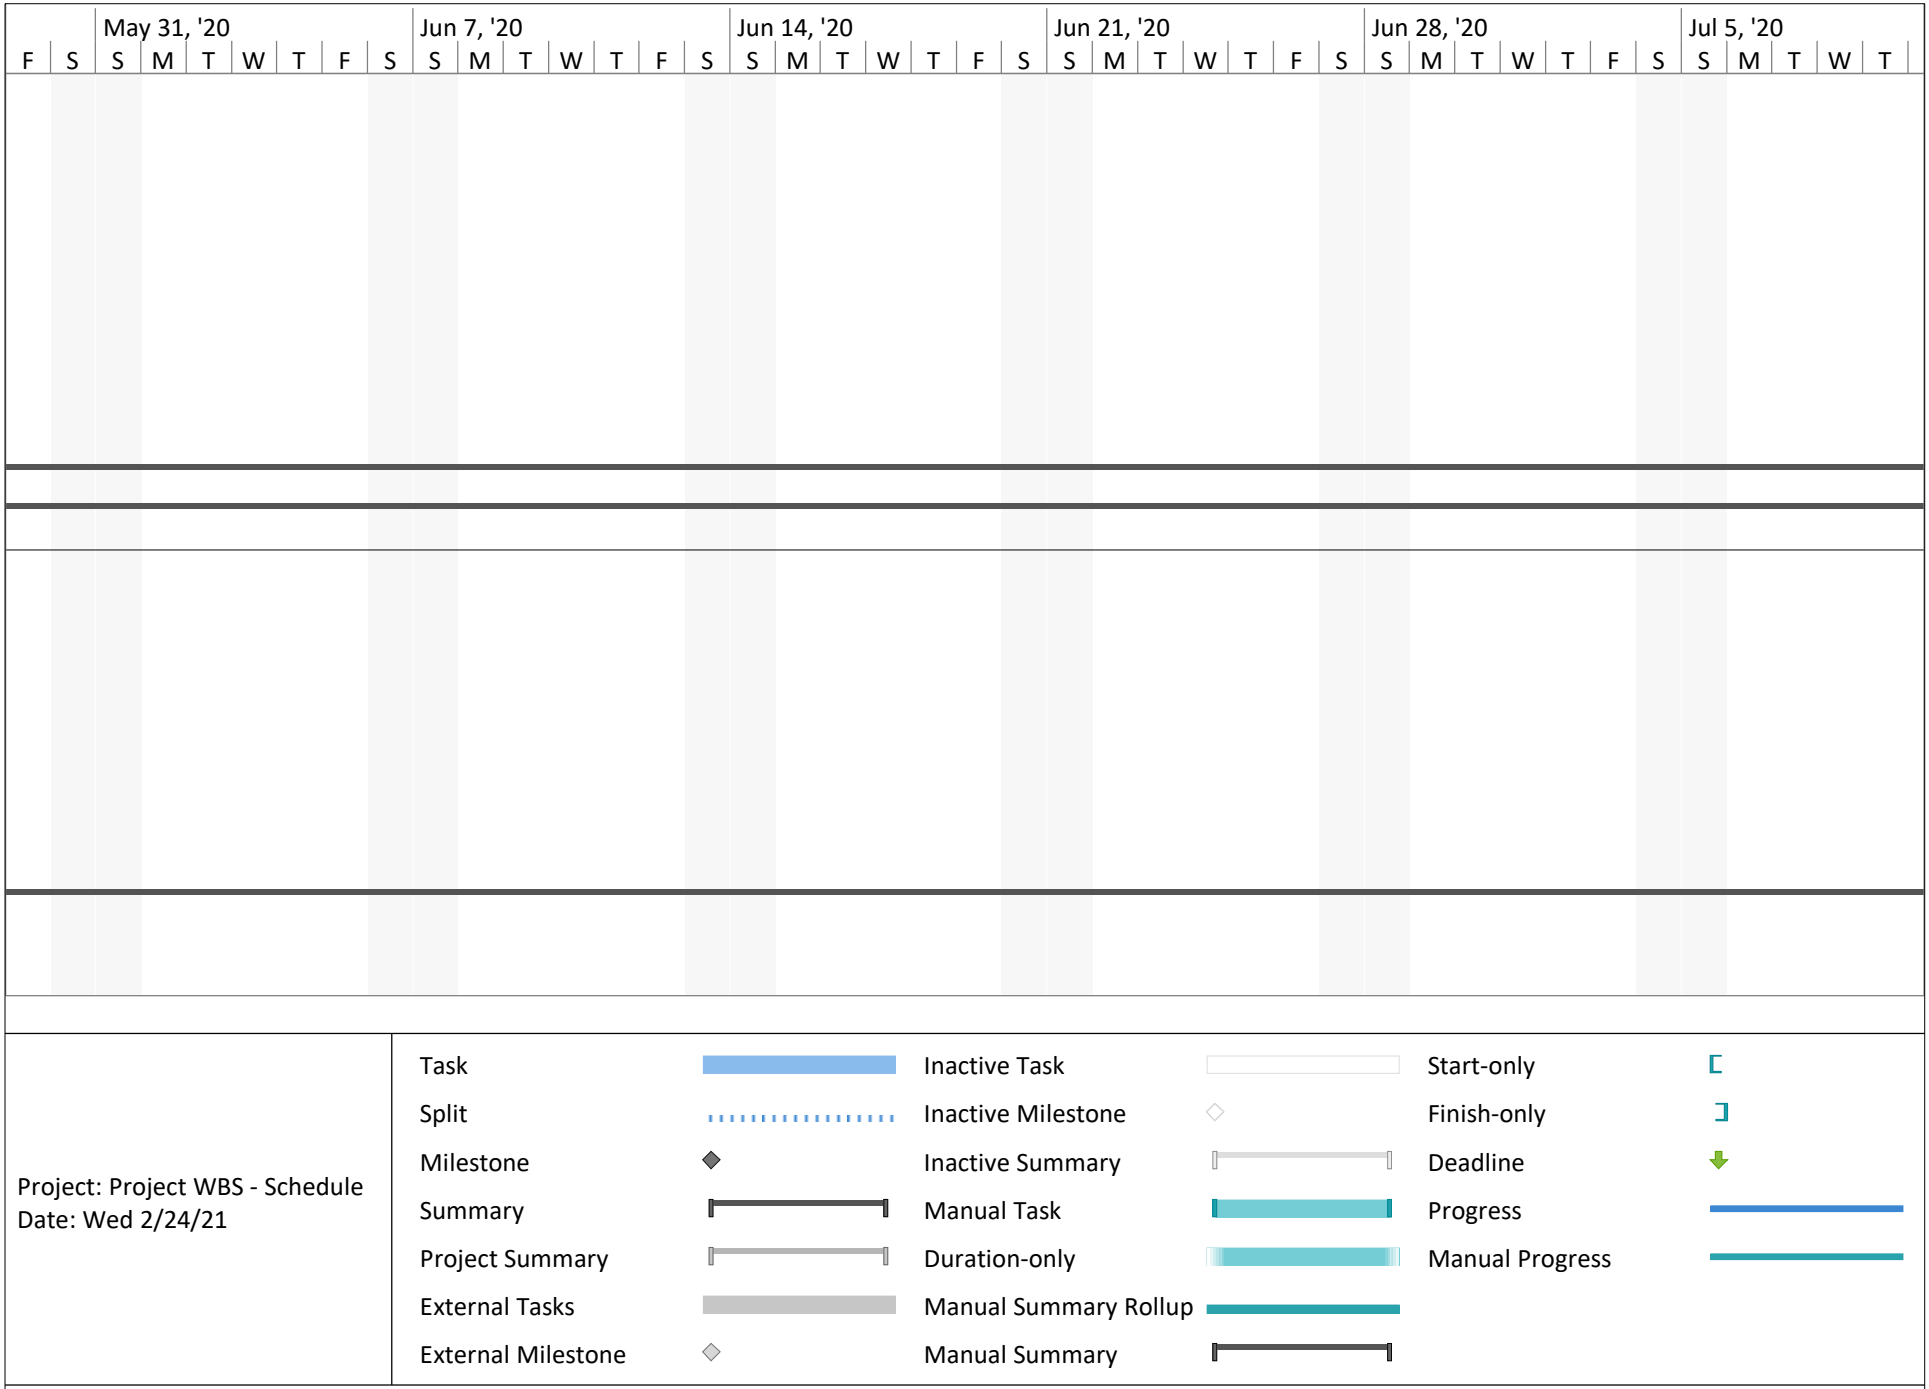
May 31, '20
Jun 7, '20
Jun 14, '20
Jun 21, '20
Jun 28, '20
Jul 5, '20
F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T
Project: Project WBS - Schedule
Date: Wed 2/24/21
Task
Split
Milestone
Summary
Project Summary
External Tasks
External Milestone
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
Deadline
Progress
Manual Progress

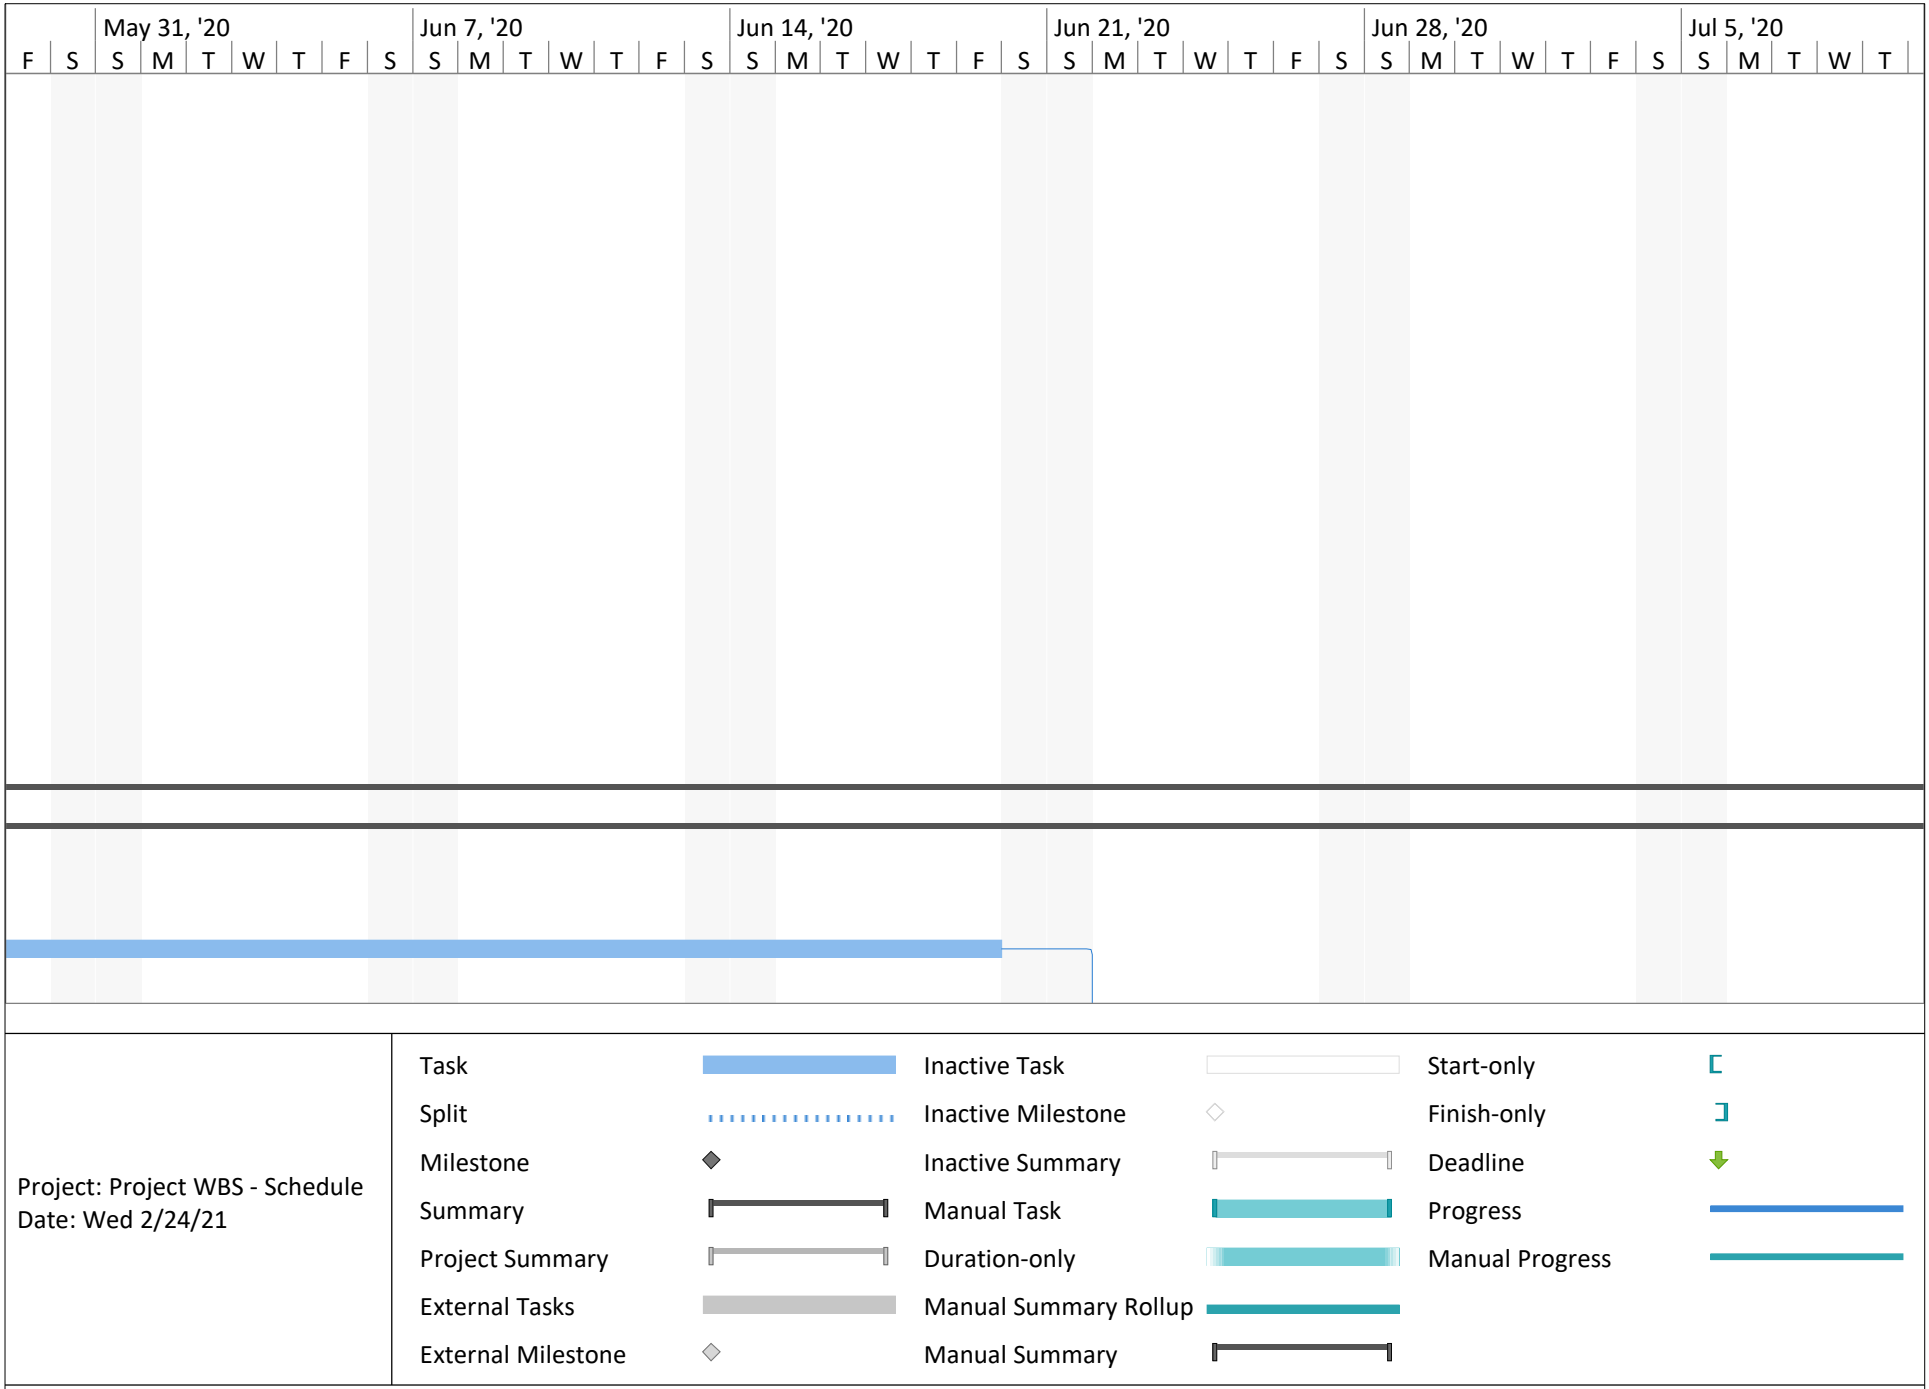
May 31, '20
Jun 7, '20
Jun 14, '20
Jun 21, '20
Jun 28, '20
Jul 5, '20
F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T
Project: Project WBS - Schedule
Date: Wed 2/24/21
Task
Split
Milestone
Summary
Project Summary
External Tasks
External Milestone
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
Deadline
Progress
Manual Progress

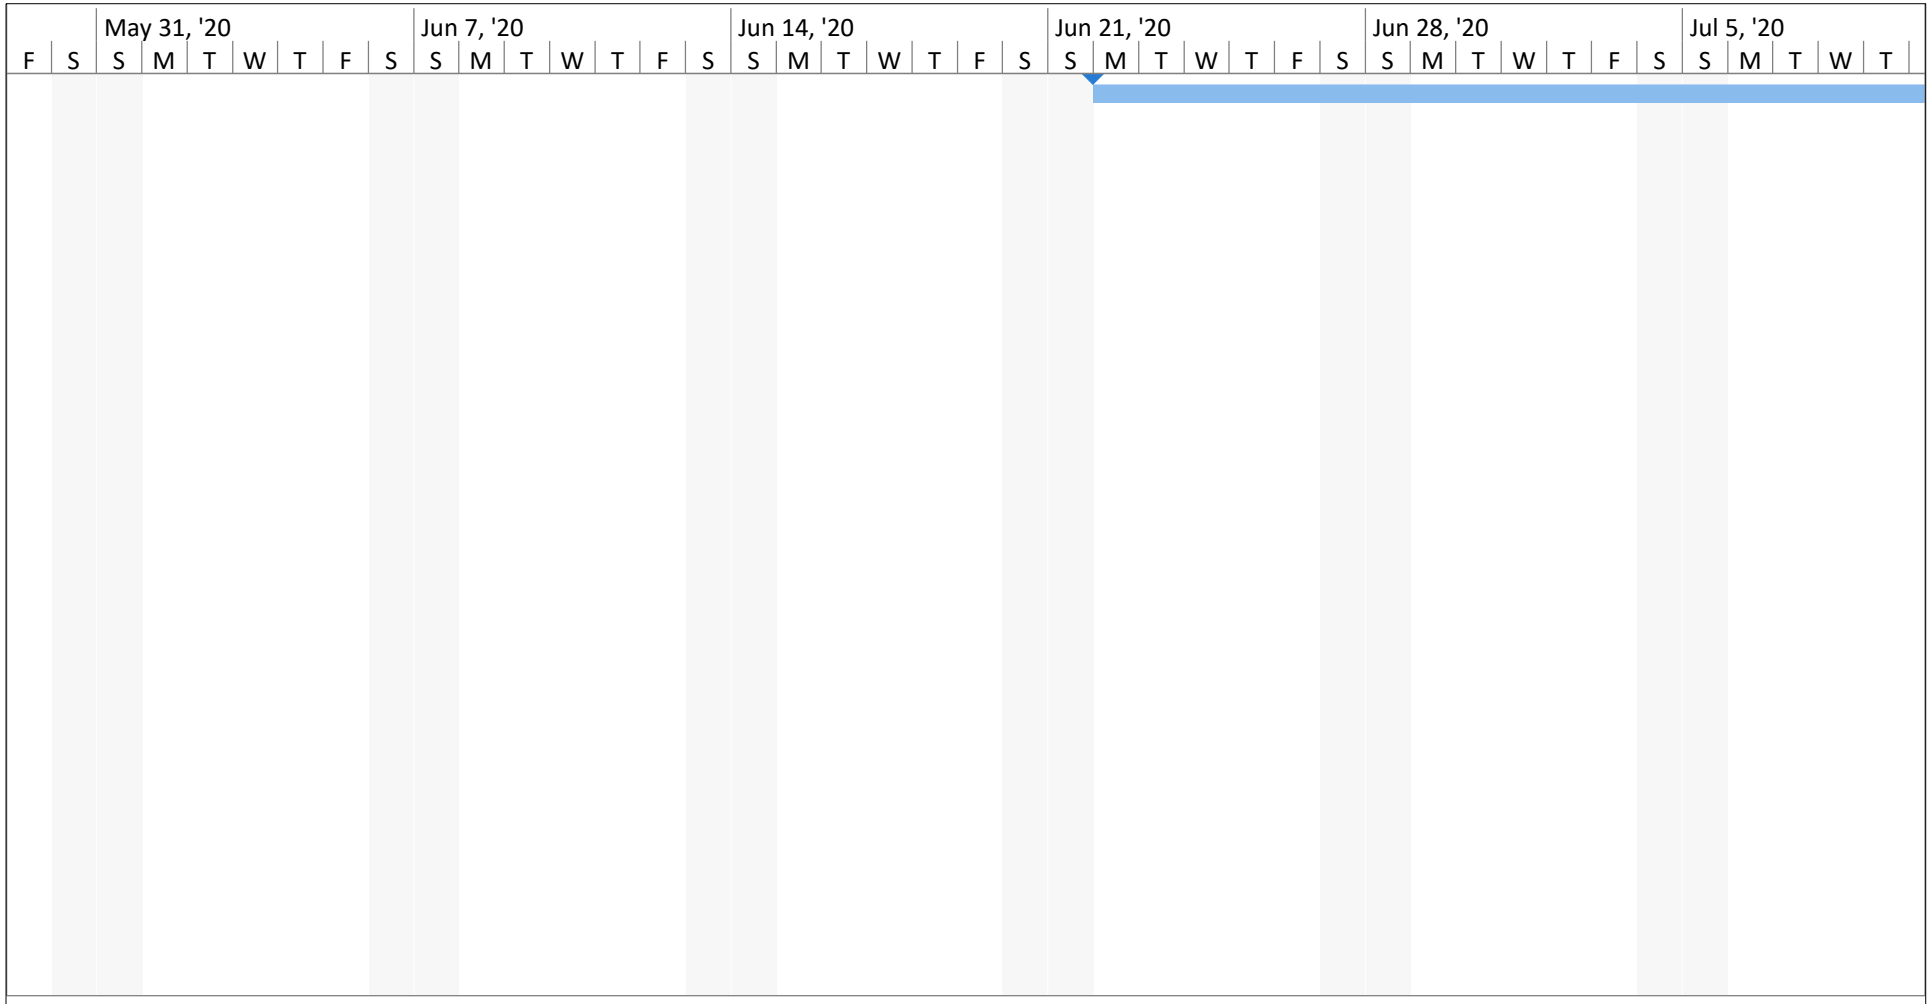


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |




Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

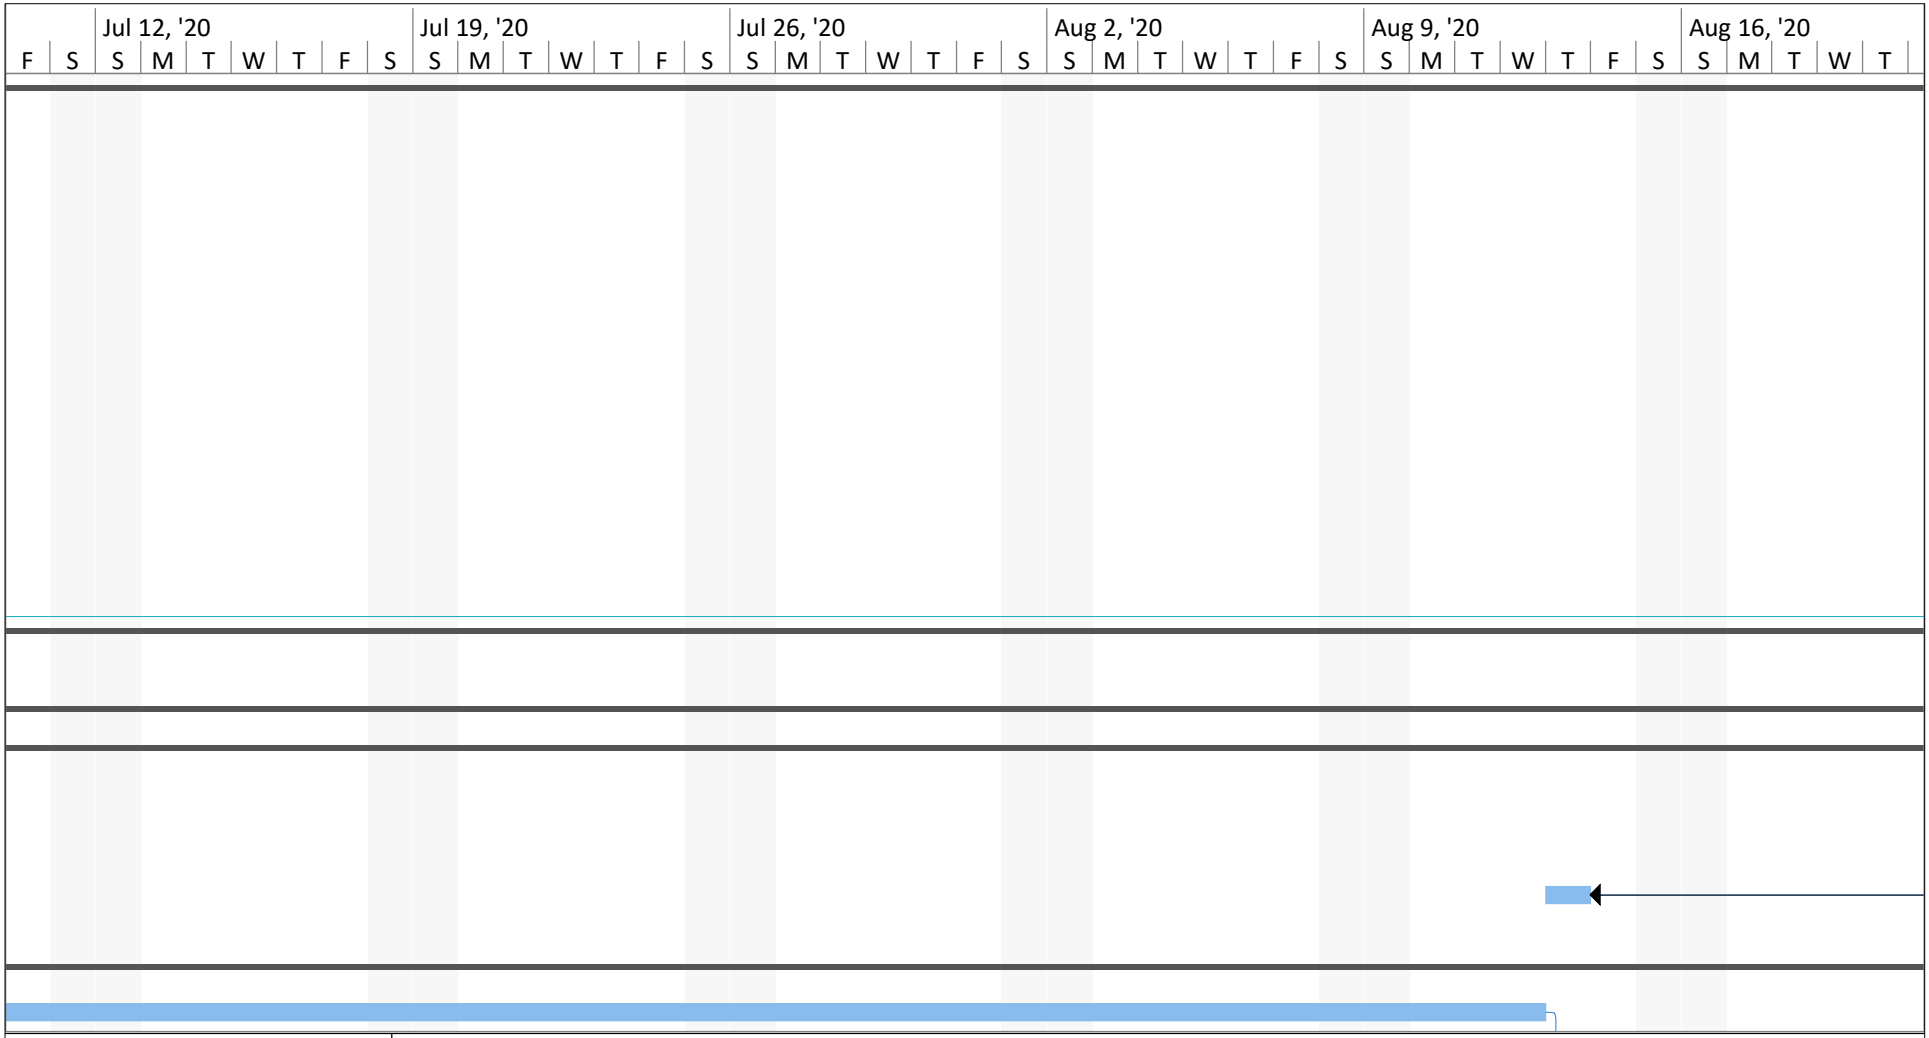


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

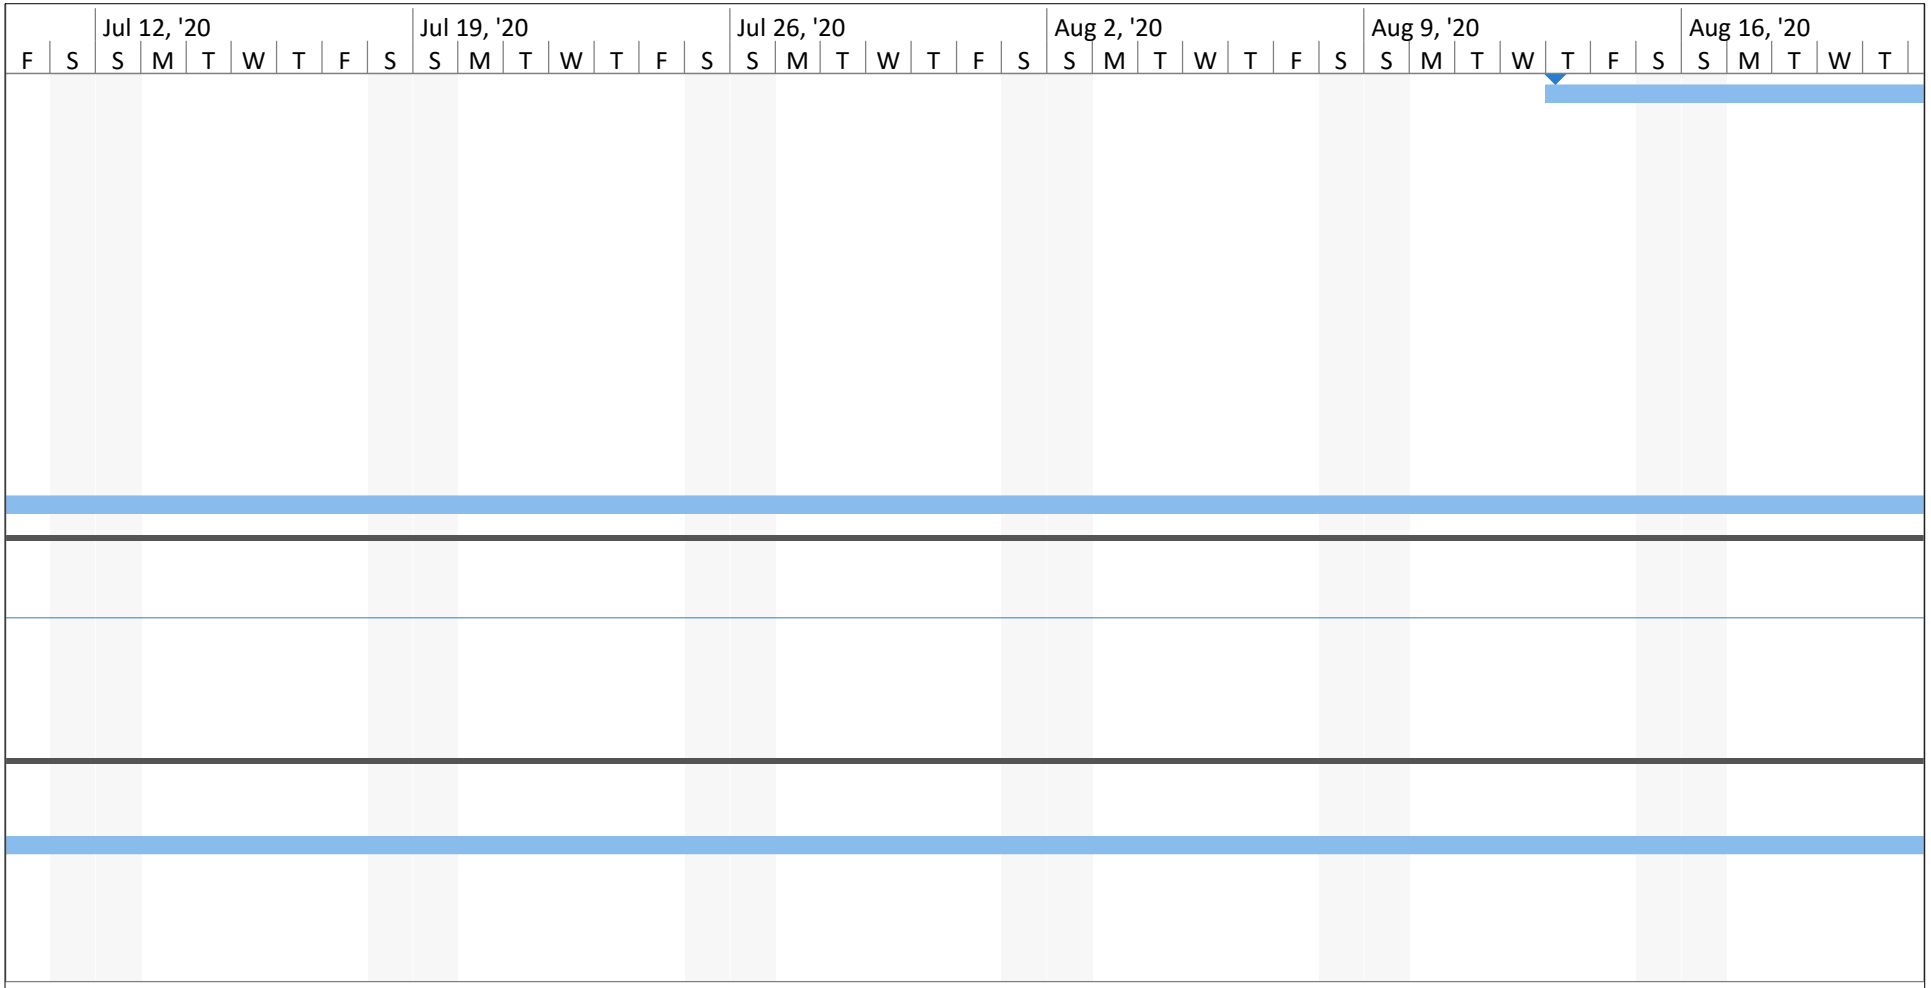


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

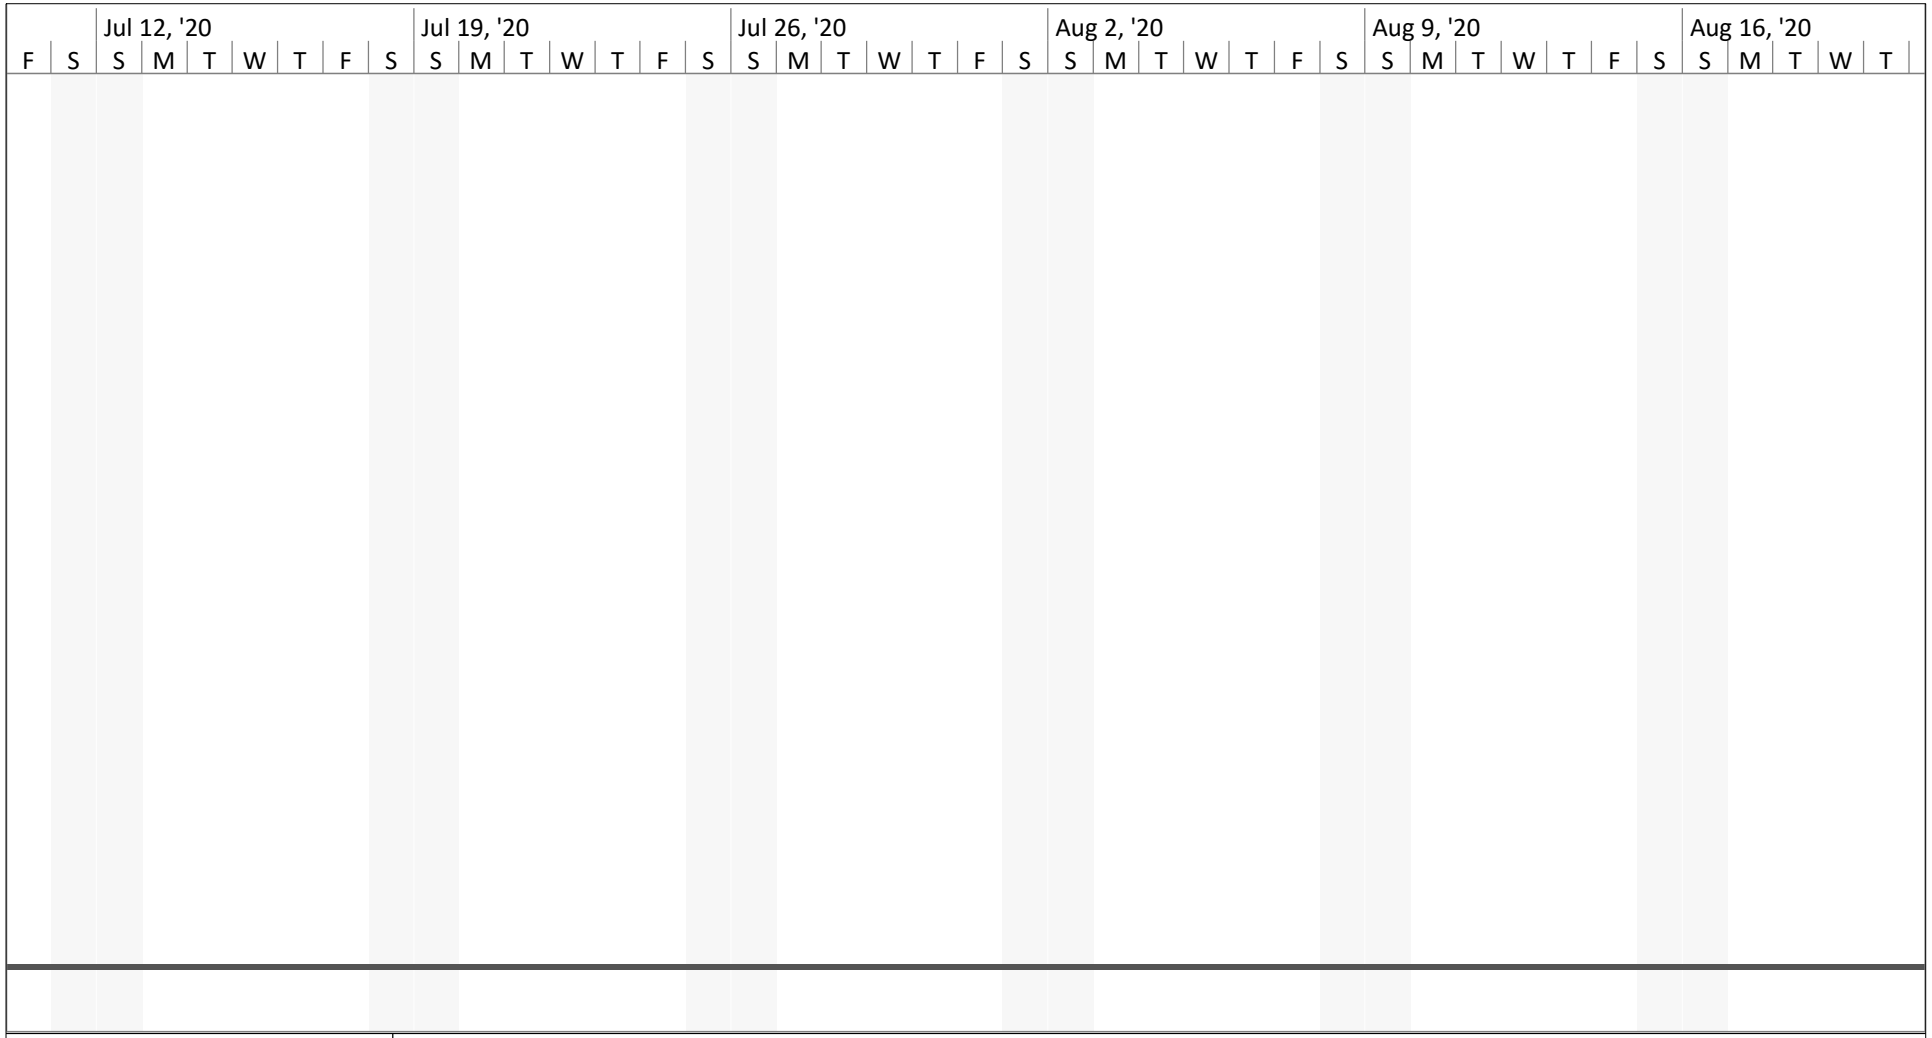


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

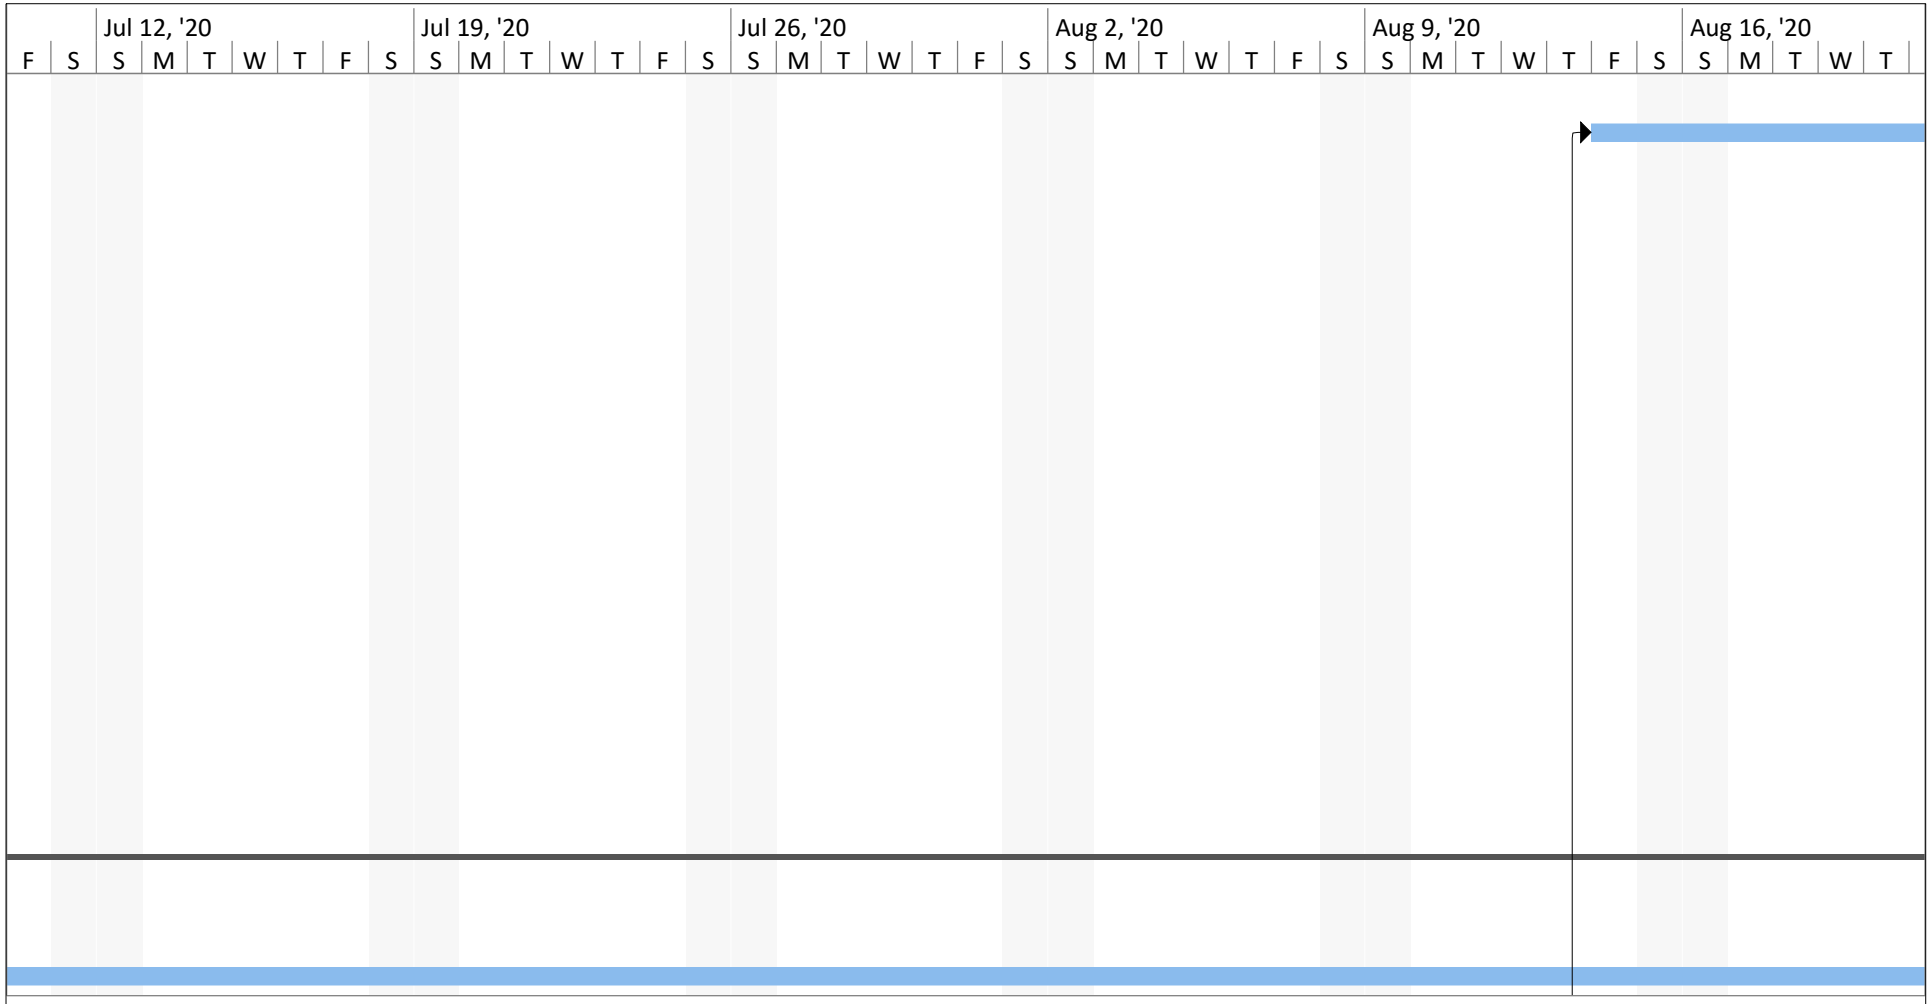


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

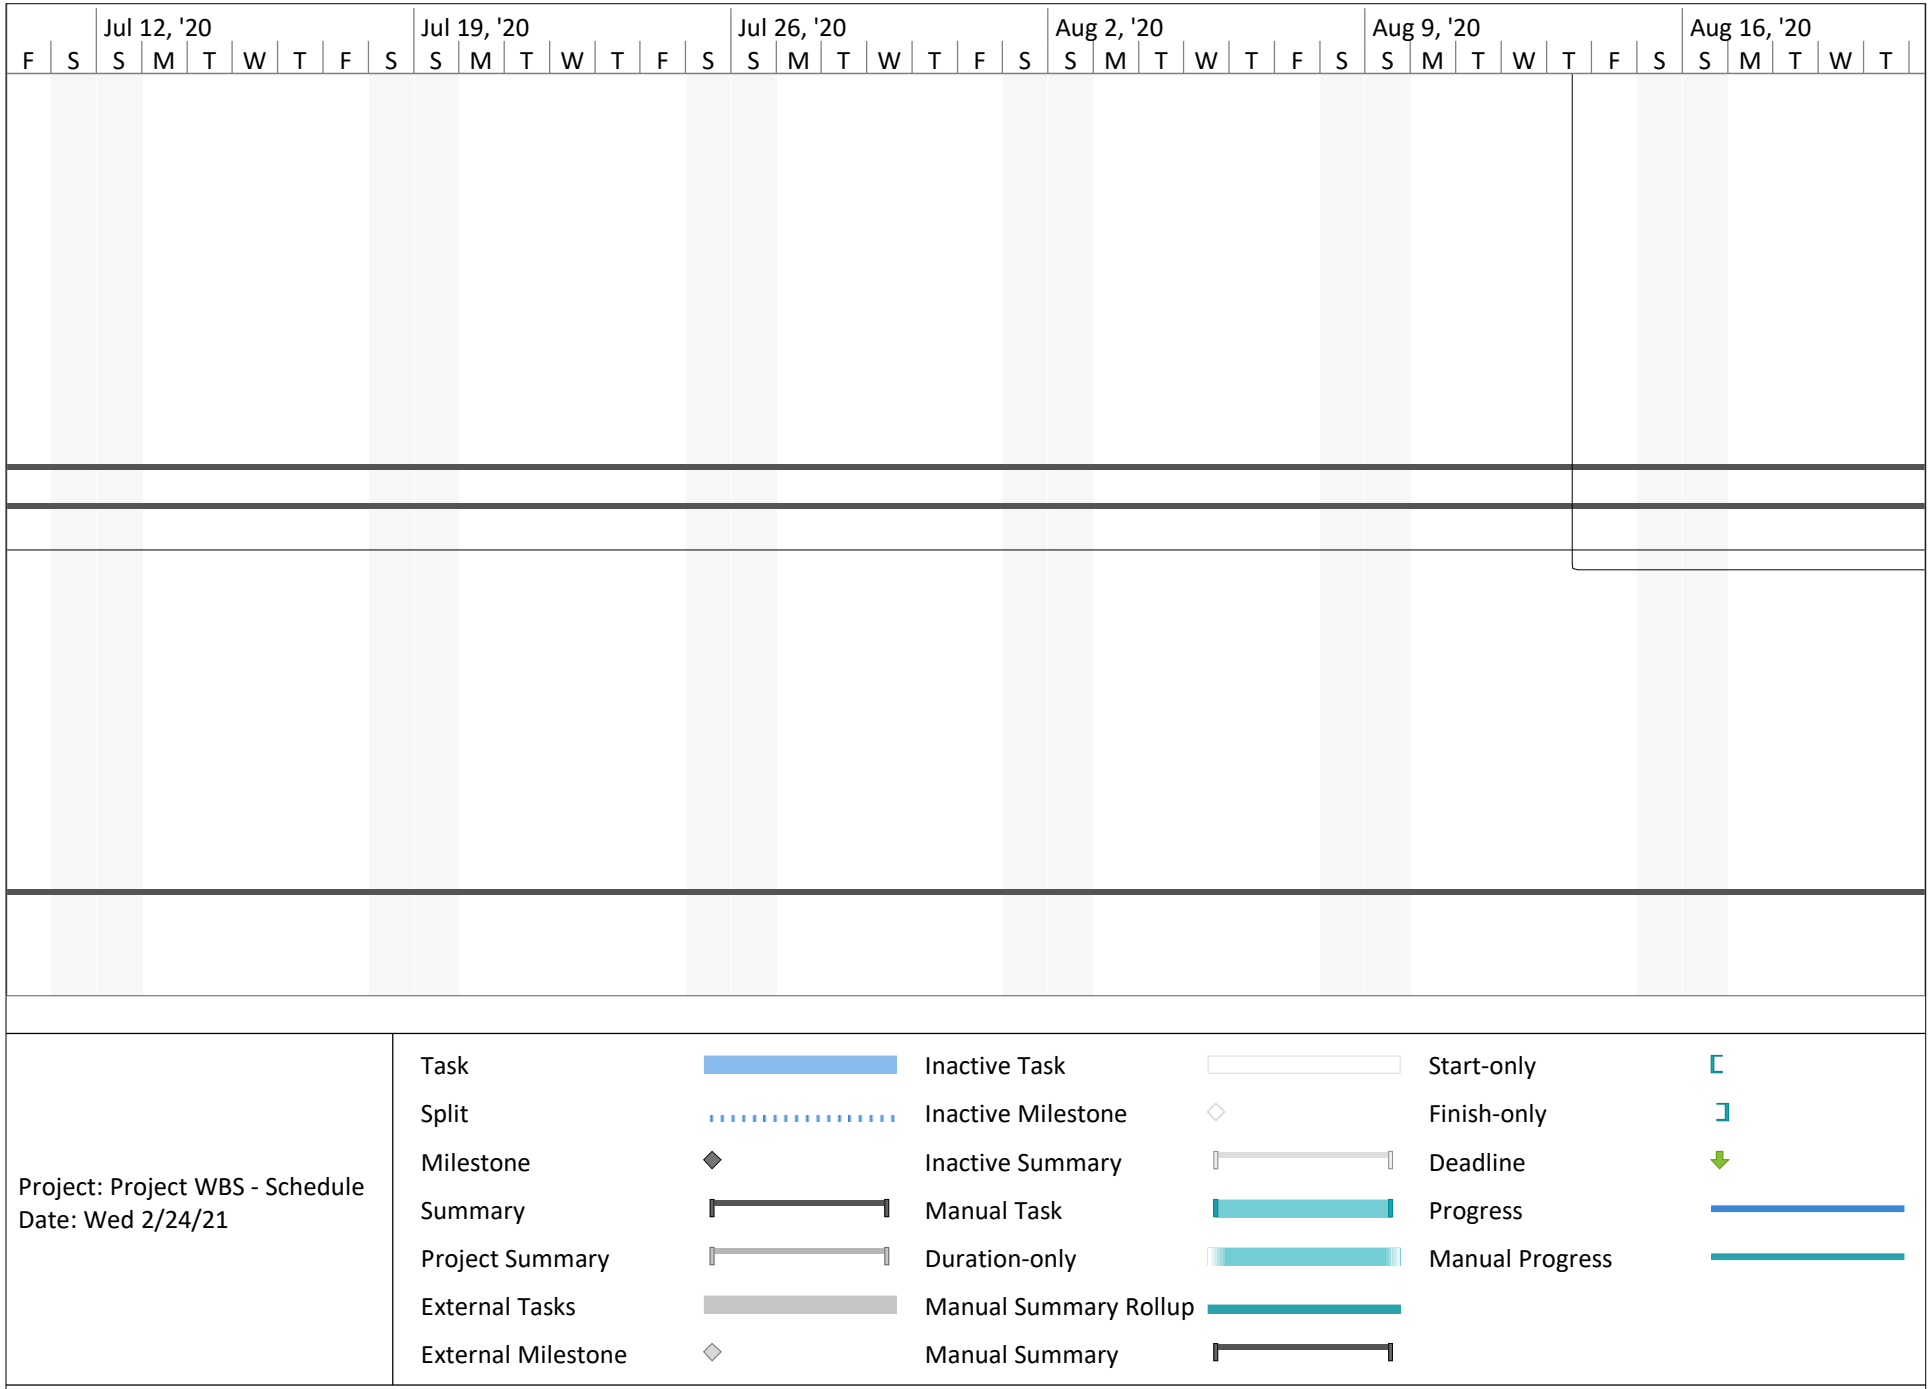
Jul 12, '20
Jul 19, '20
Jul 26, '20
Aug 2, '20
Aug 9, '20
Aug 16, '20
F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T
Project: Project WBS - Schedule
Date: Wed 2/24/21
Task
Split
Milestone
Summary
Project Summary
External Tasks
External Milestone
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
Deadline
Progress
Manual Progress

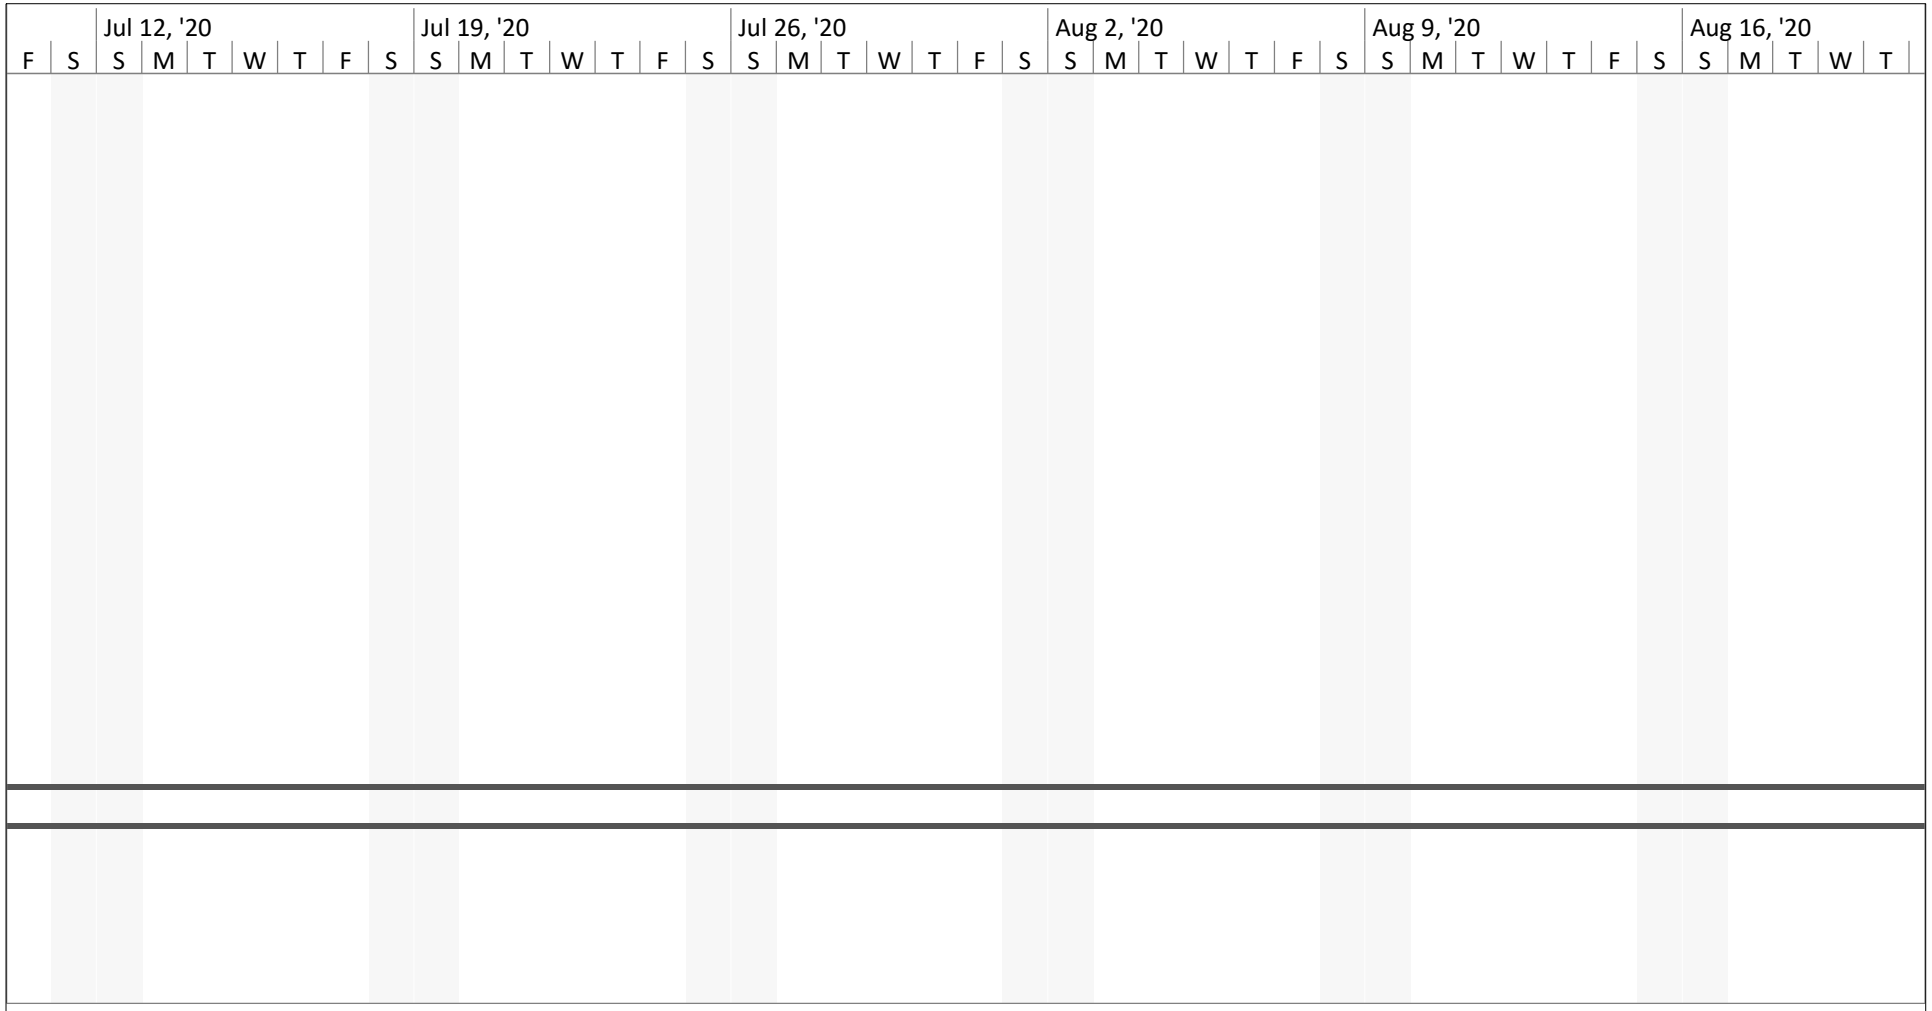


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

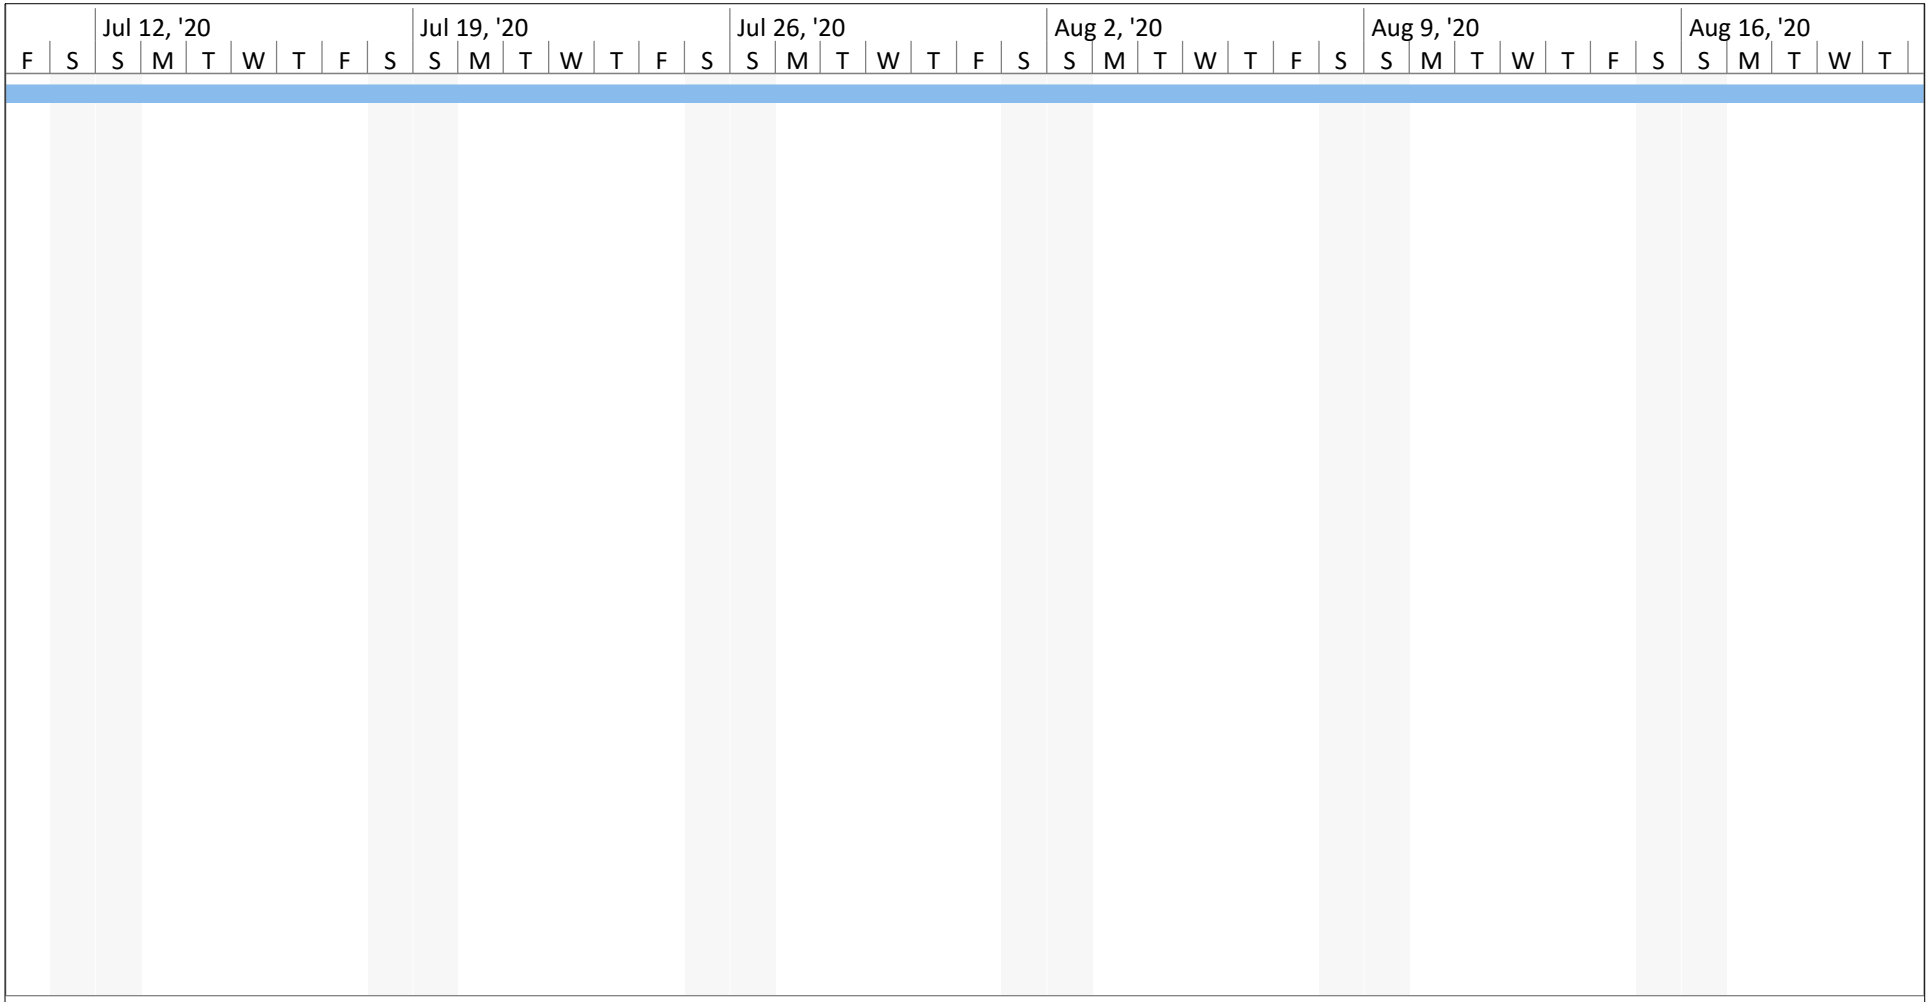


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |




Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

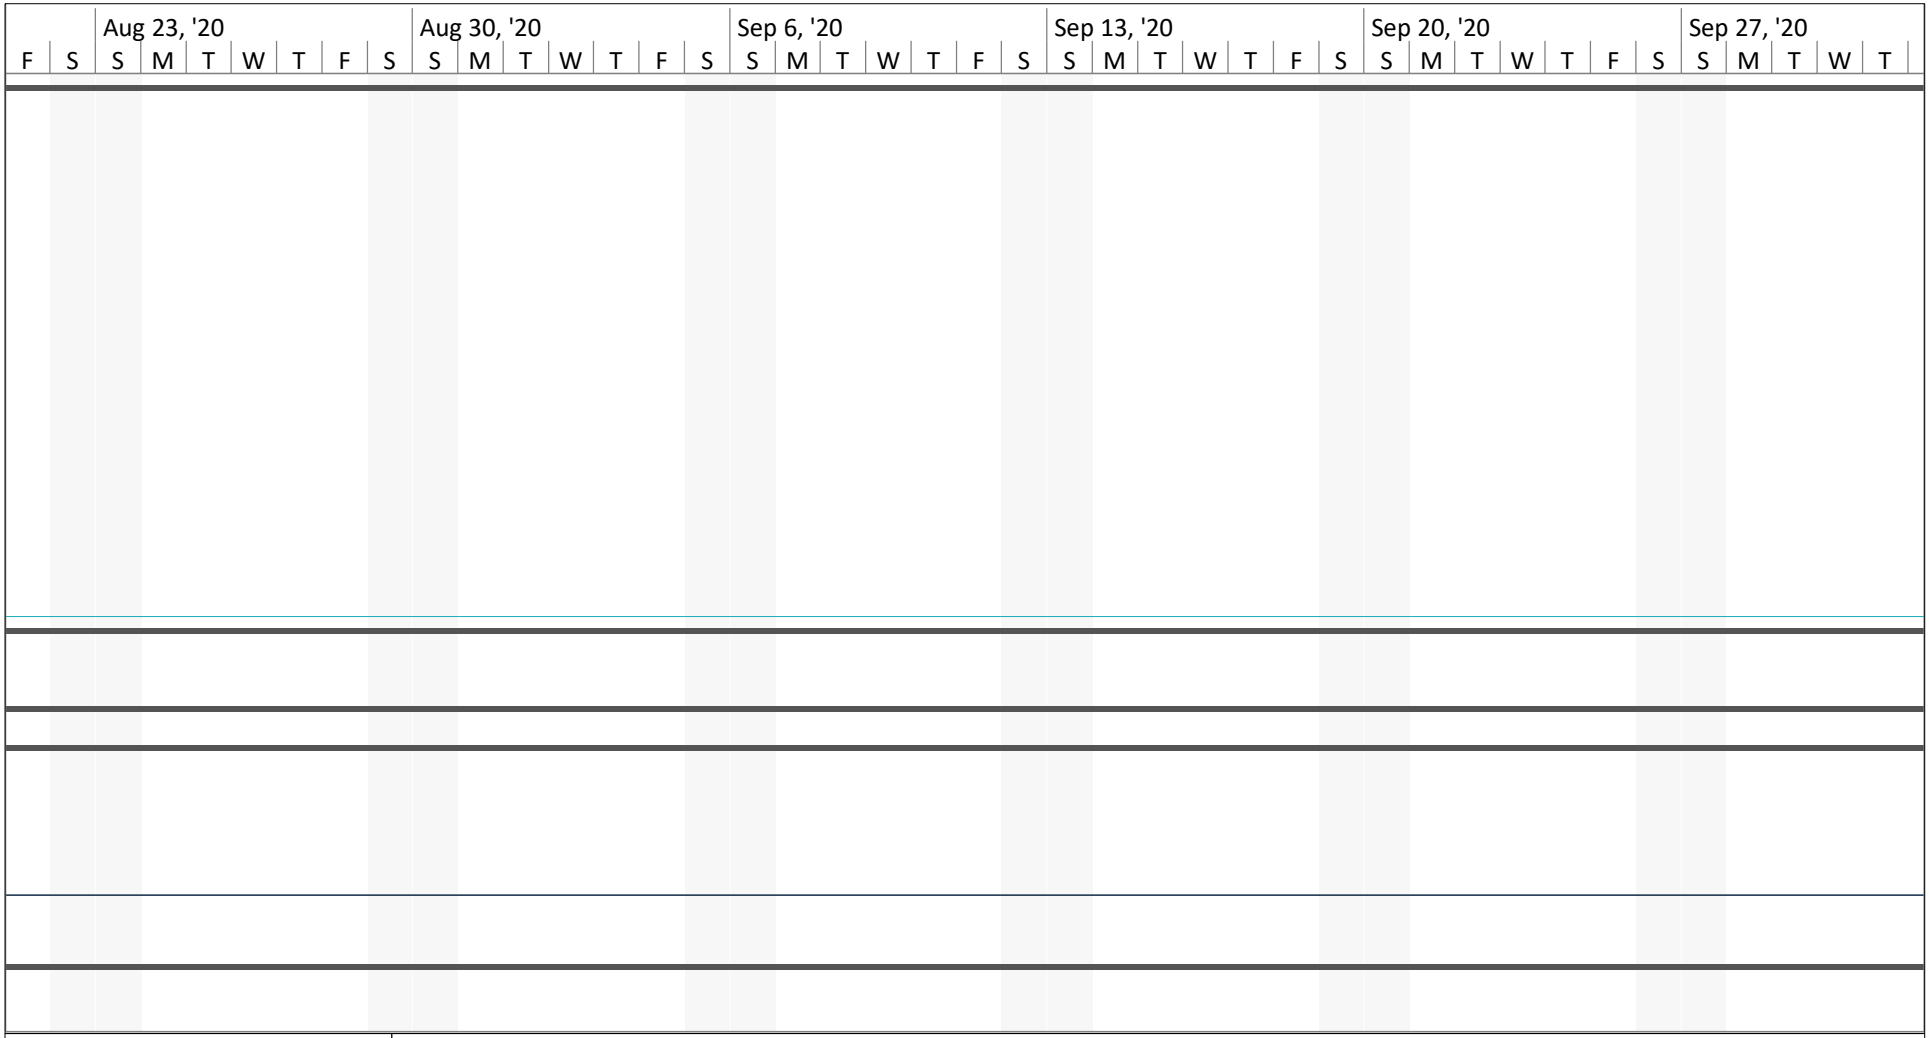


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

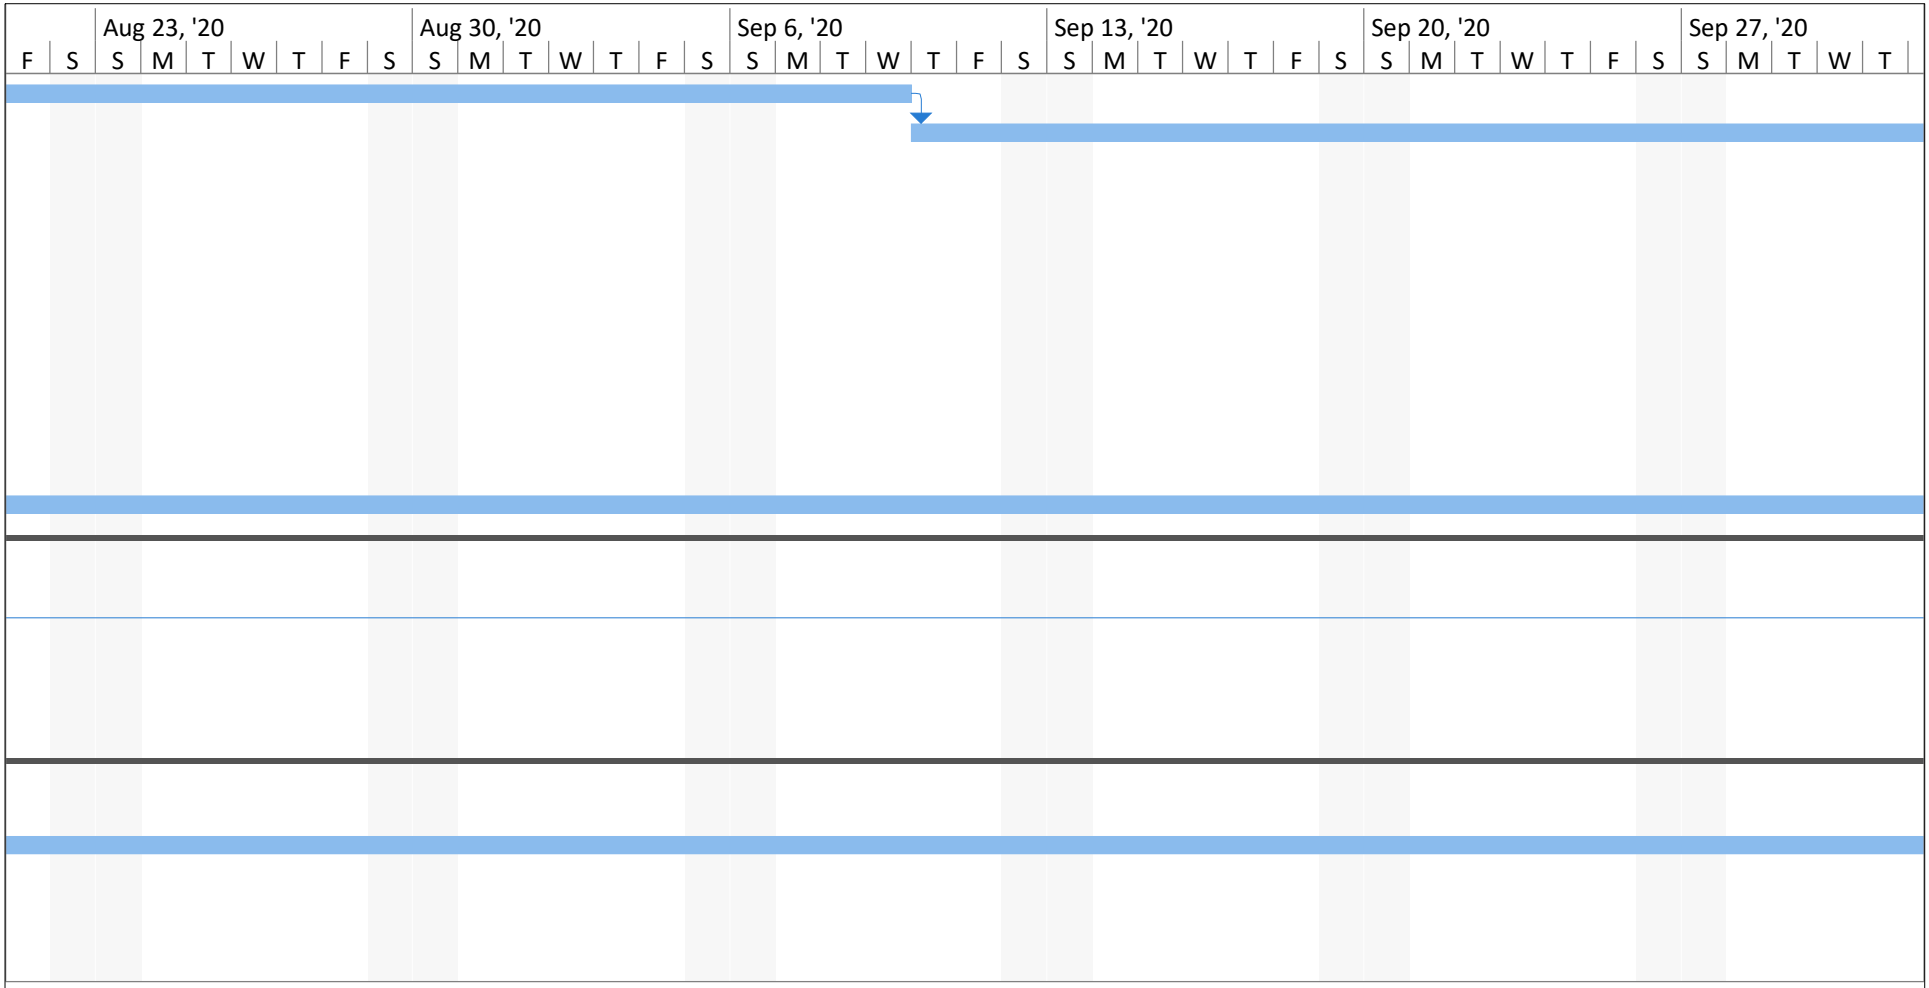


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

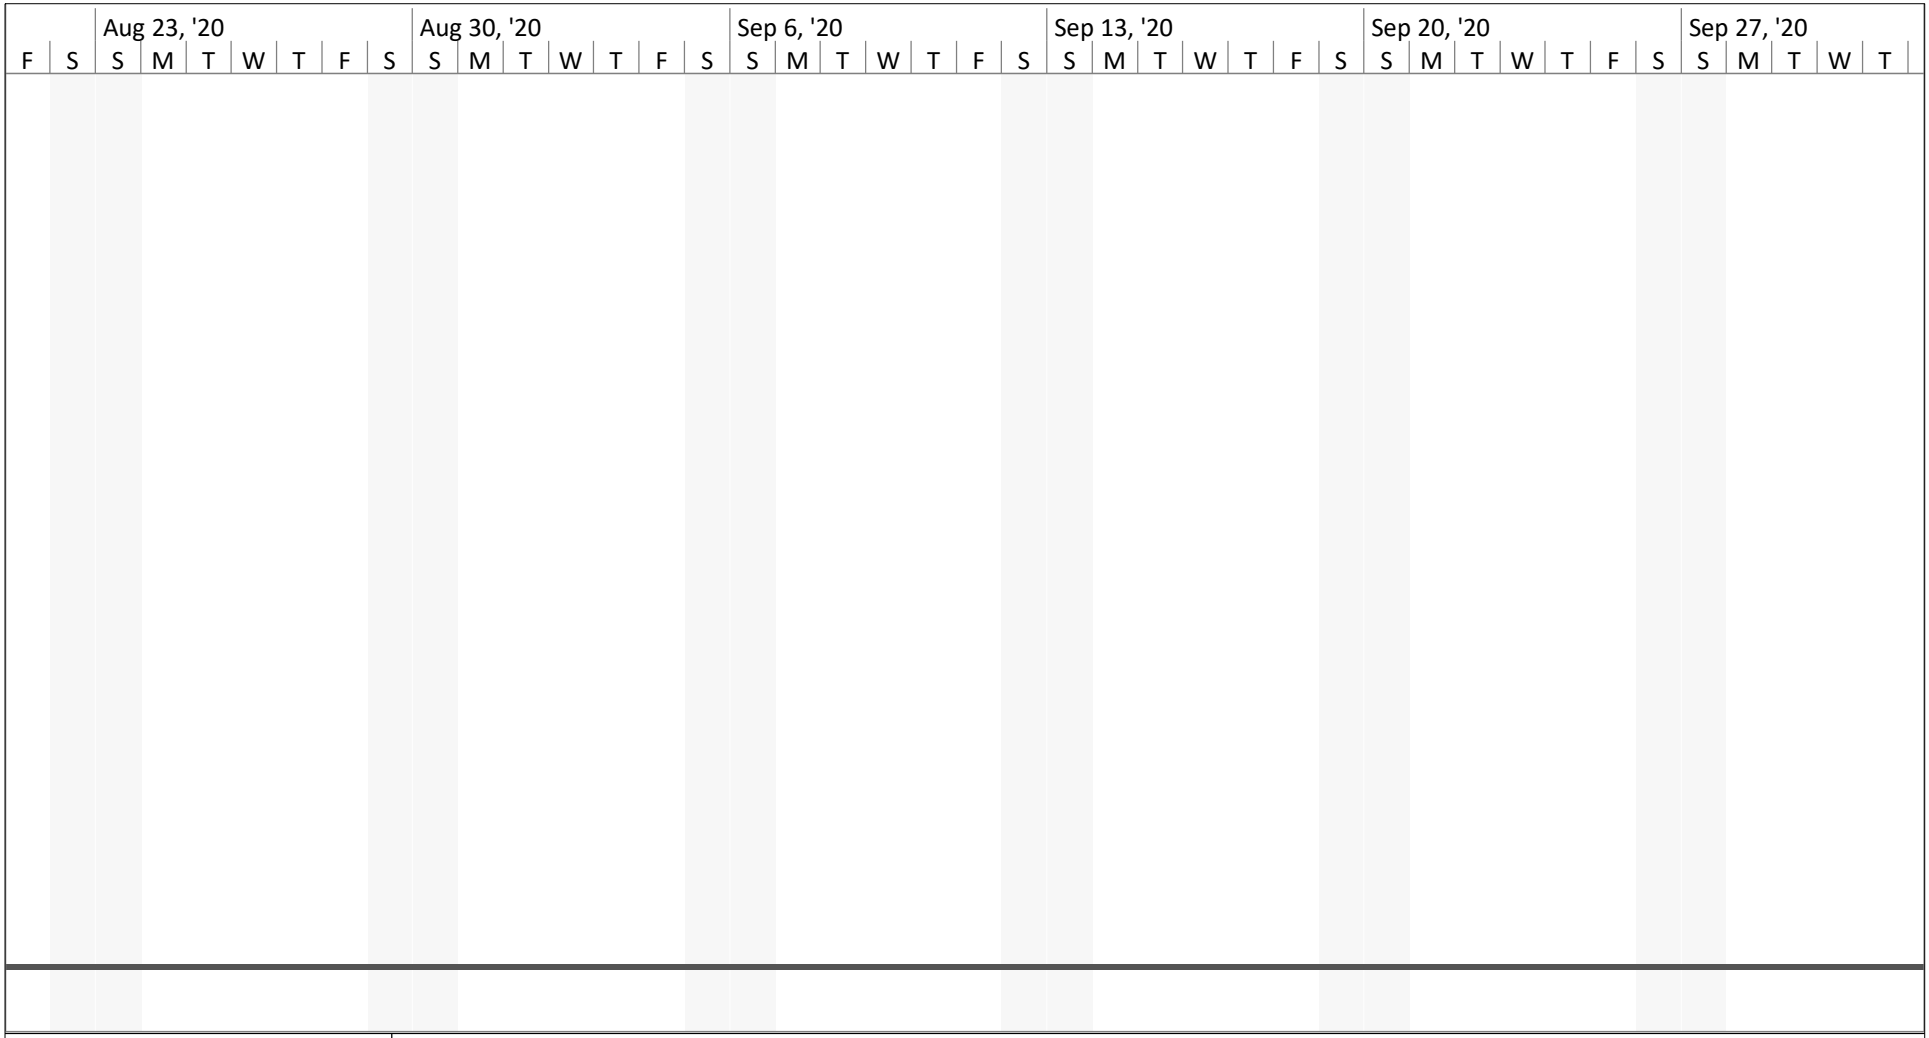


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

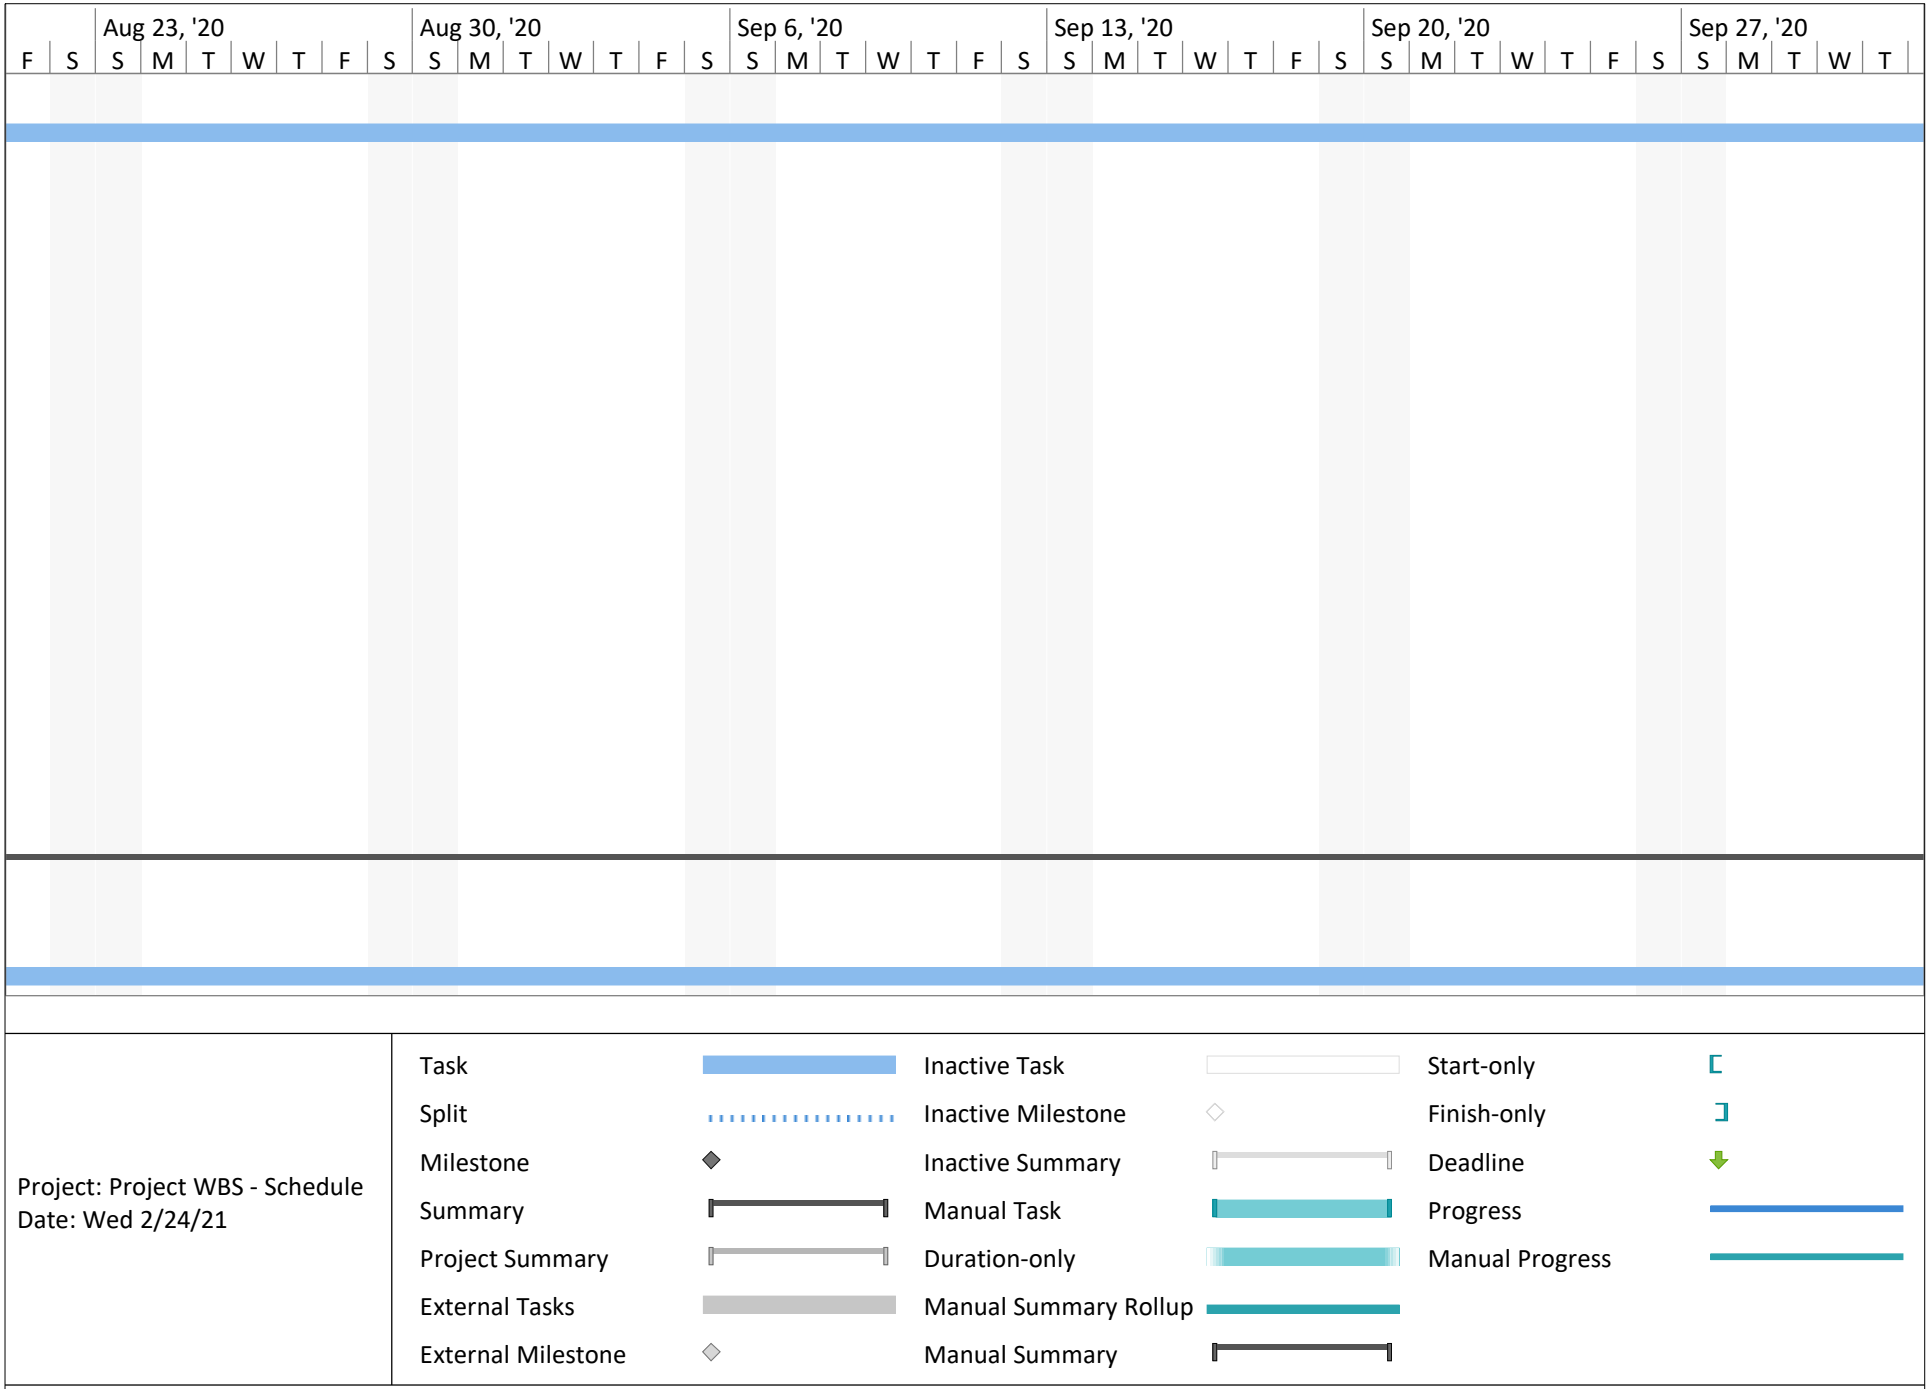


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

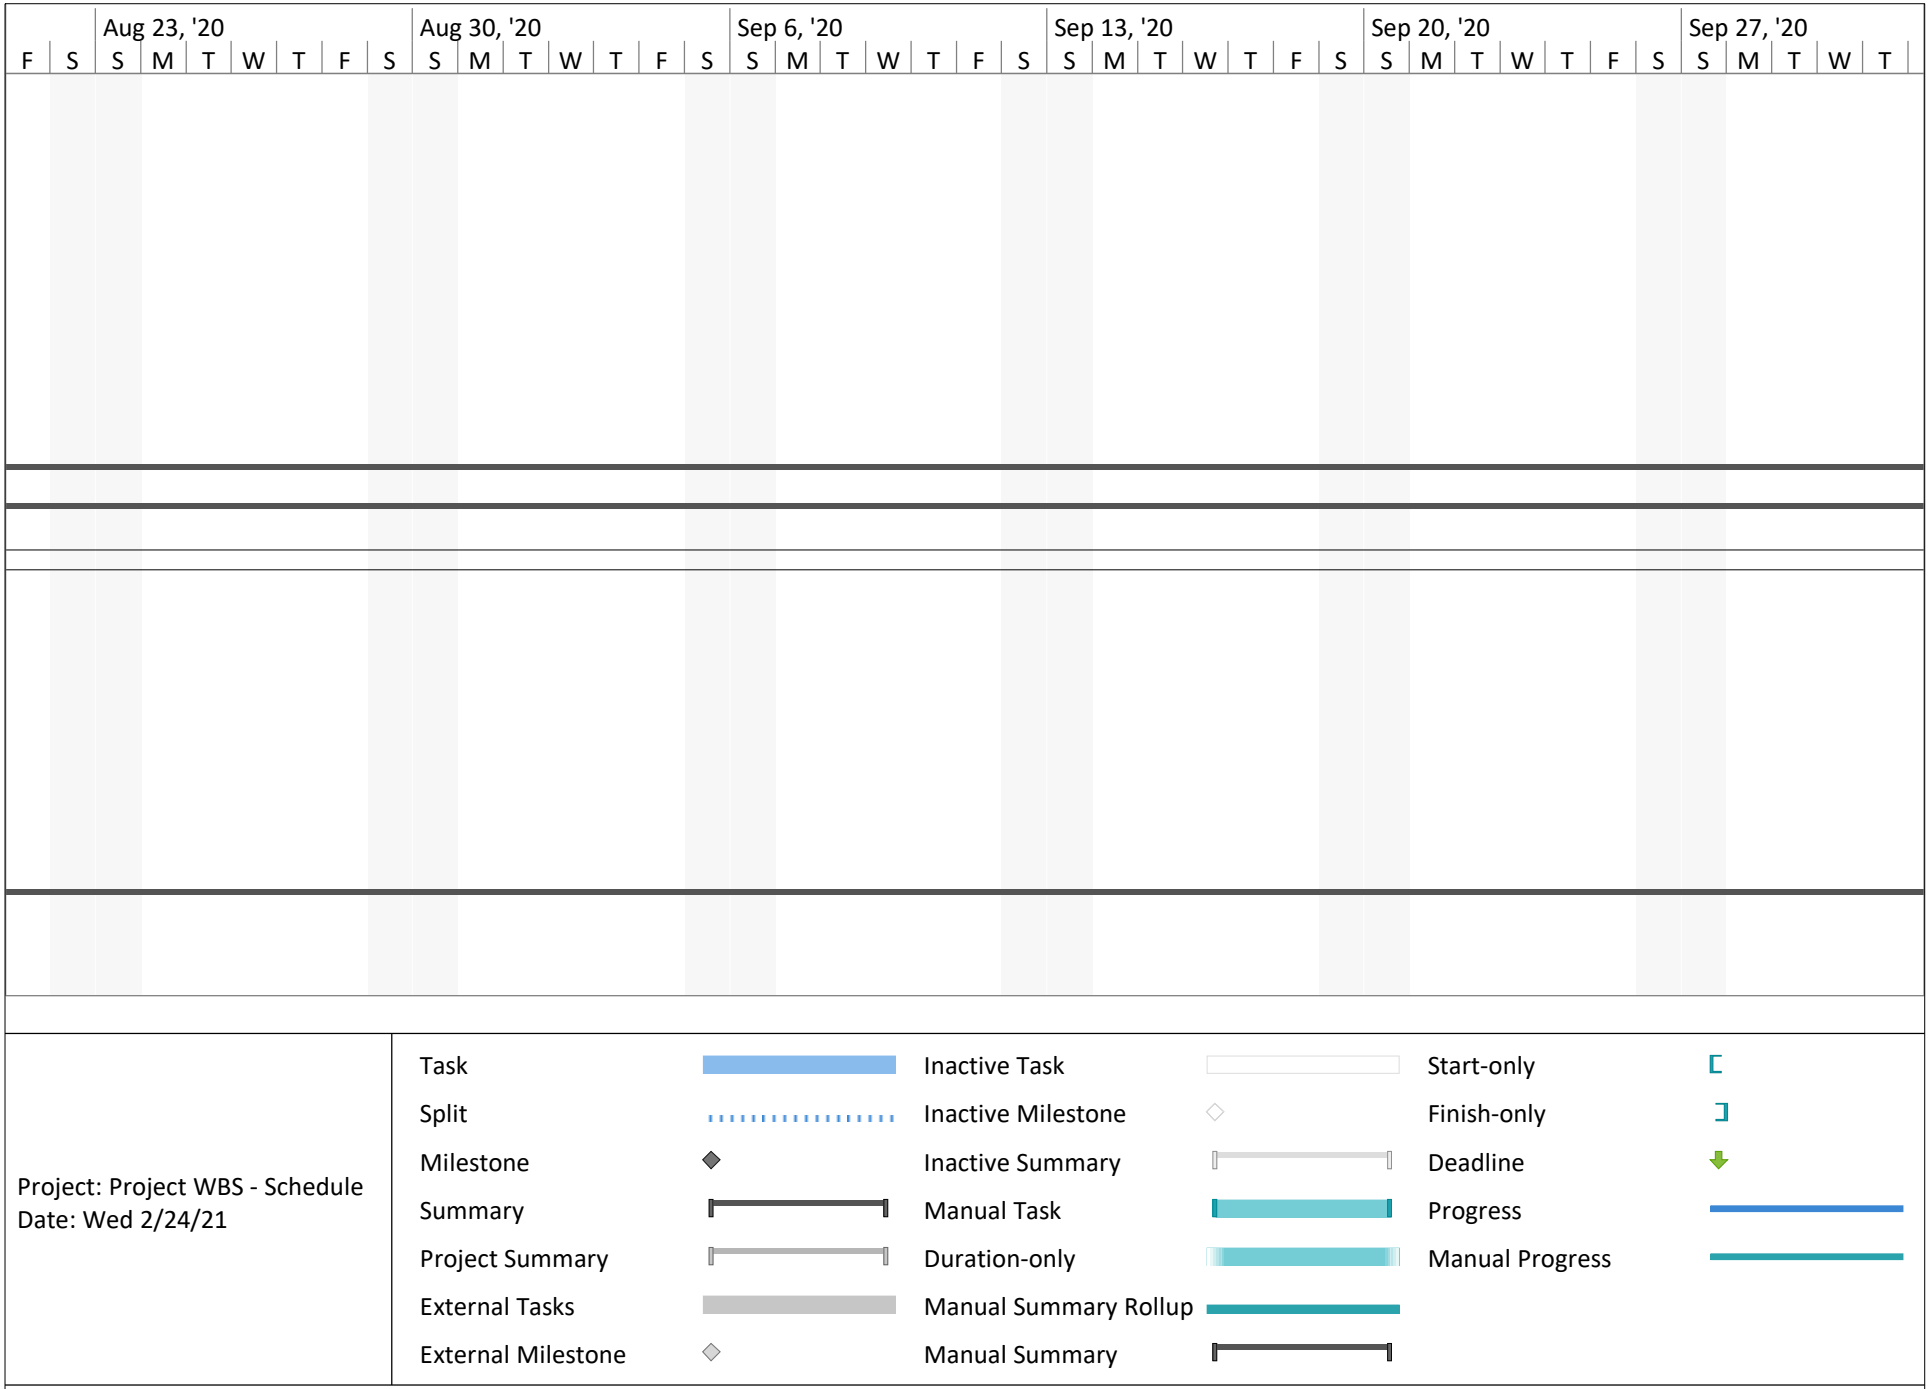
Aug 23, '20
Aug 30, '20
Sep 6, '20
Sep 13, '20
Sep 20, '20
Sep 27, '20
F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T
Project: Project WBS - Schedule
Date: Wed 2/24/21
Task
Split
Milestone
Summary
Project Summary
External Tasks
External Milestone
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
Deadline
Progress
Manual Progress

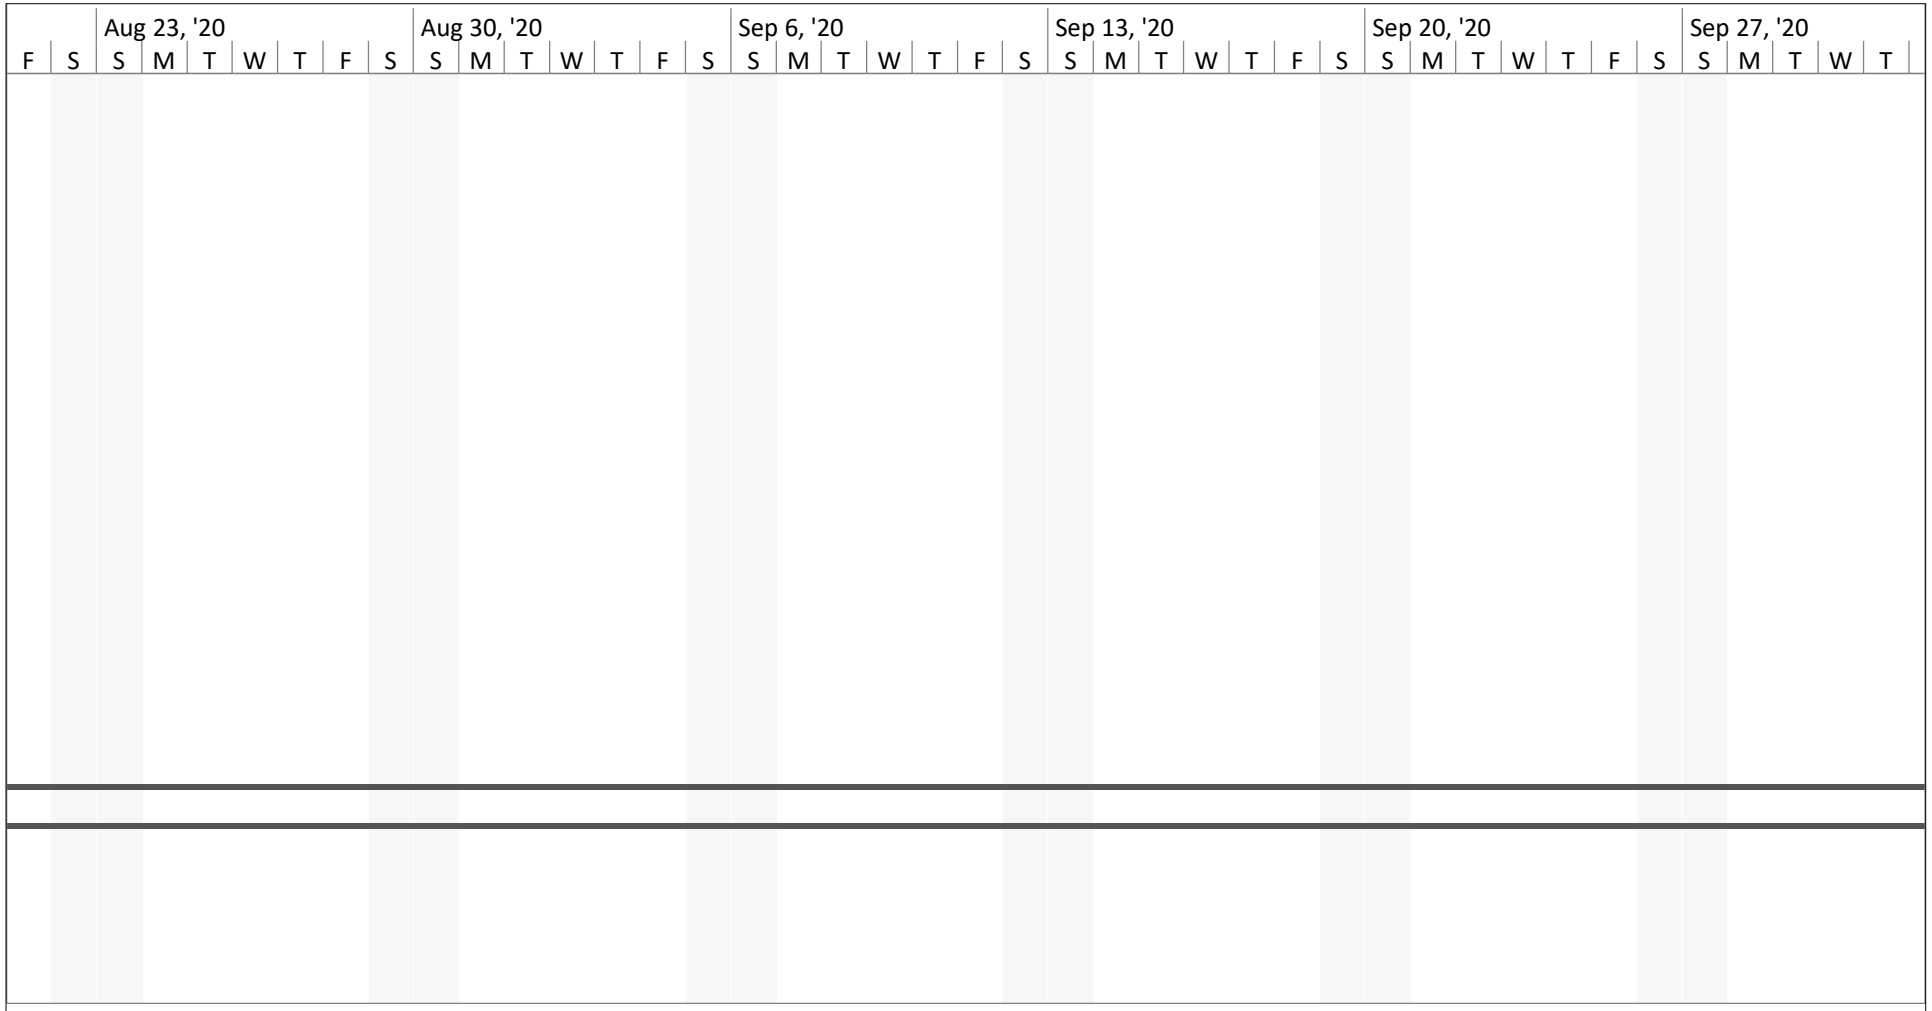


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

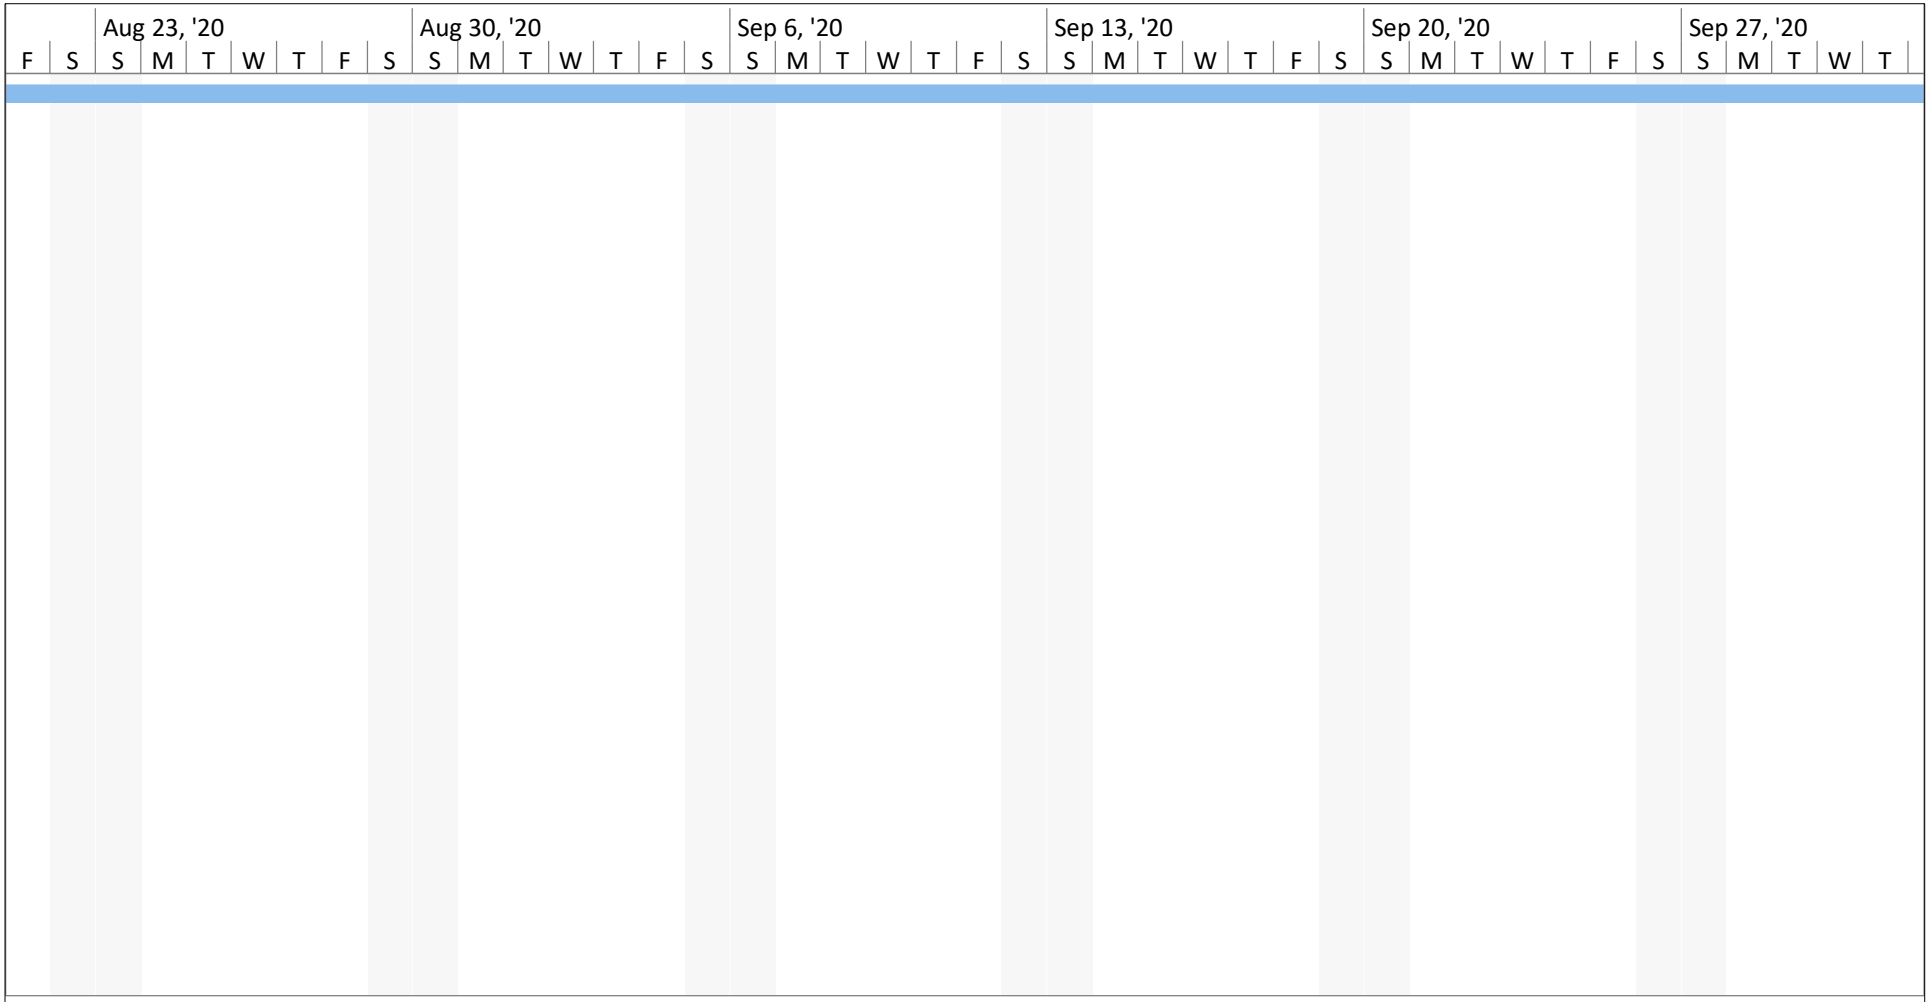


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |




Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

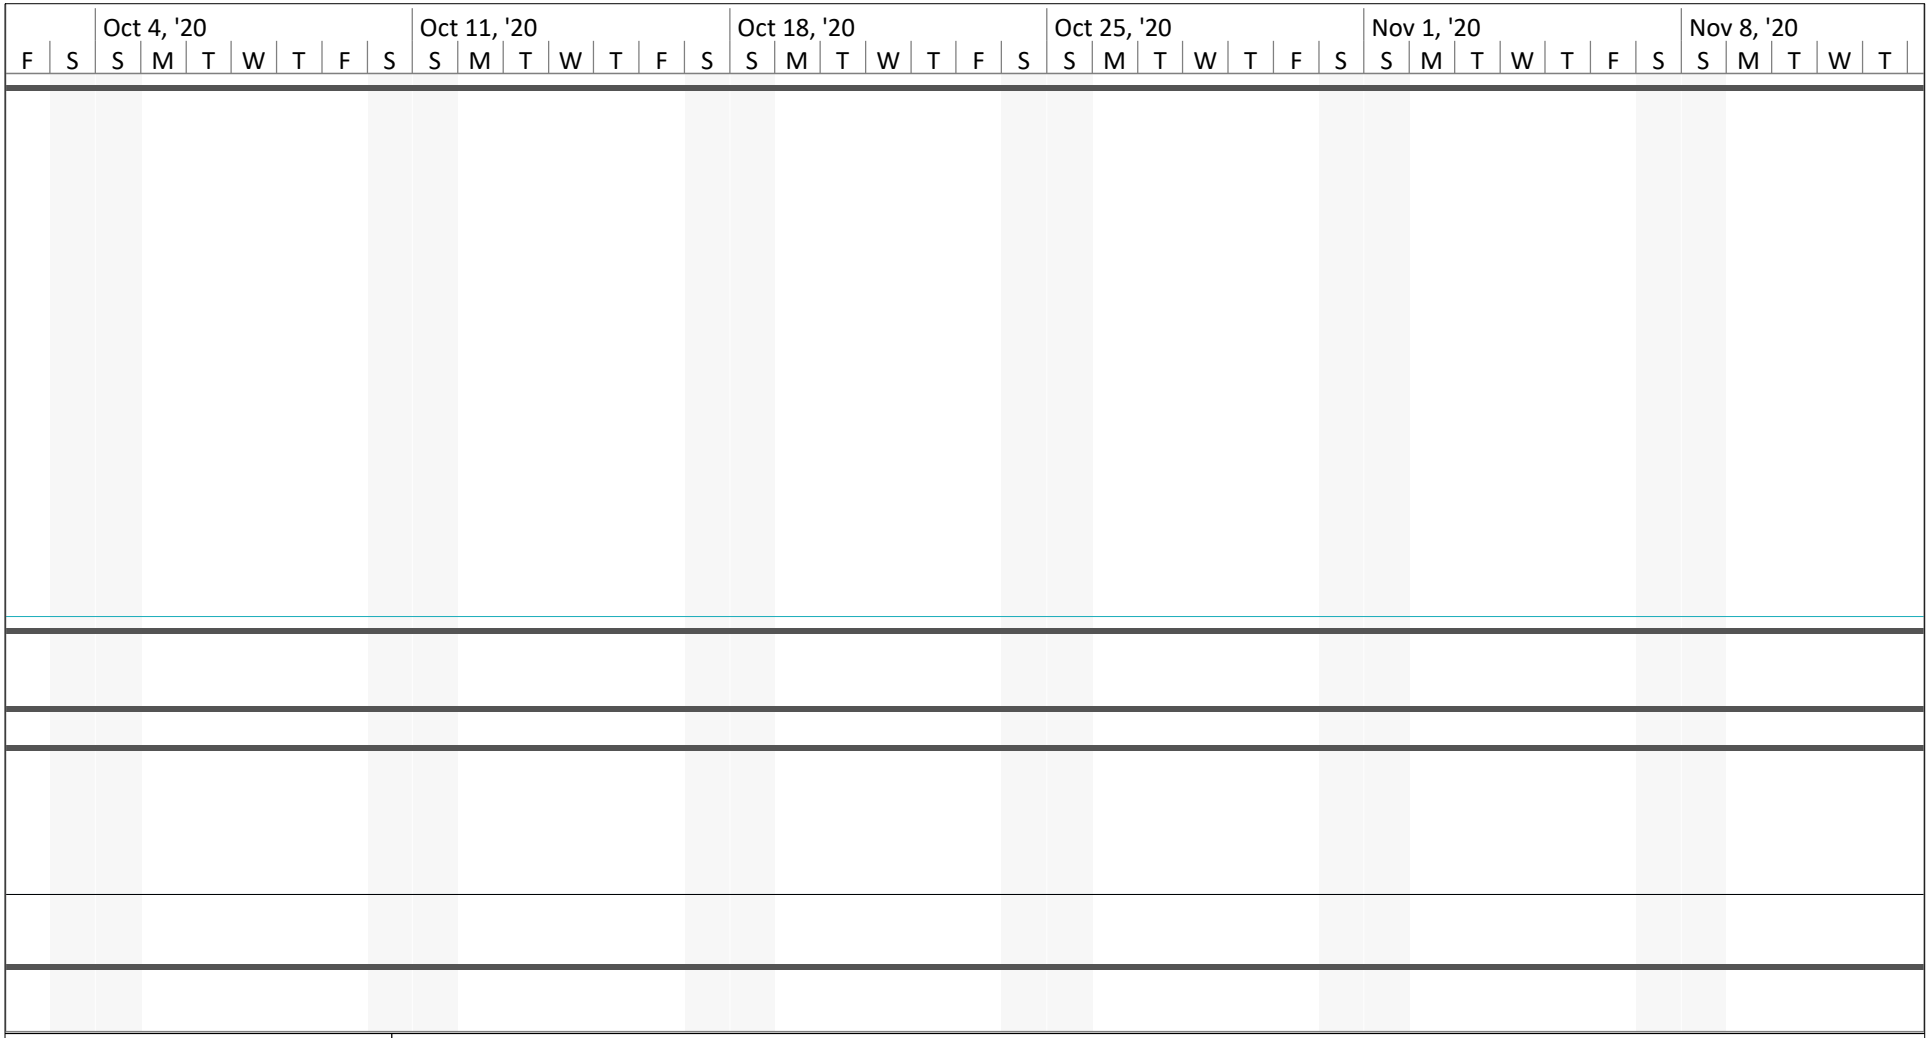


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

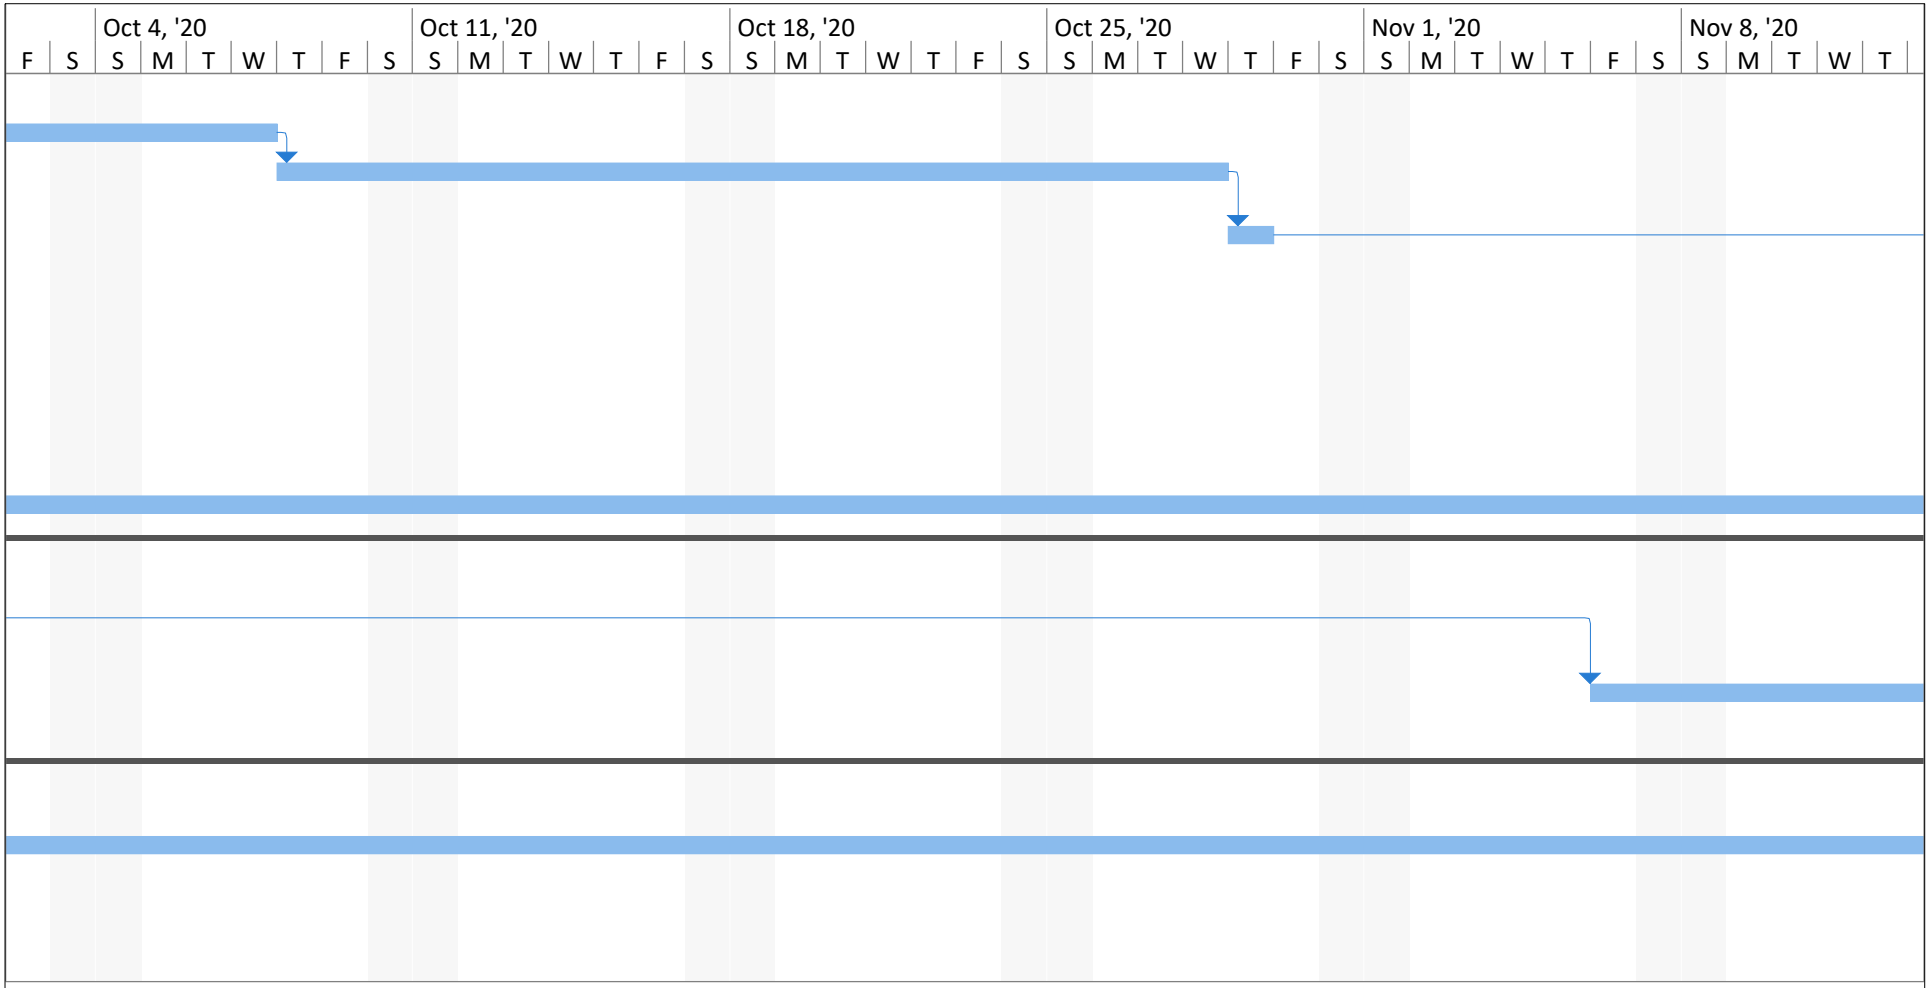


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

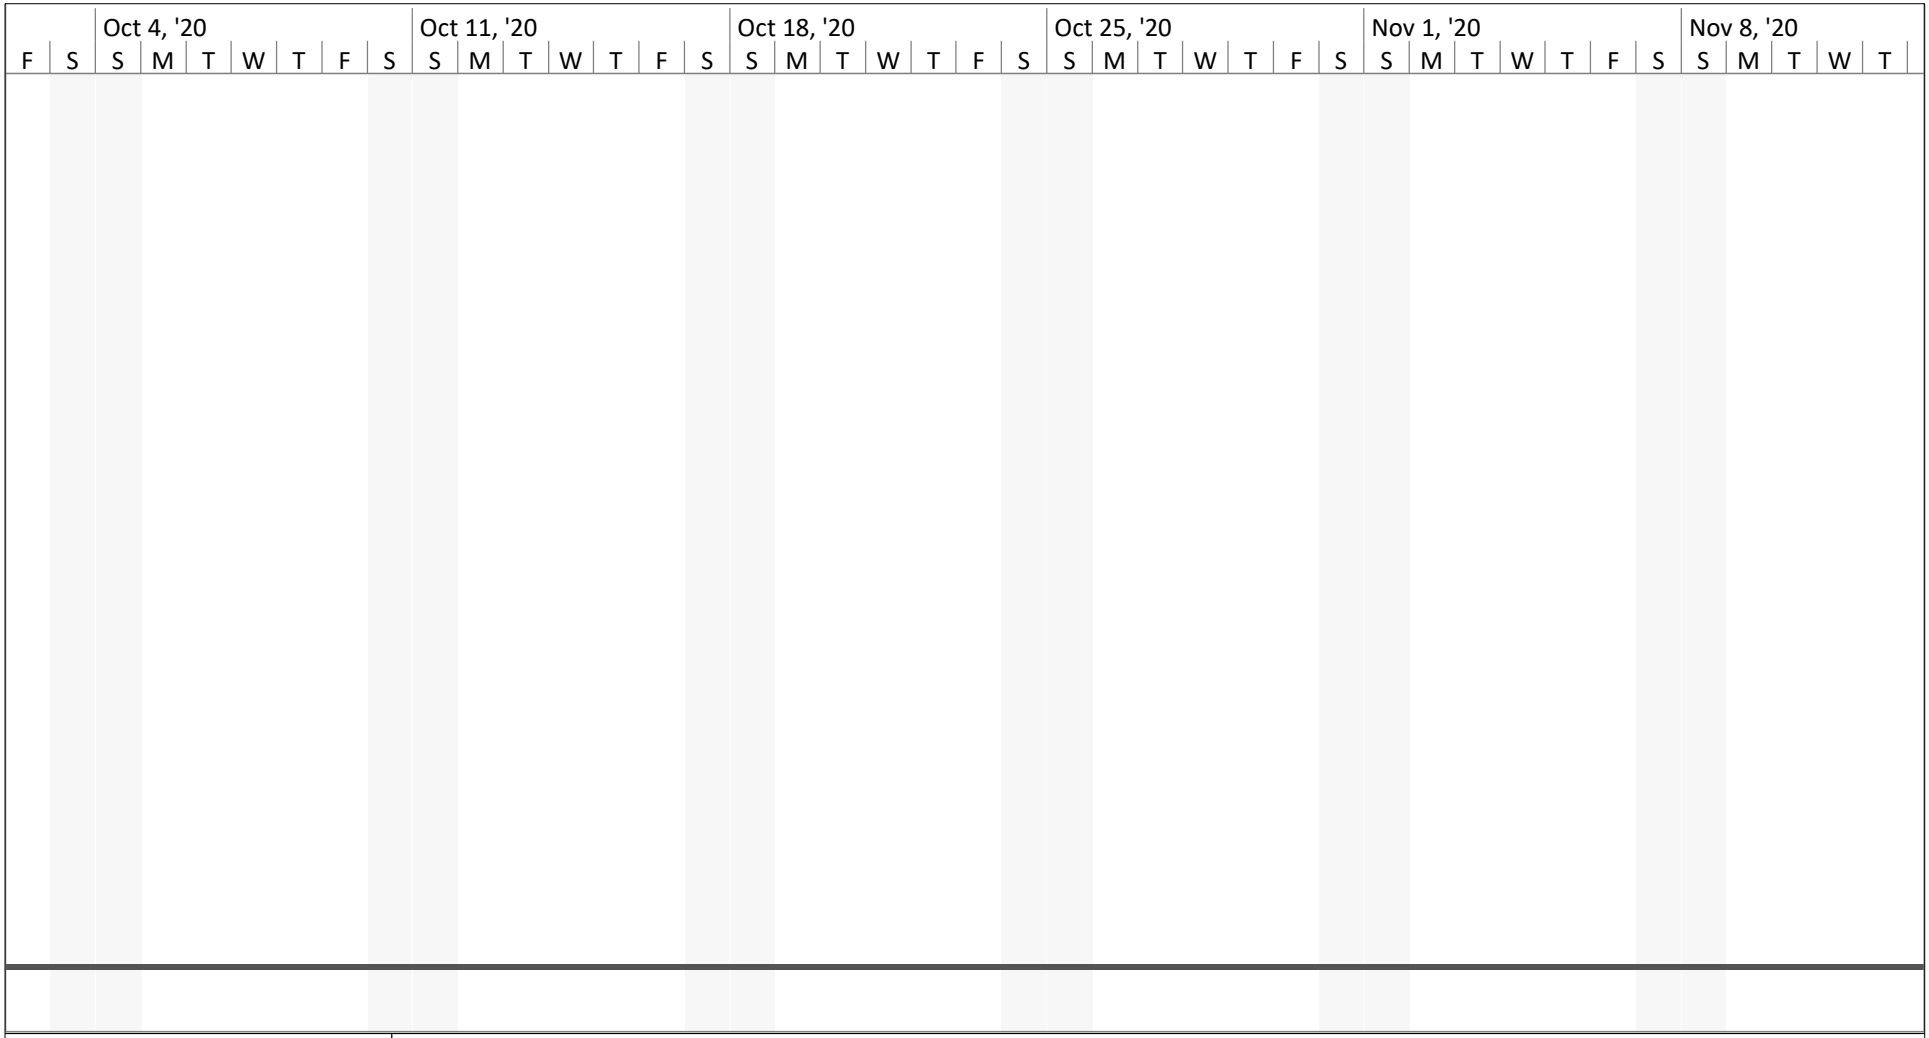


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

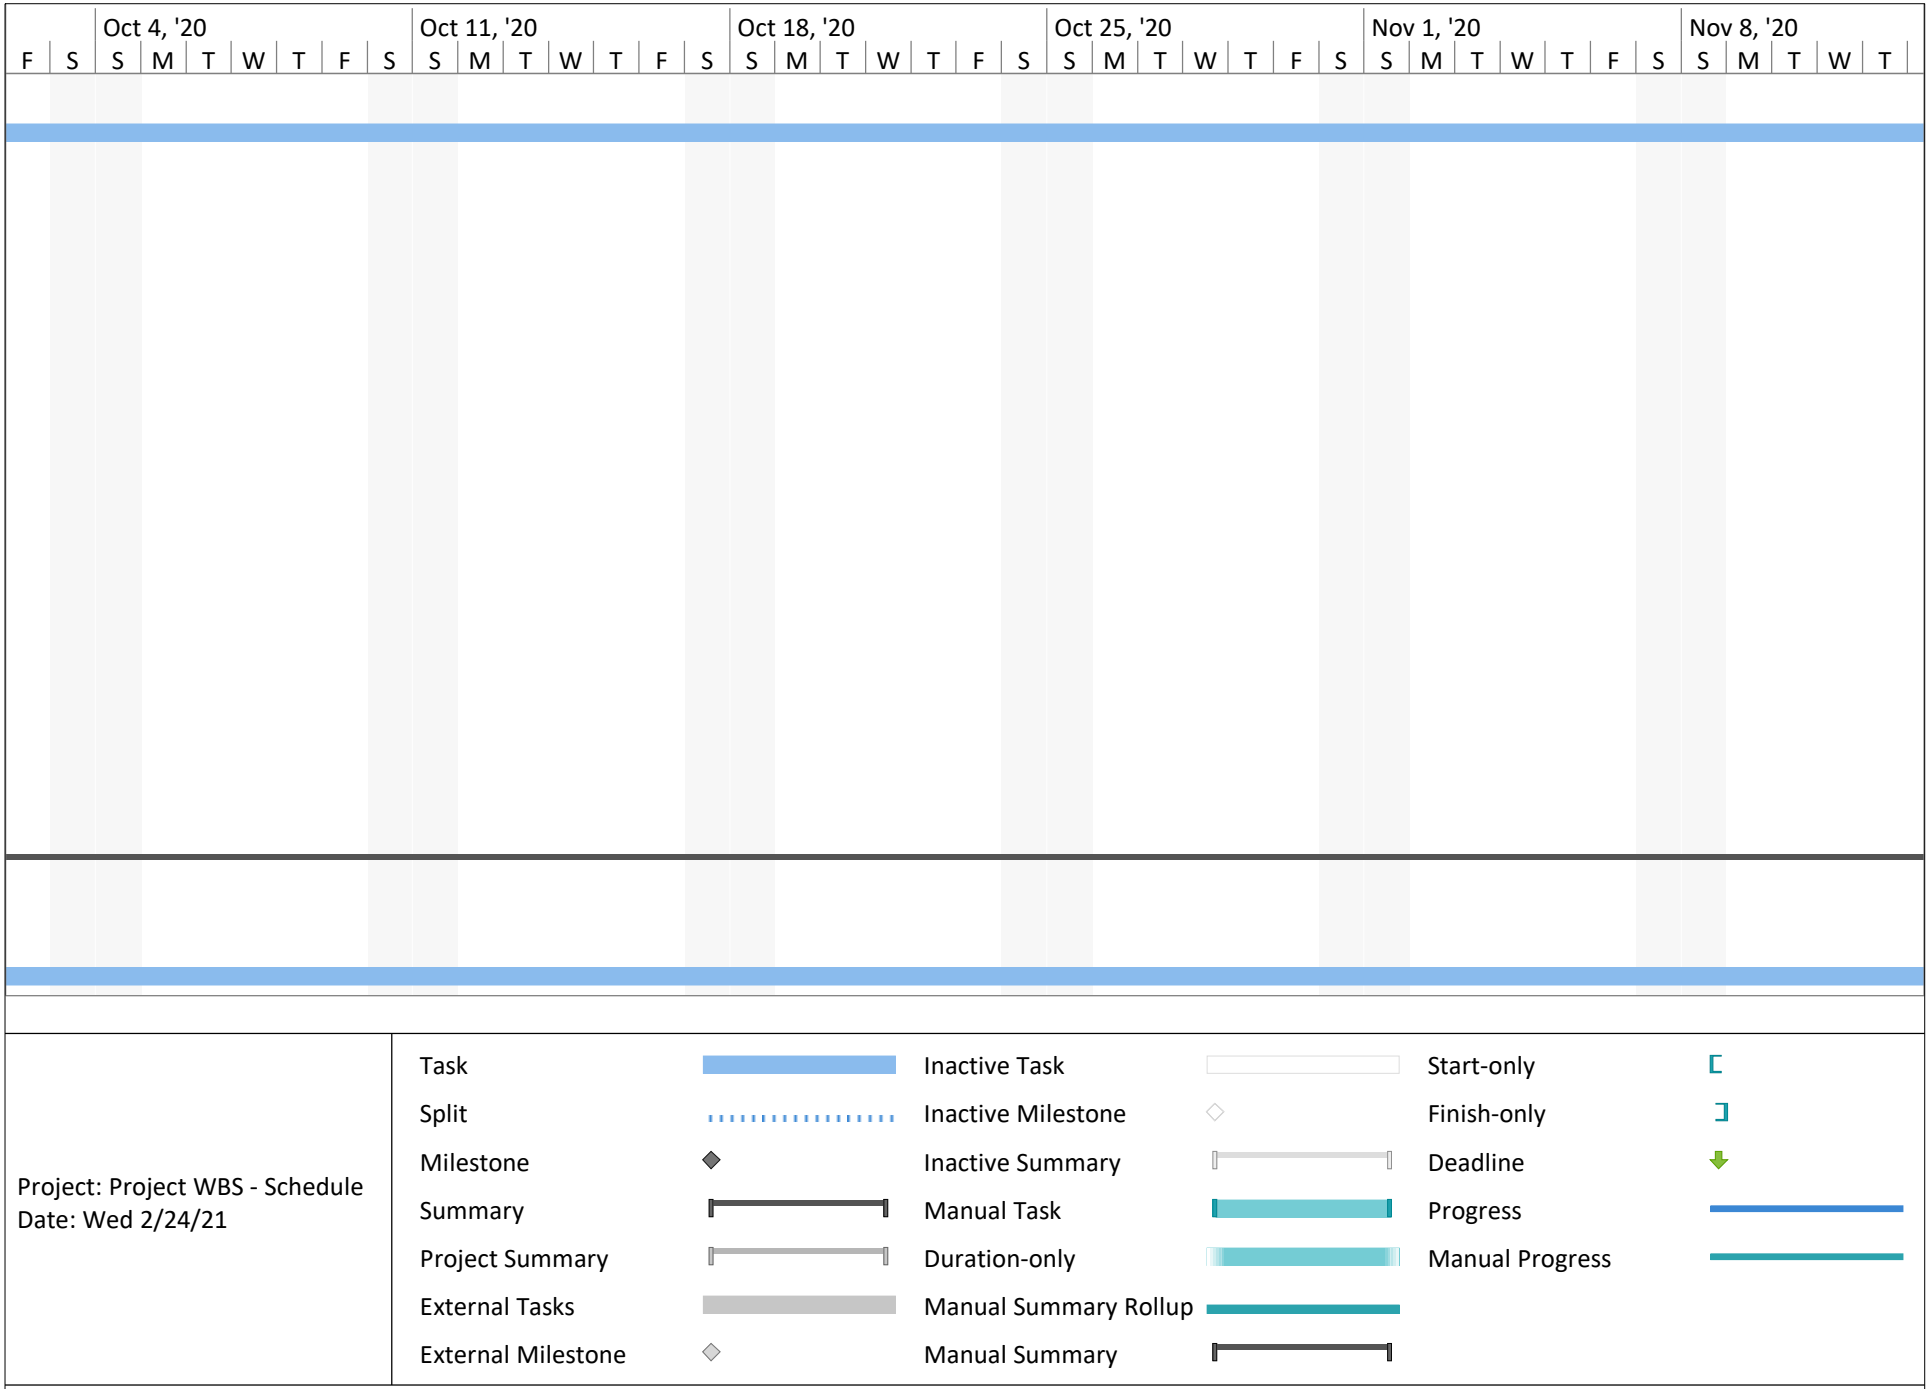
Oct 4, '20
Oct 11, '20
Oct 18, '20
Oct 25, '20
Nov 1, '20
Nov 8, '20
F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T
Project: Project WBS - Schedule
Date: Wed 2/24/21
Task
Split
Milestone
Summary
Project Summary
External Tasks
External Milestone
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
Deadline
Progress
Manual Progress

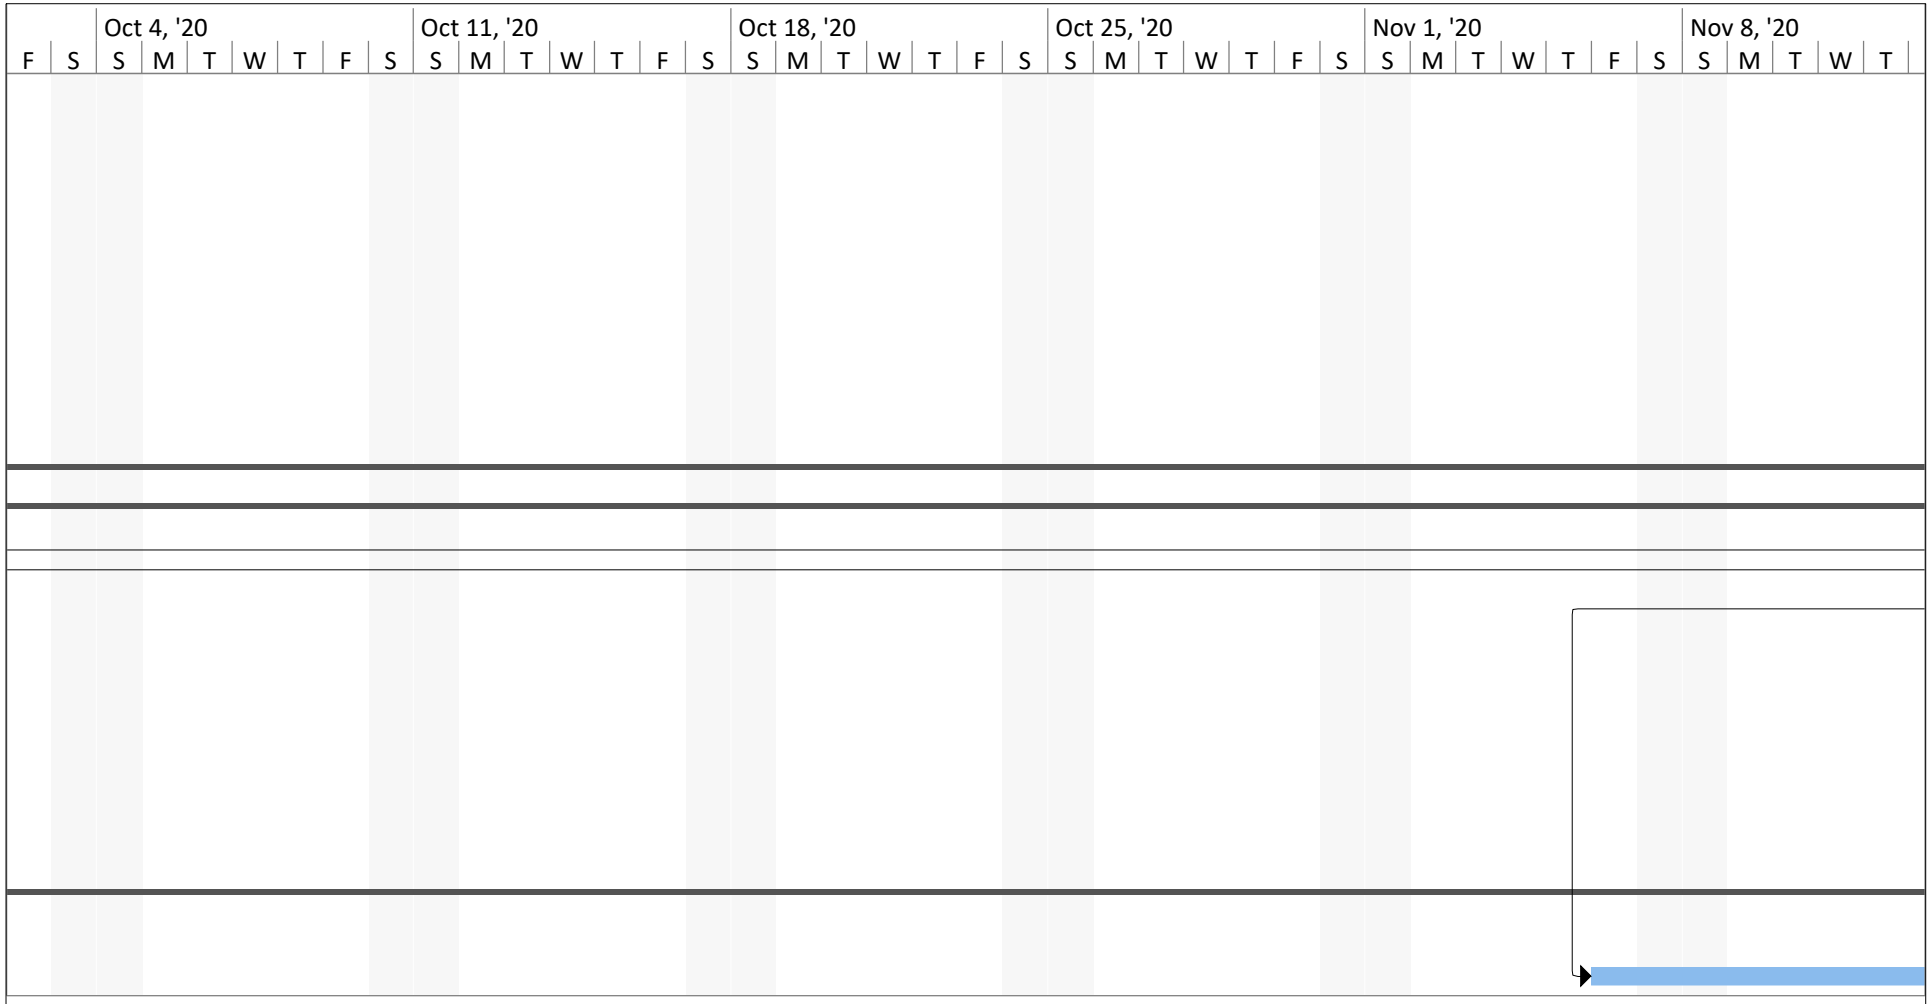


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

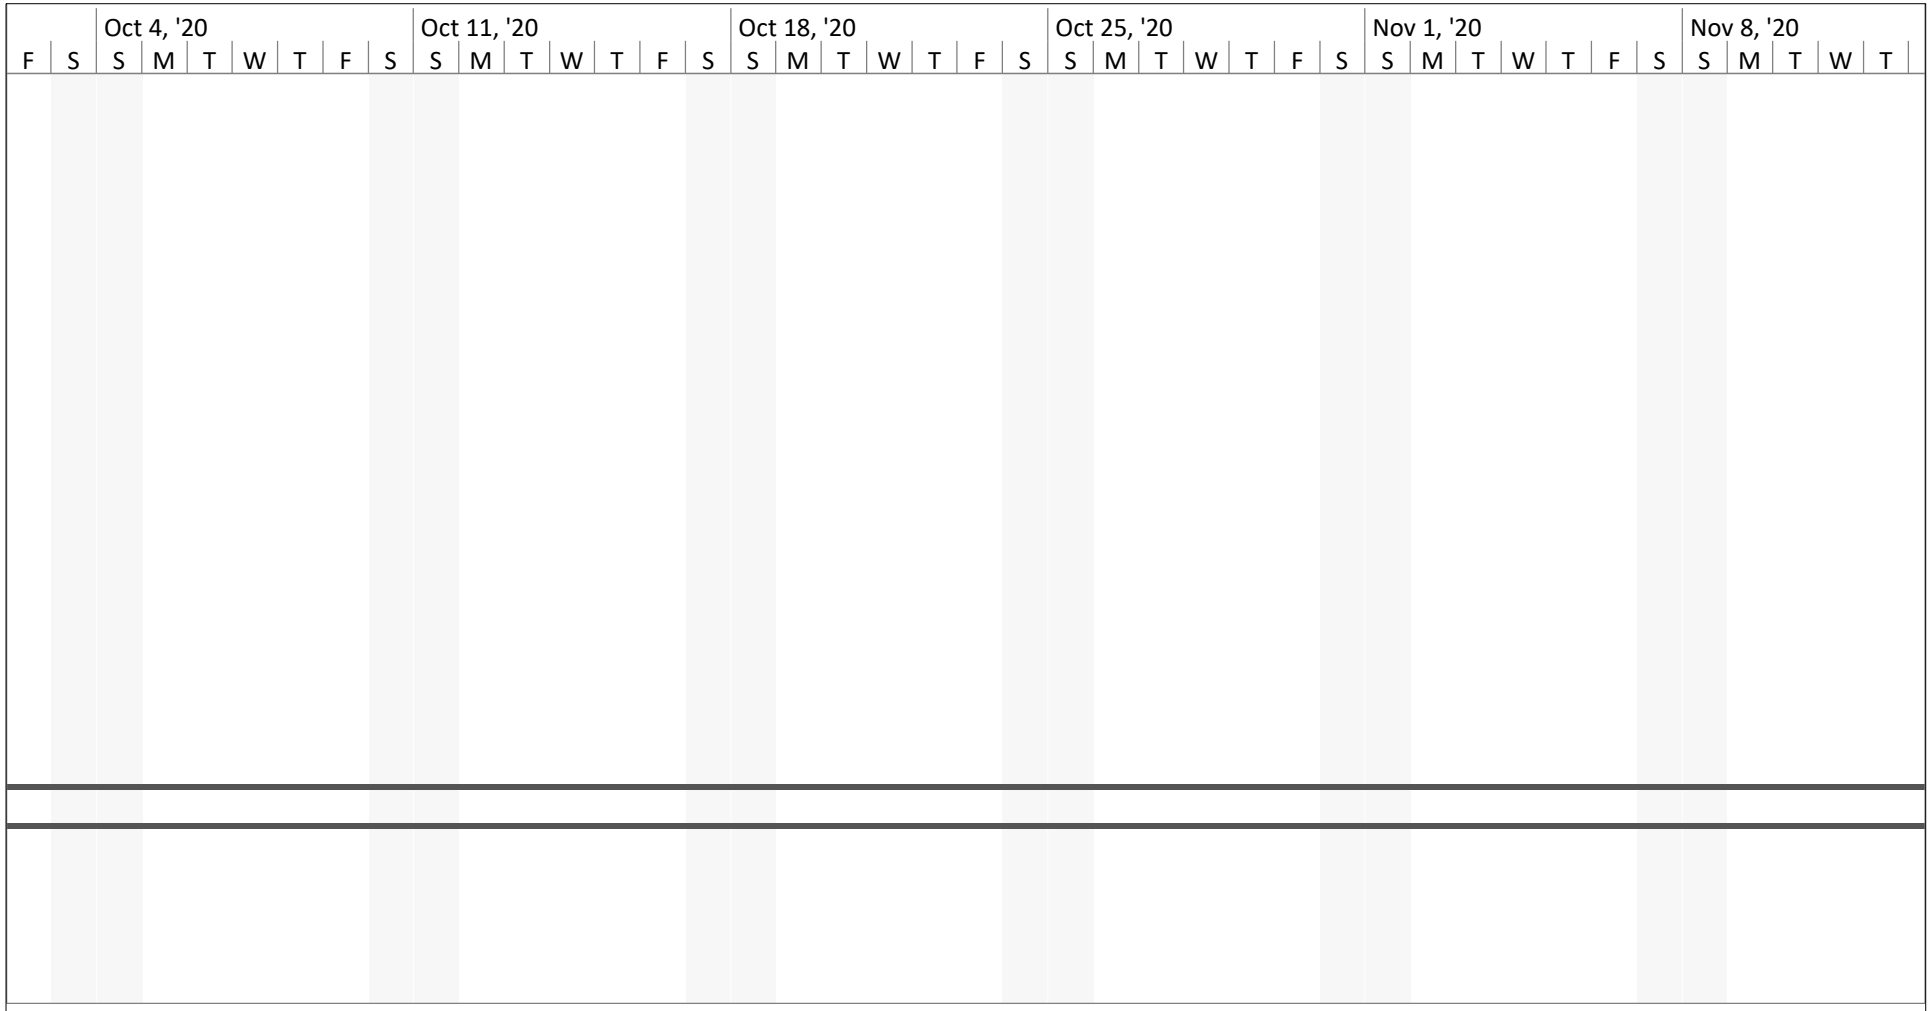


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

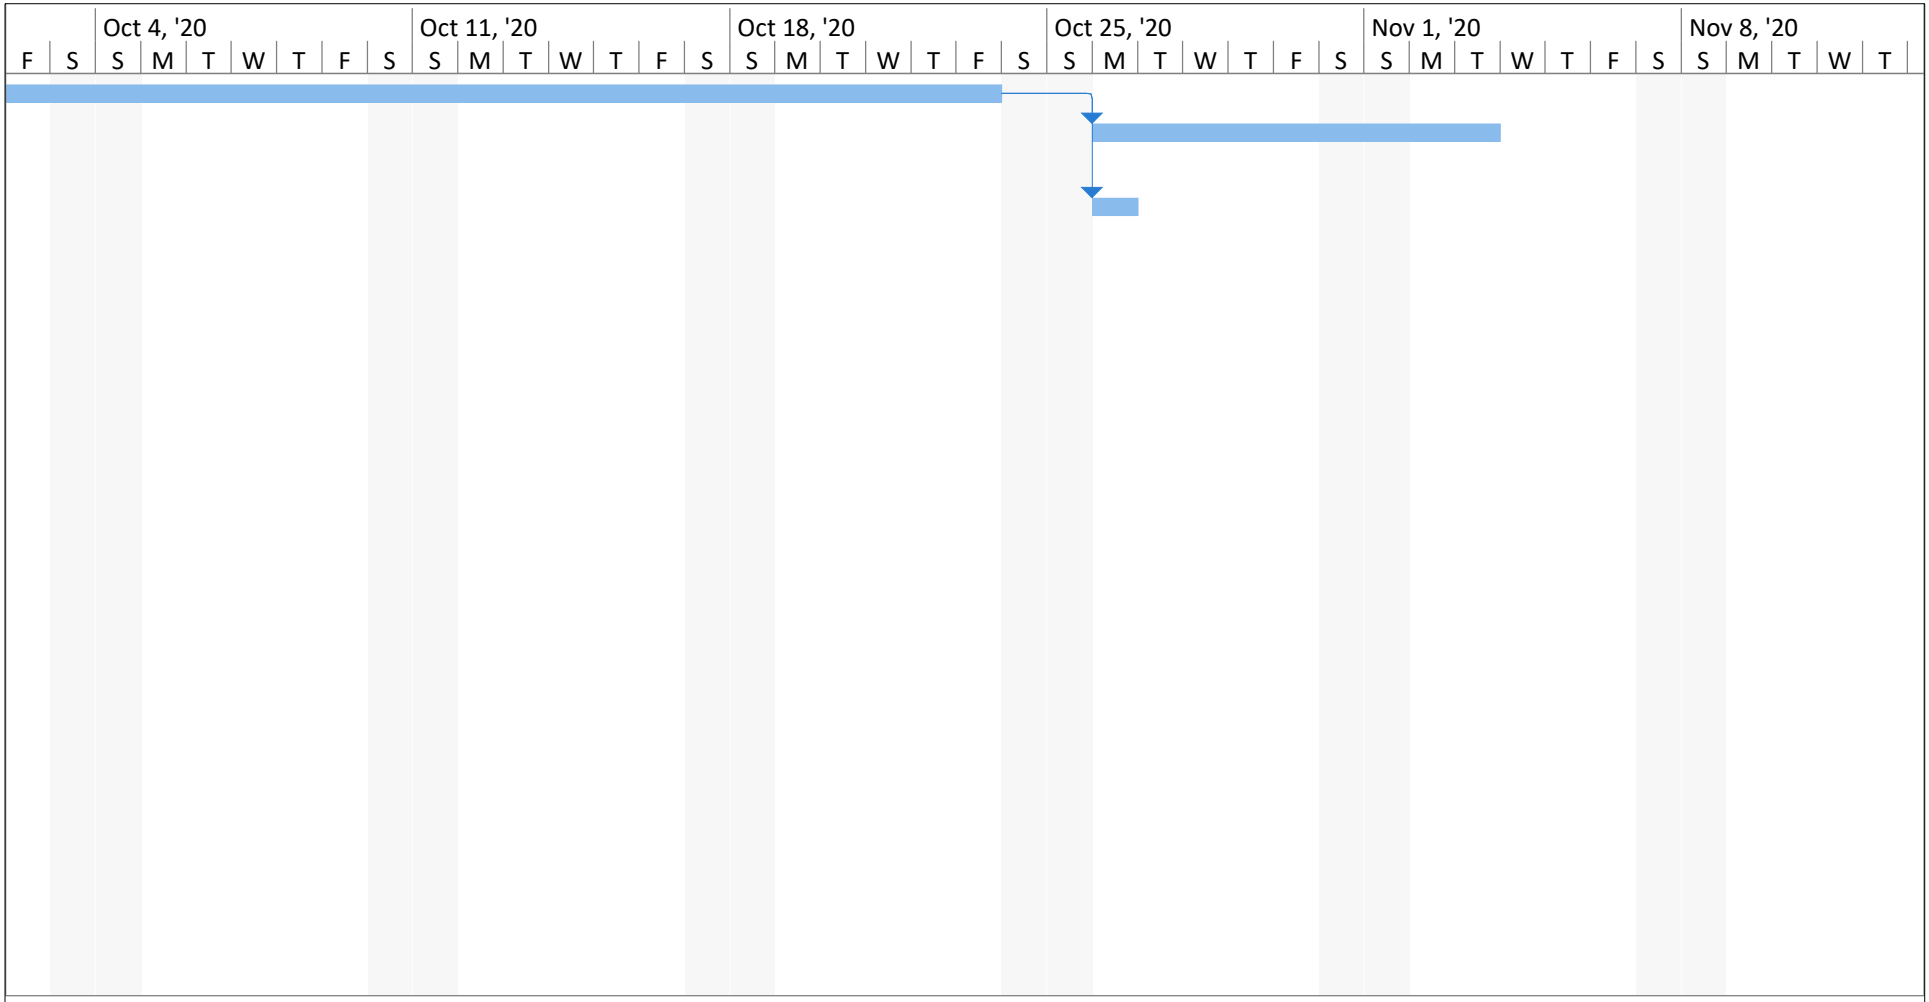


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |




Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

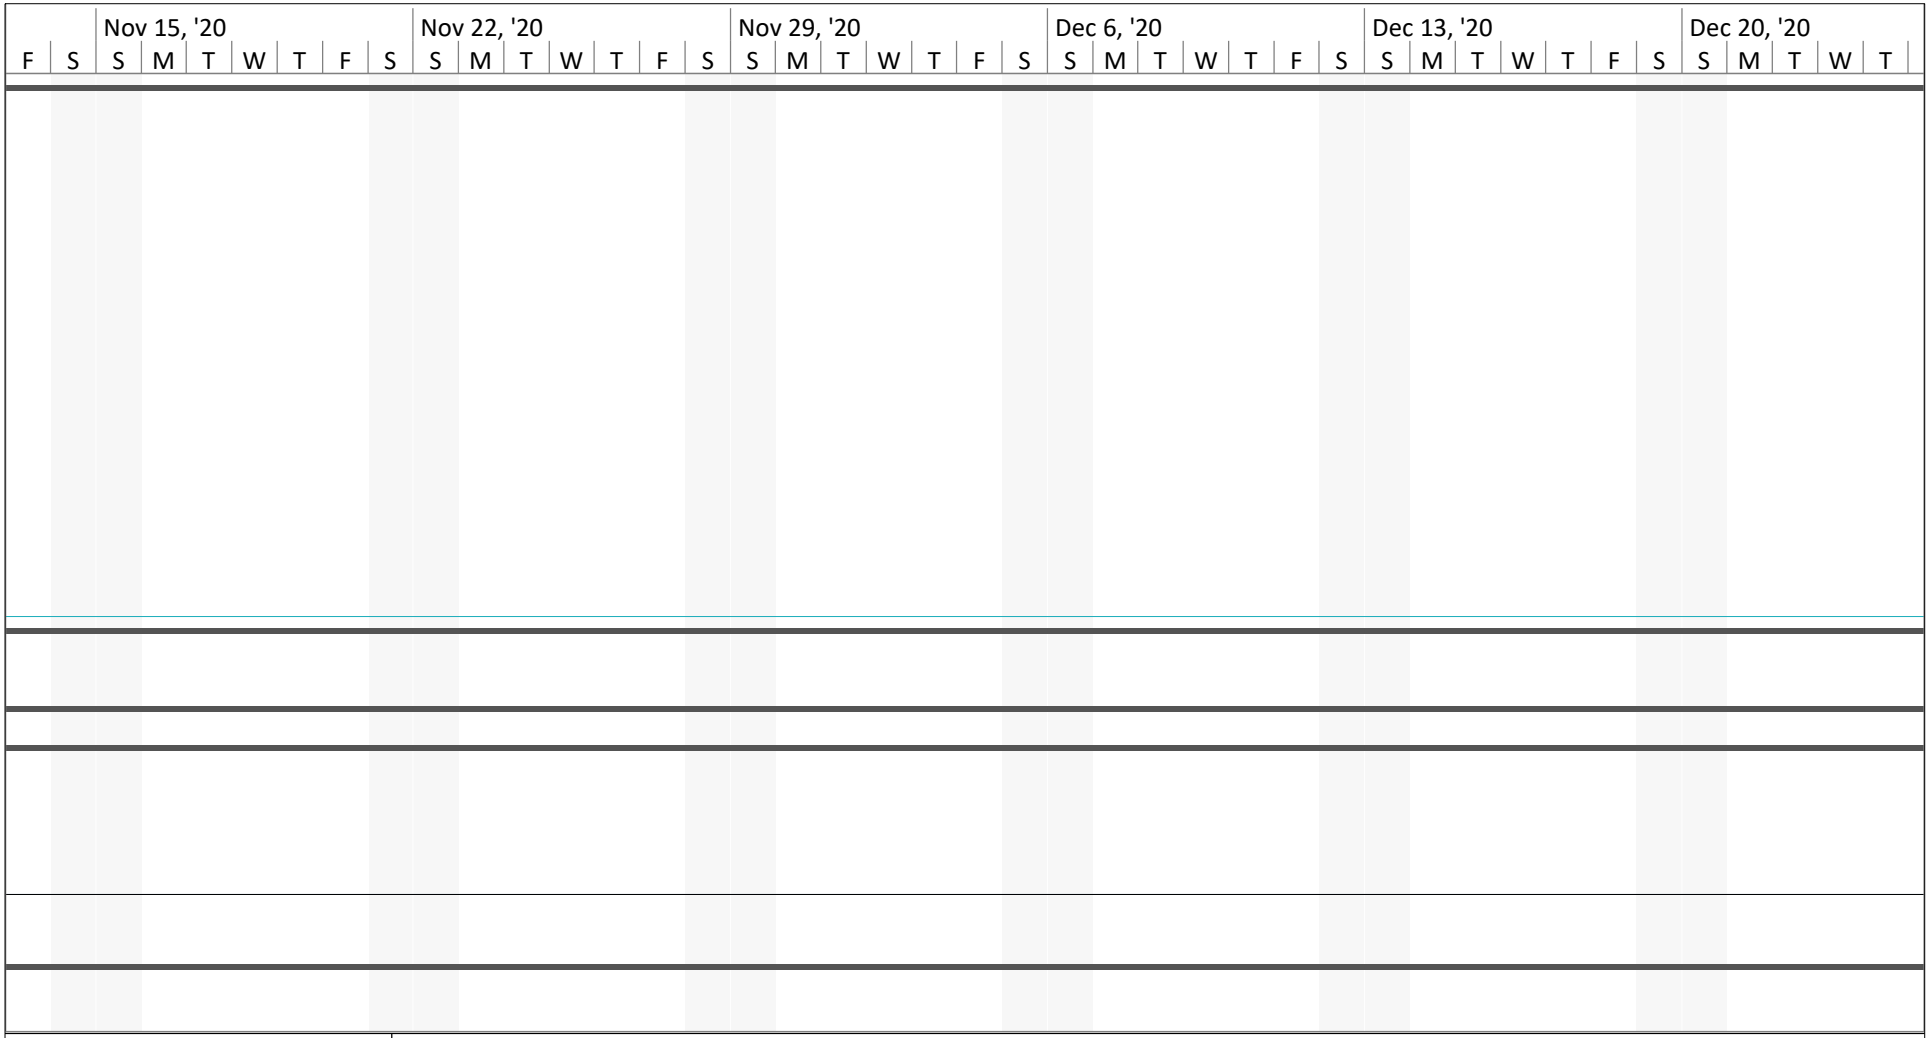


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

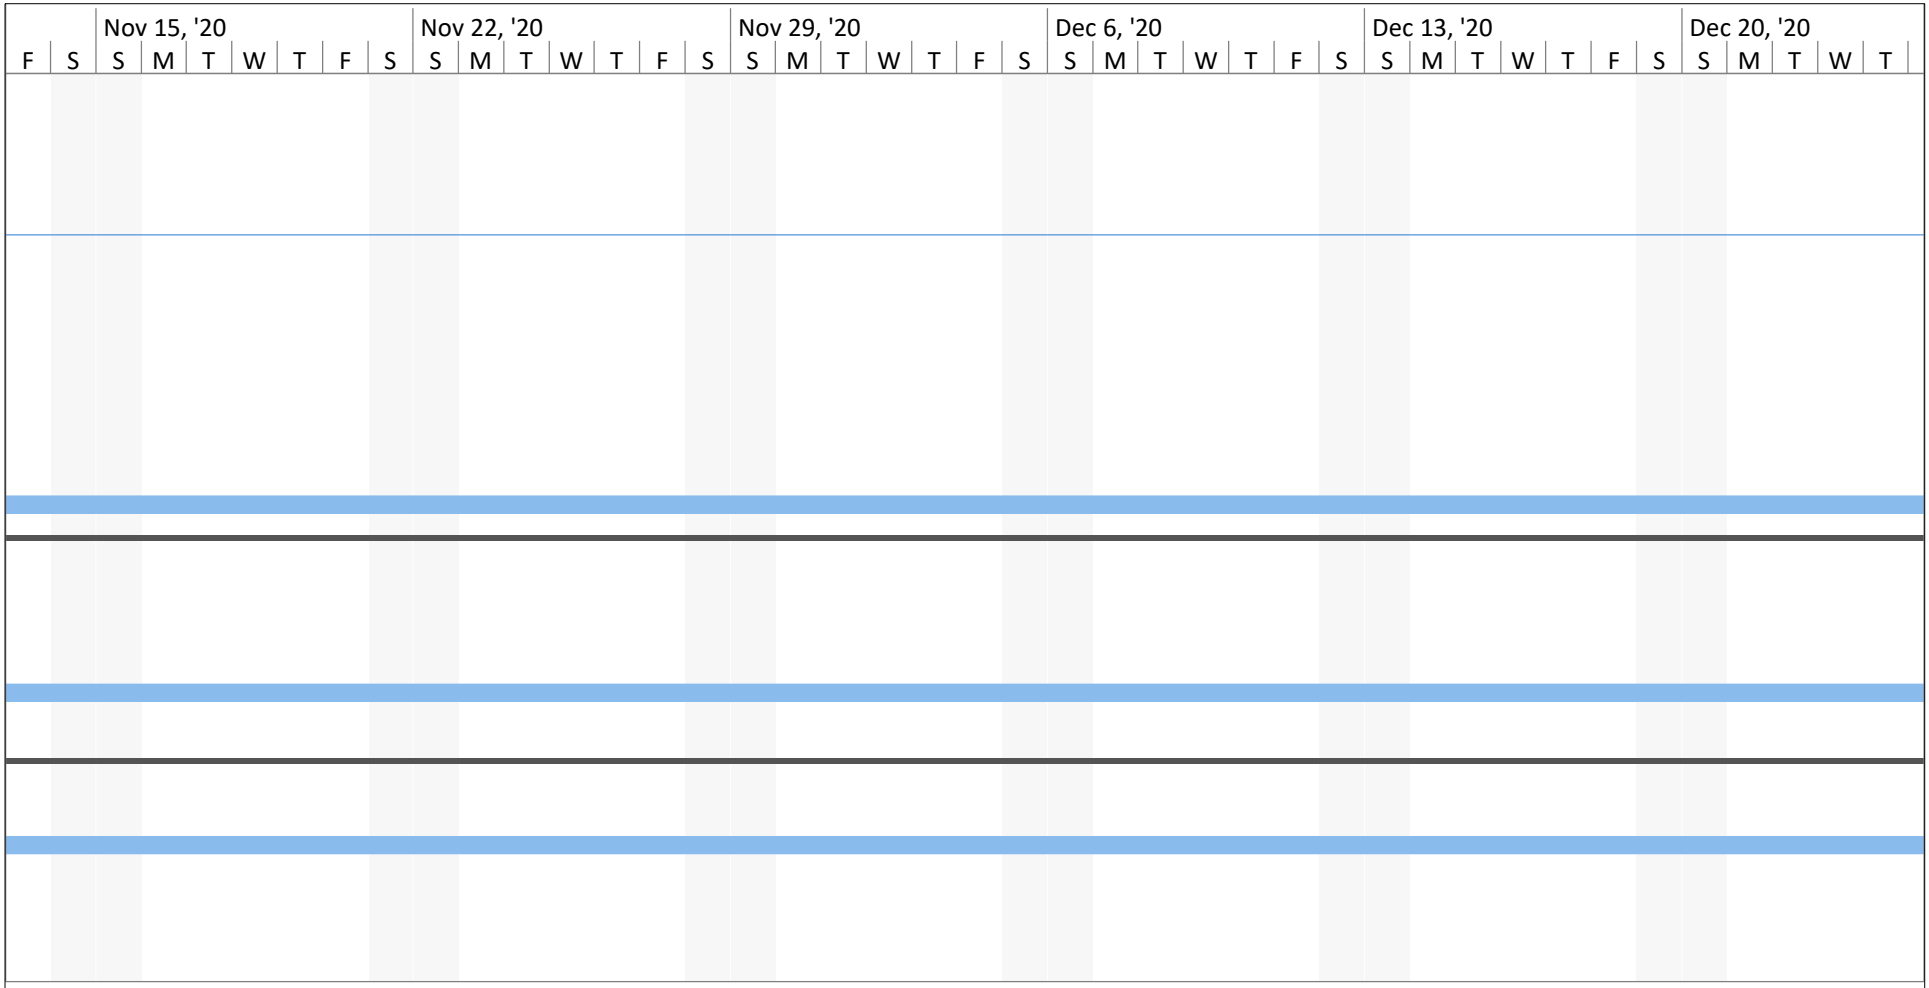


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

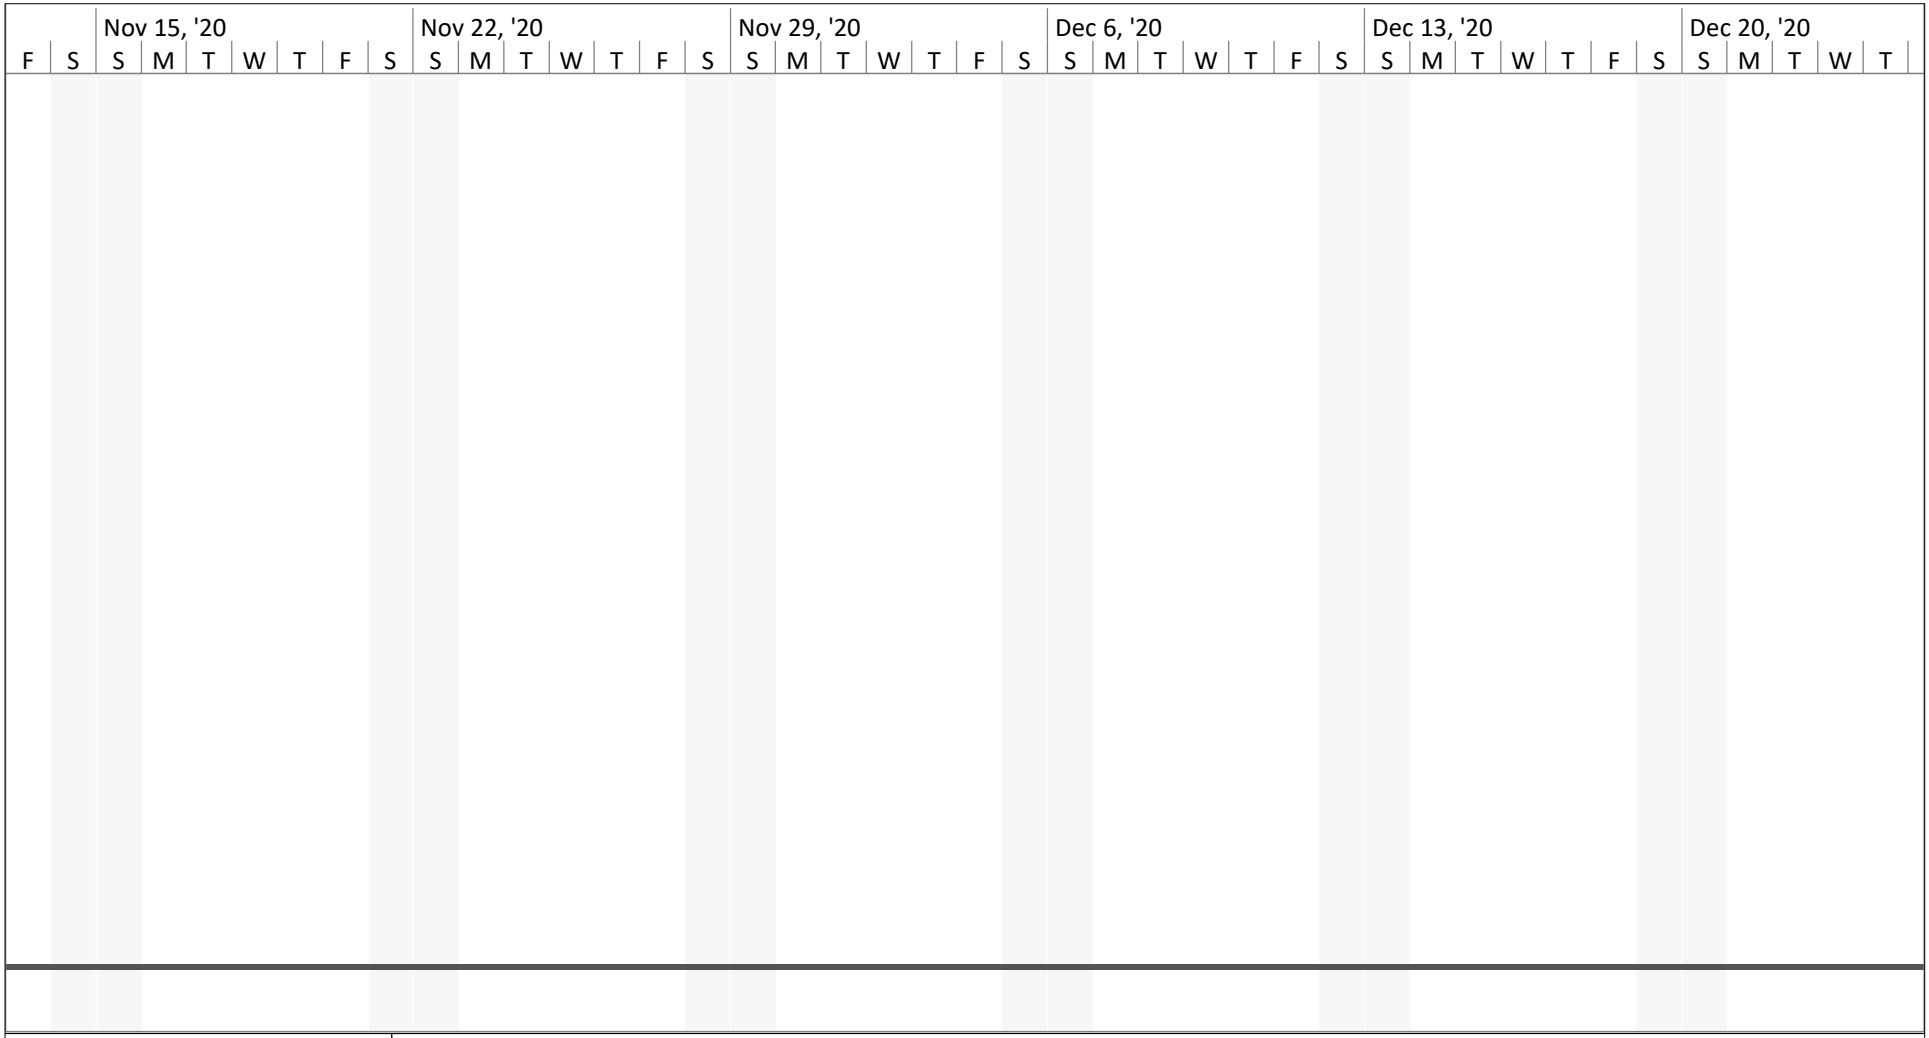


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

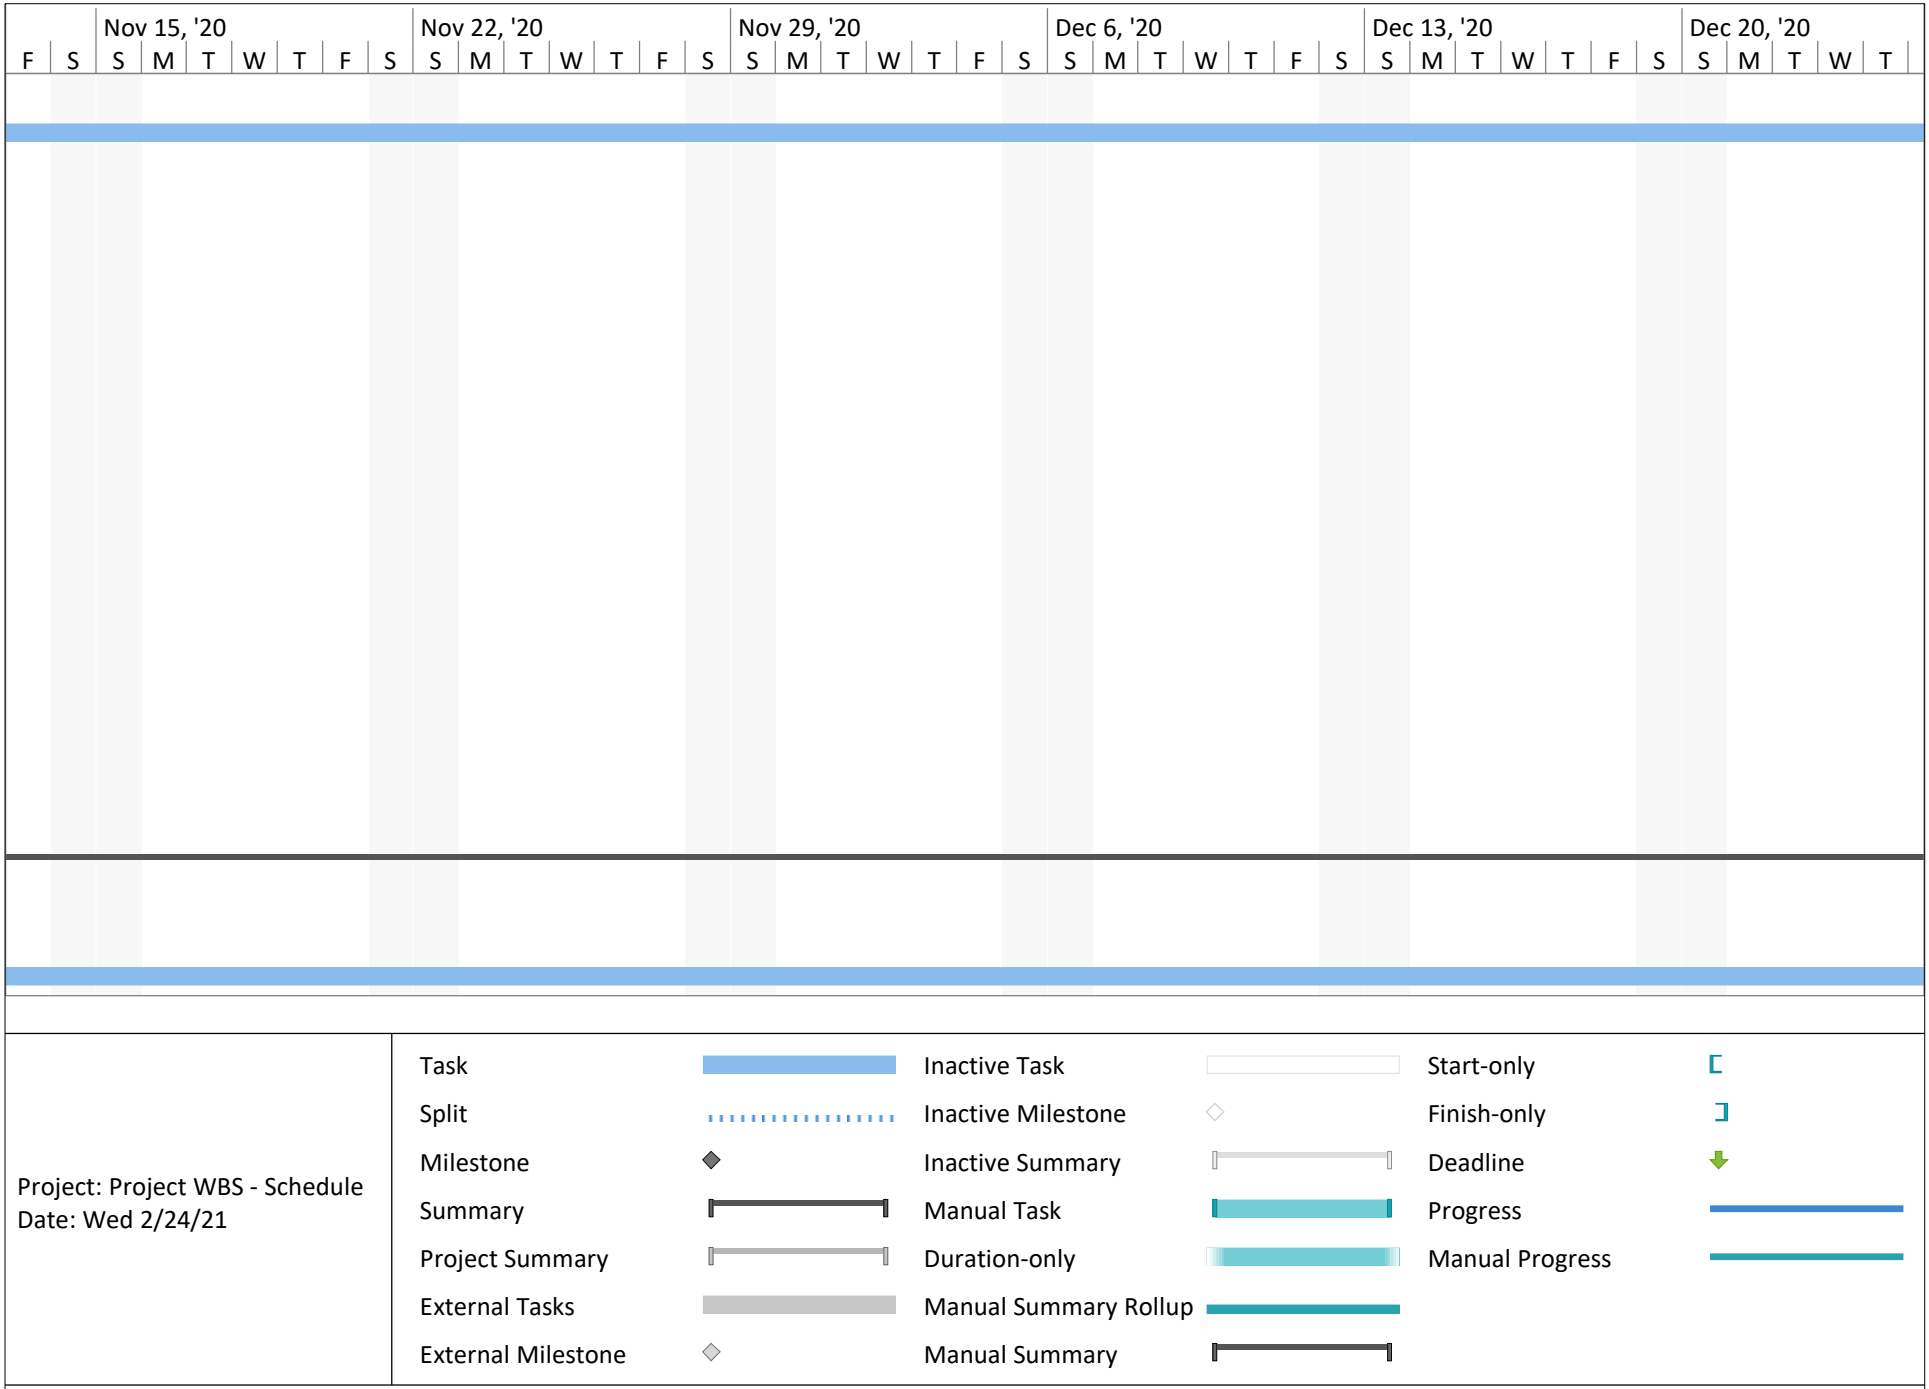
Nov 15, '20
Nov 22, '20
Nov 29, '20
Dec 6, '20
Dec 13, '20
Dec 20, '20
F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T
Project: Project WBS - Schedule
Date: Wed 2/24/21
Task
Split
Milestone
Summary
Project Summary
External Tasks
External Milestone
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
Deadline
Progress
Manual Progress

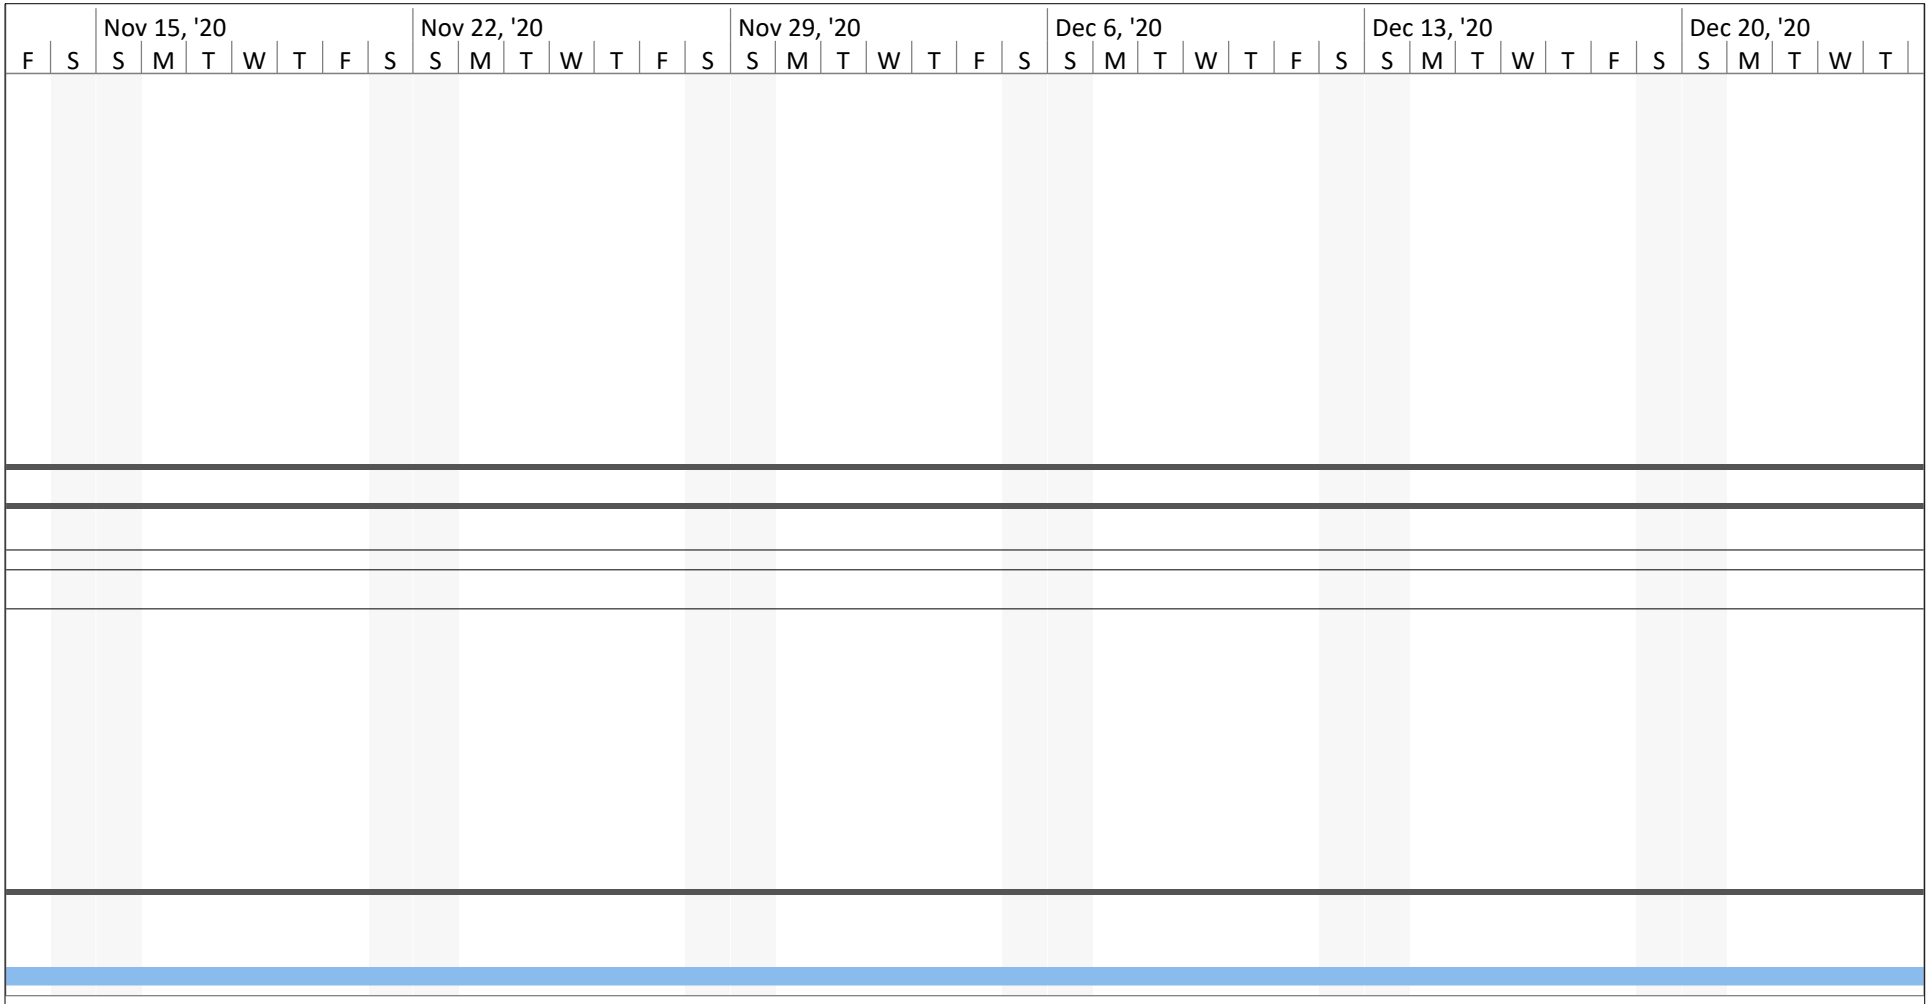


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

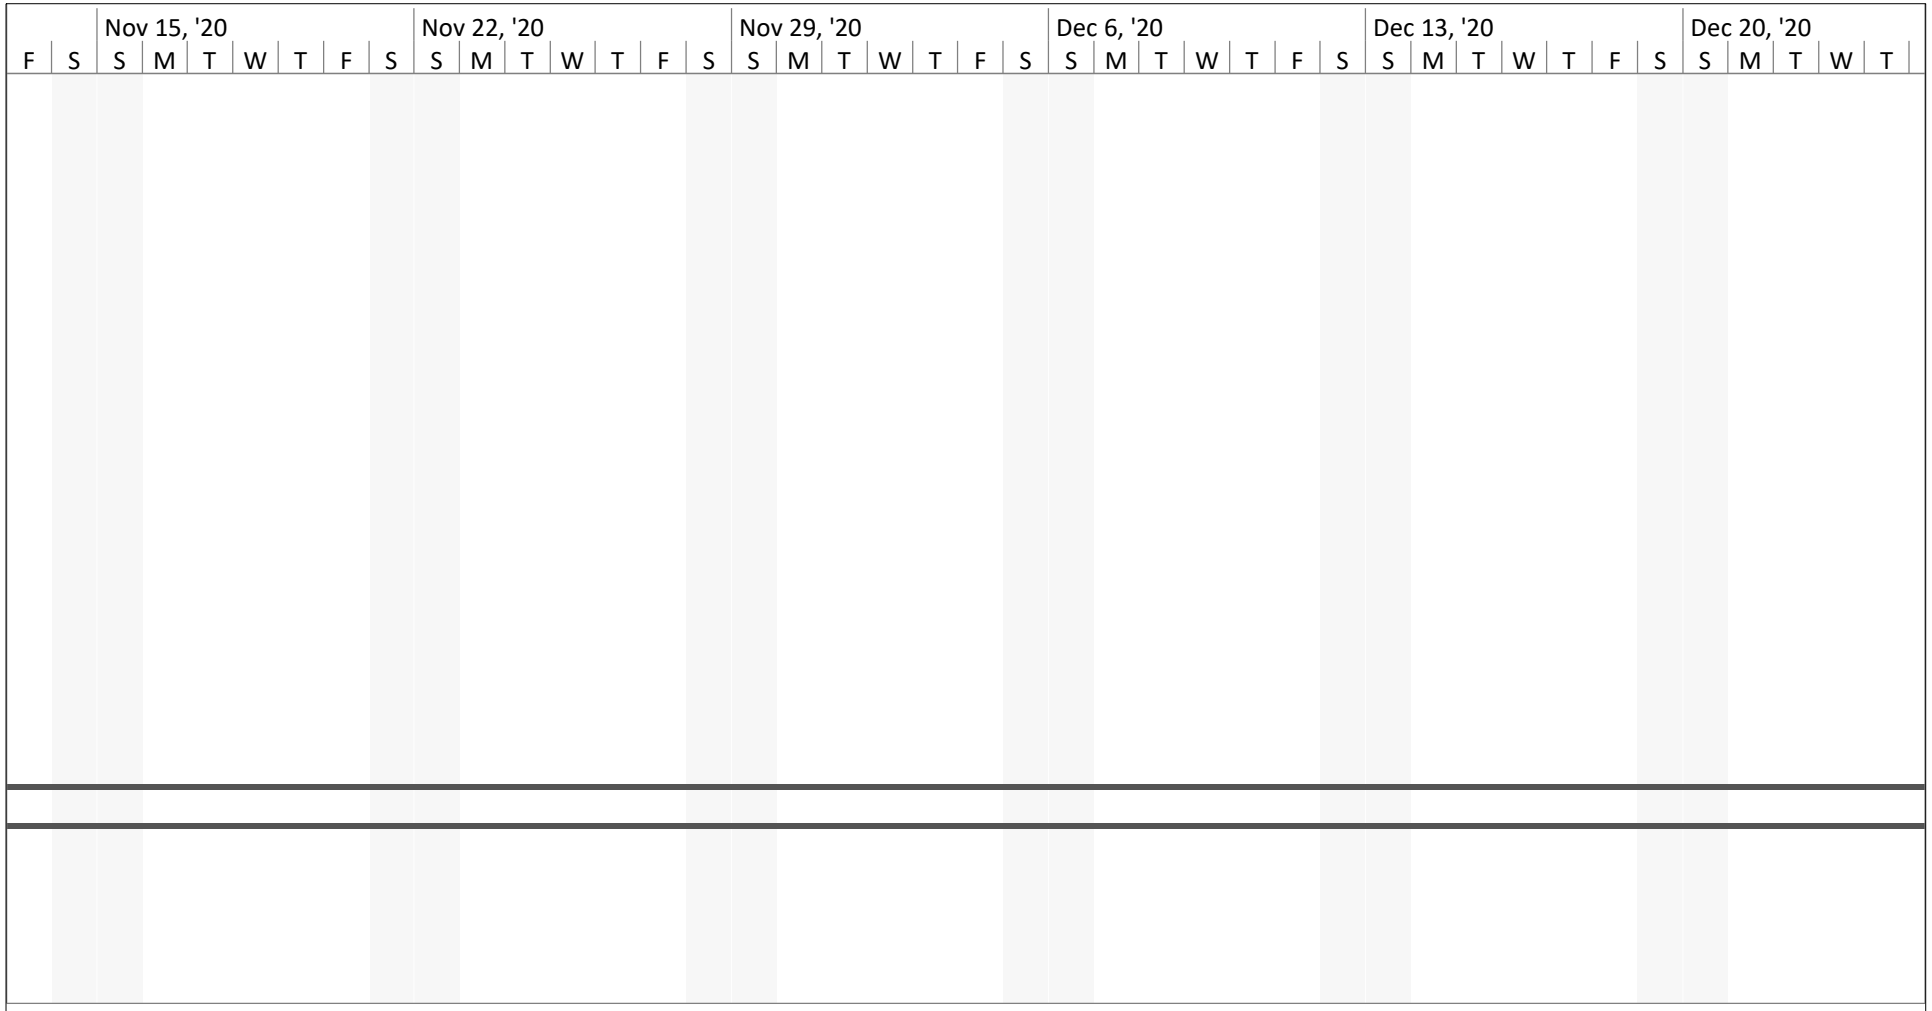


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

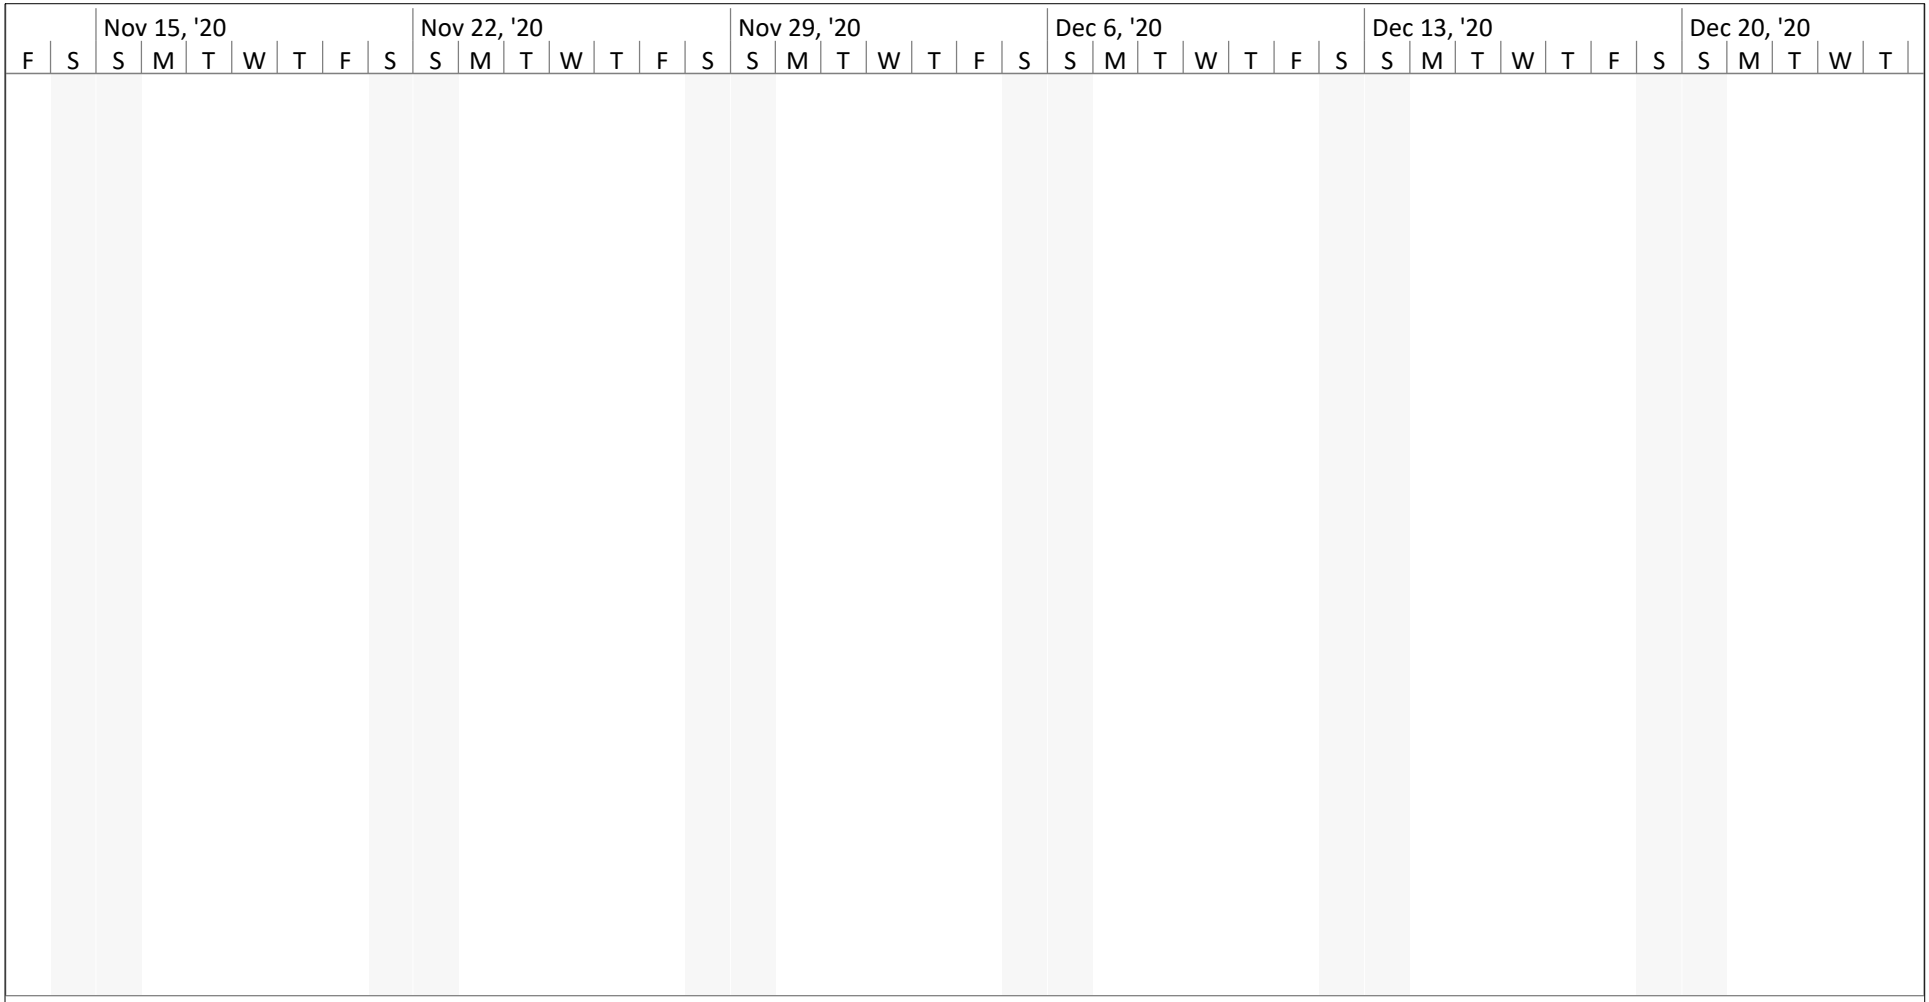


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |




Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

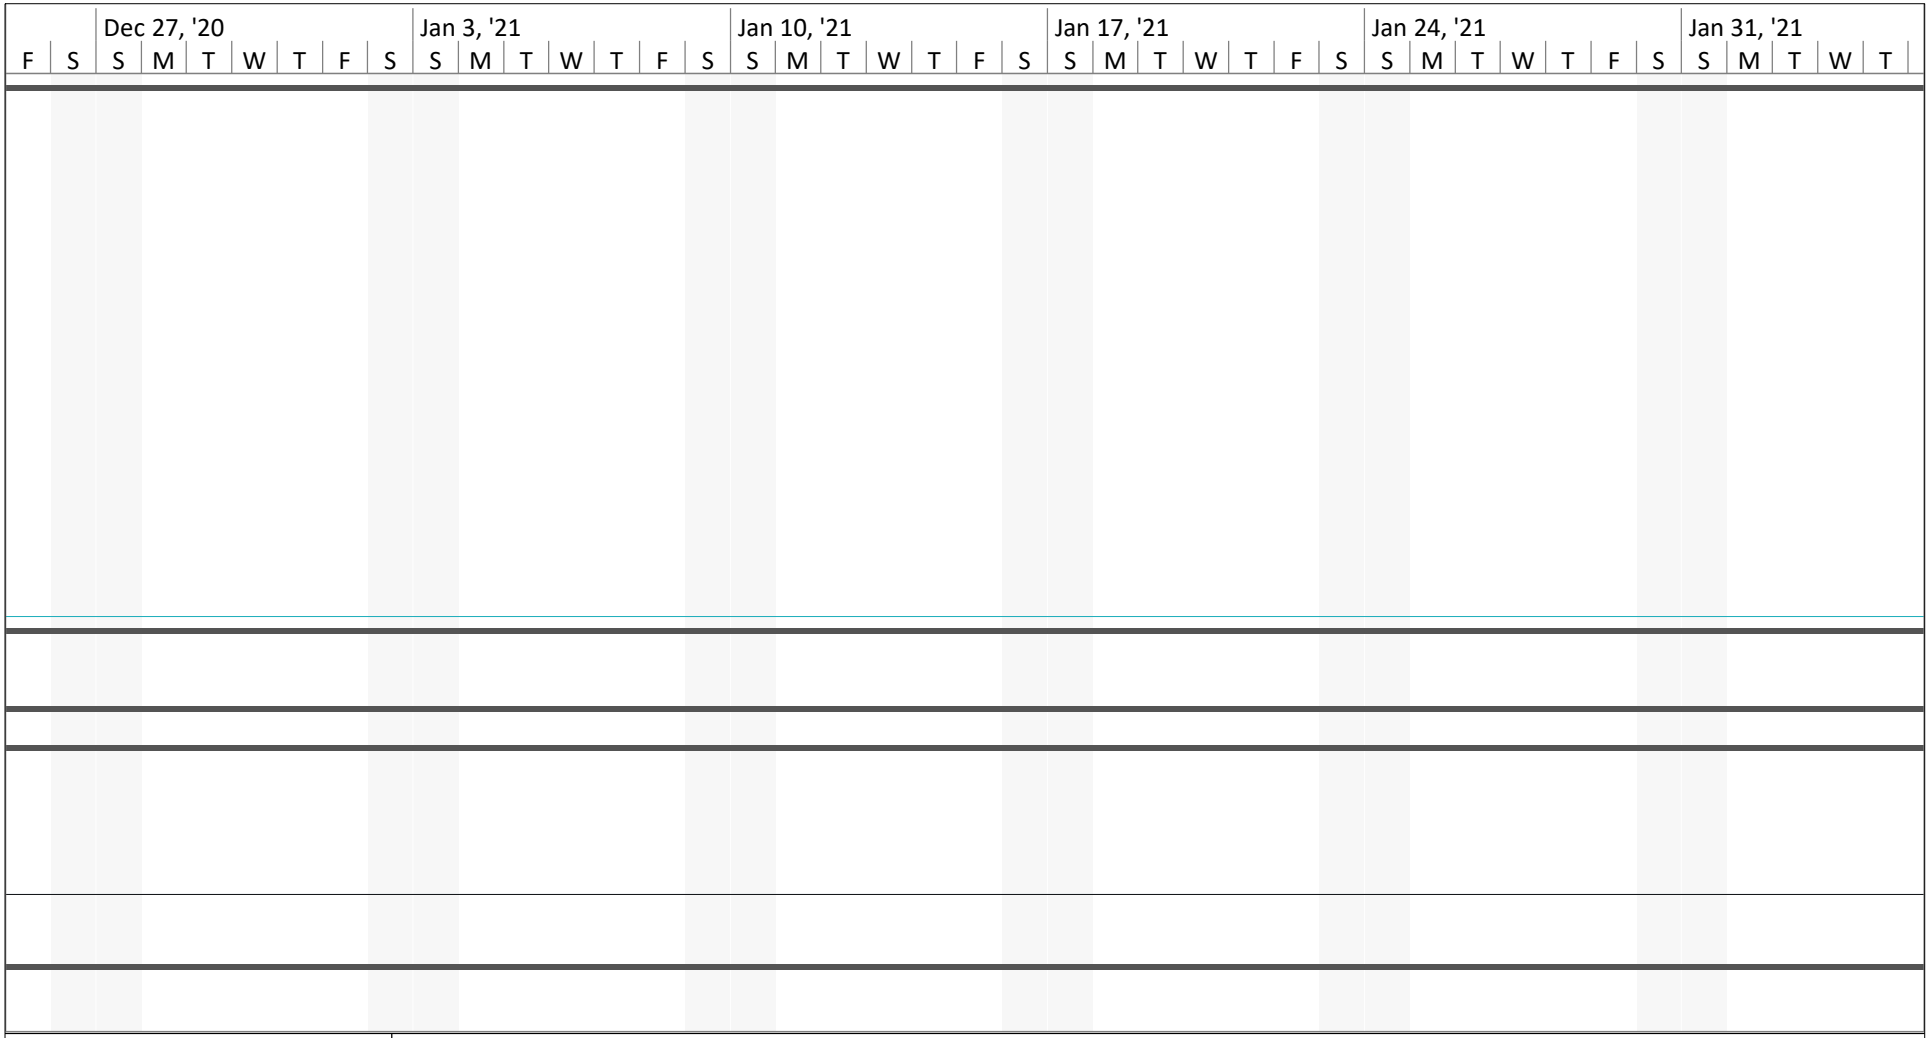


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

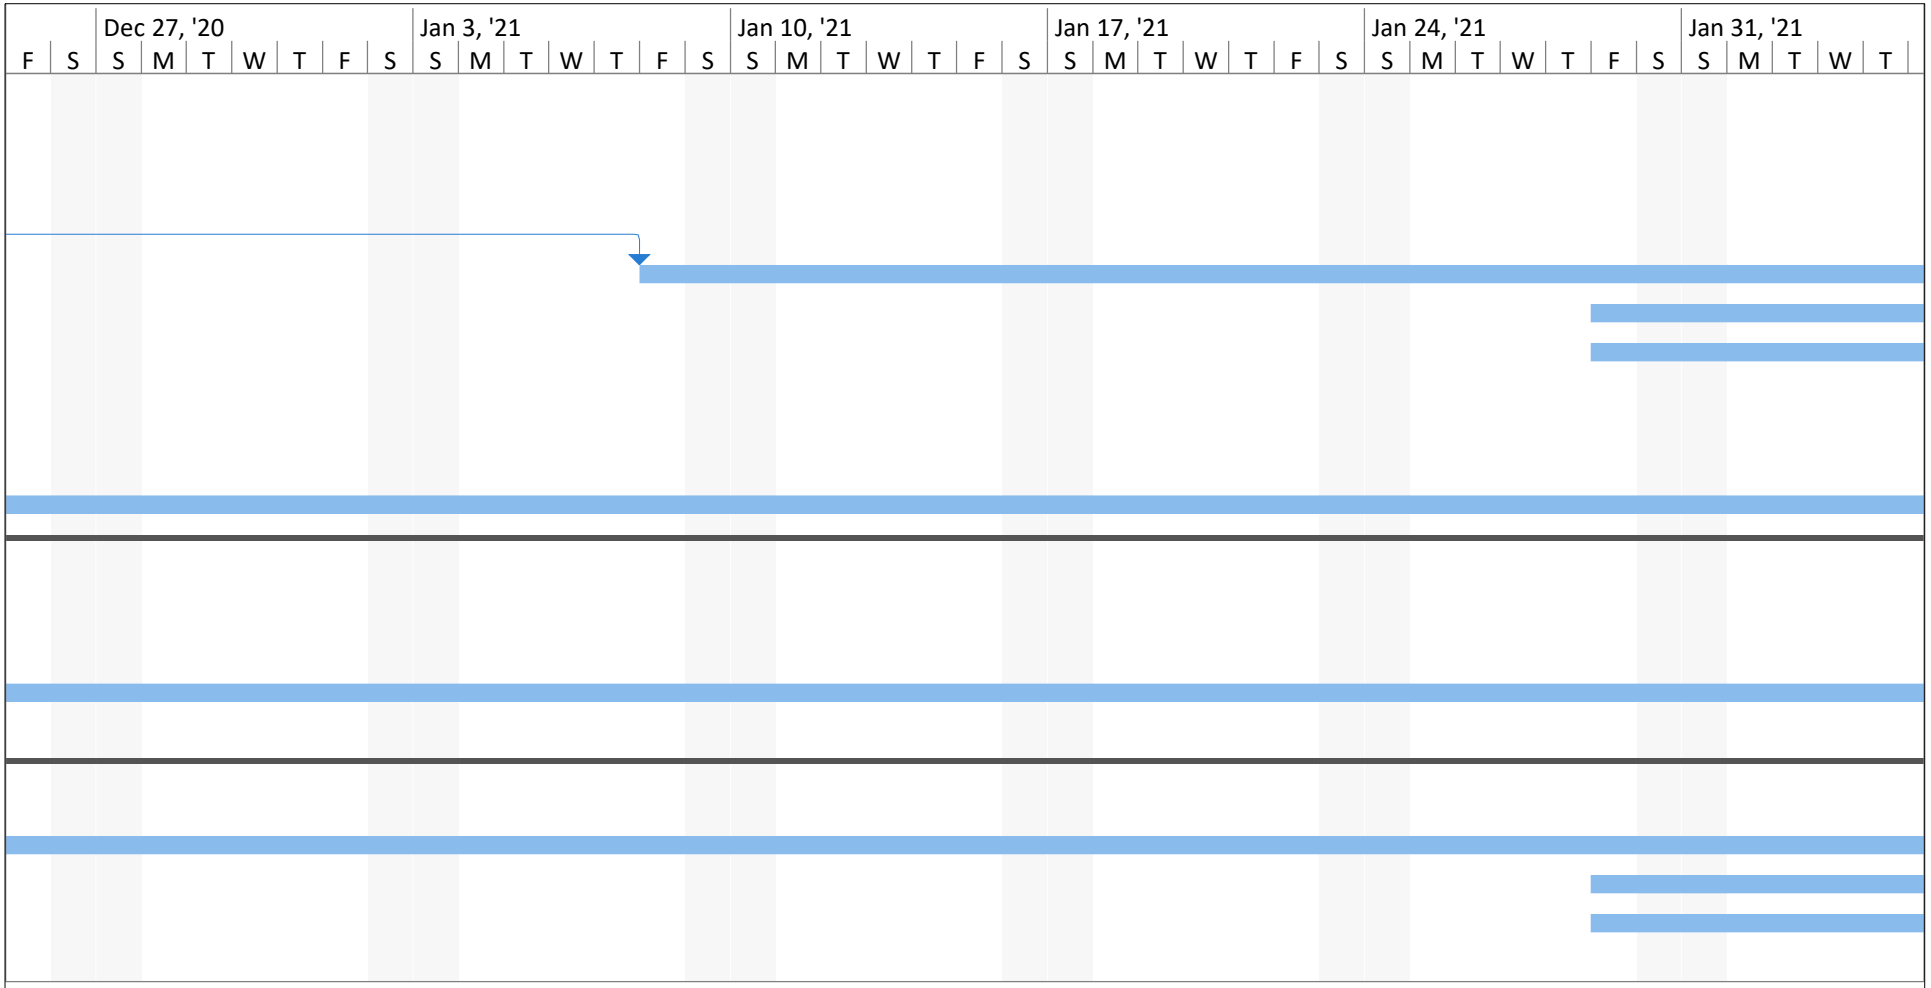


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

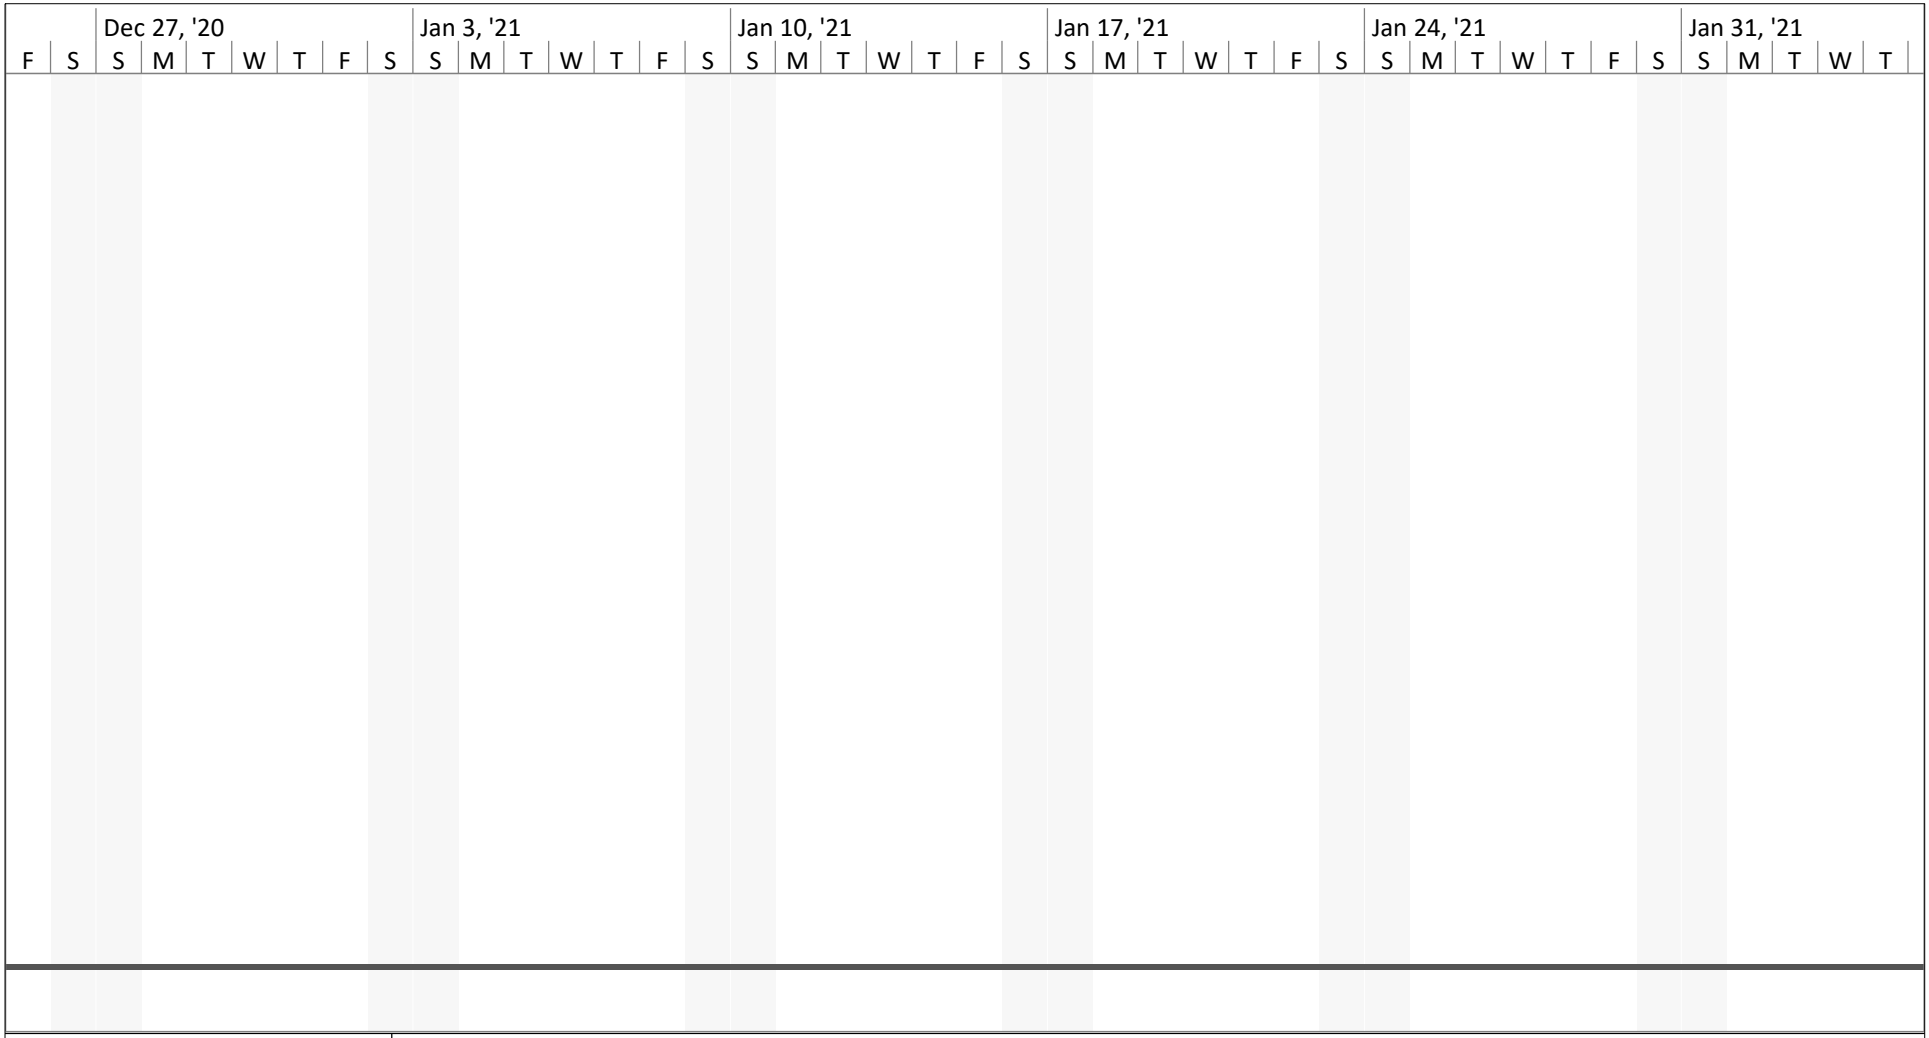


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

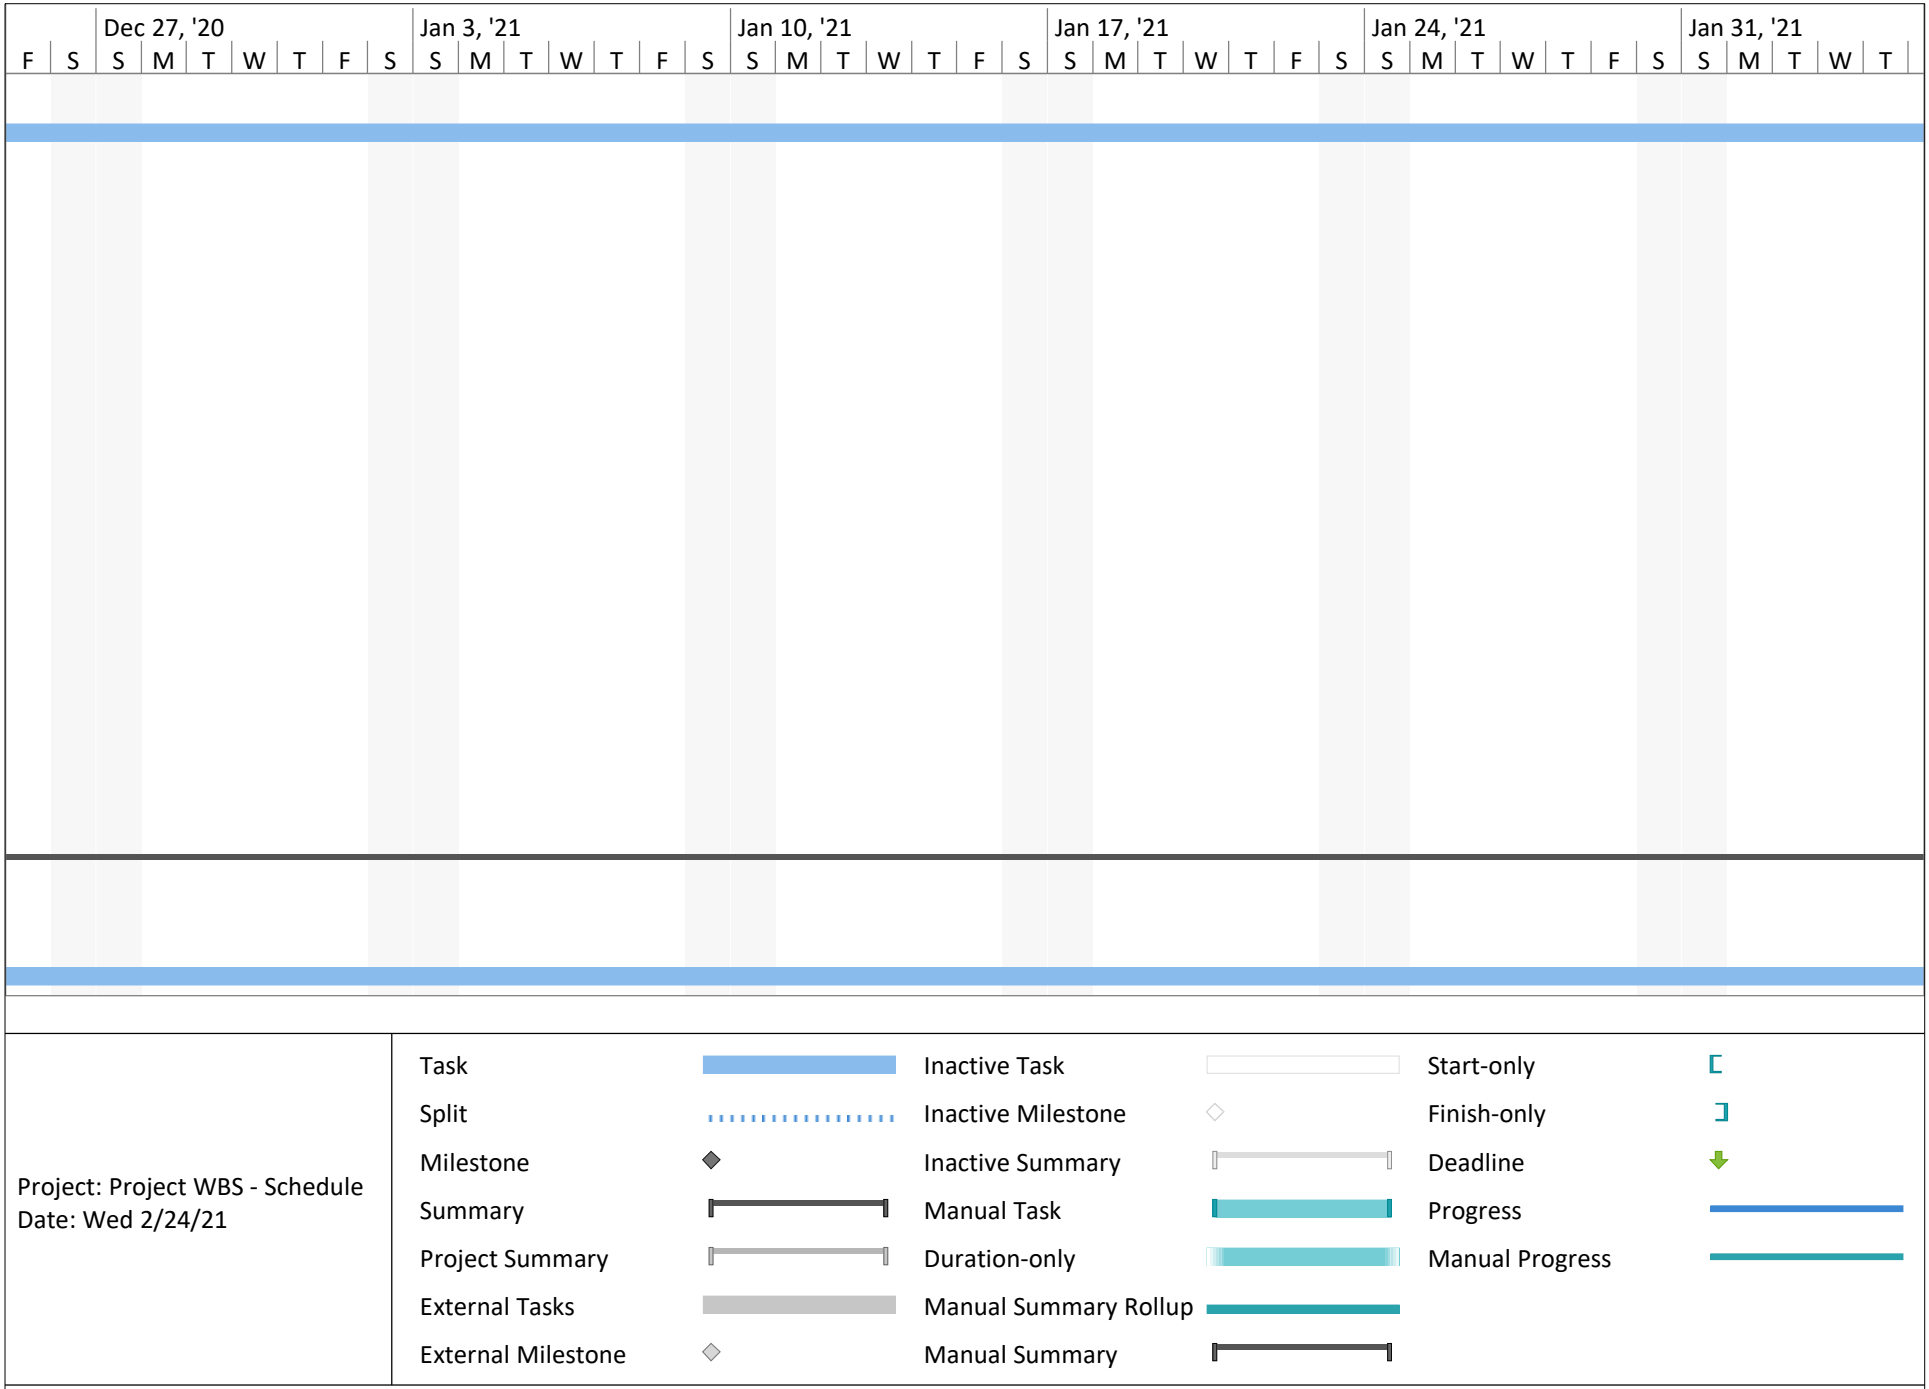


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

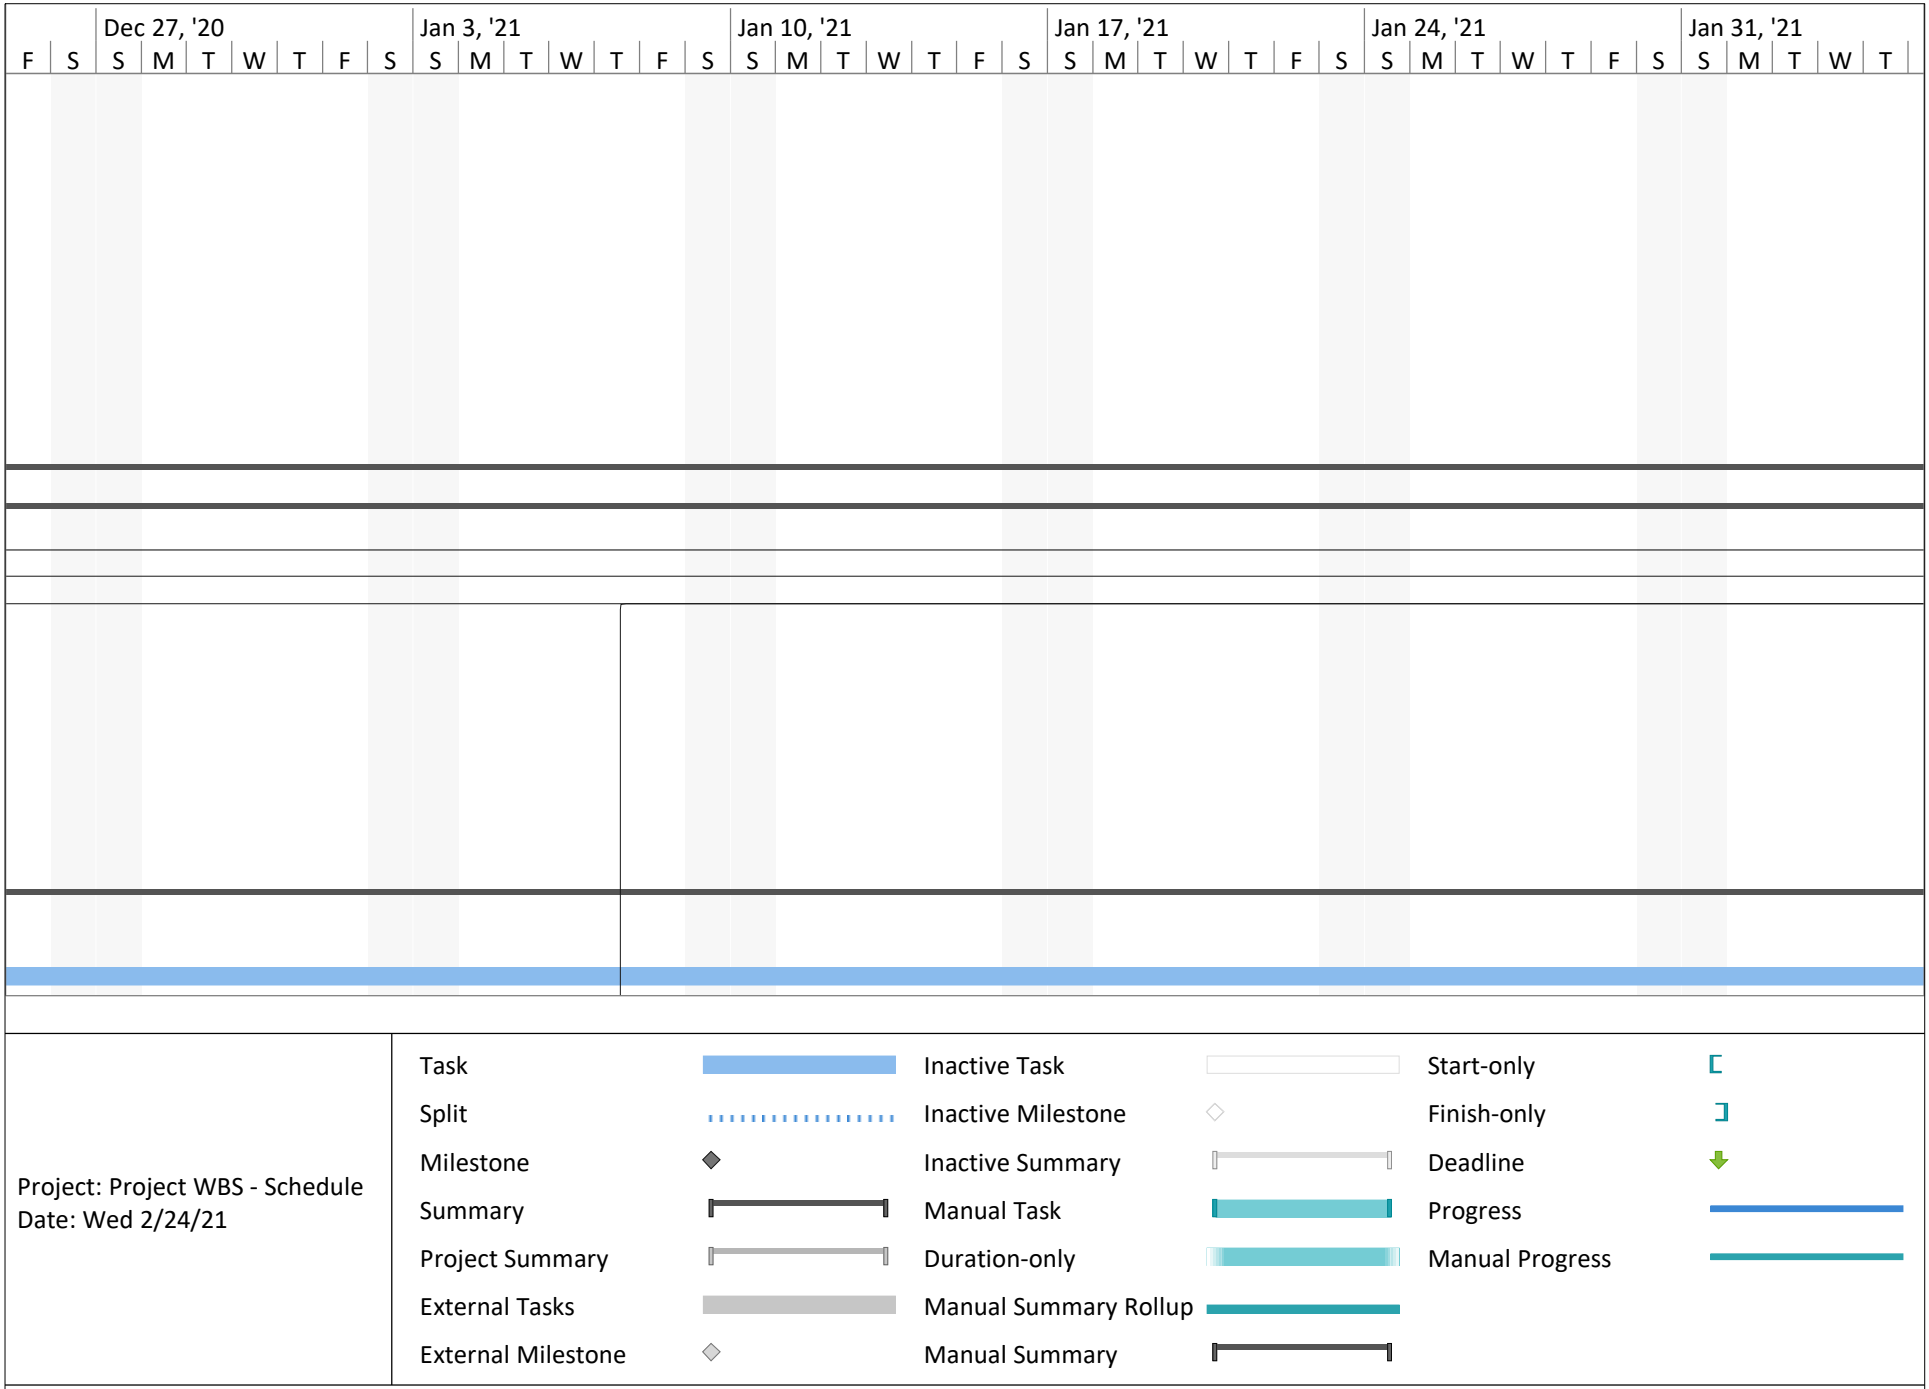
Dec 27, '20
Jan 3, '21
Jan 10, '21
Jan 17, '21
Jan 24, '21
Jan 31, '21
F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T
Project: Project WBS - Schedule
Date: Wed 2/24/21
Task
Split
Milestone
Summary
Project Summary
External Tasks
External Milestone
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
Deadline
Progress
Manual Progress

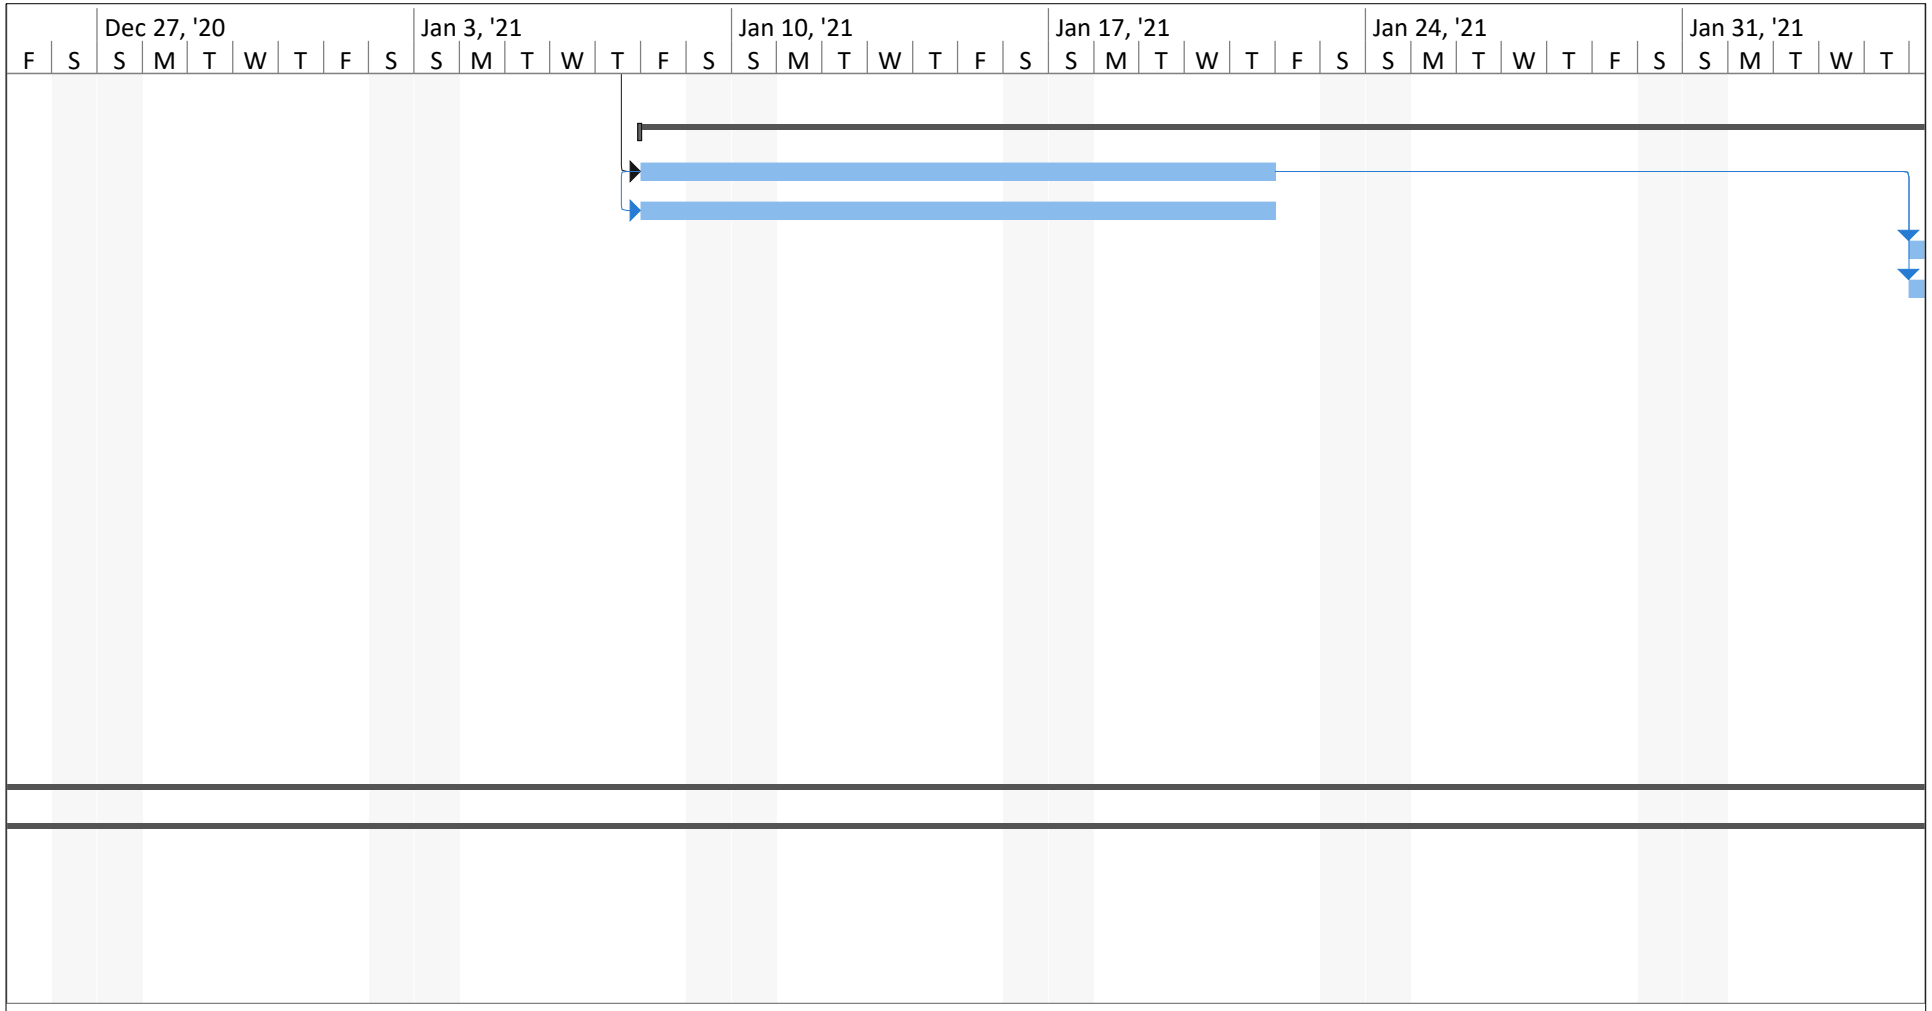


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

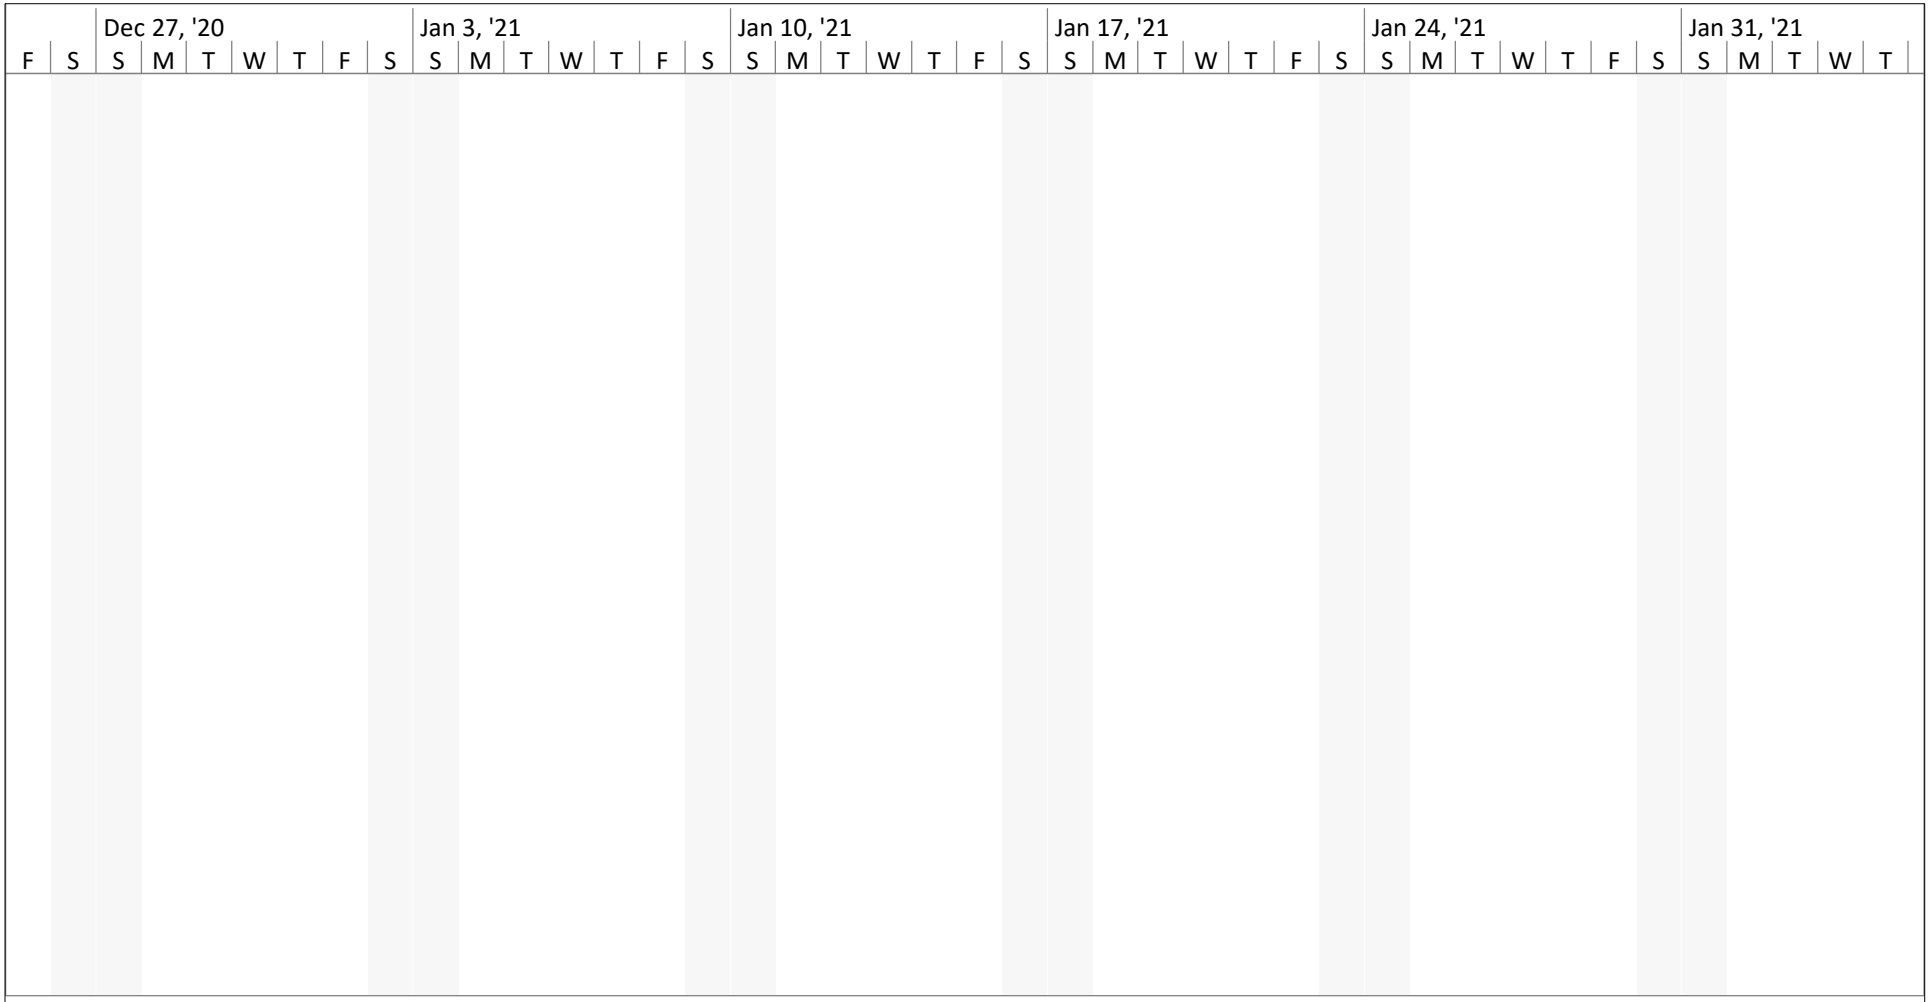


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |




Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

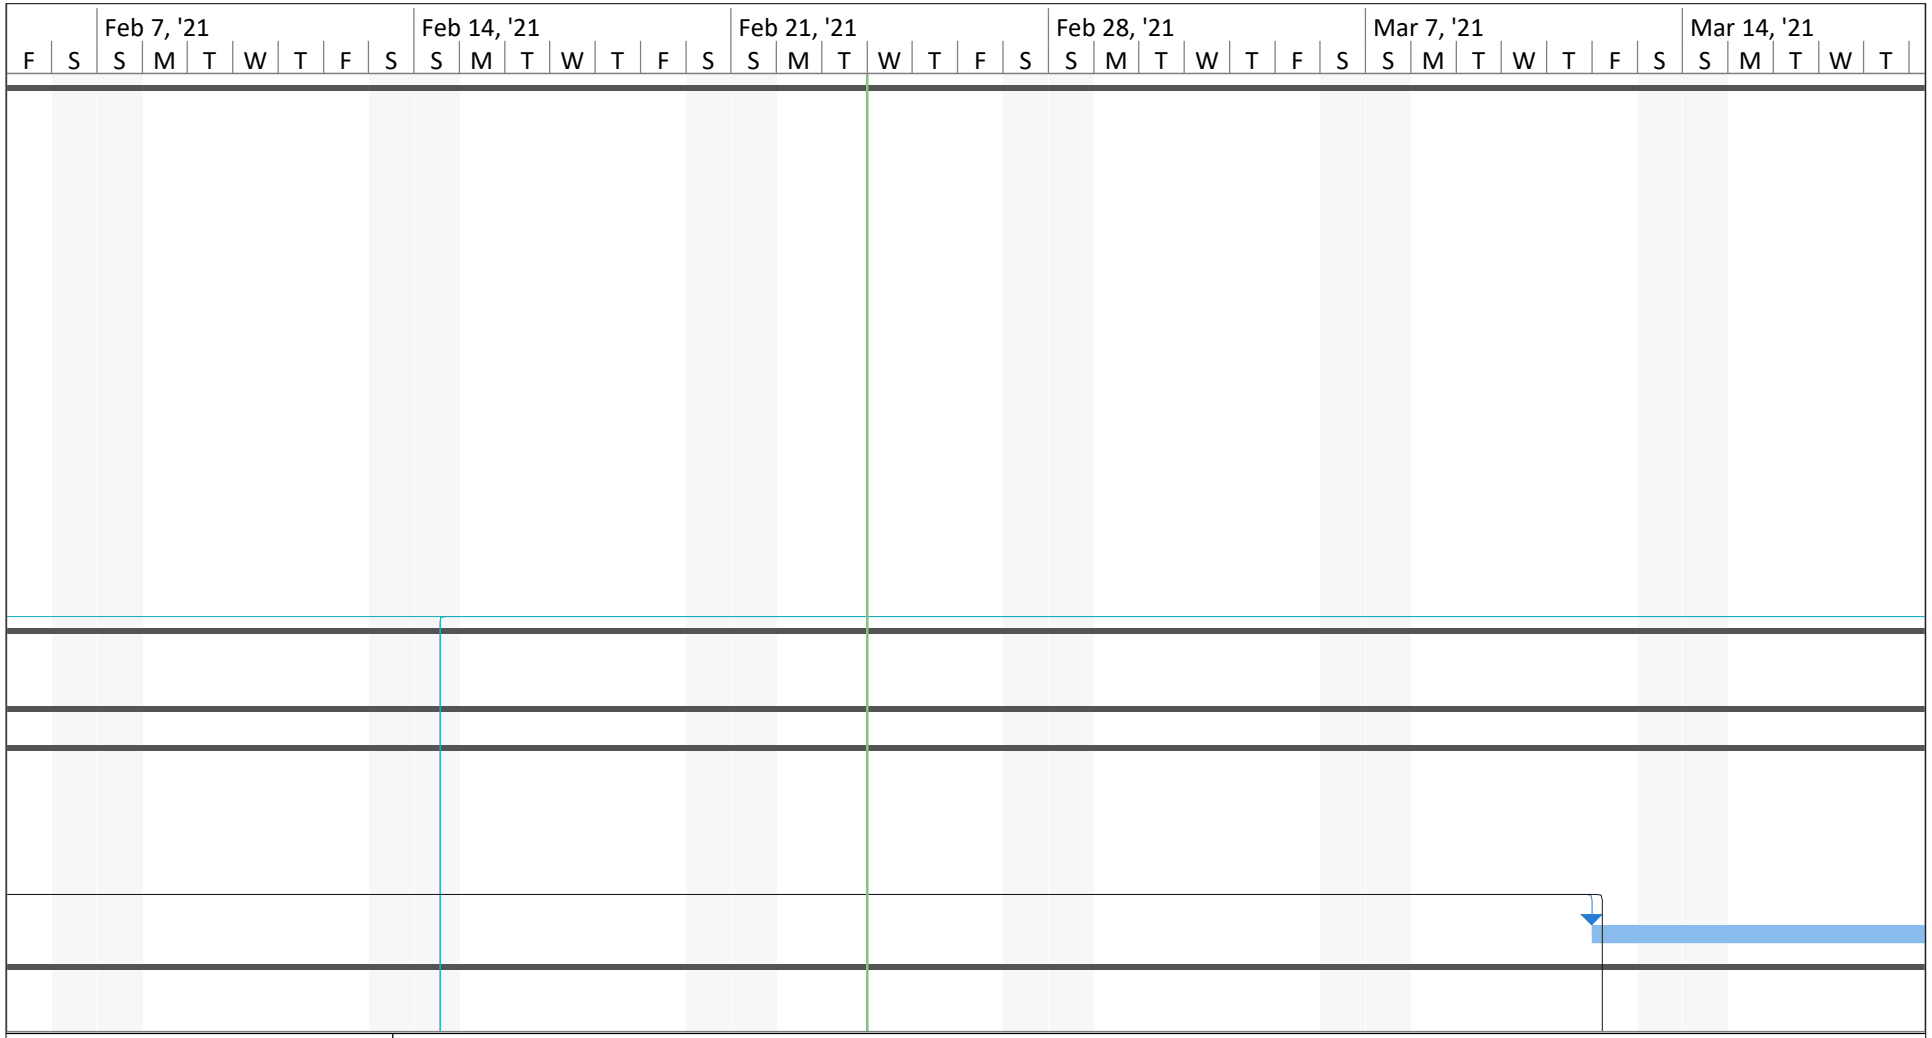


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

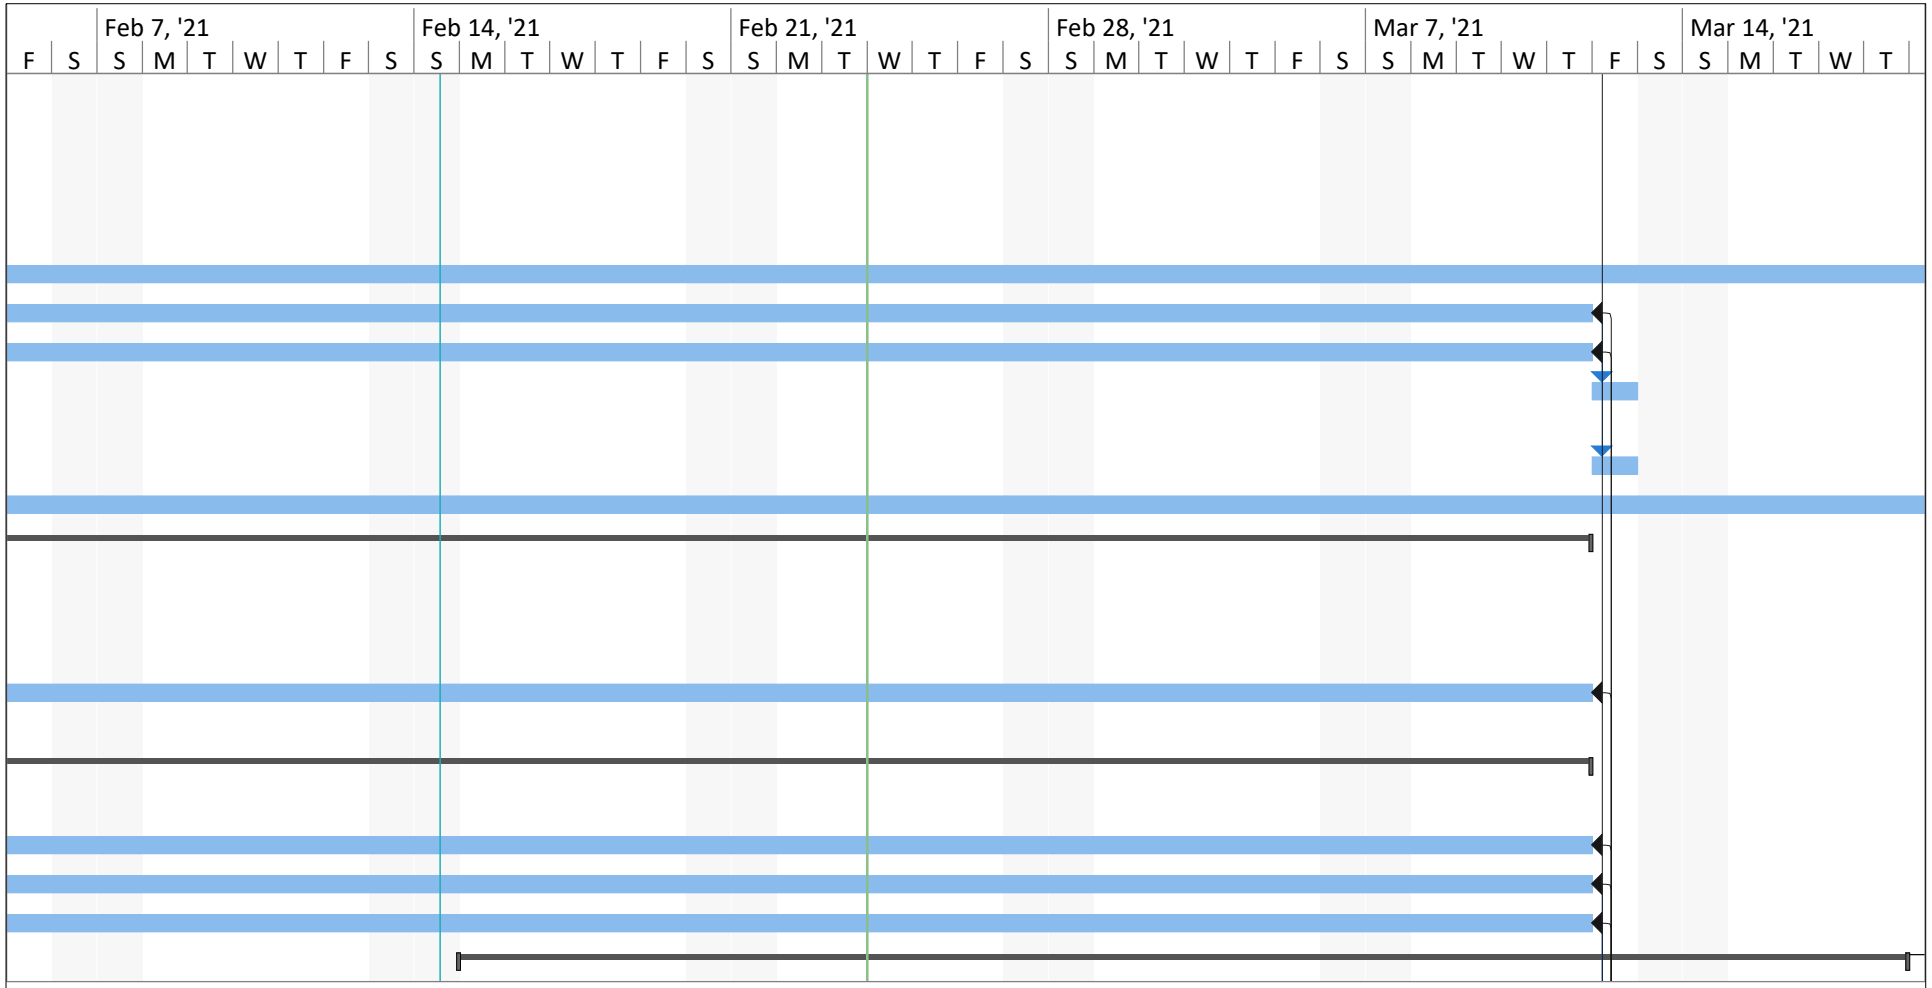


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

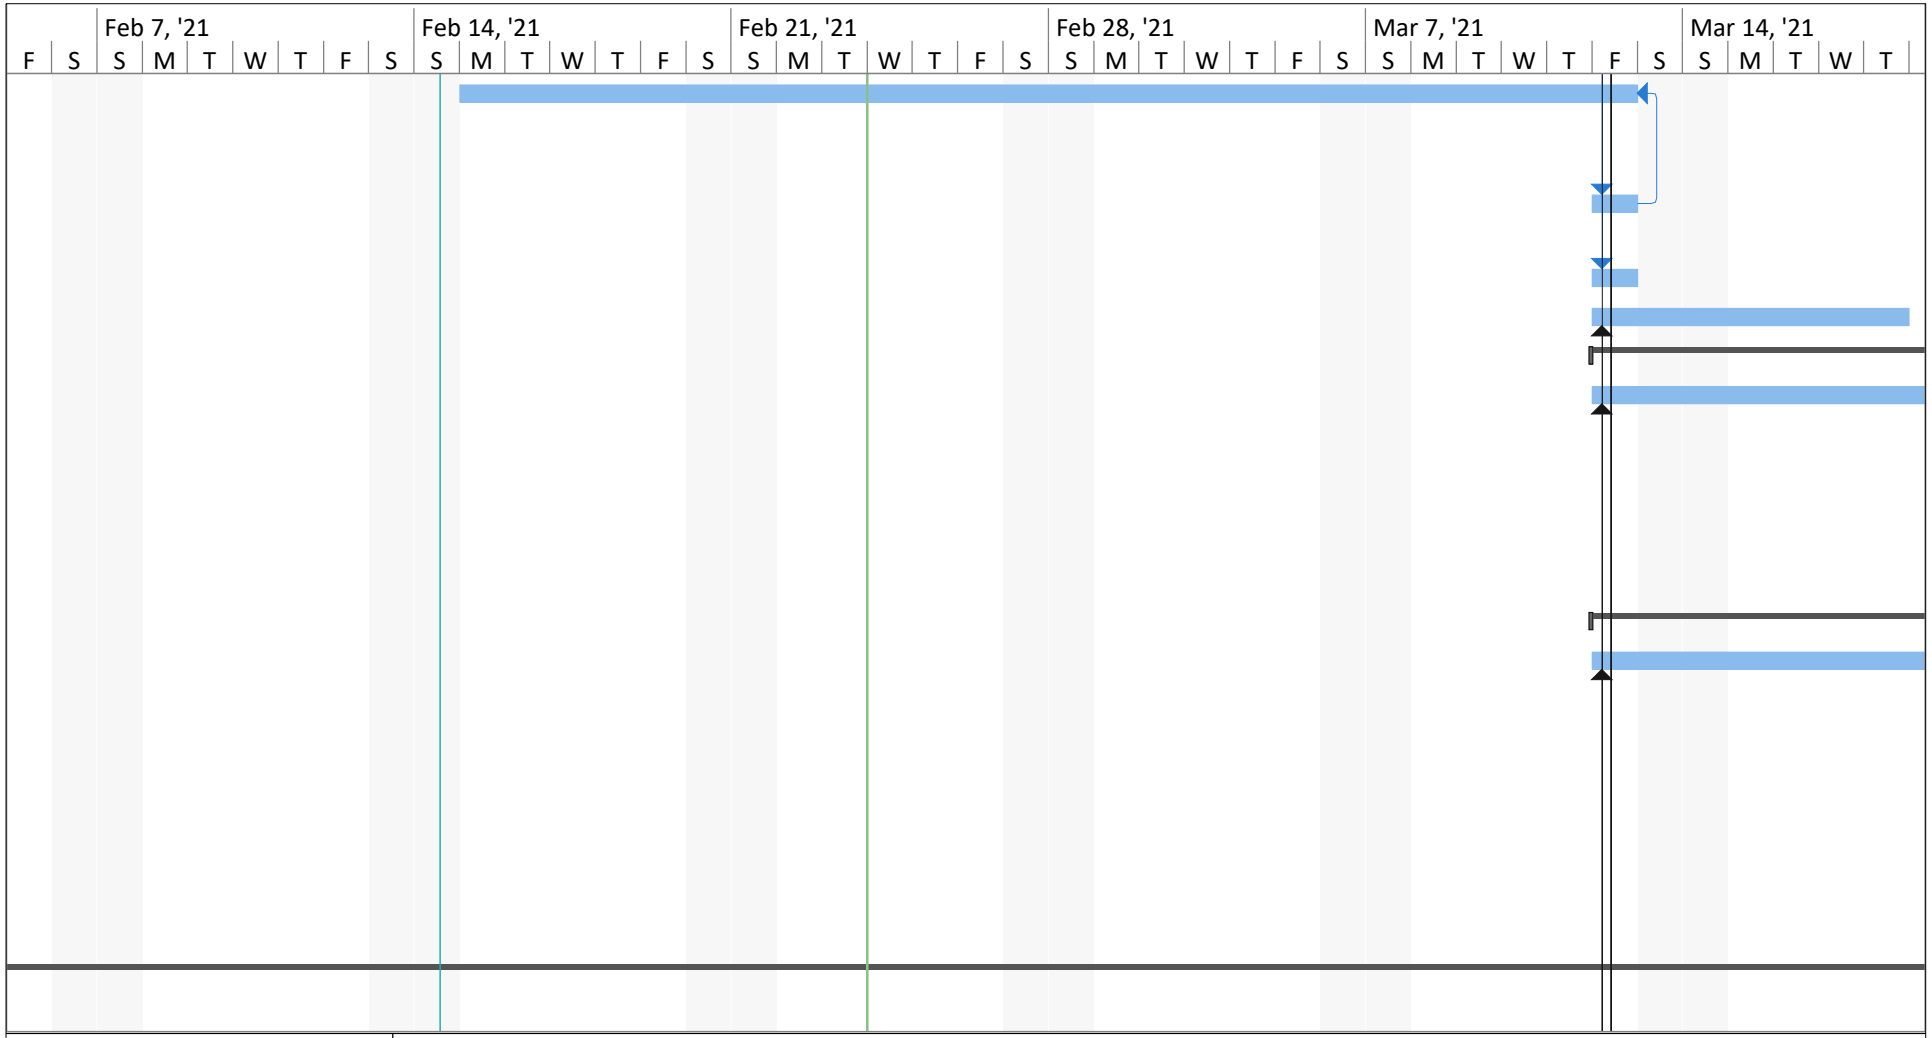


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

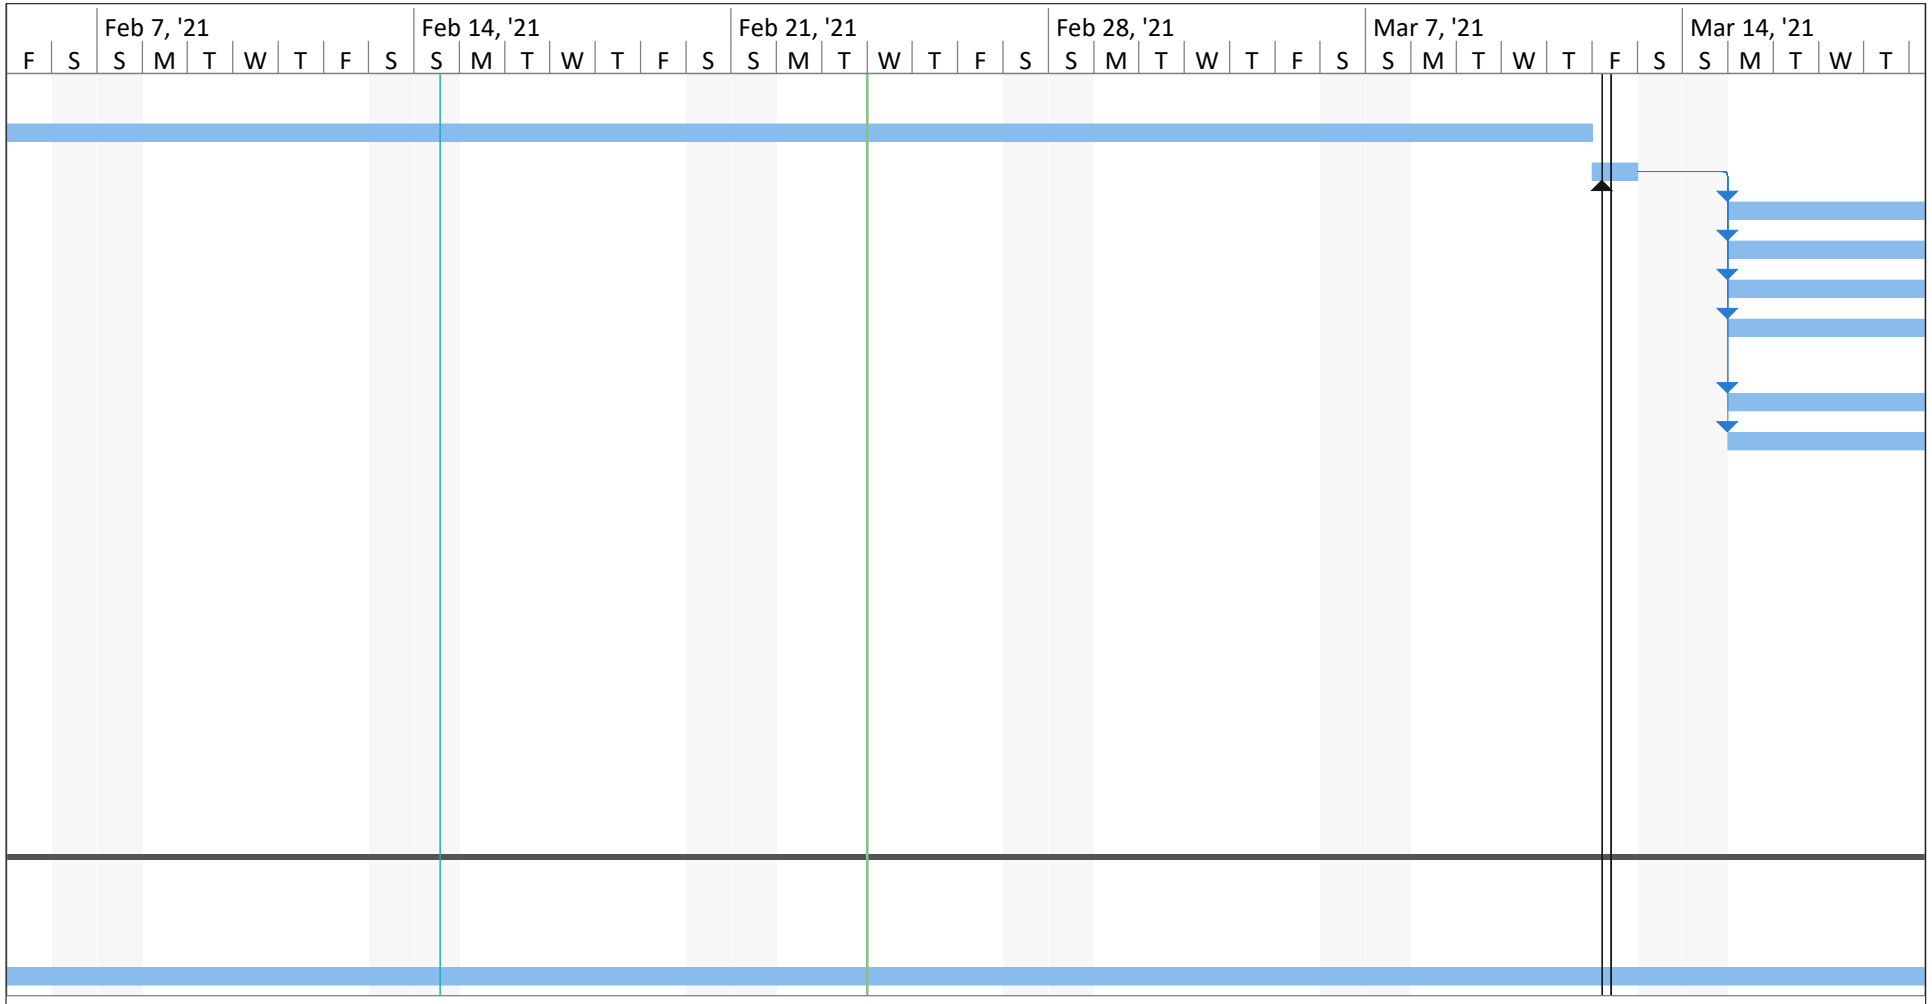


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

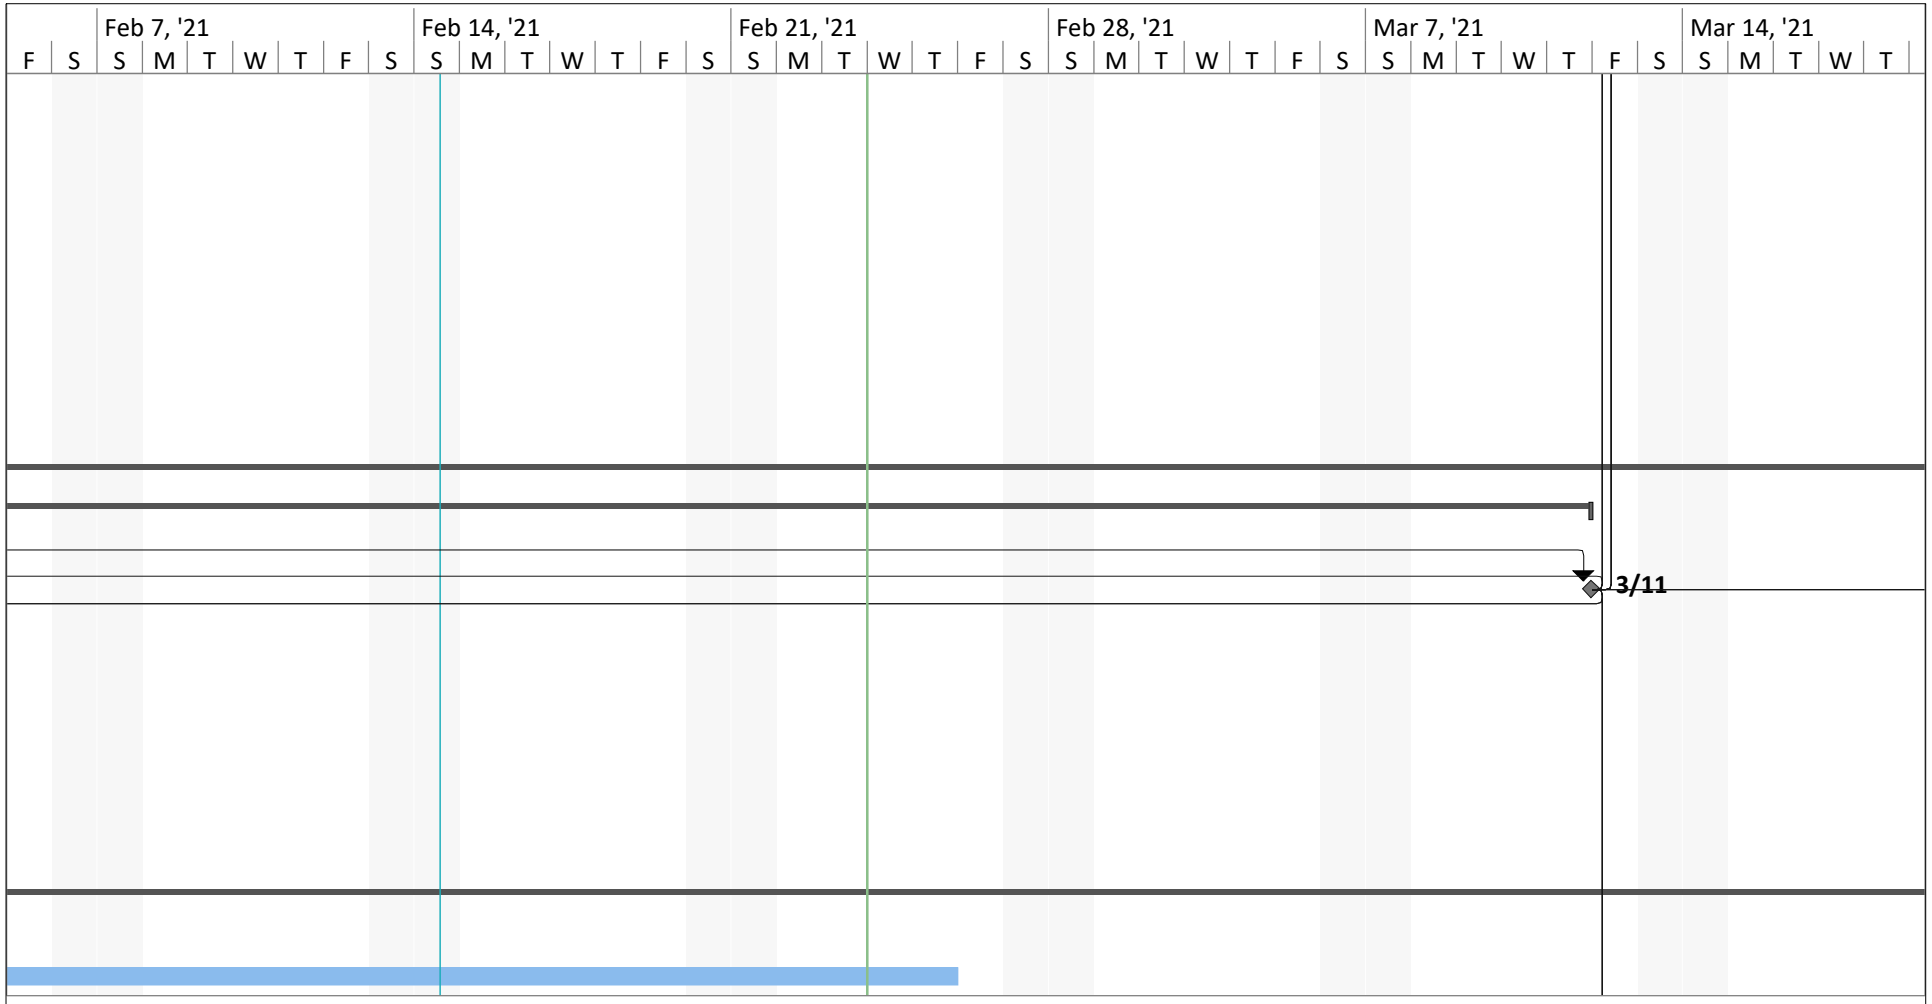


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

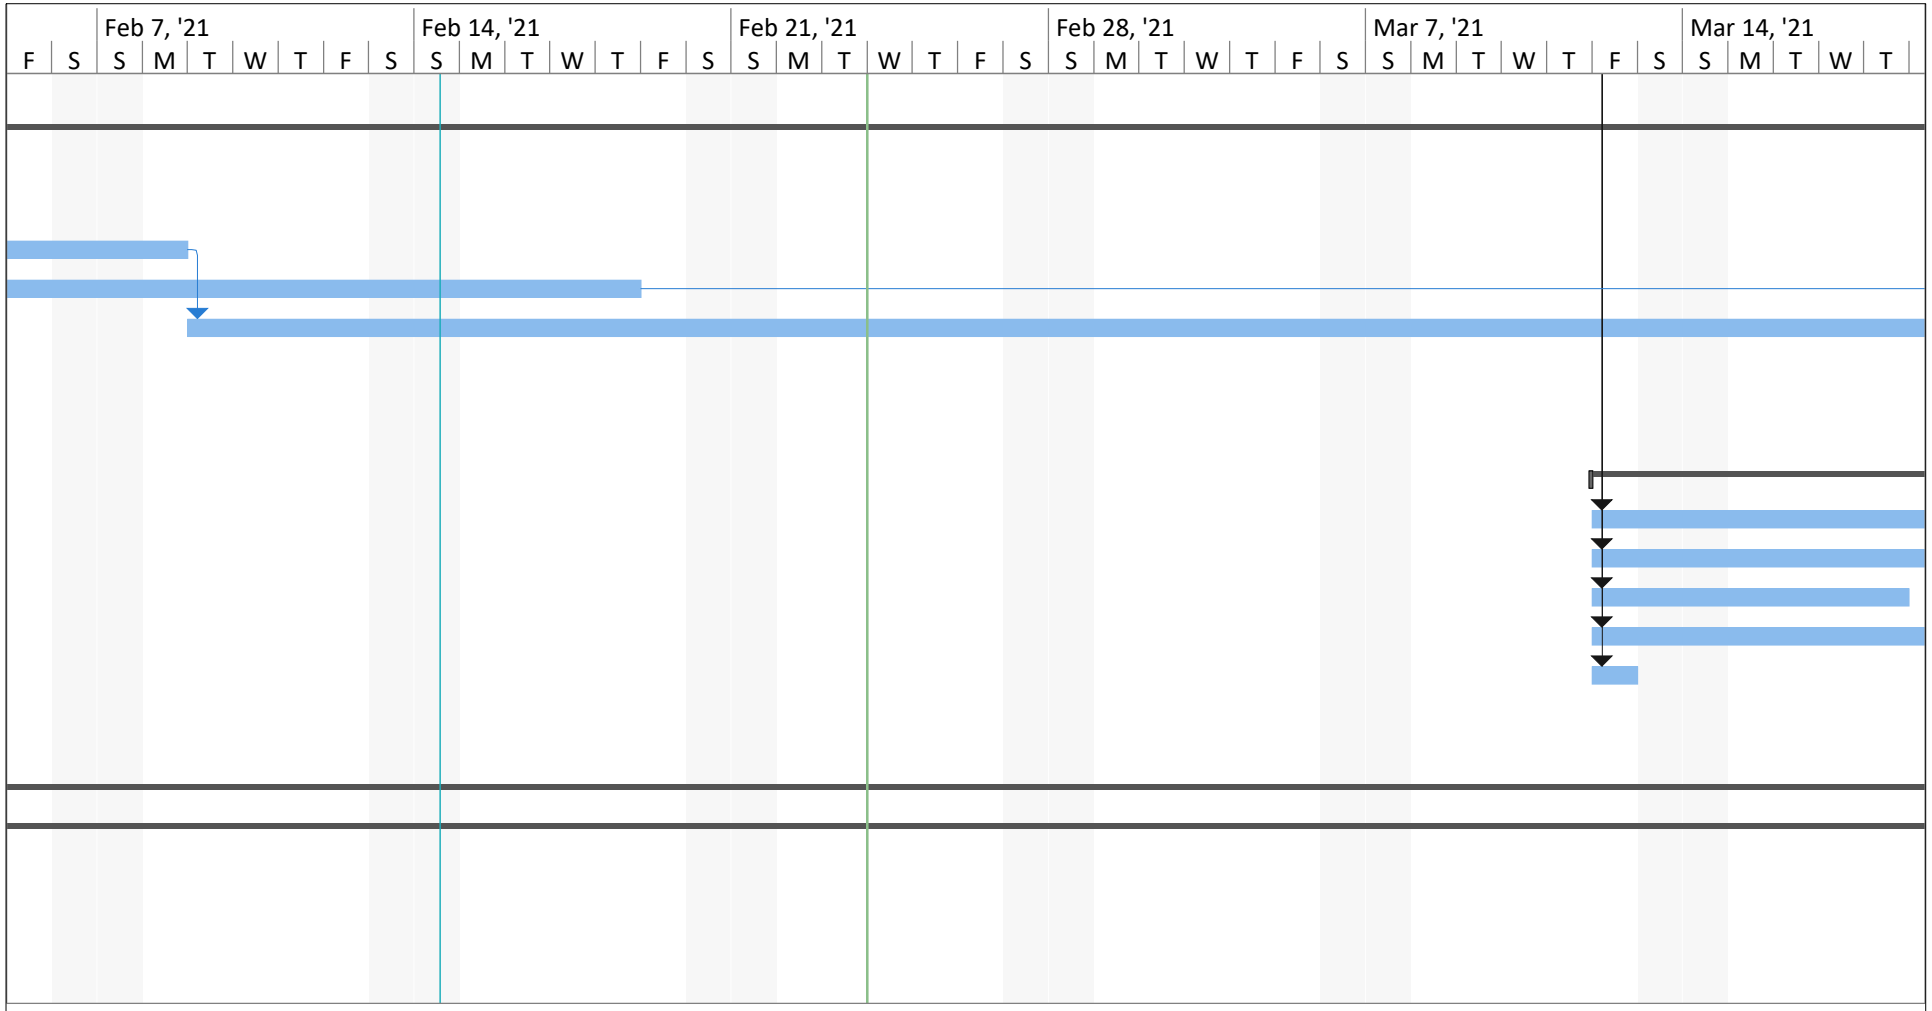


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

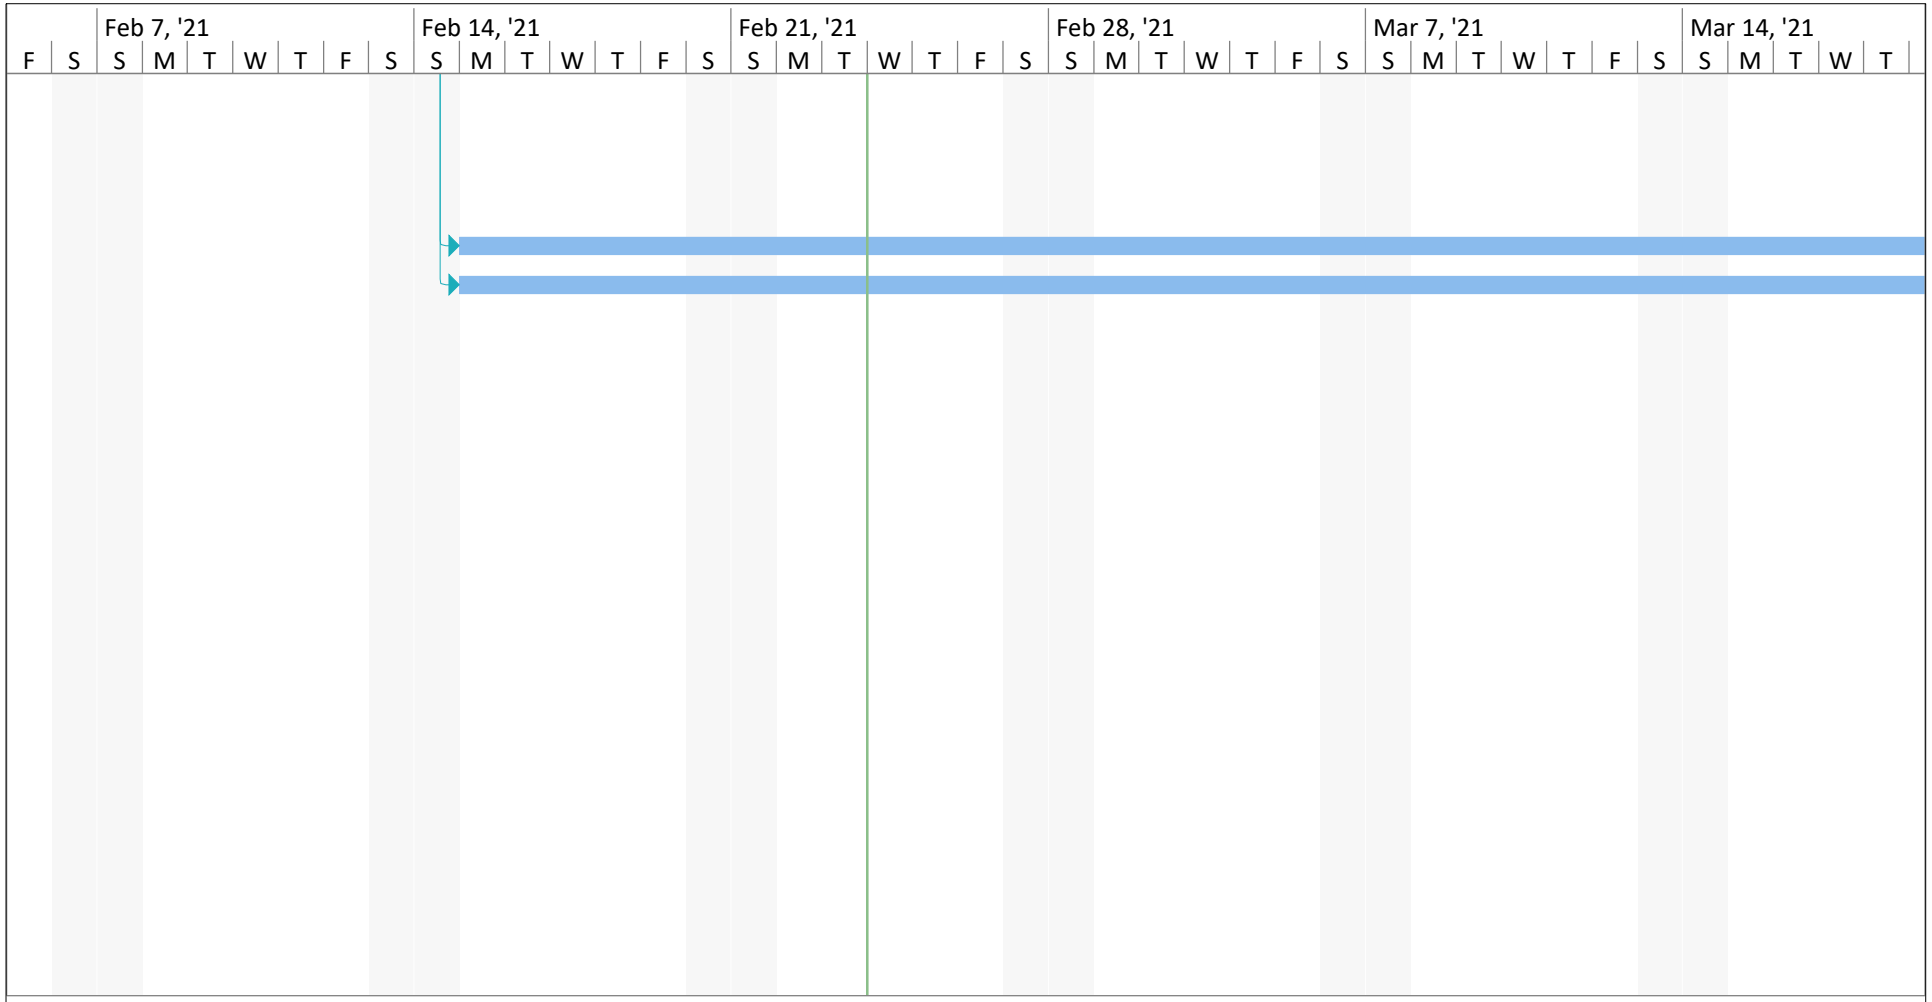


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |




Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

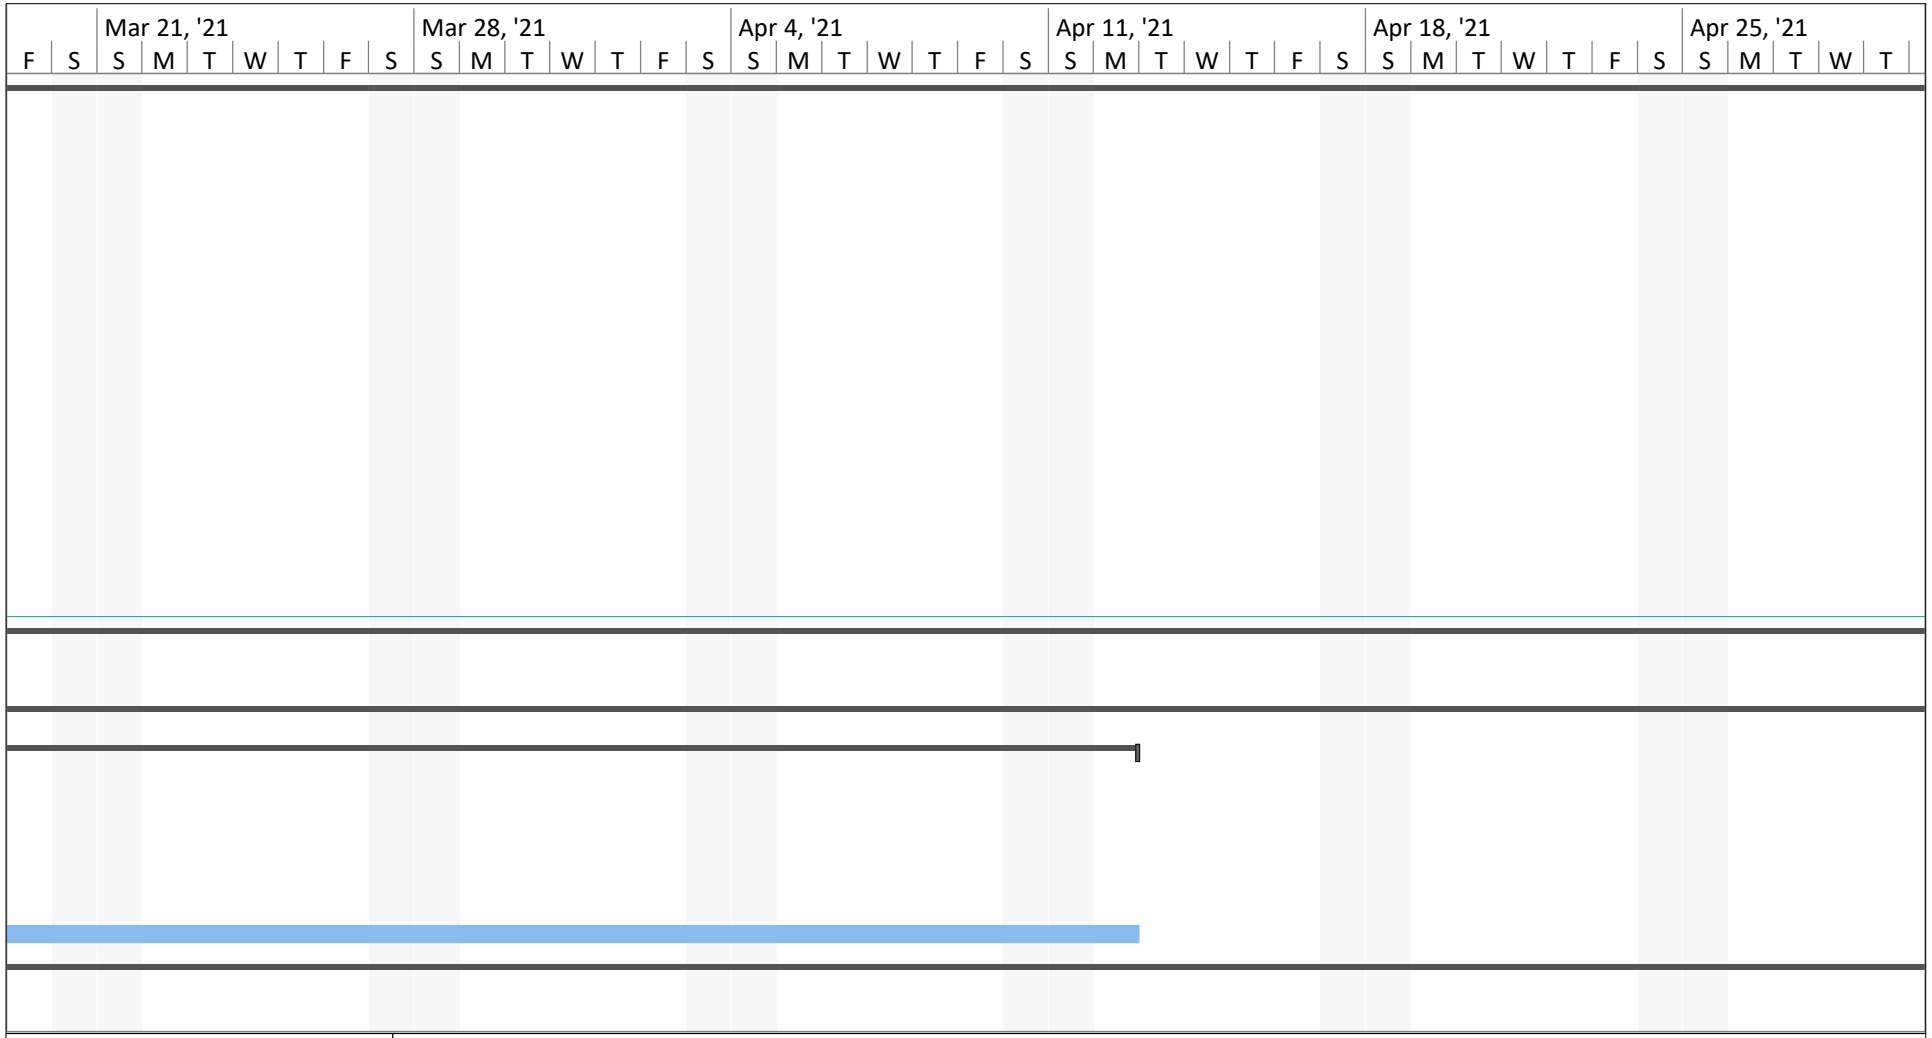


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

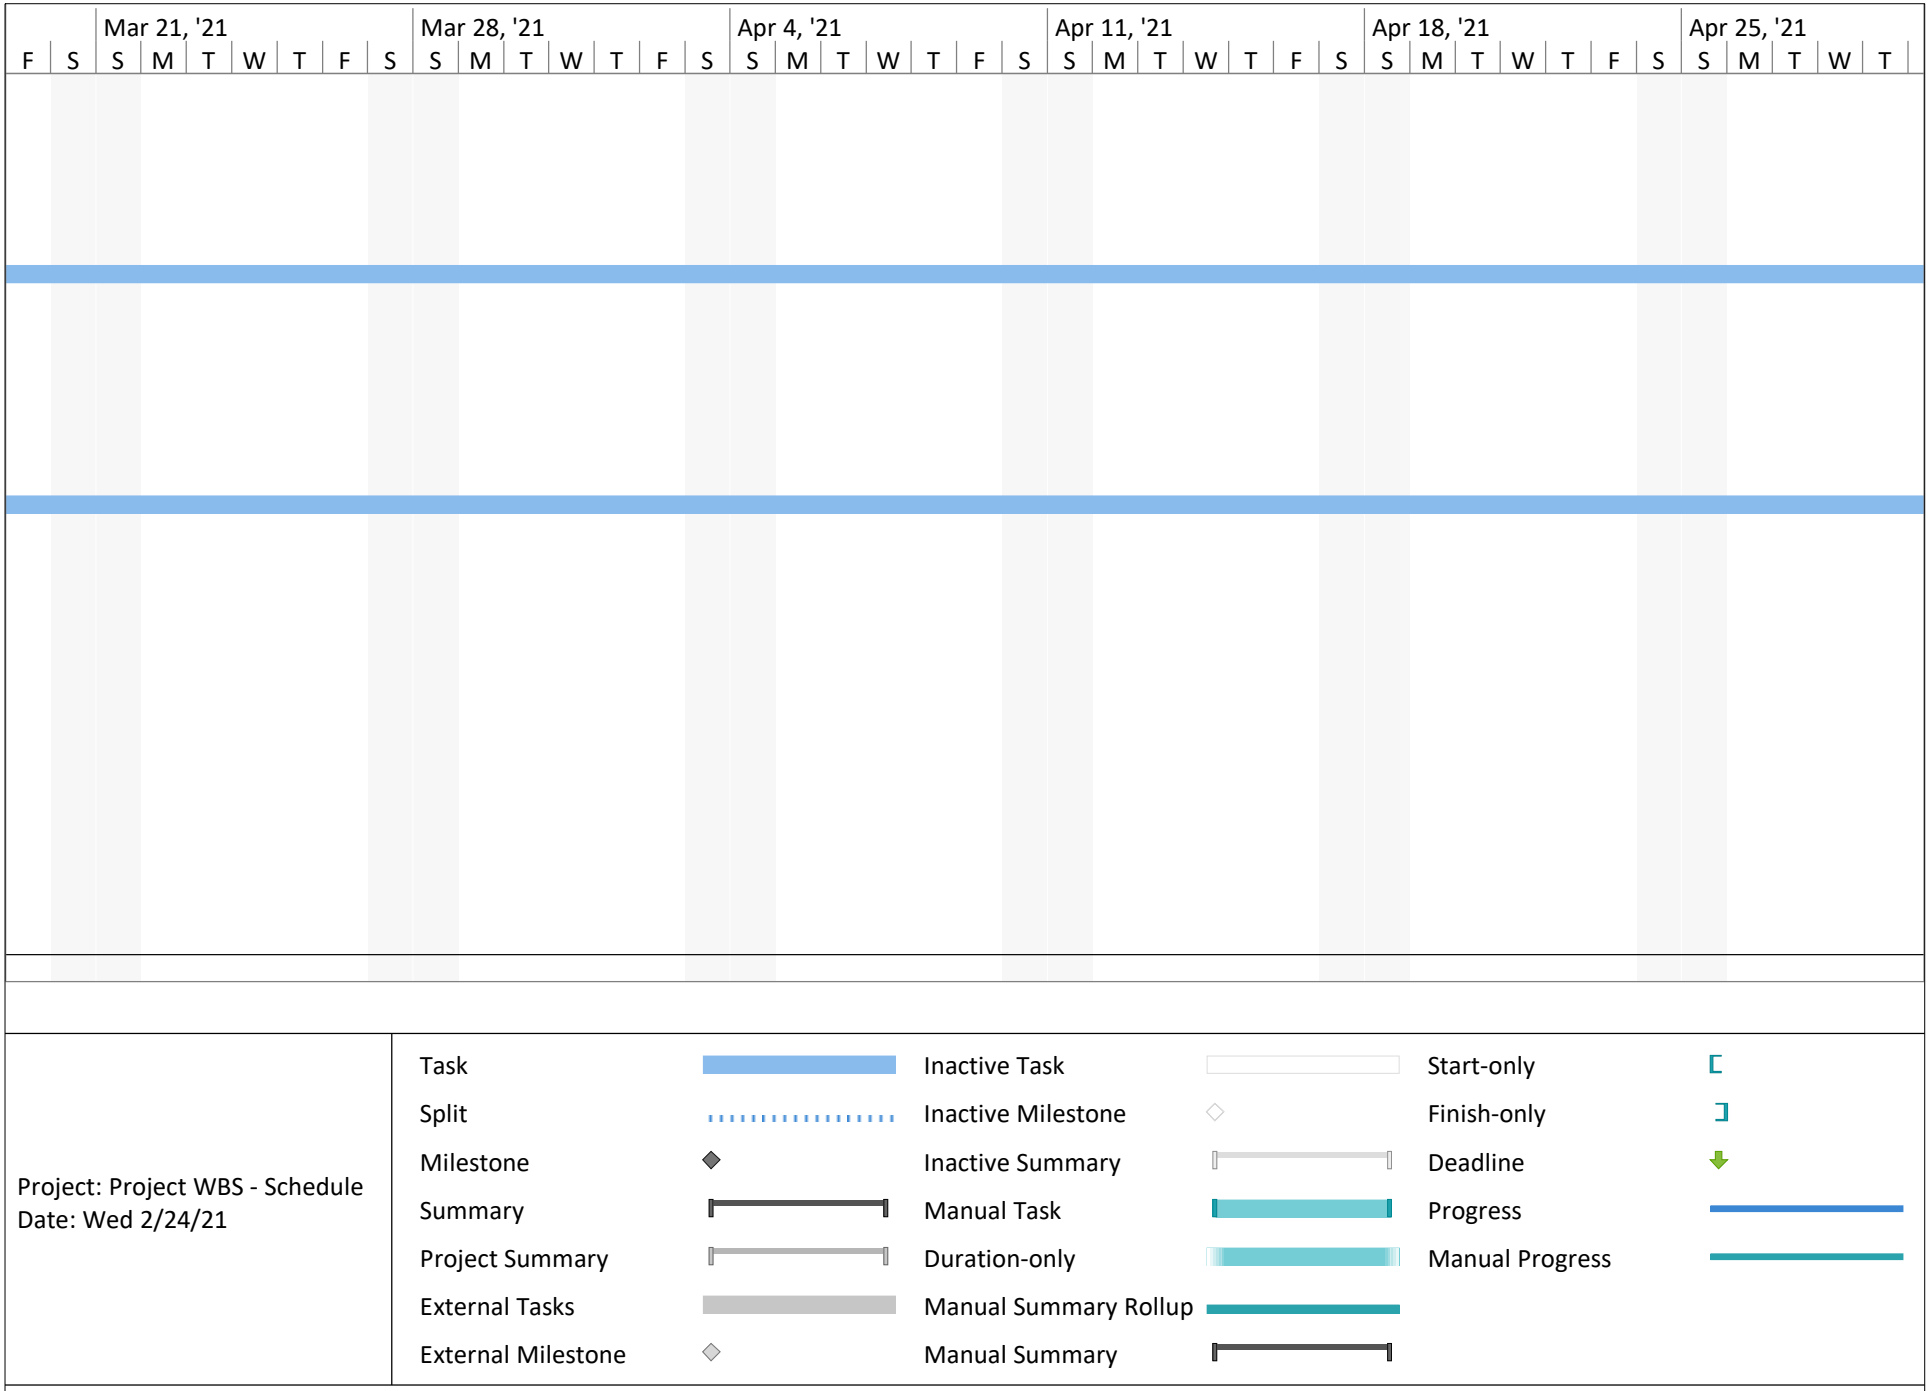
Mar 21, '21
Mar 28, '21
Apr 4, '21
Apr 11, '21
Apr 18, '21
Apr 25, '21
F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S
Project: Project WBS - Schedule
Date: Wed 2/24/21
Task
Split
Milestone
Summary
Project Summary
External Tasks
External Milestone
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
Deadline
Progress
Manual Progress

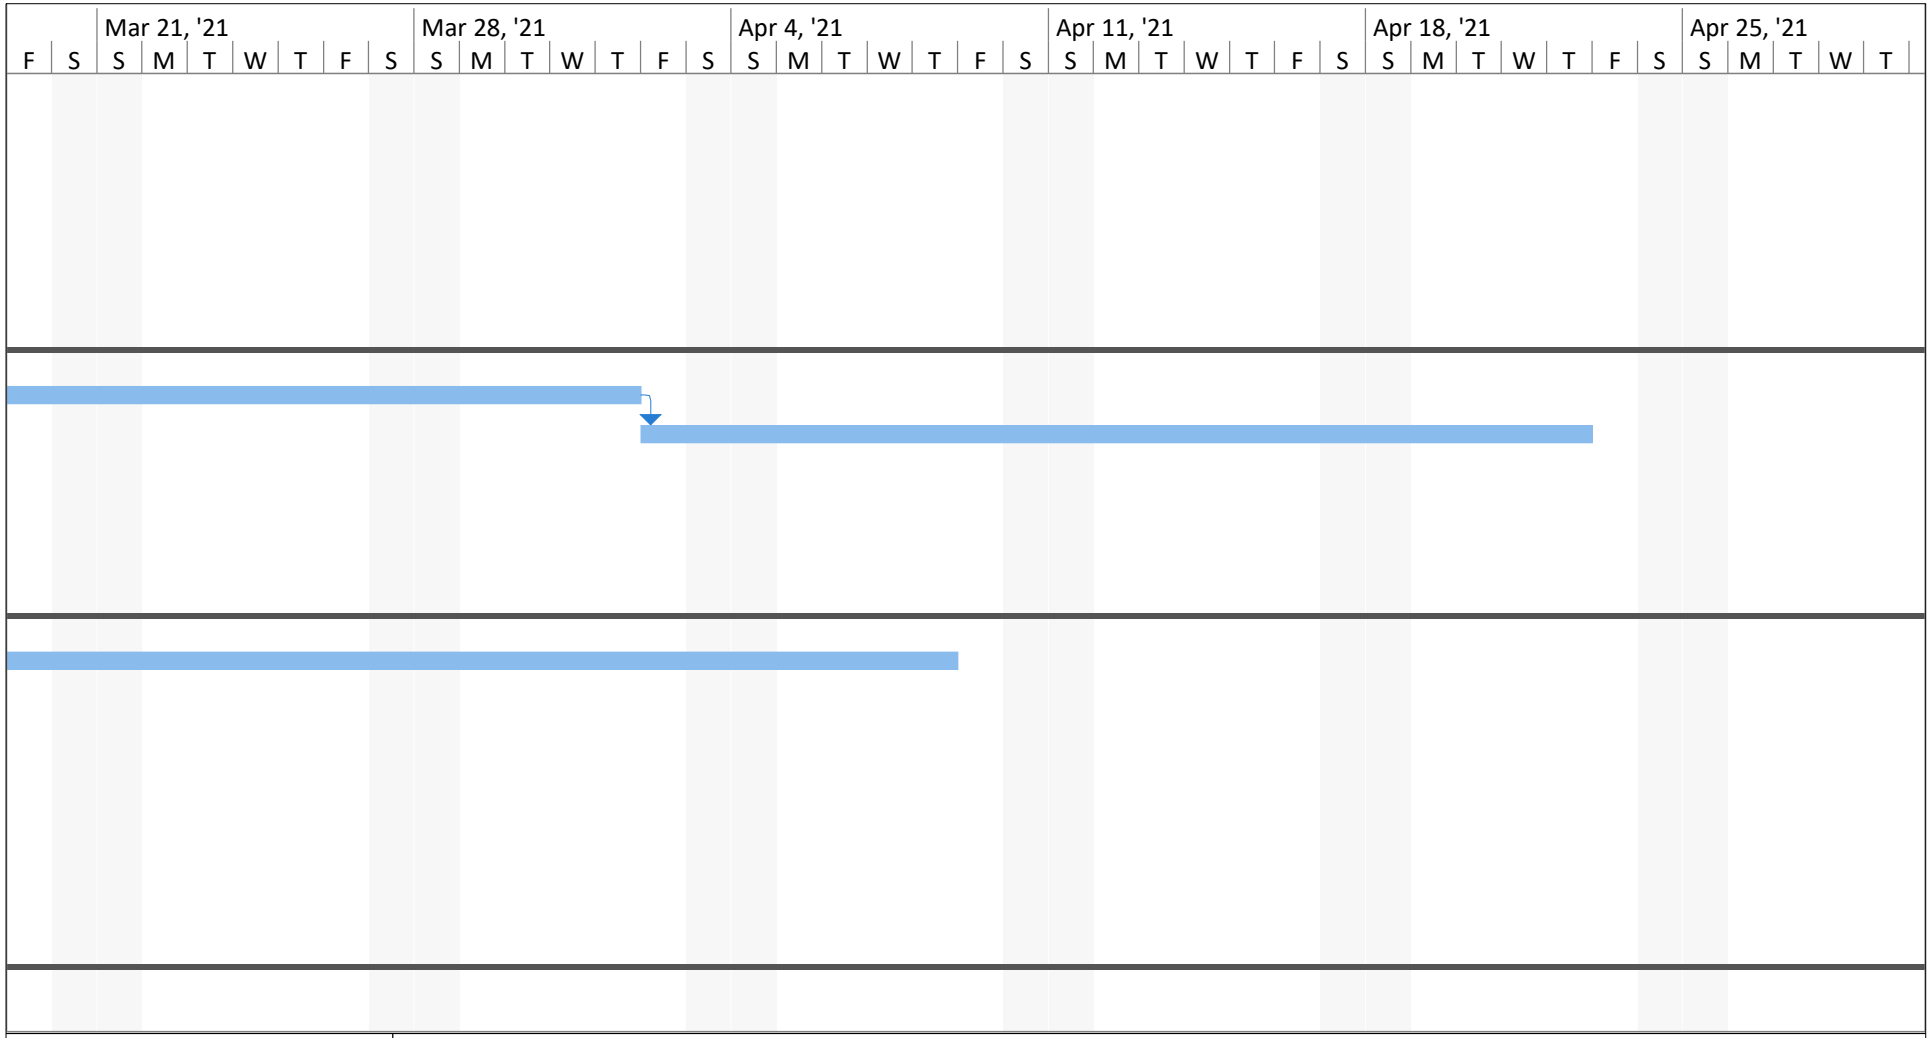


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

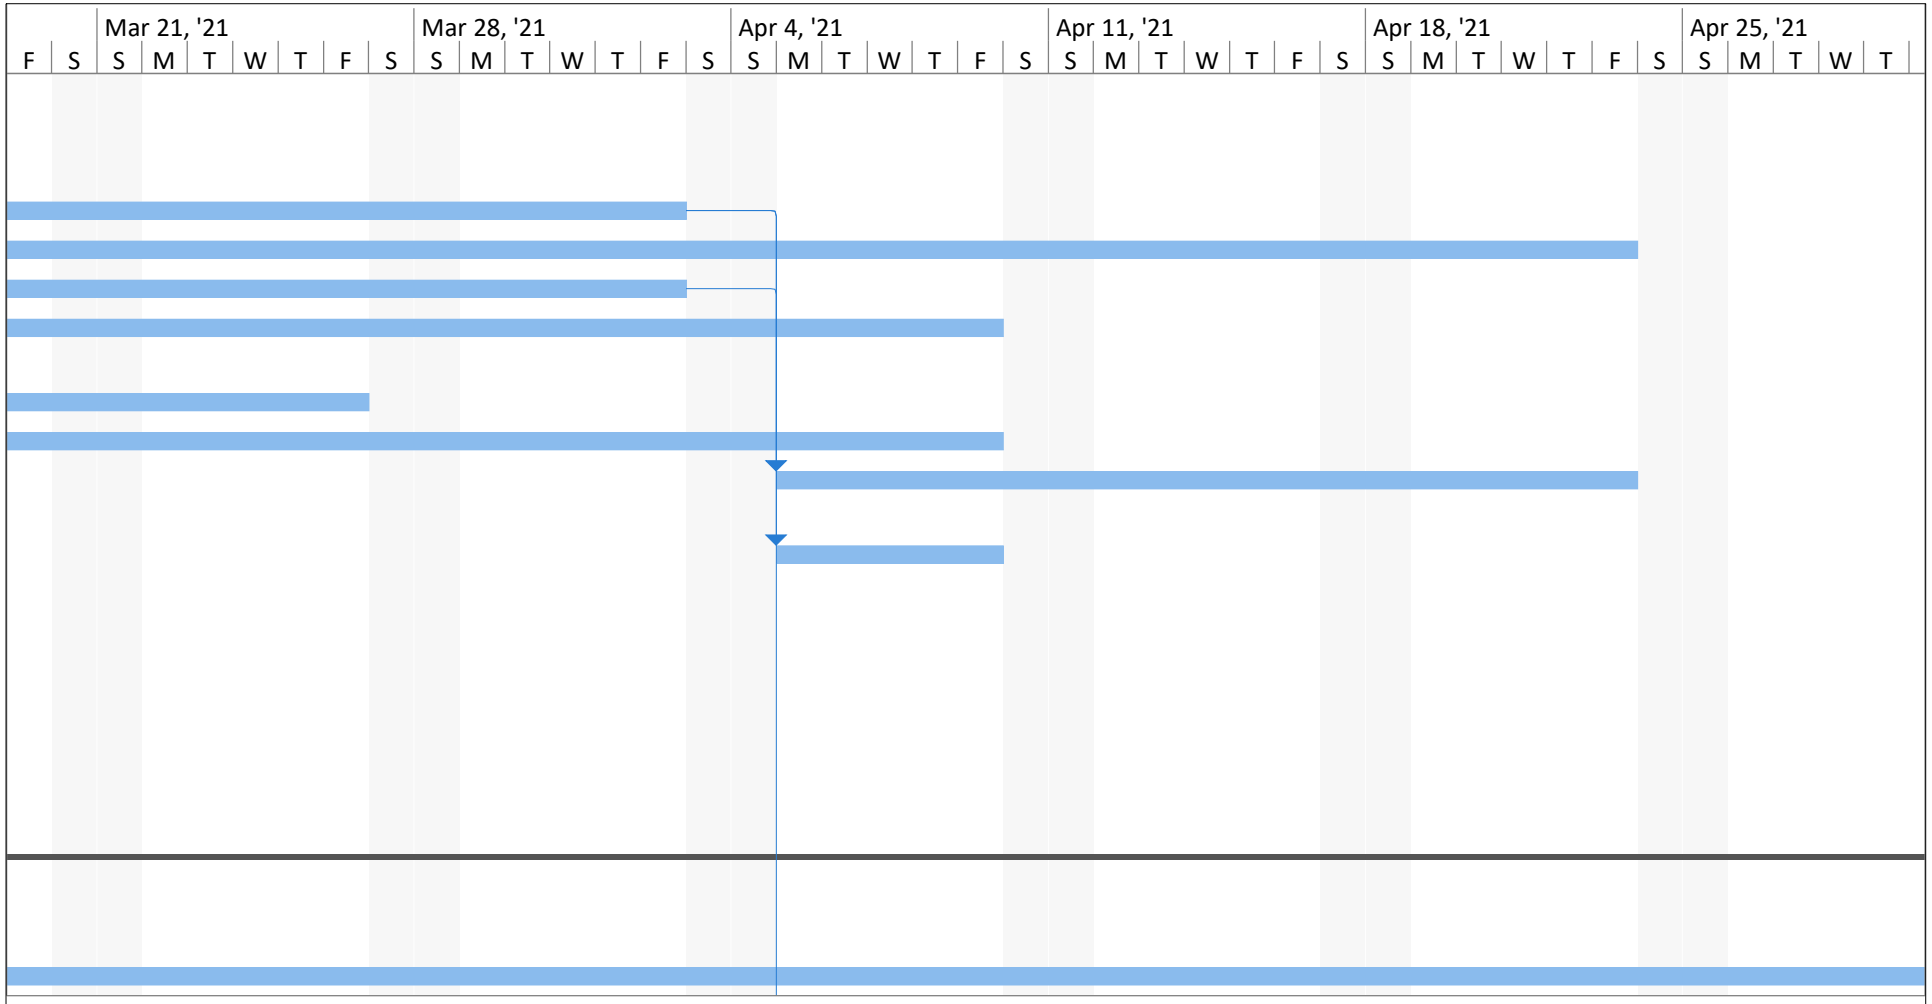


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

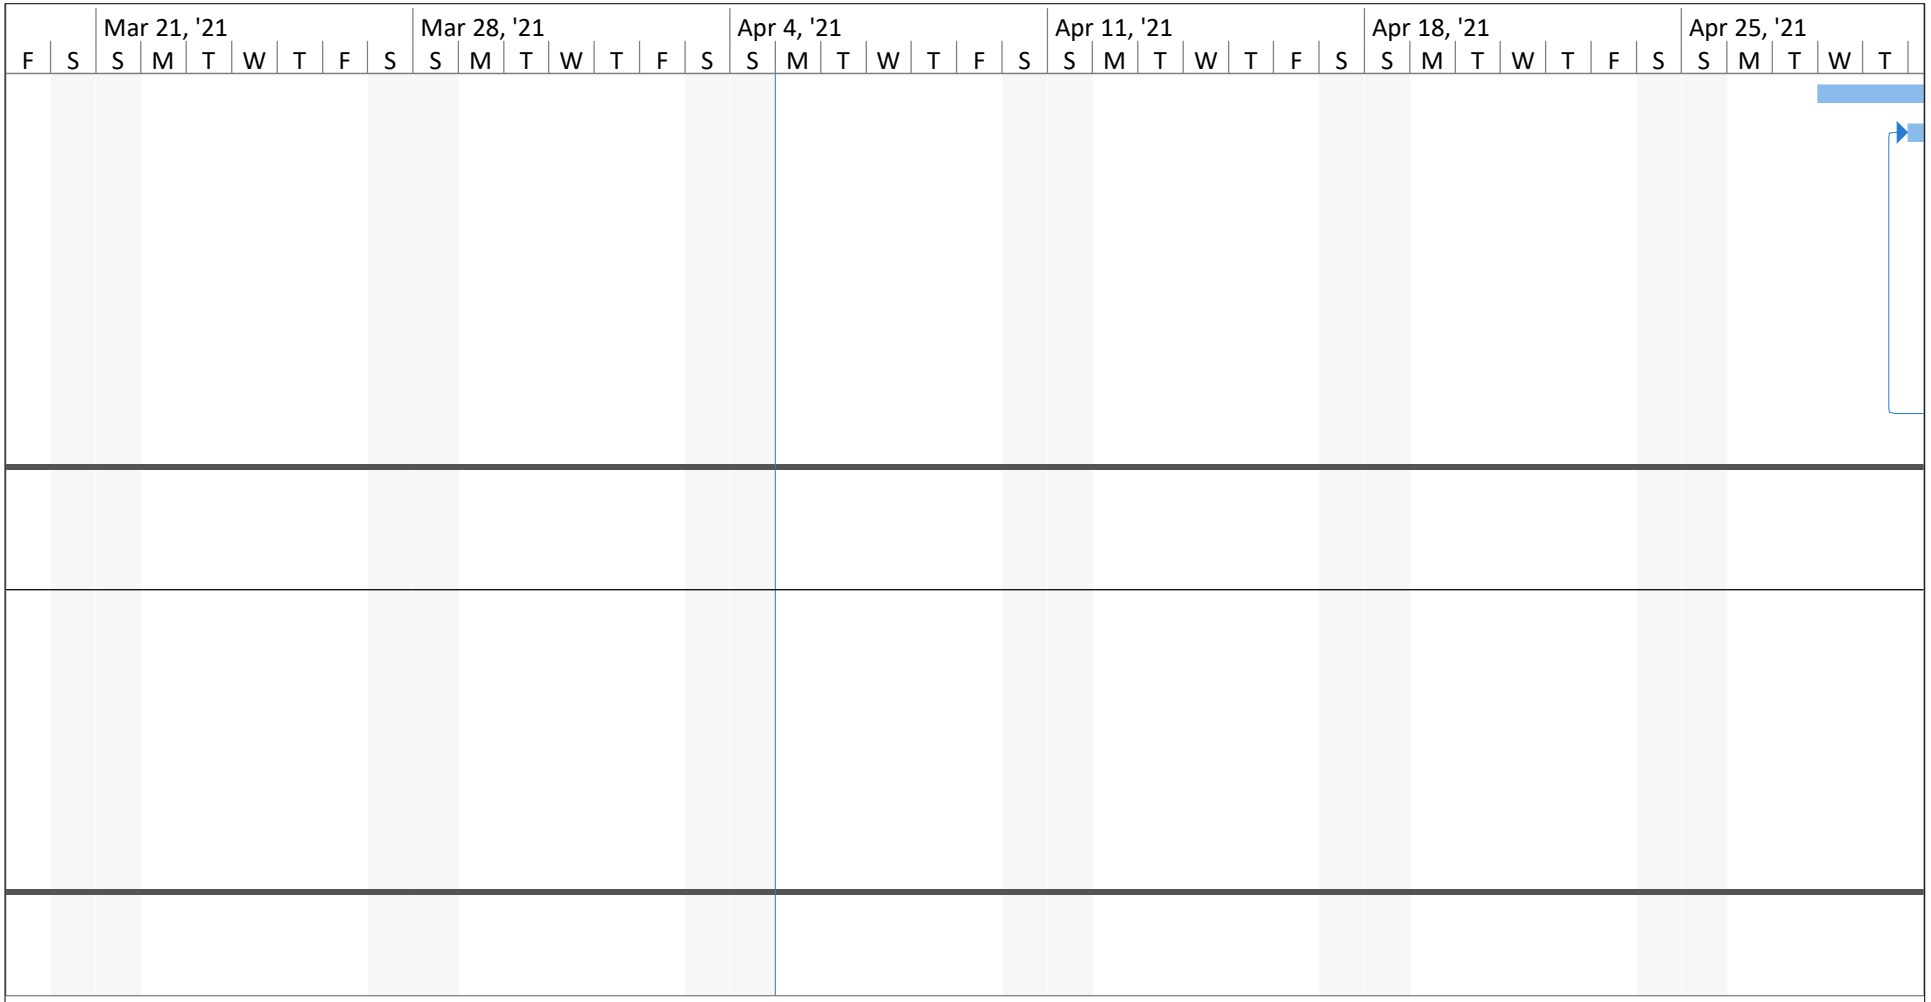


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

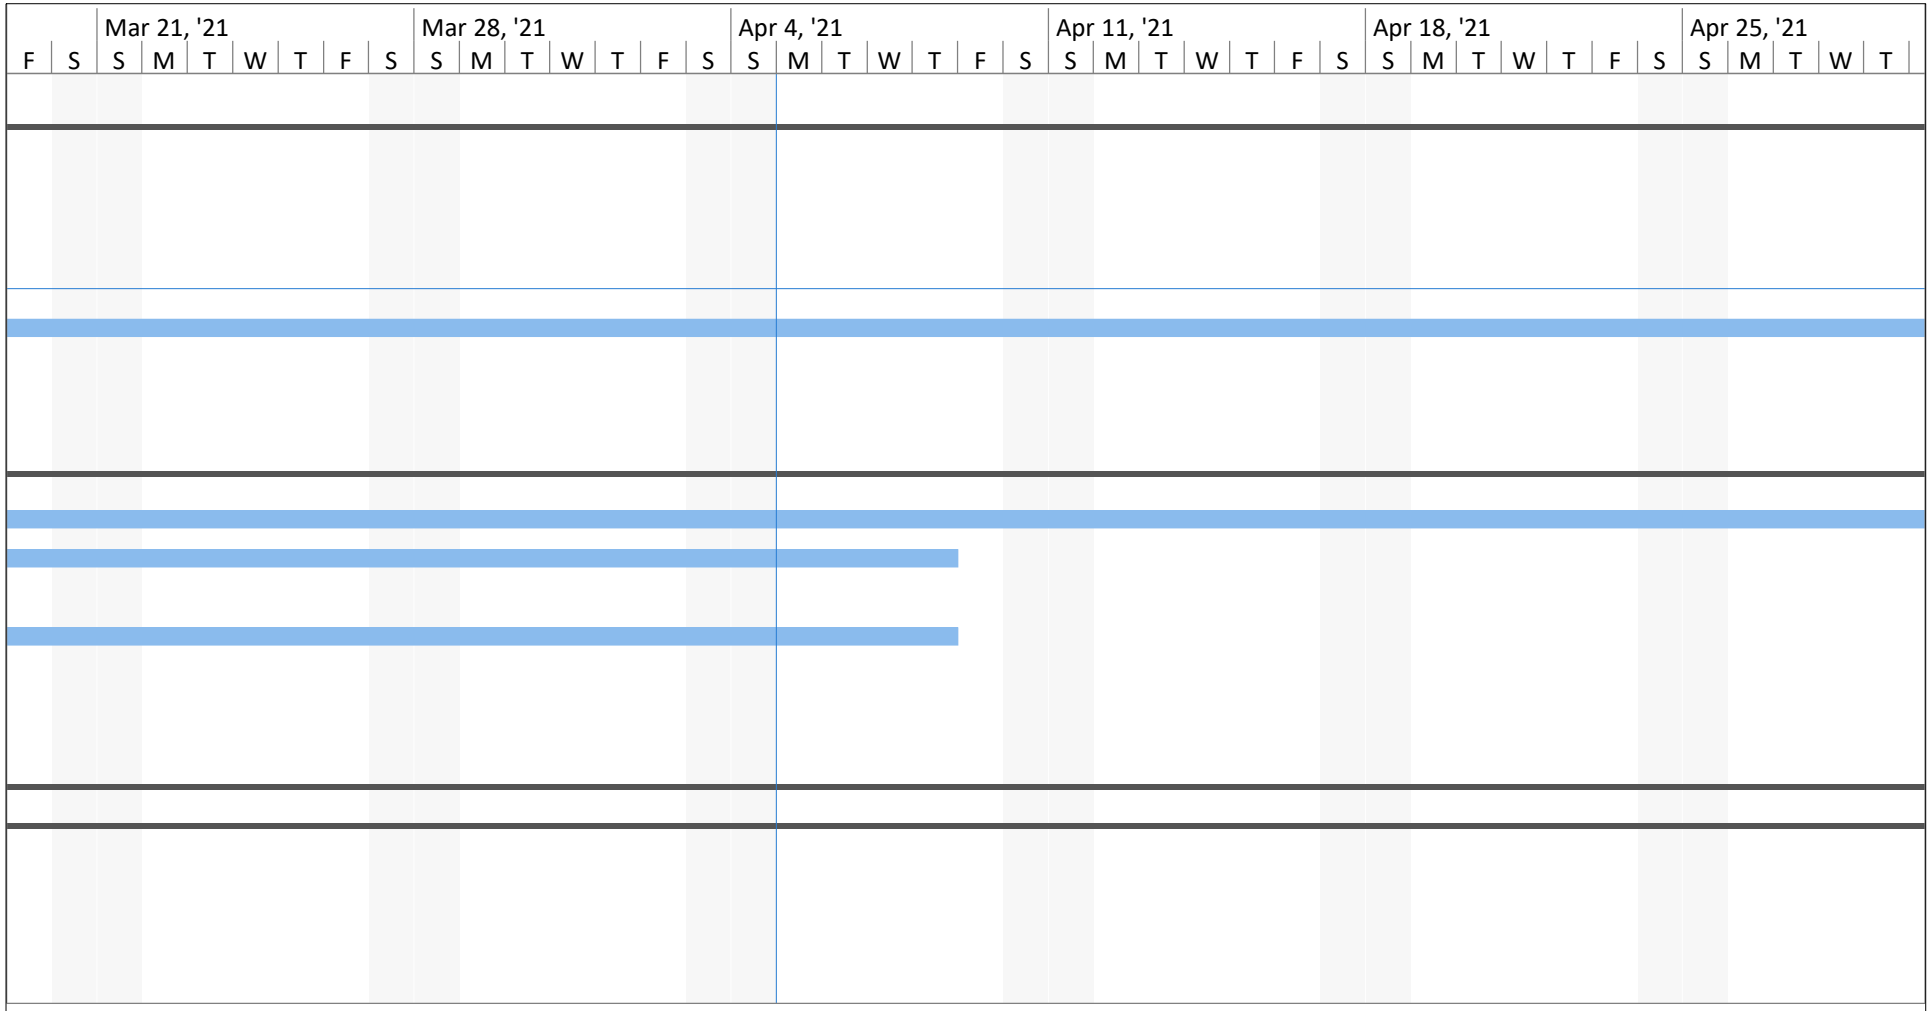


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

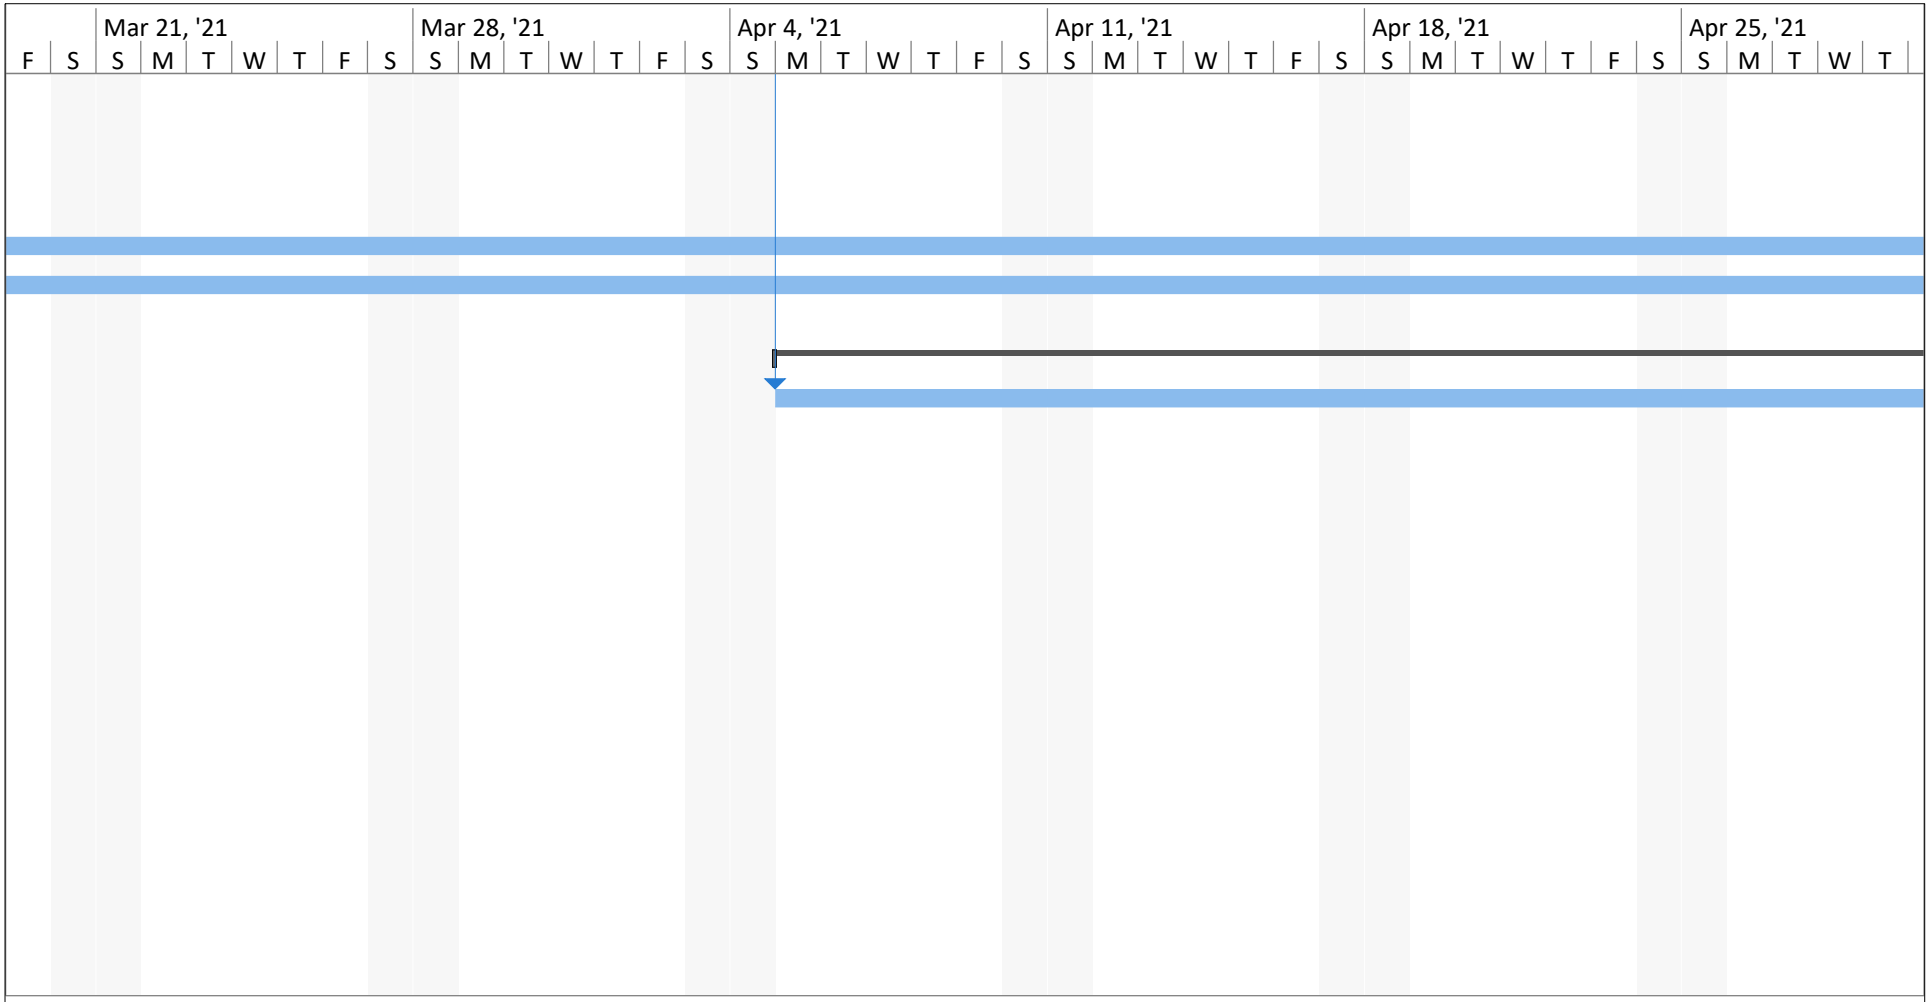


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |




Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

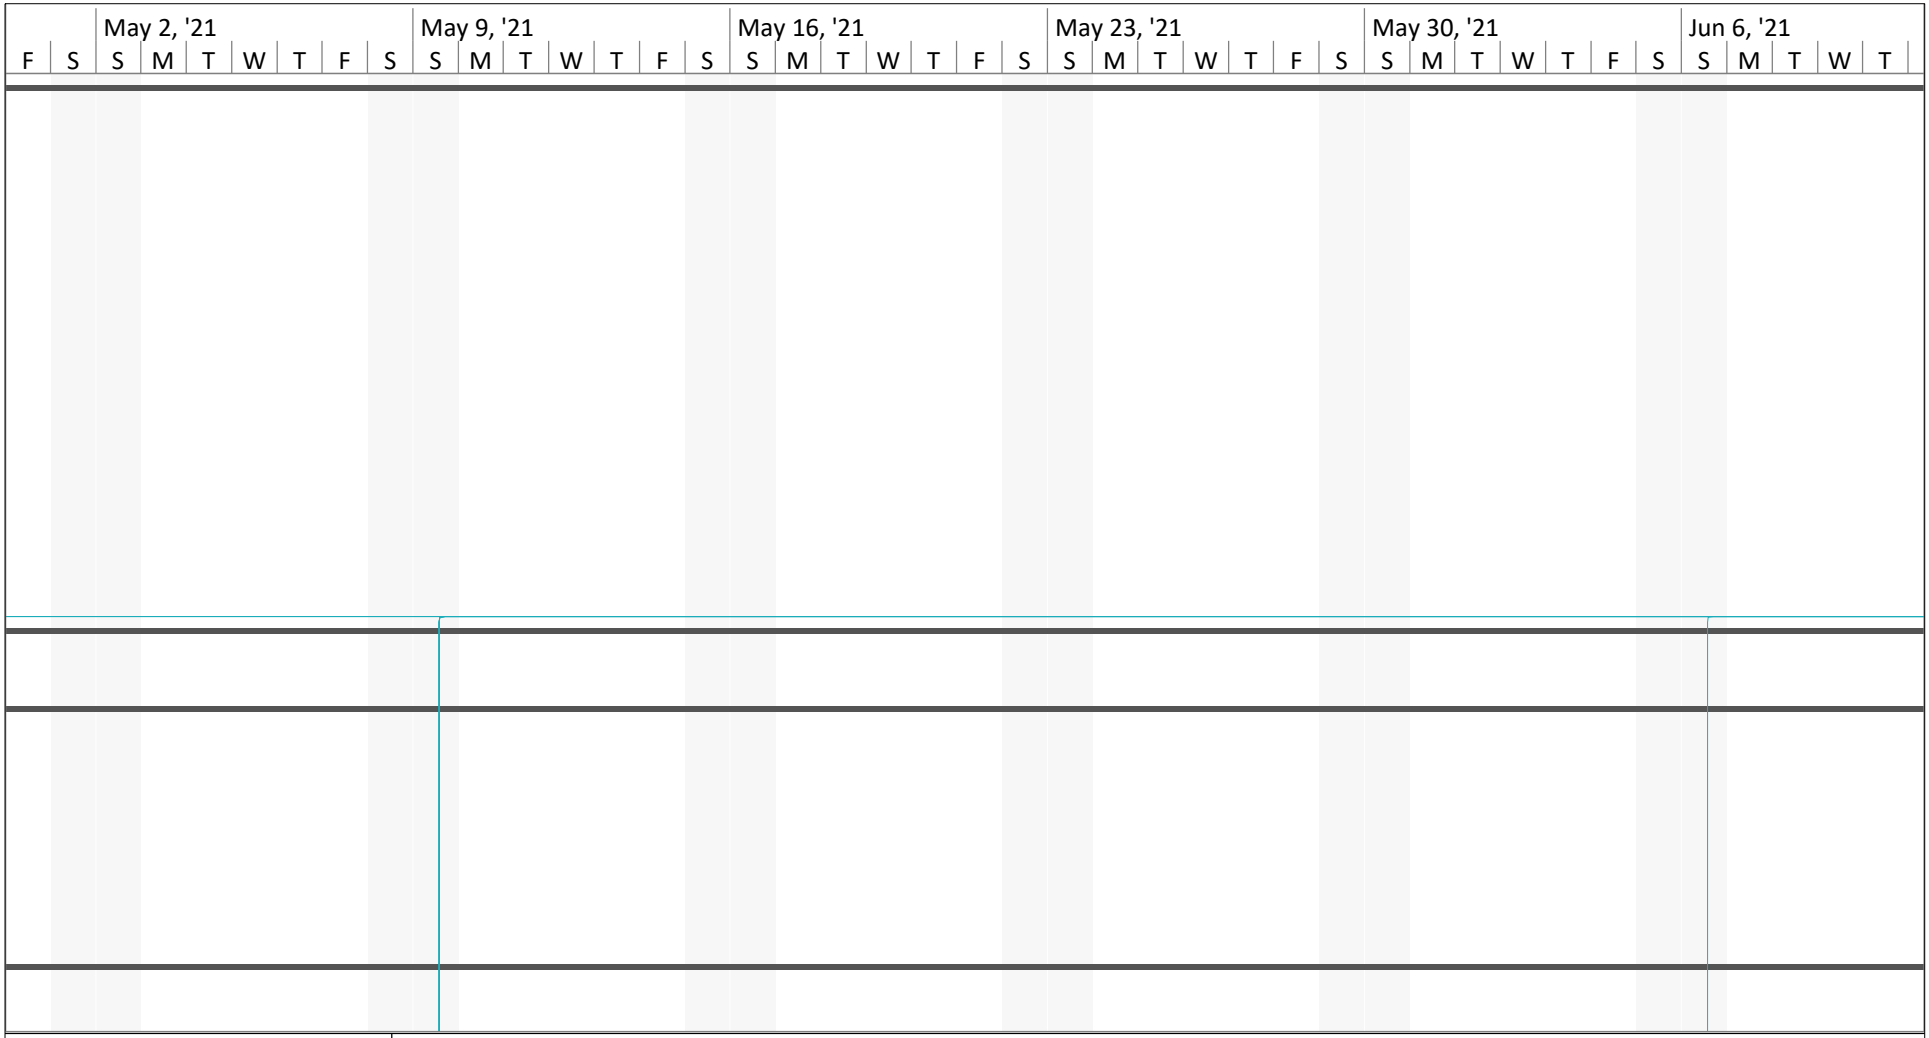


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

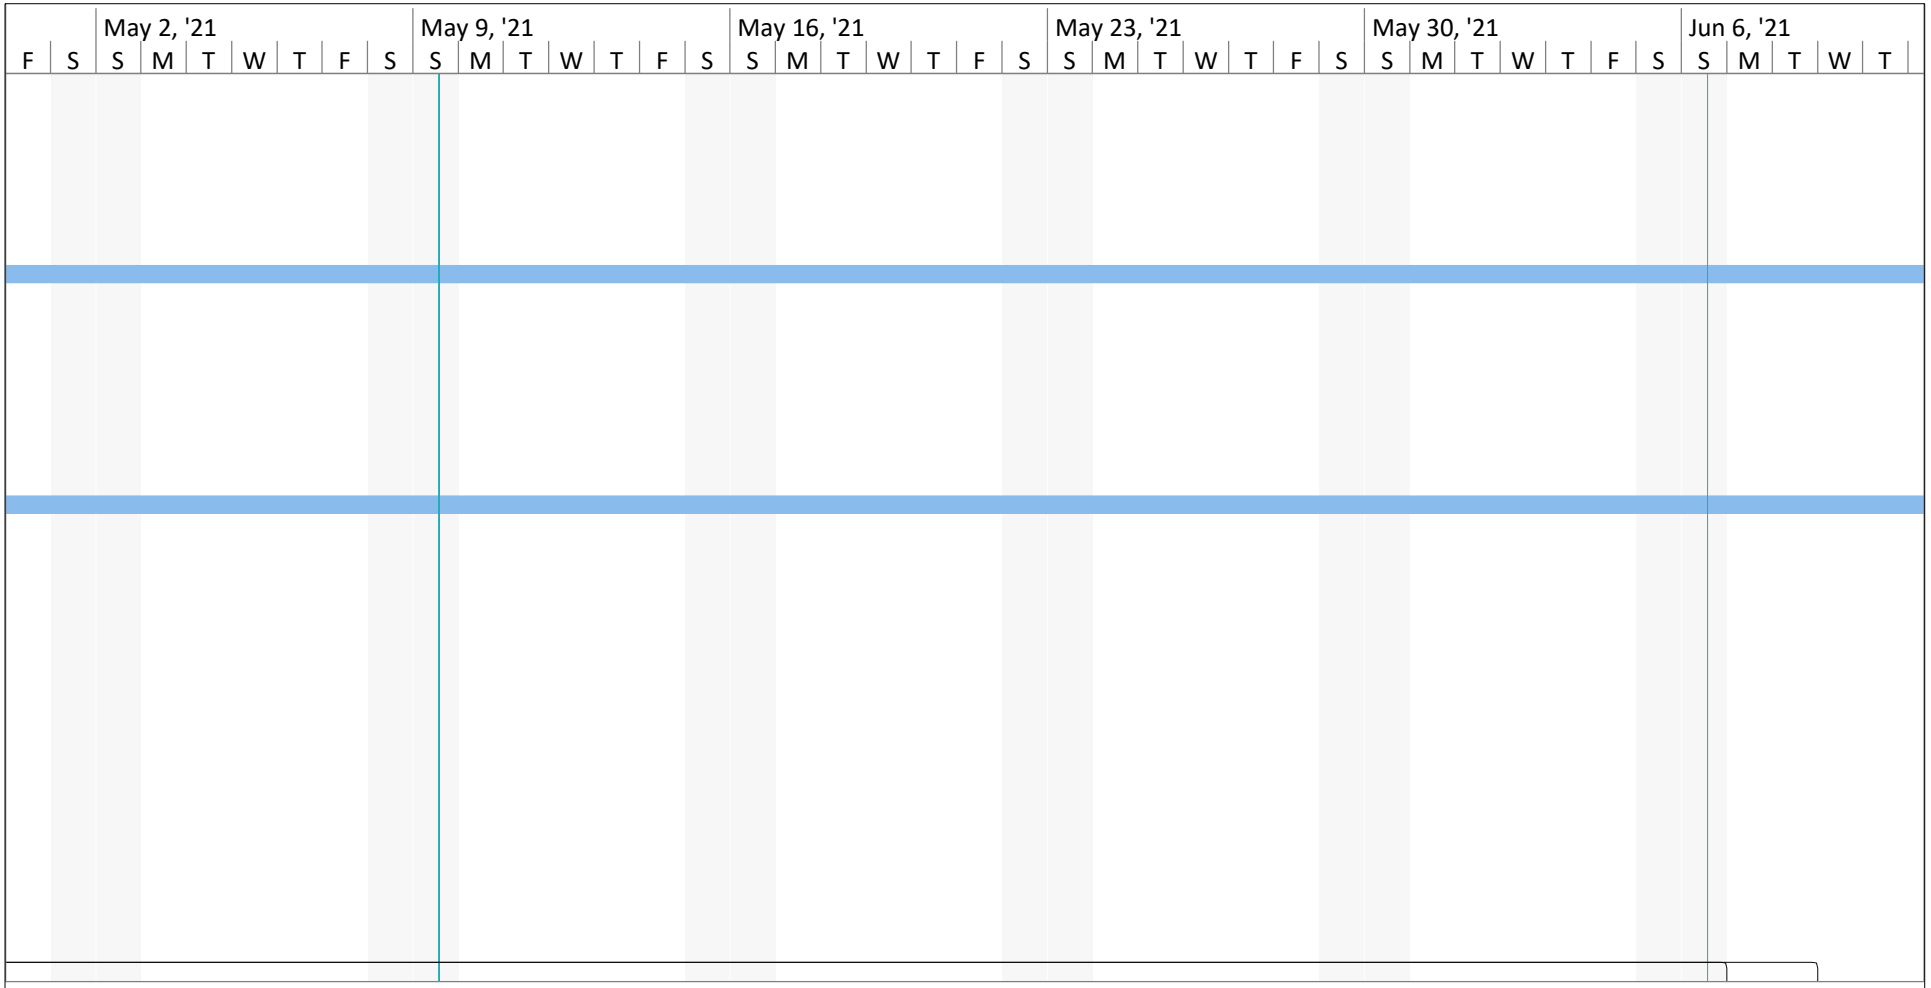


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

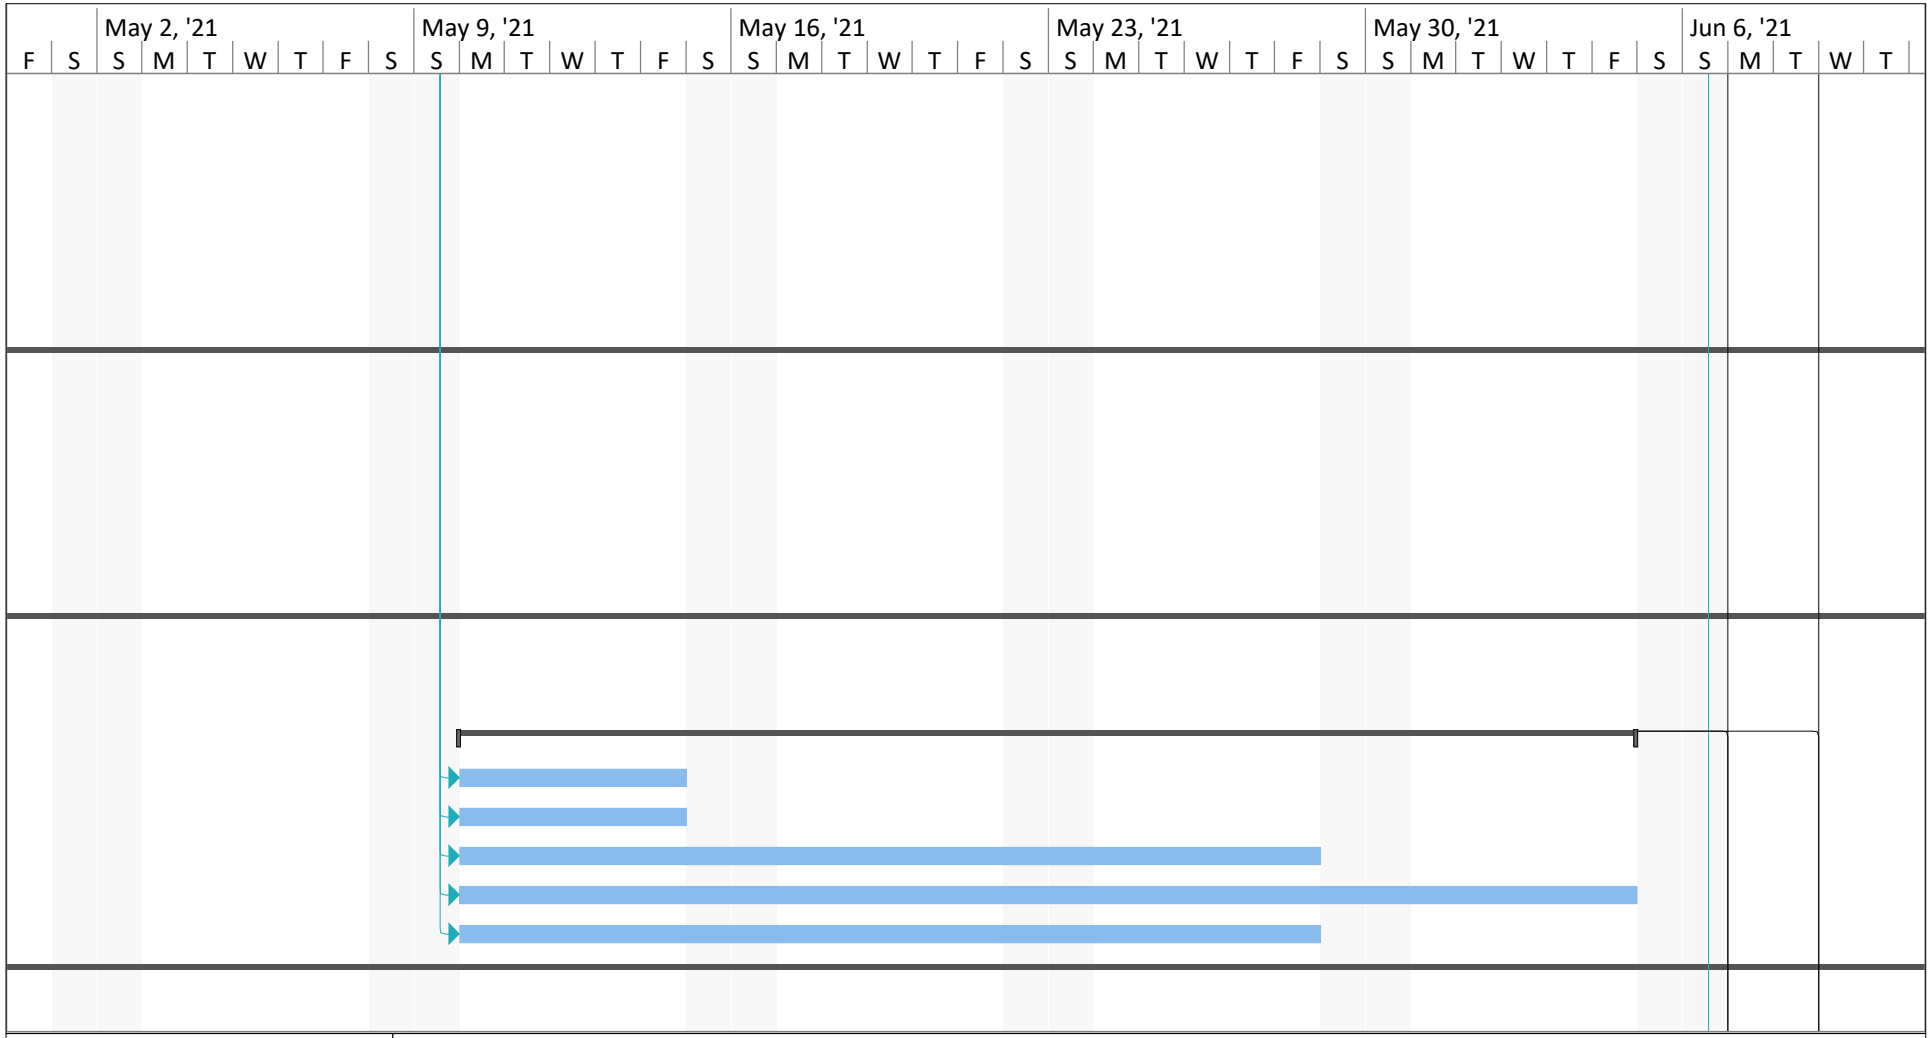


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

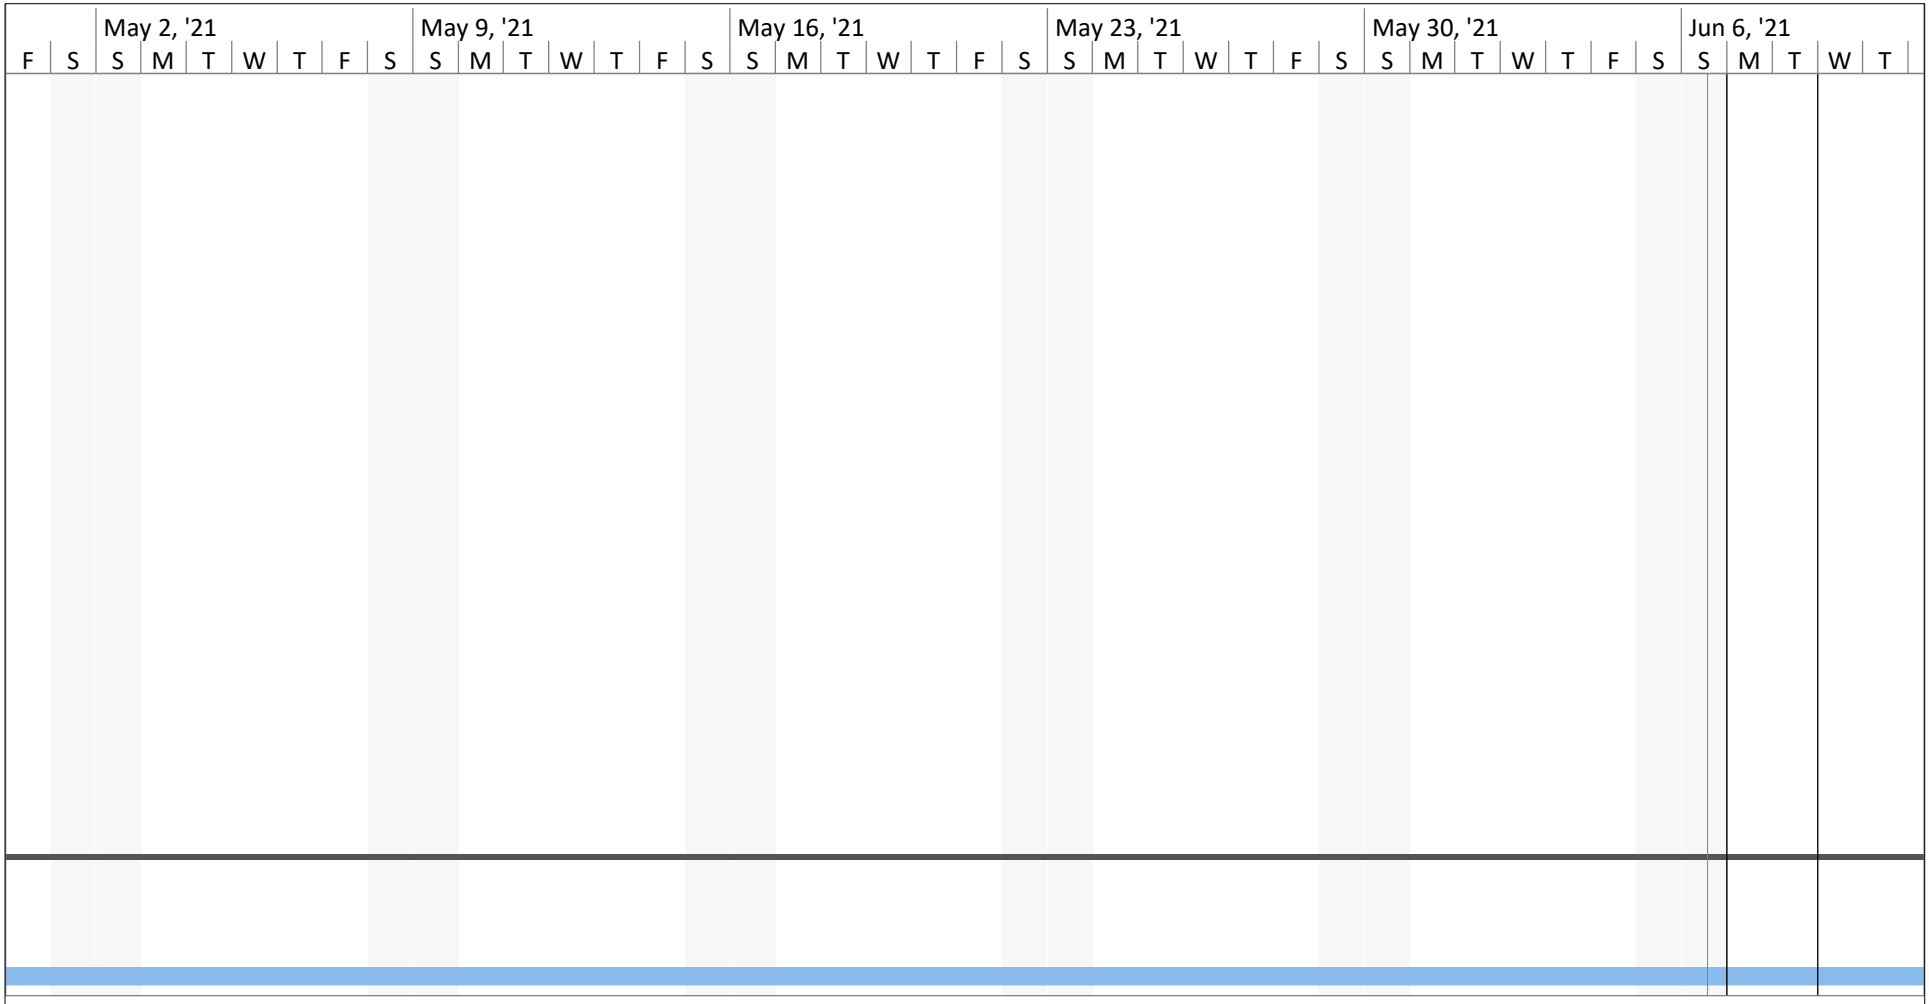


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

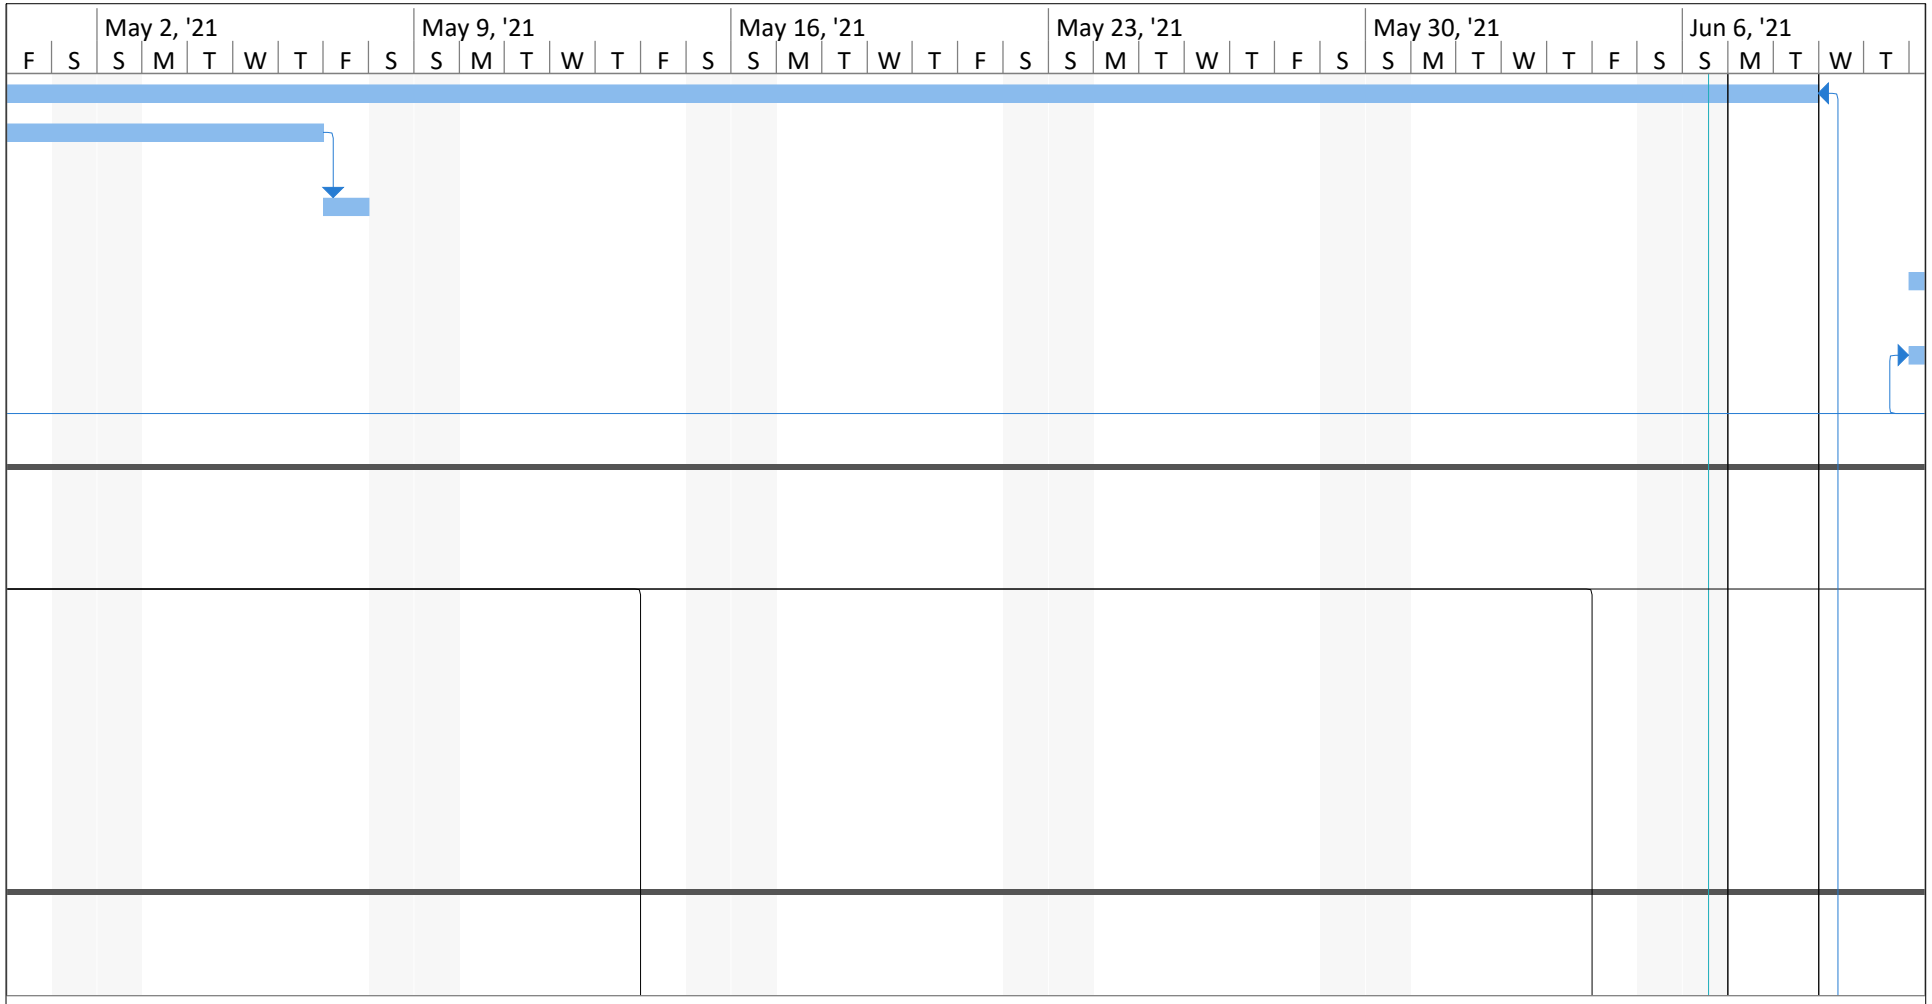


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

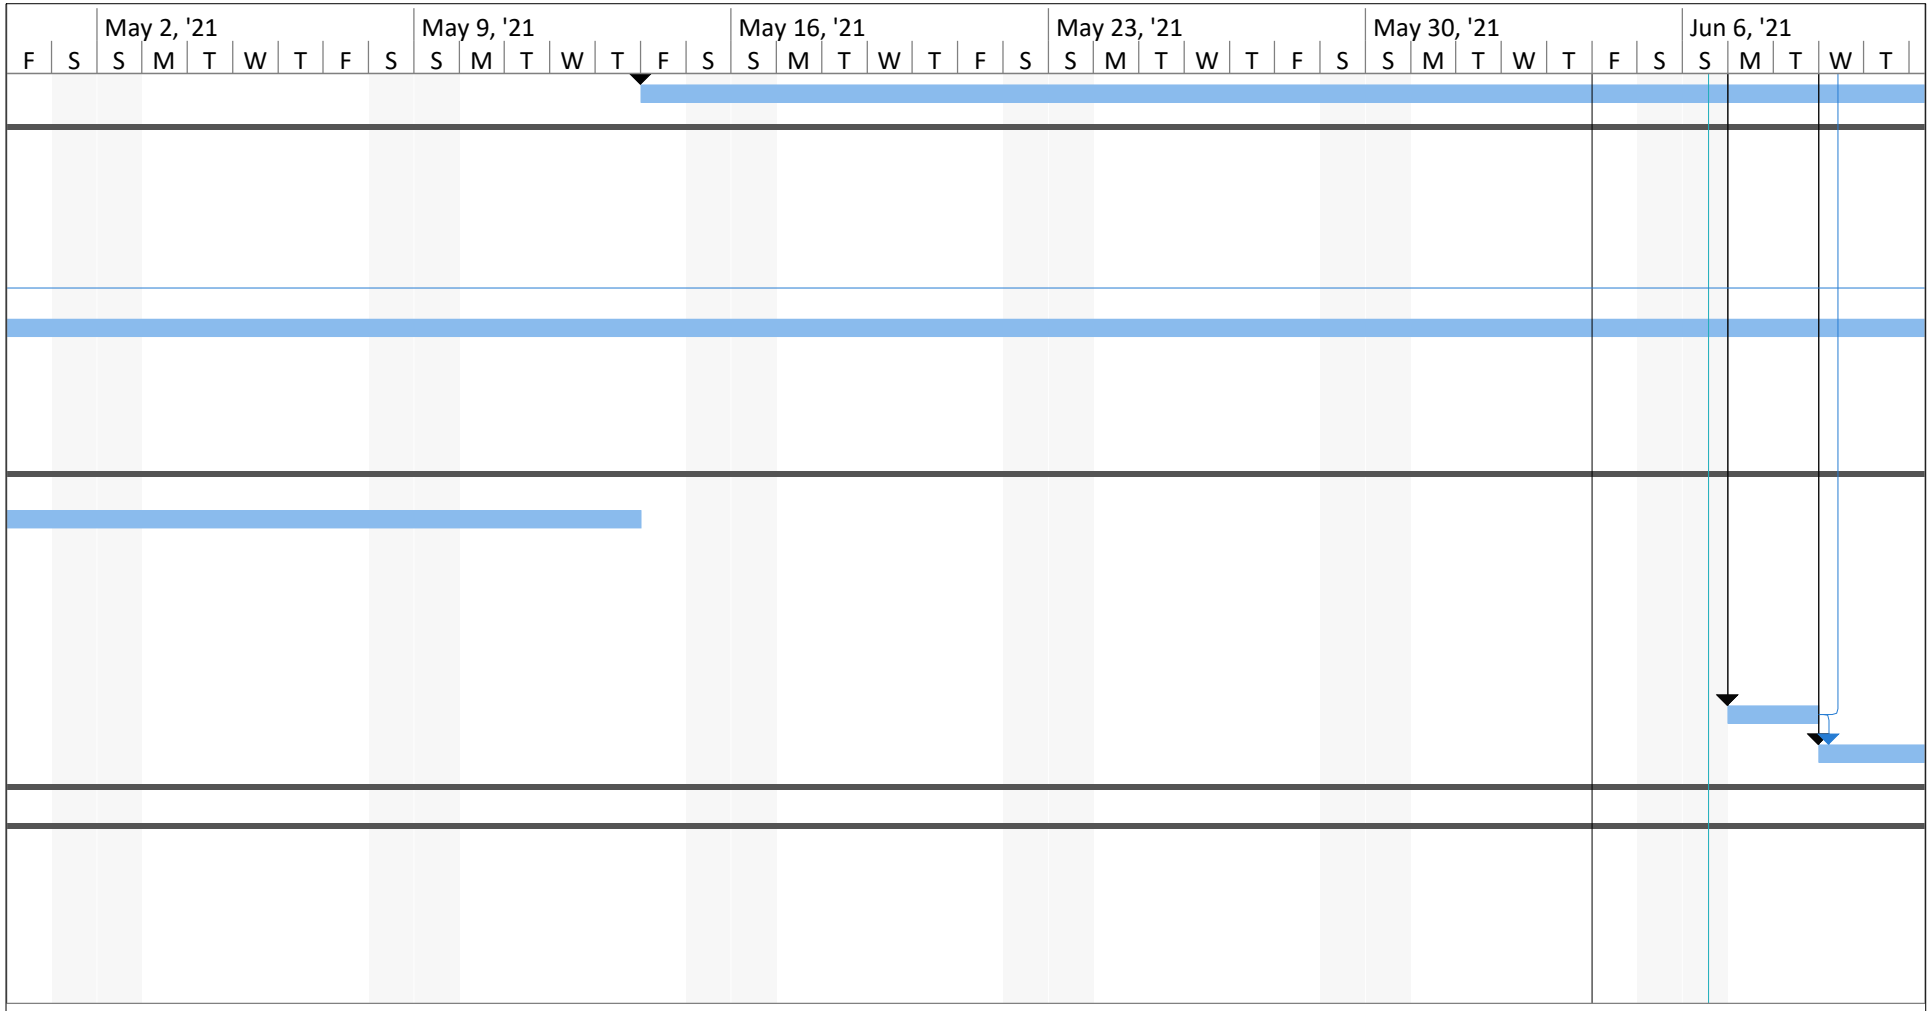


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

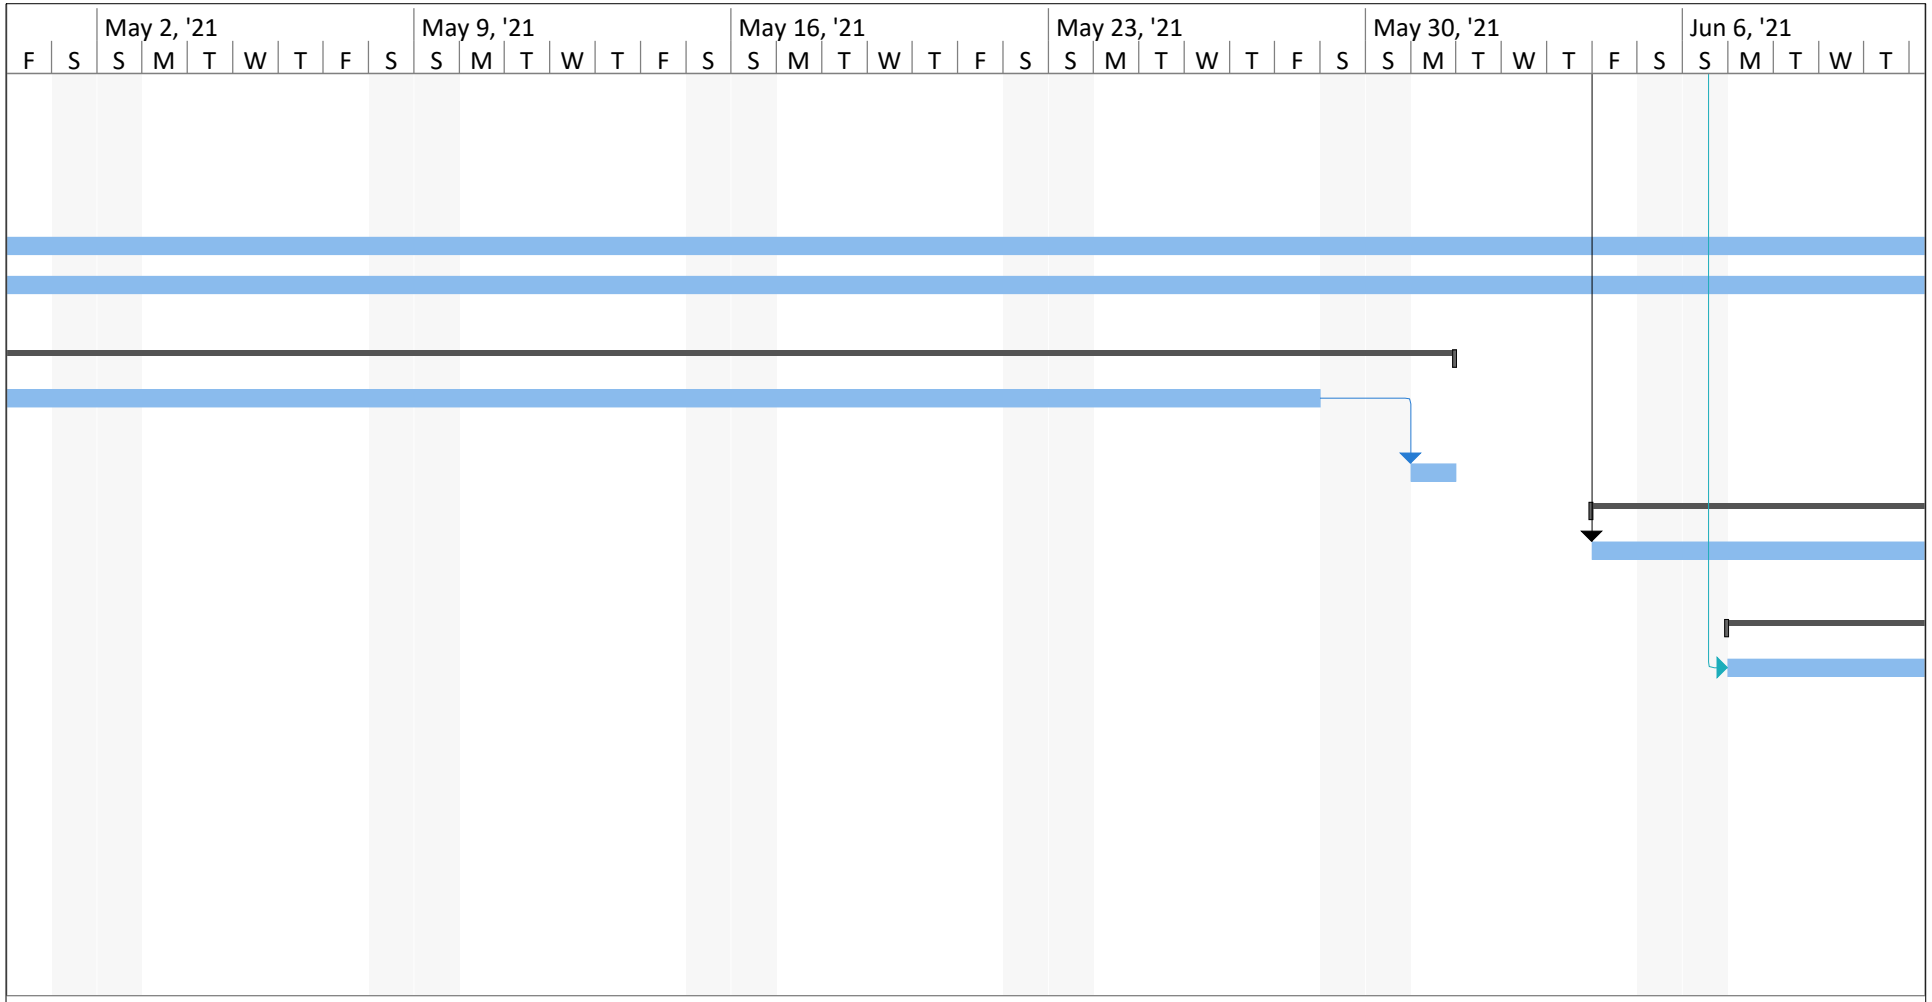


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |




Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

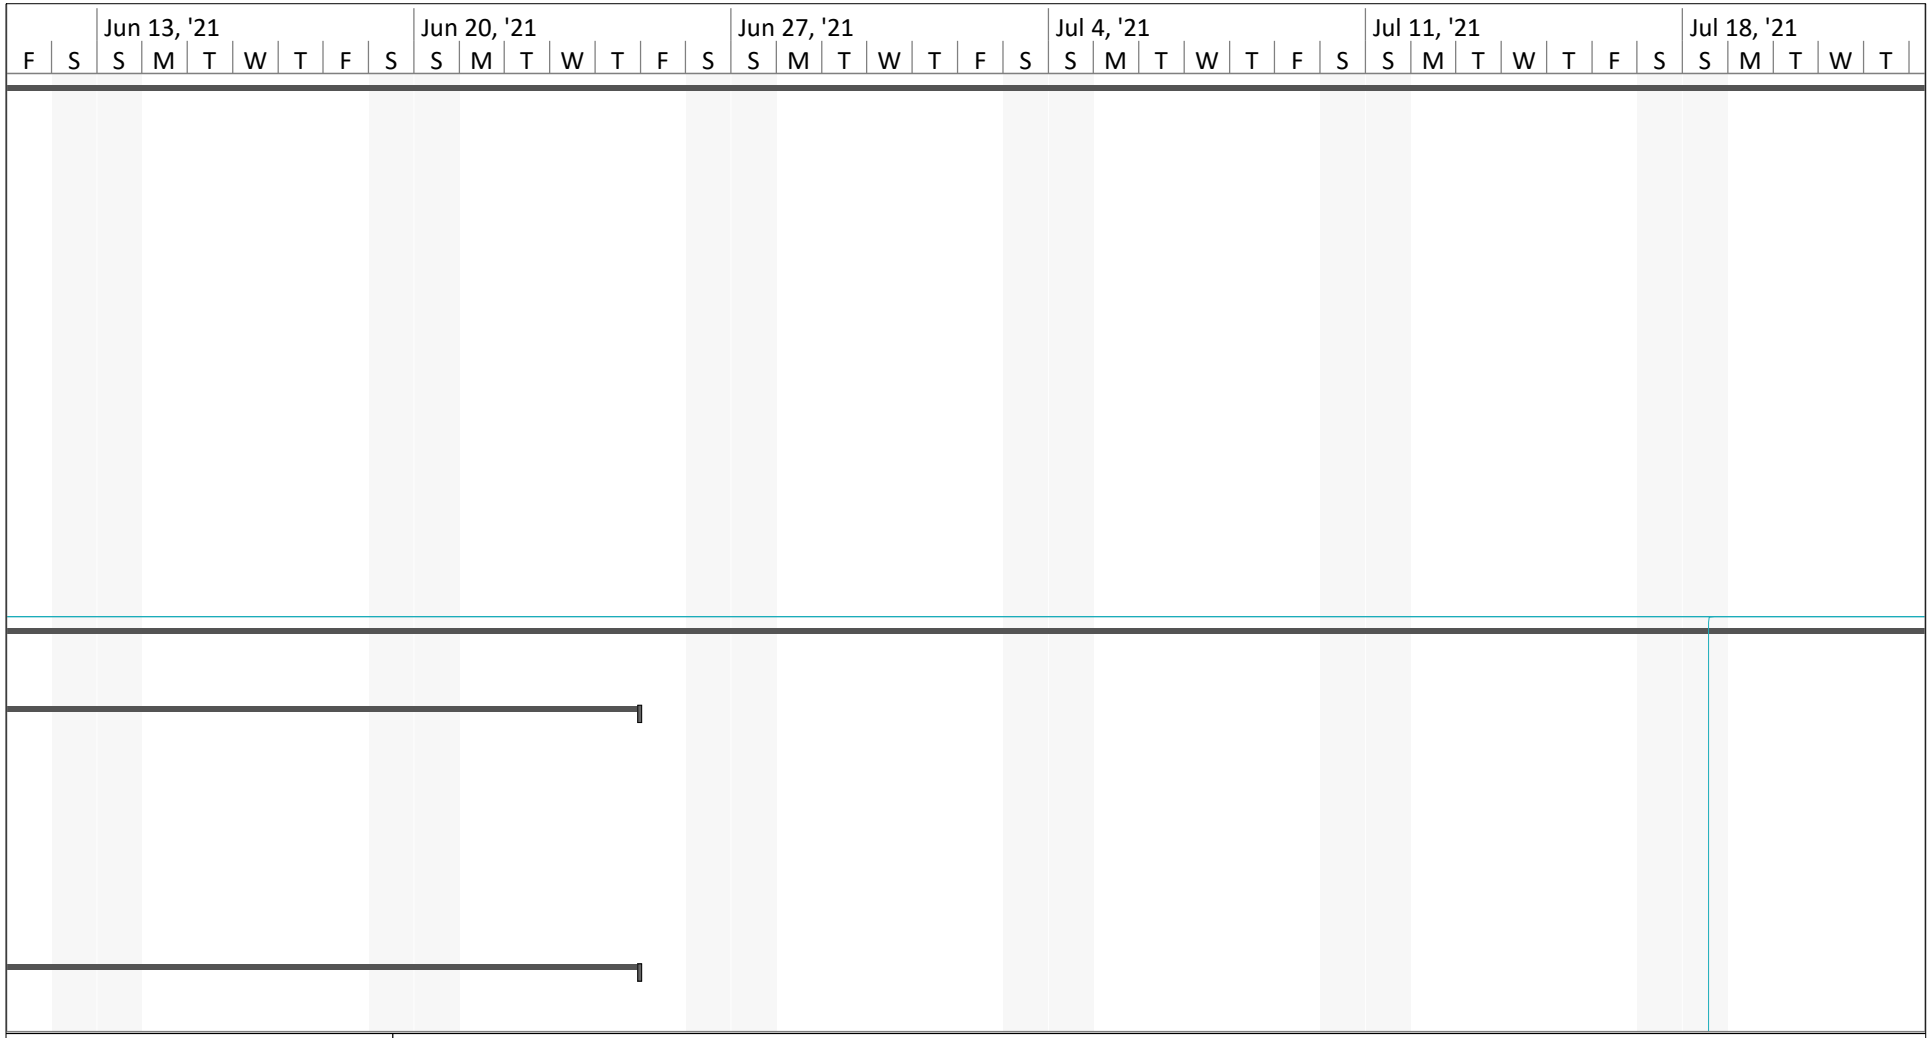


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

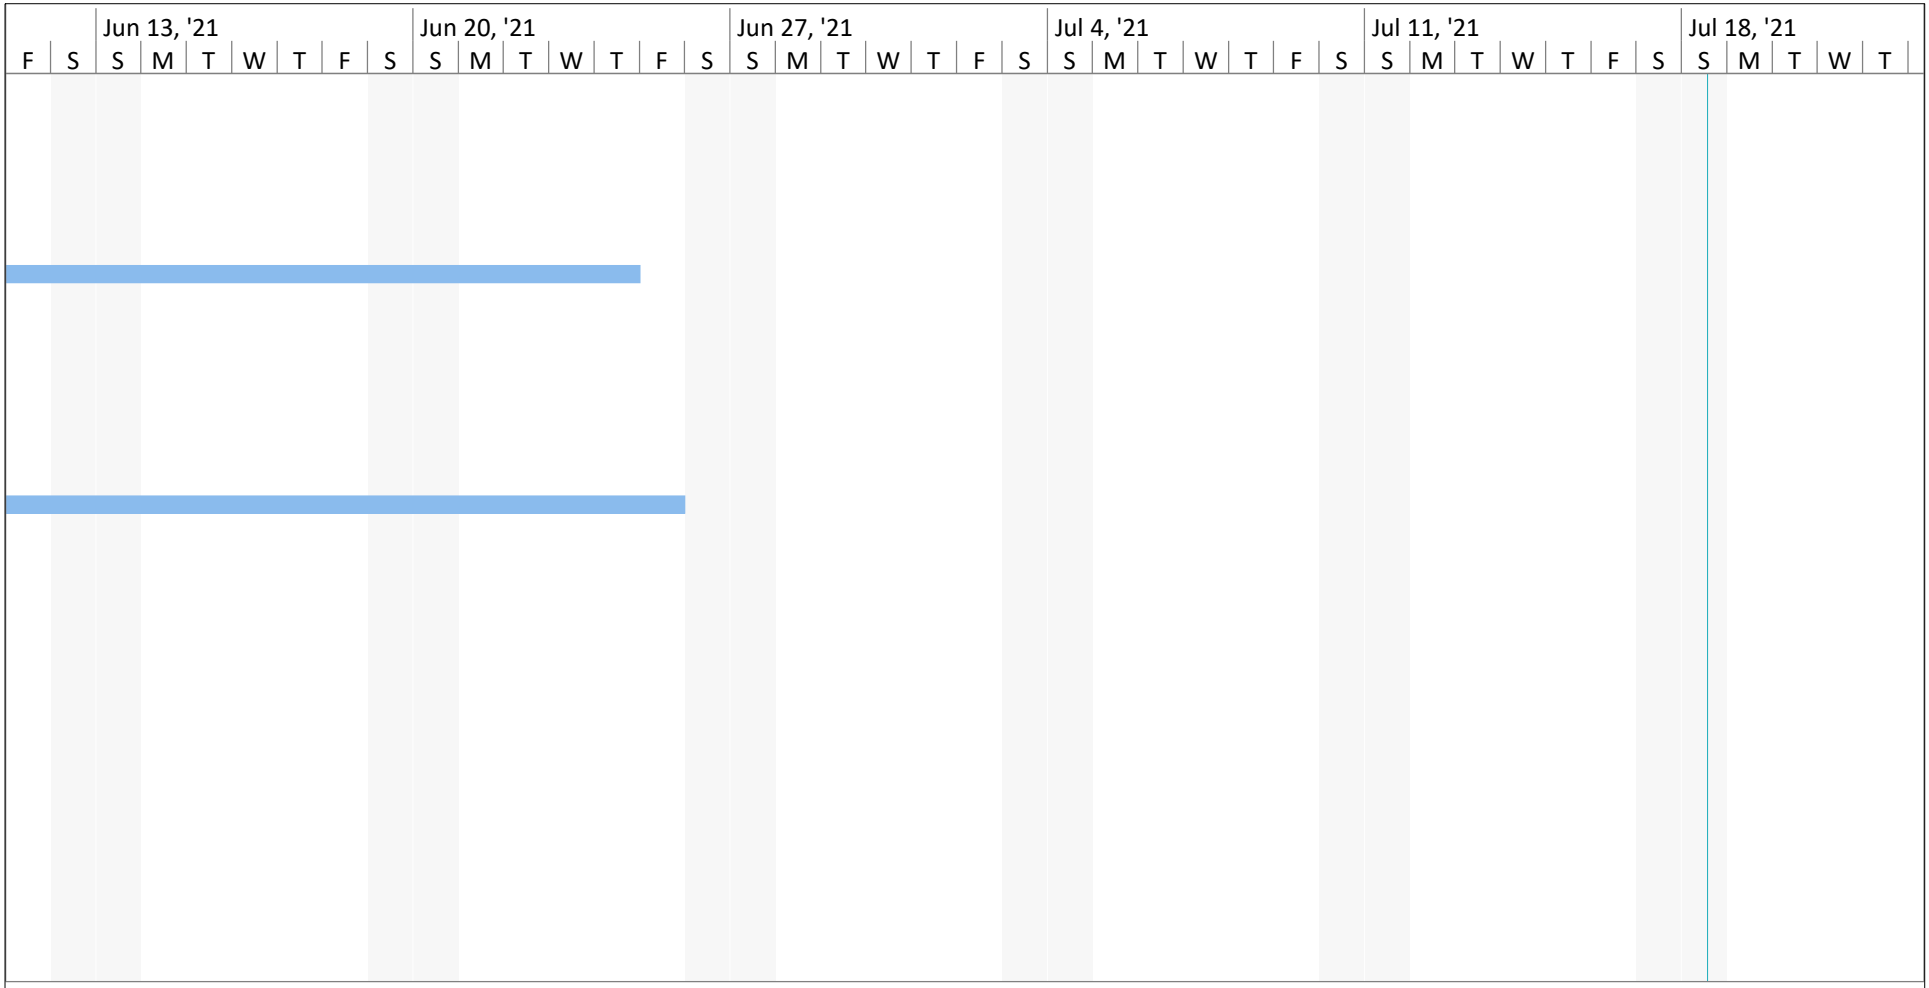


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

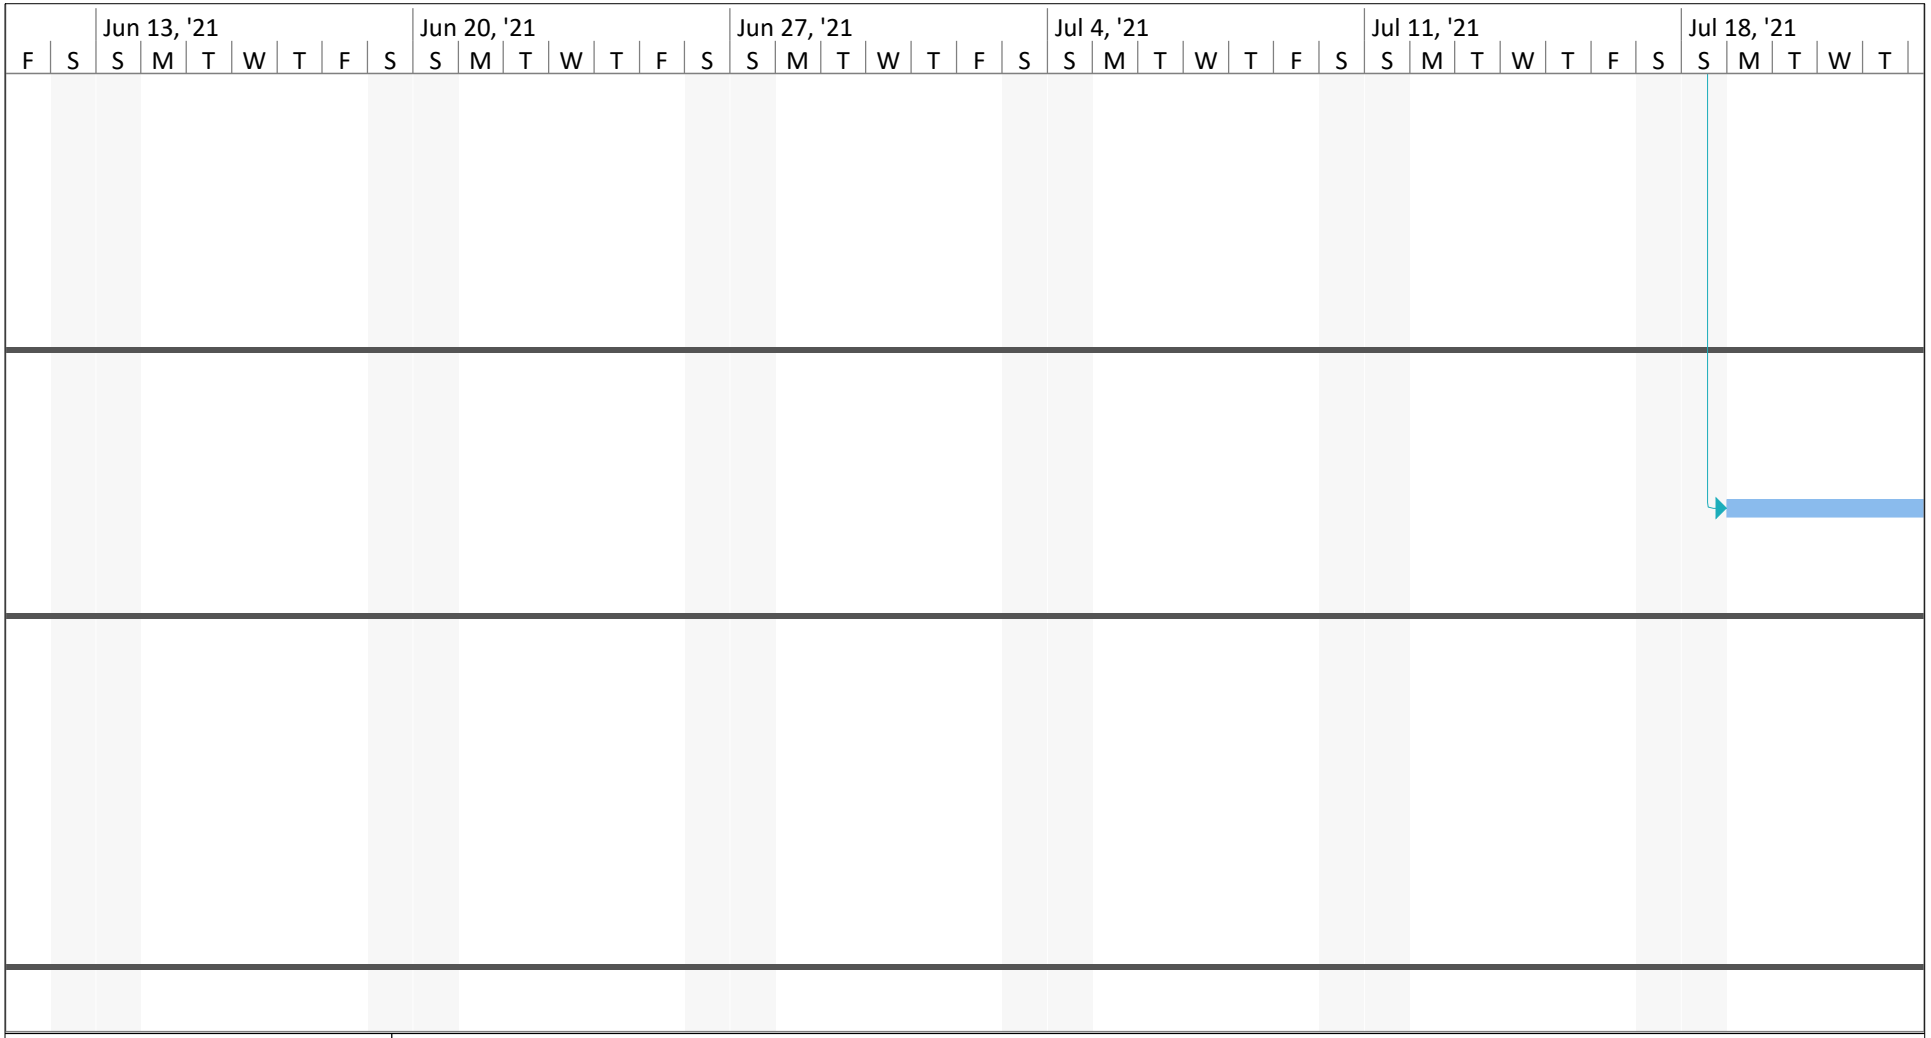


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

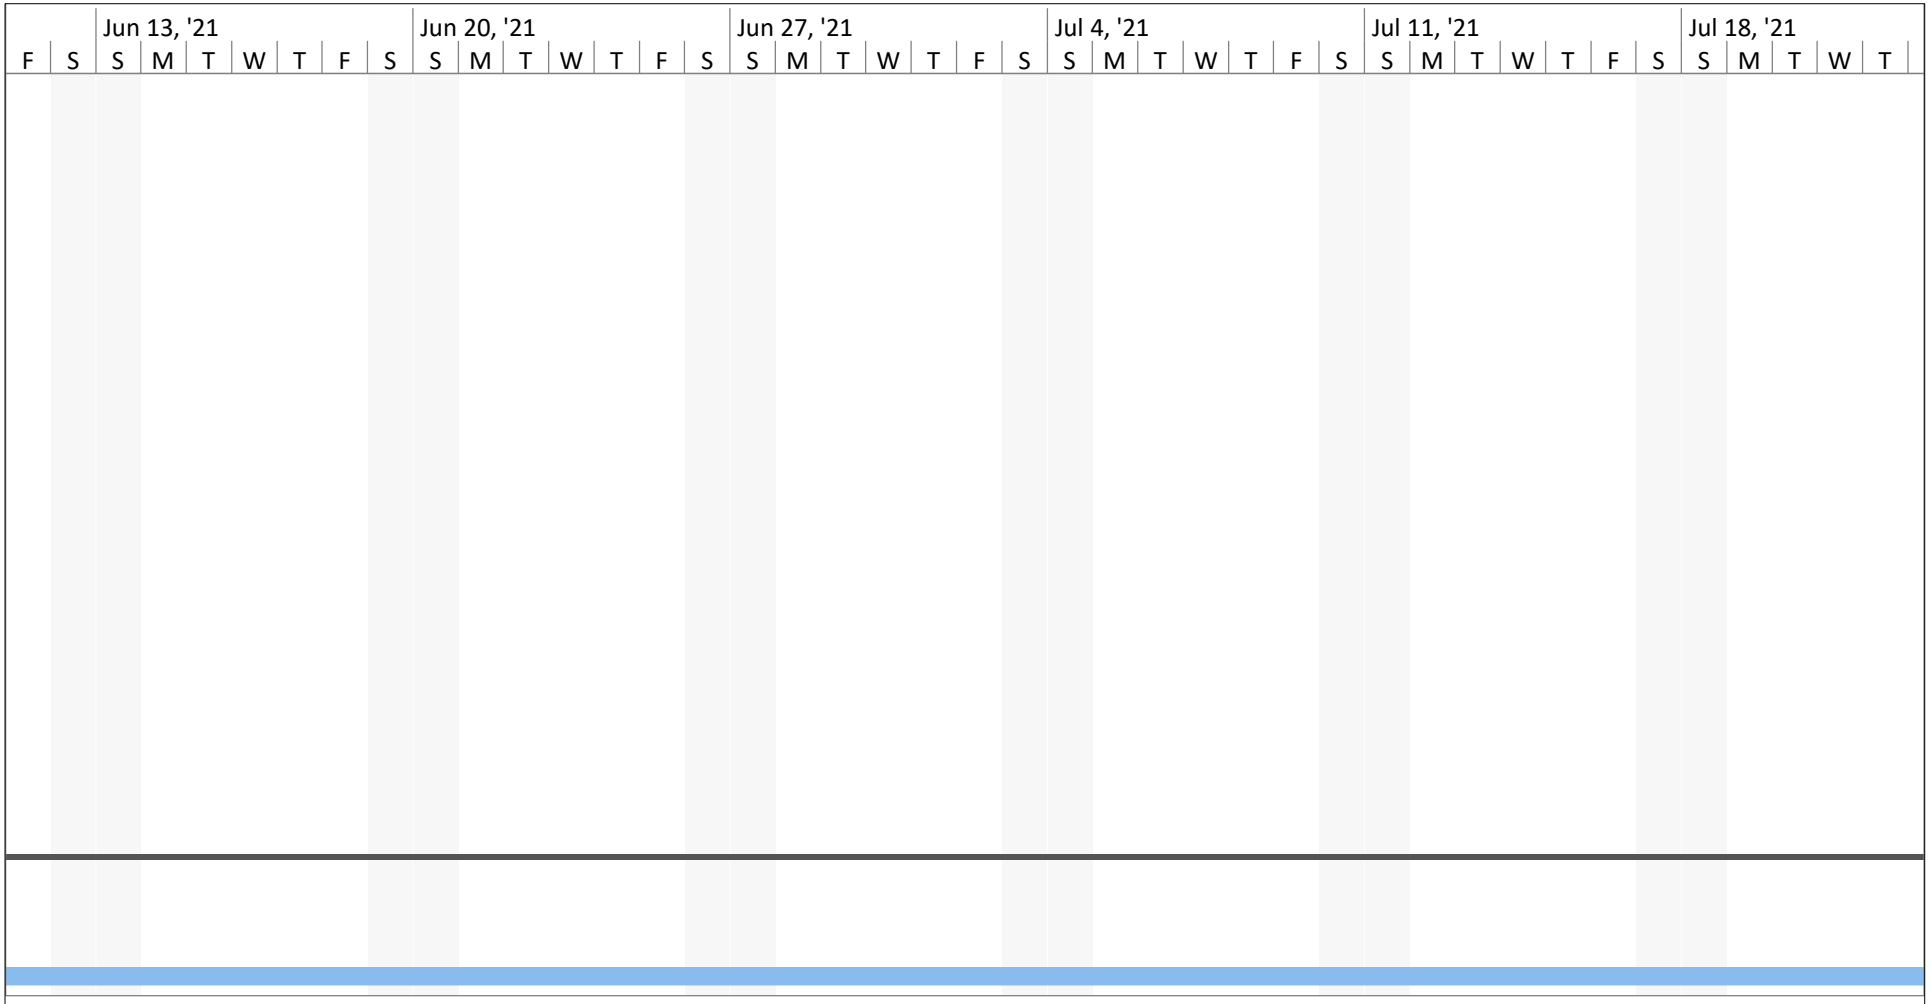


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

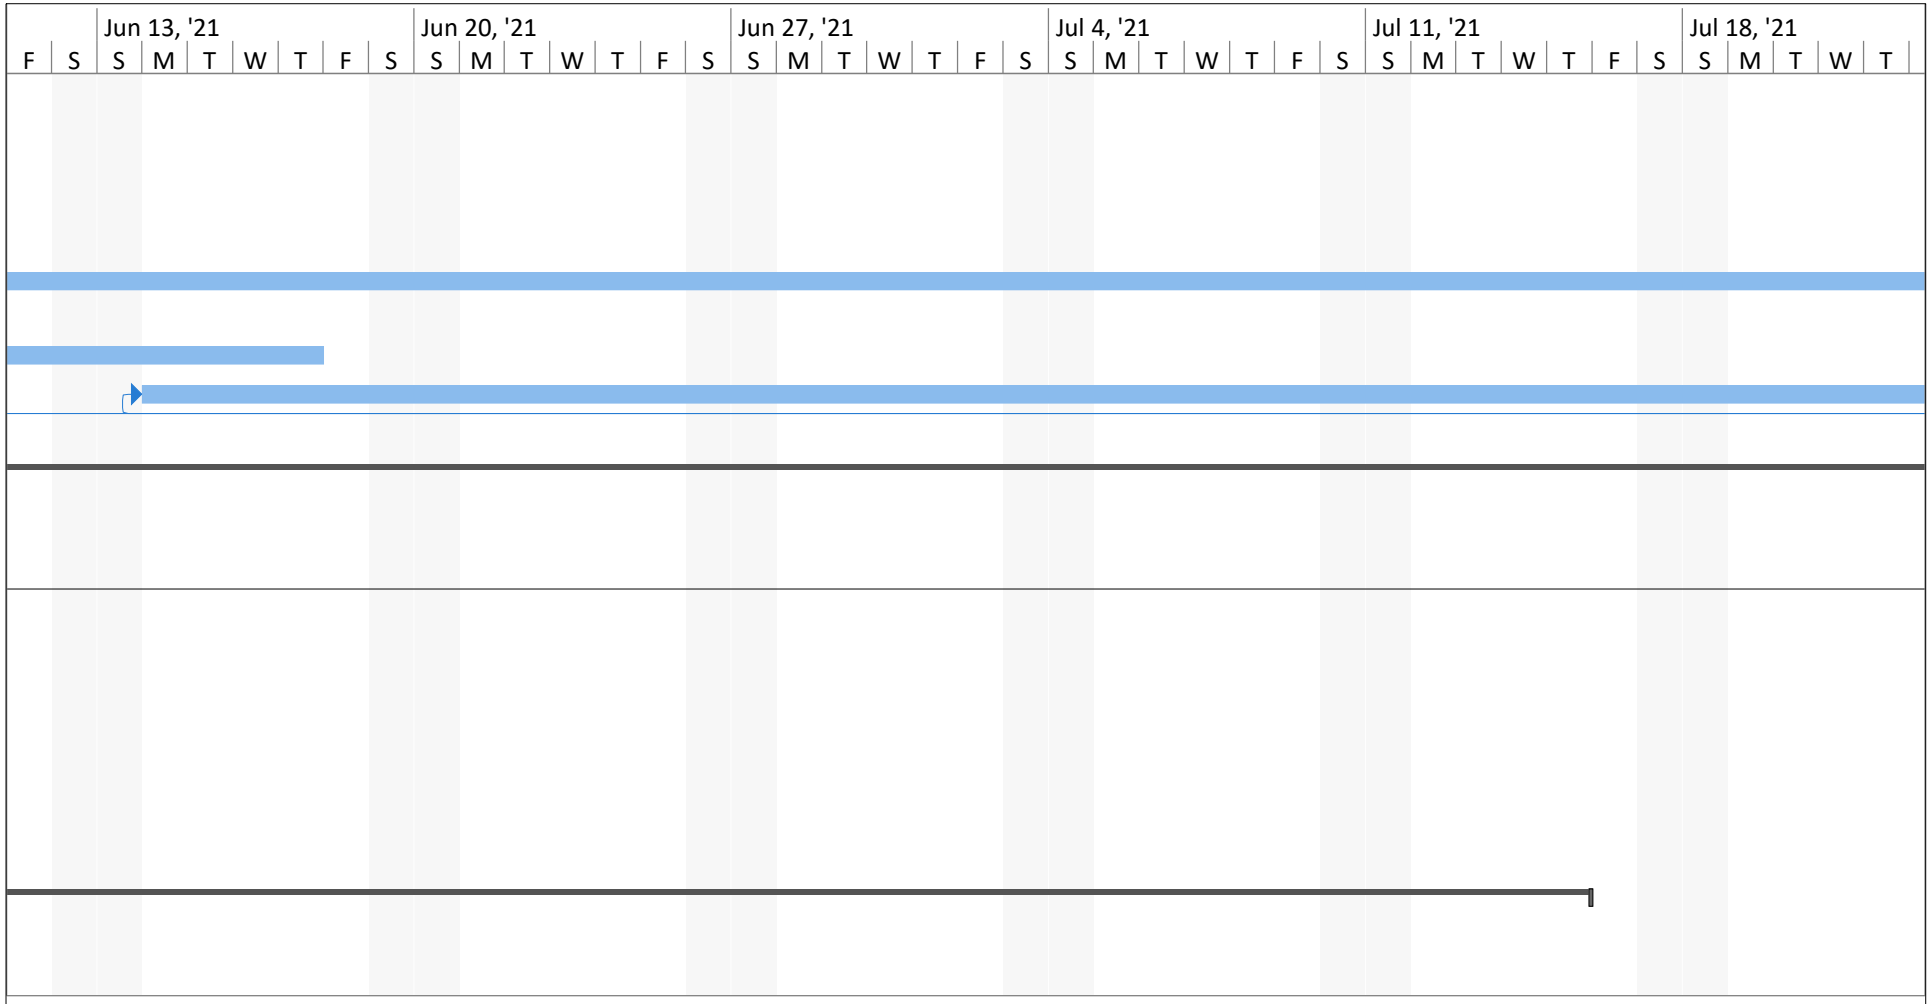


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

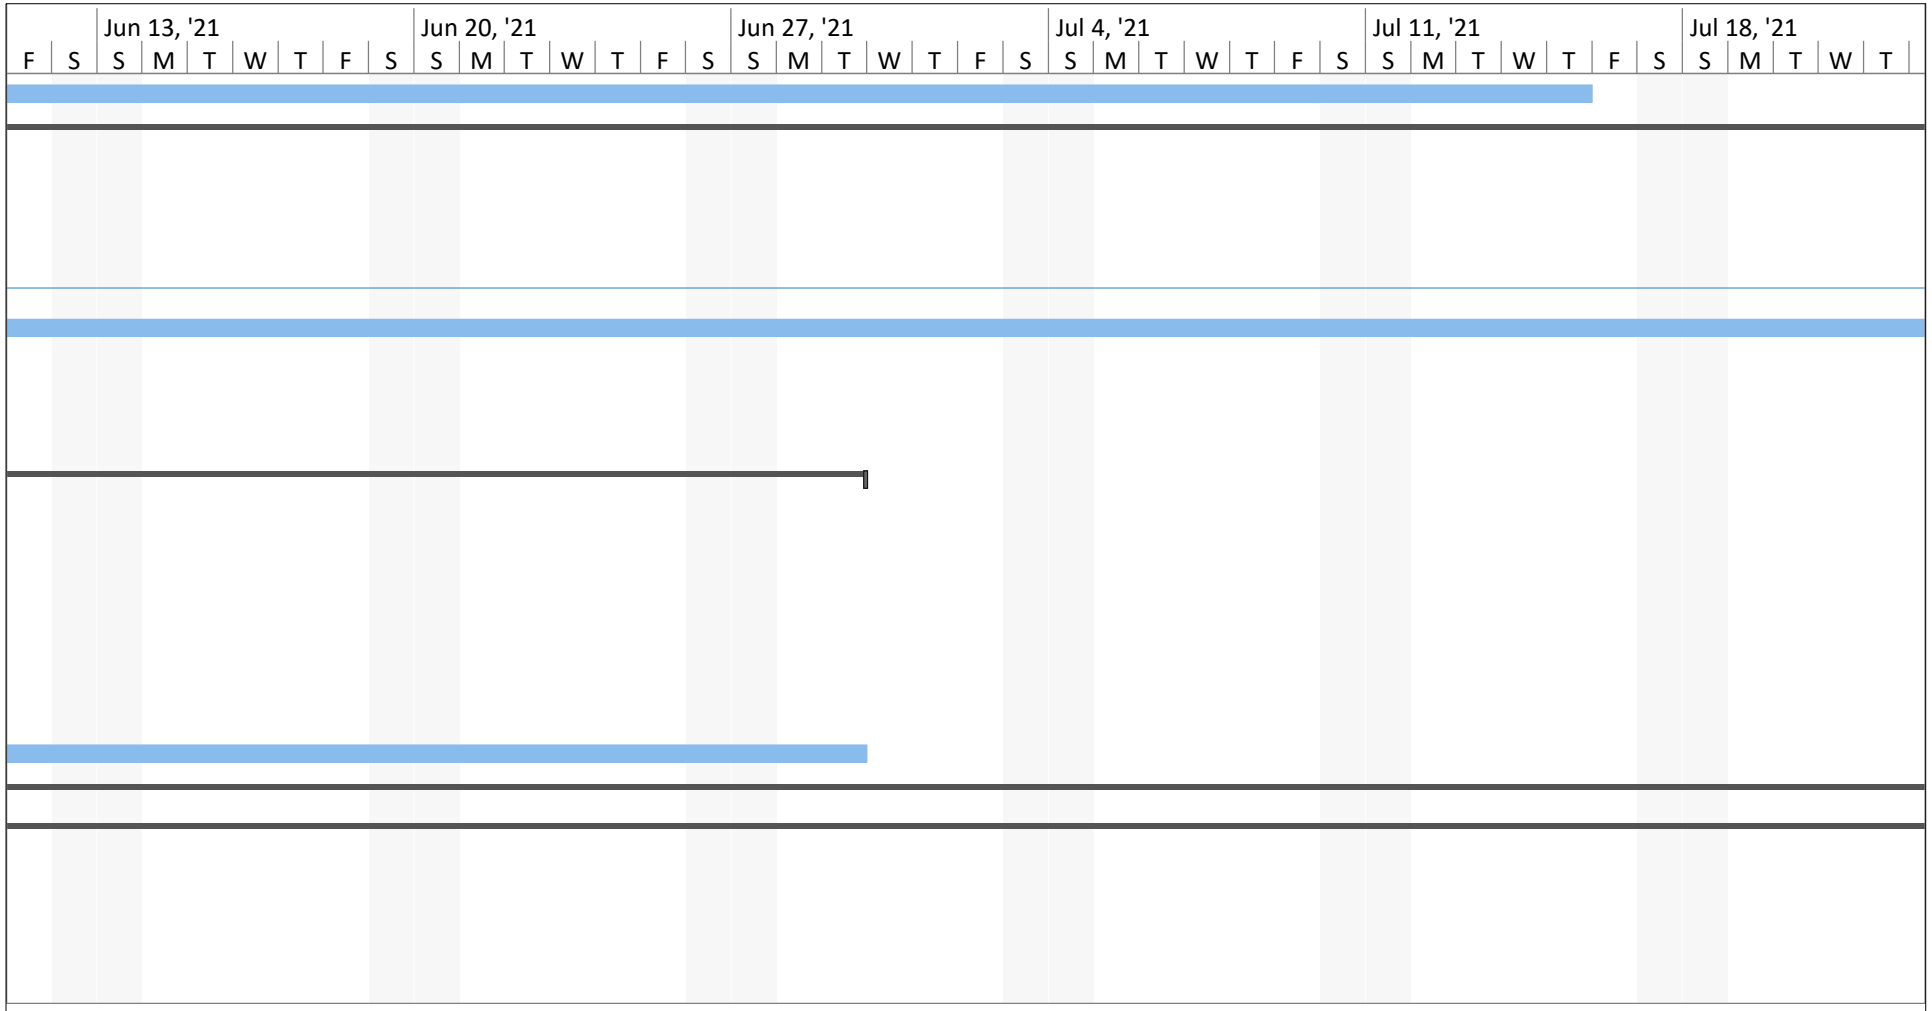


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

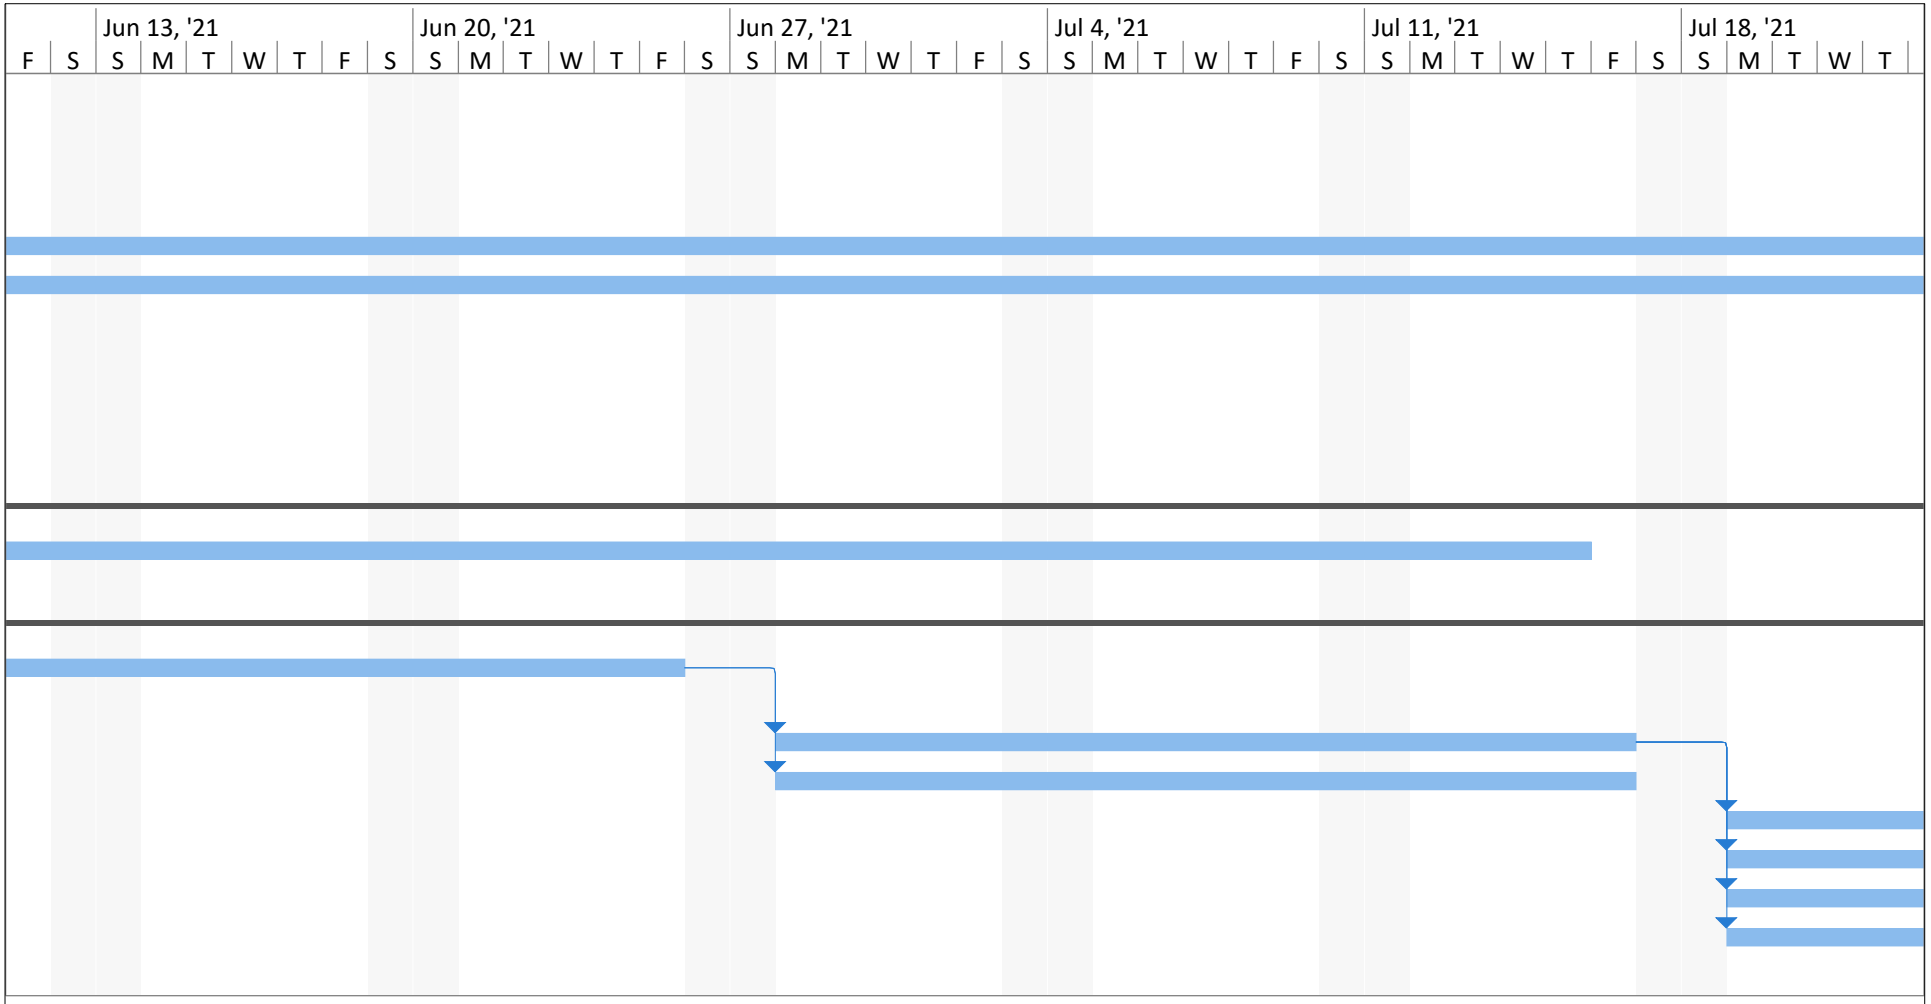


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |




Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

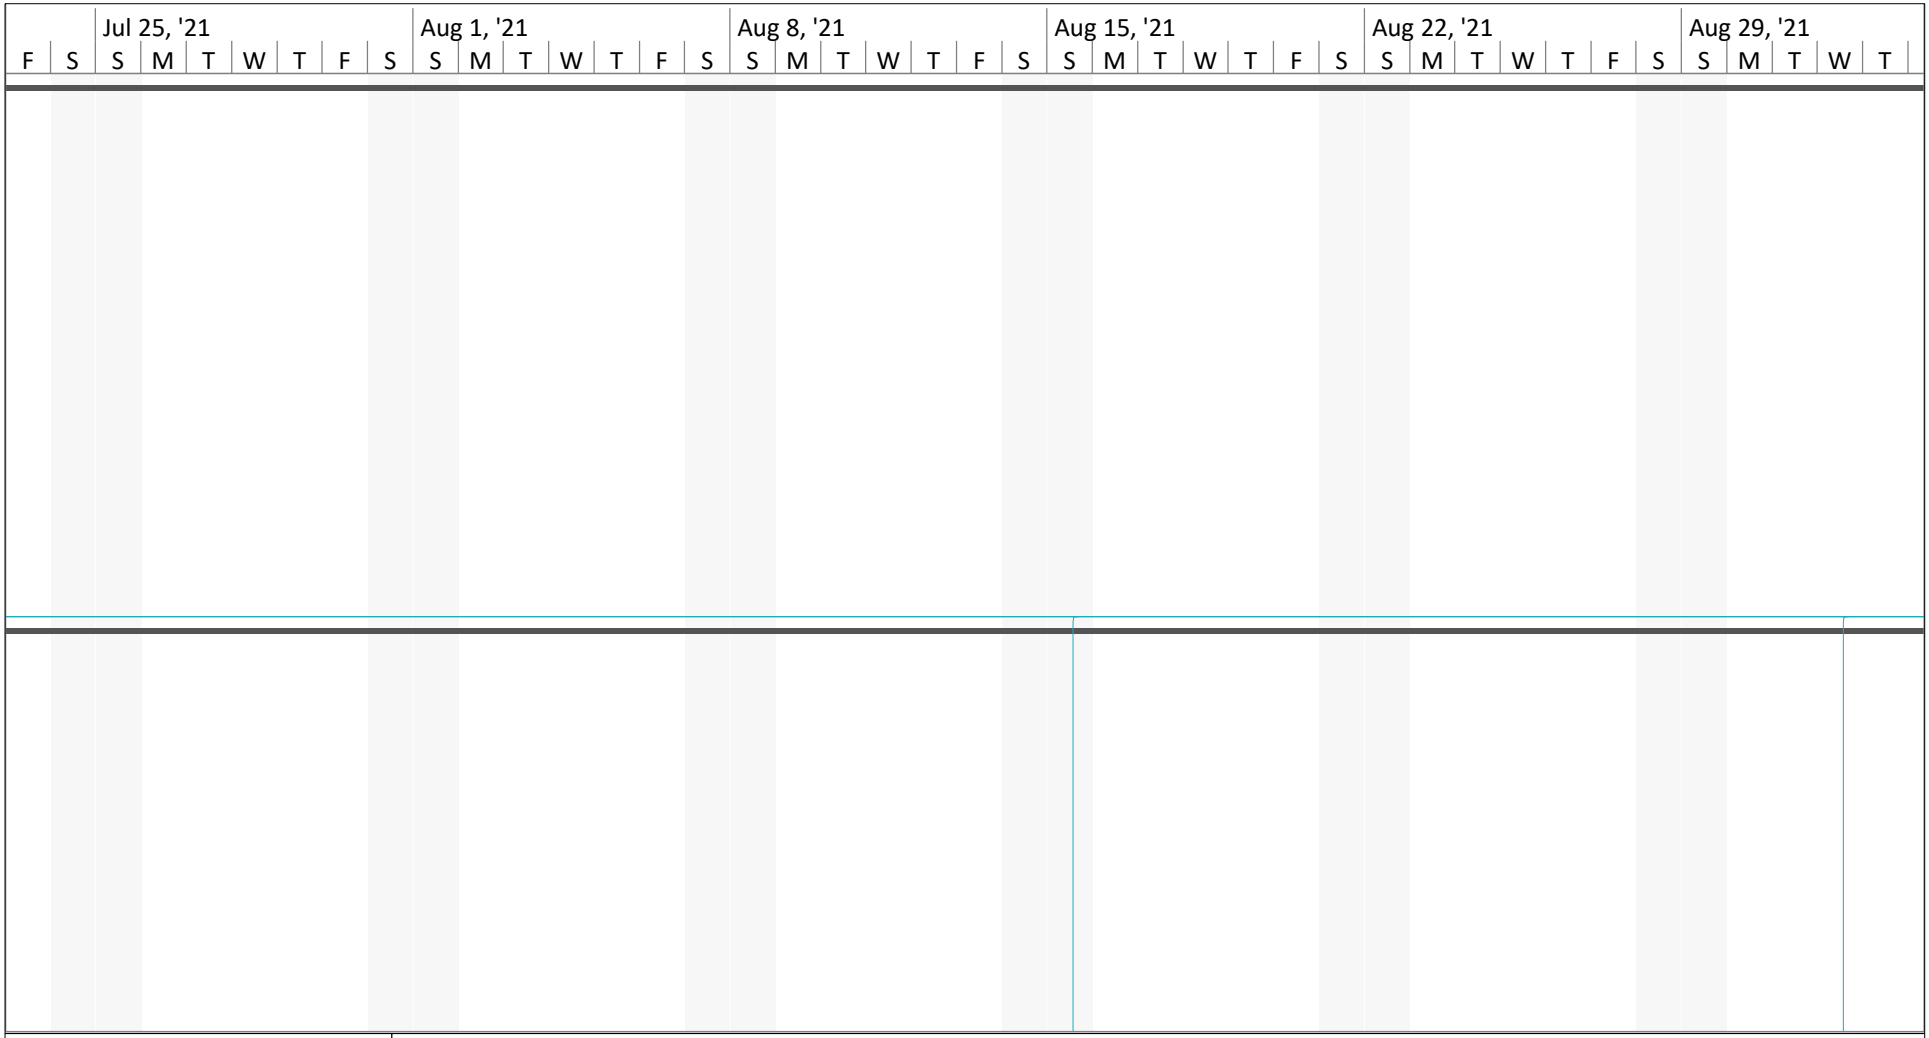


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

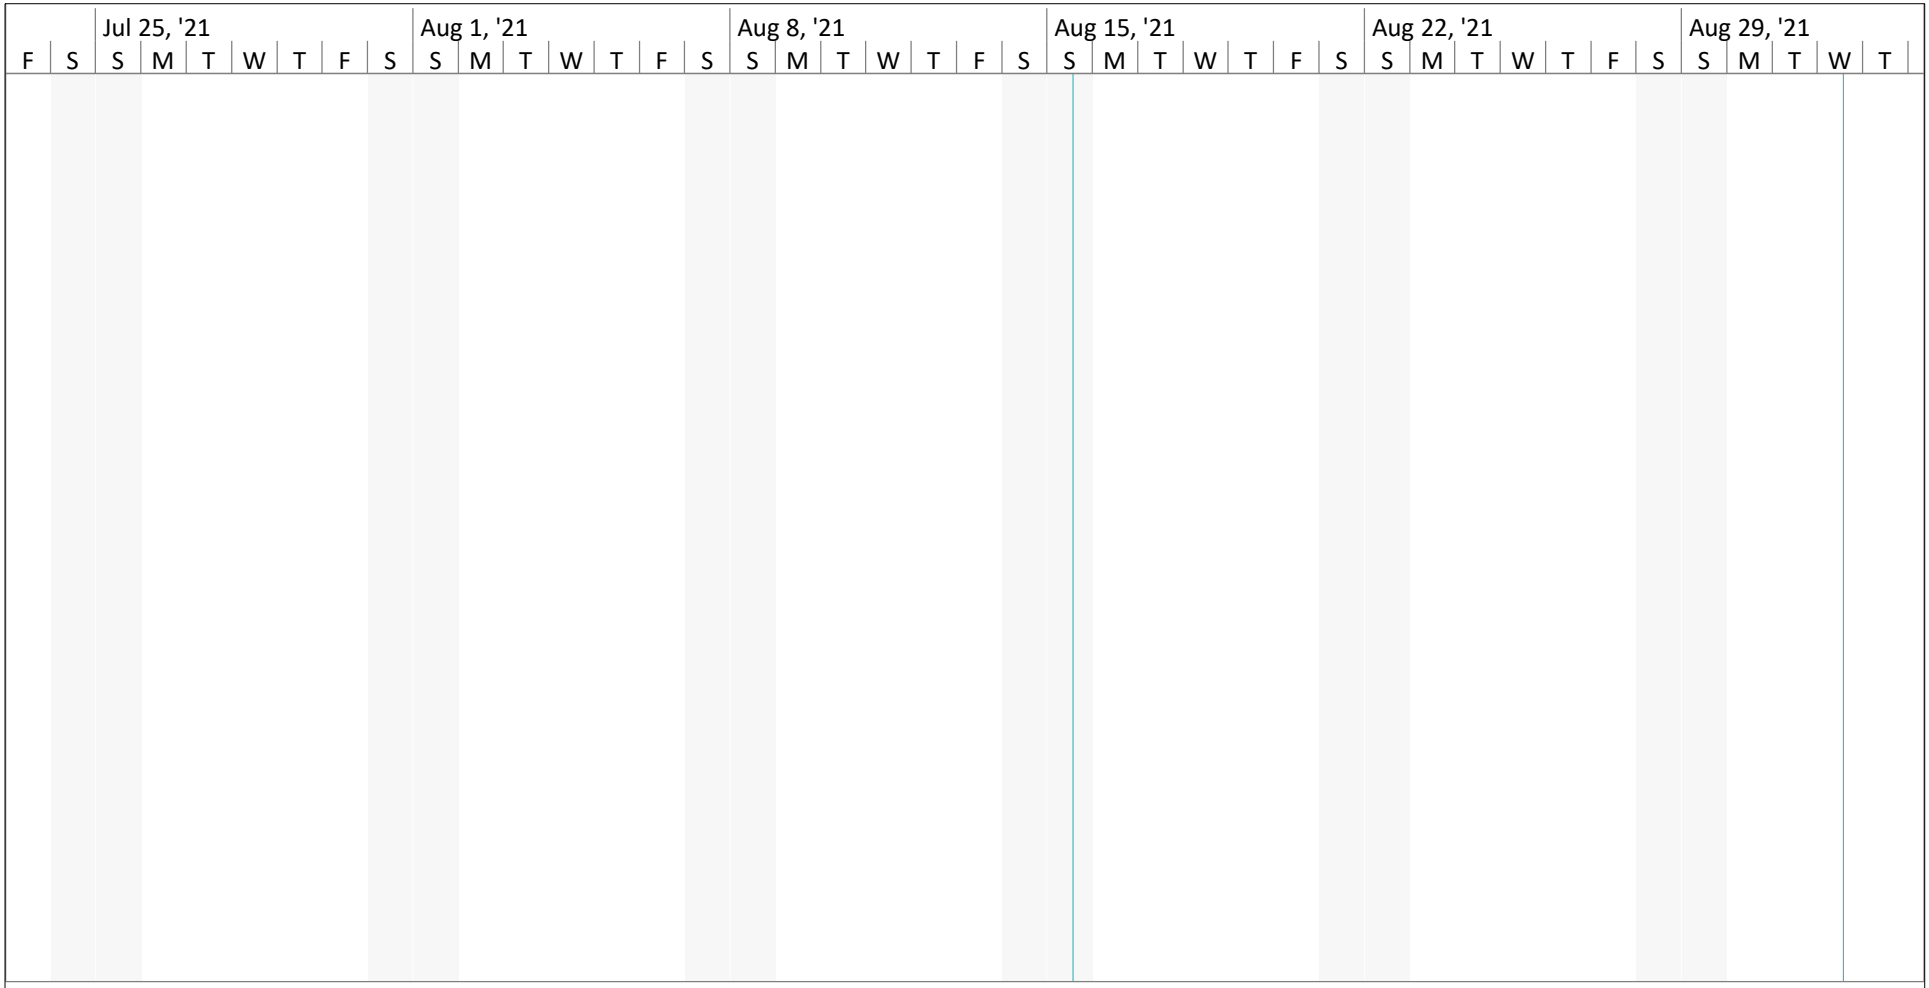


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

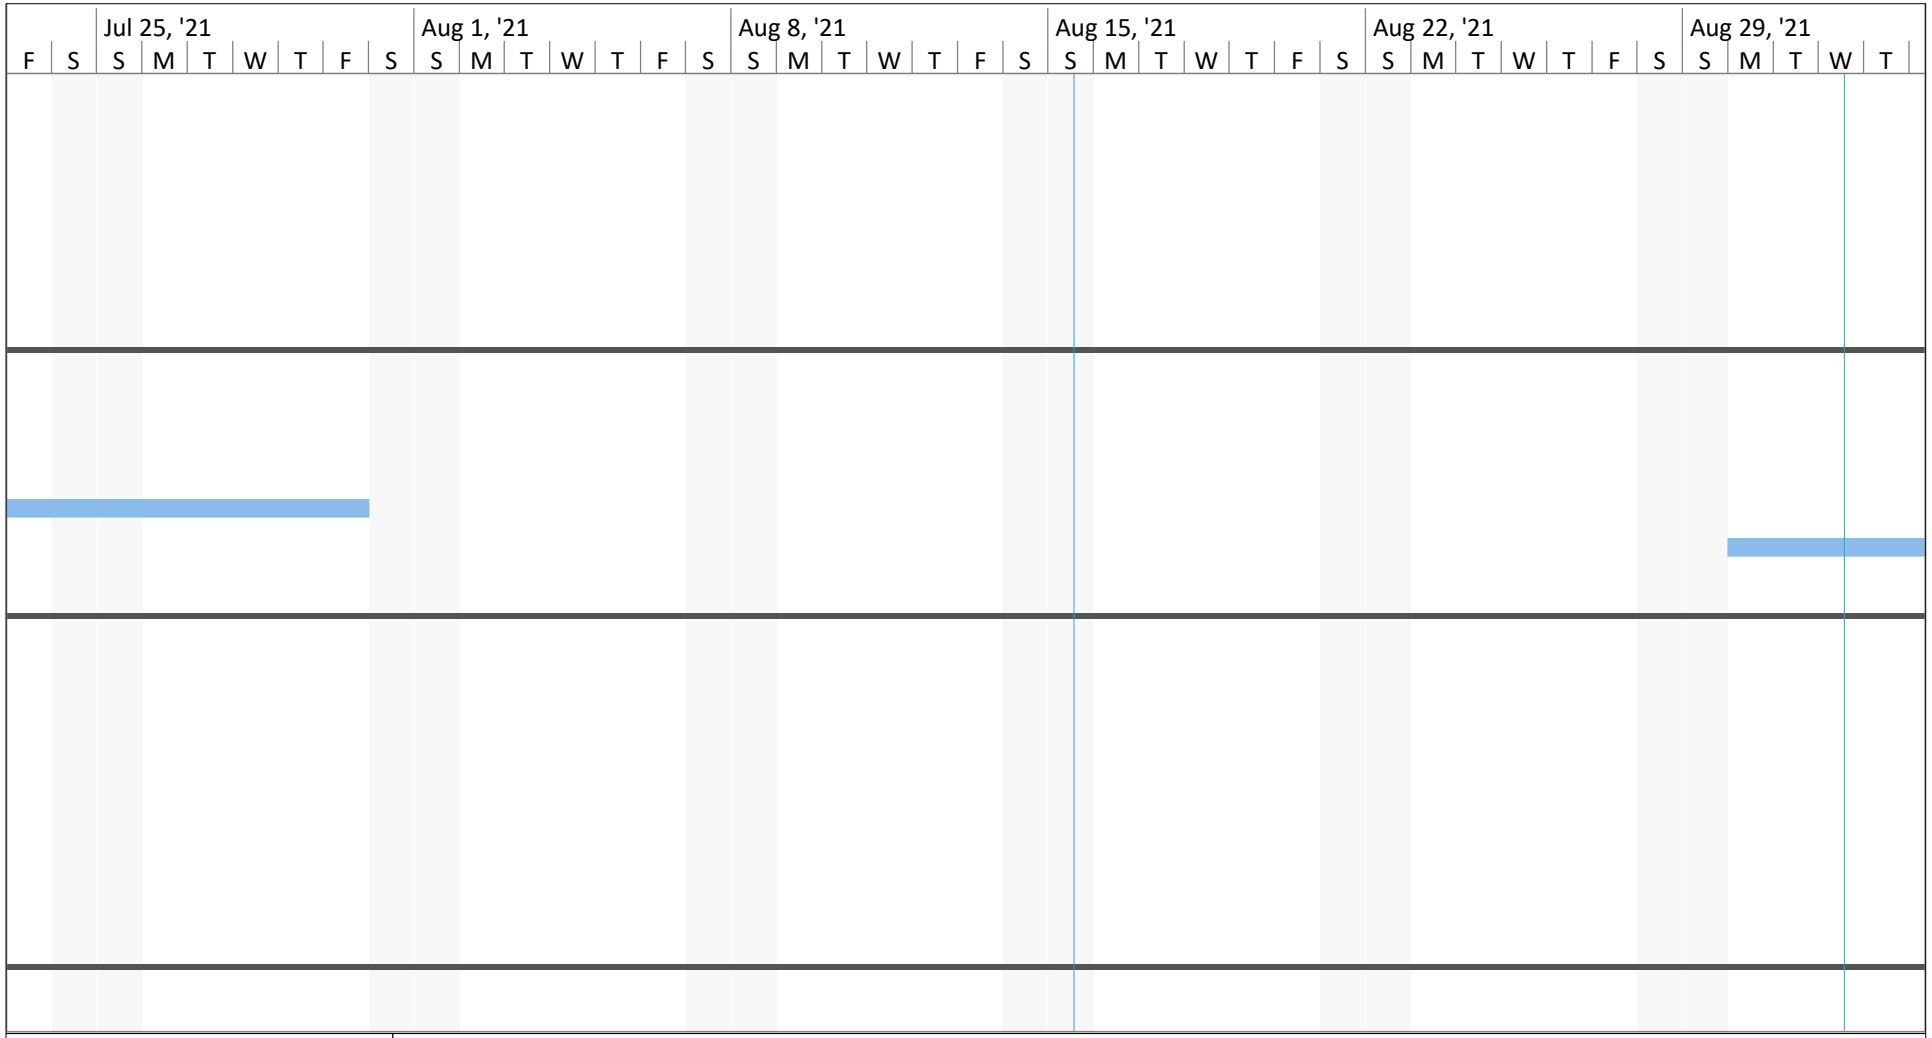


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

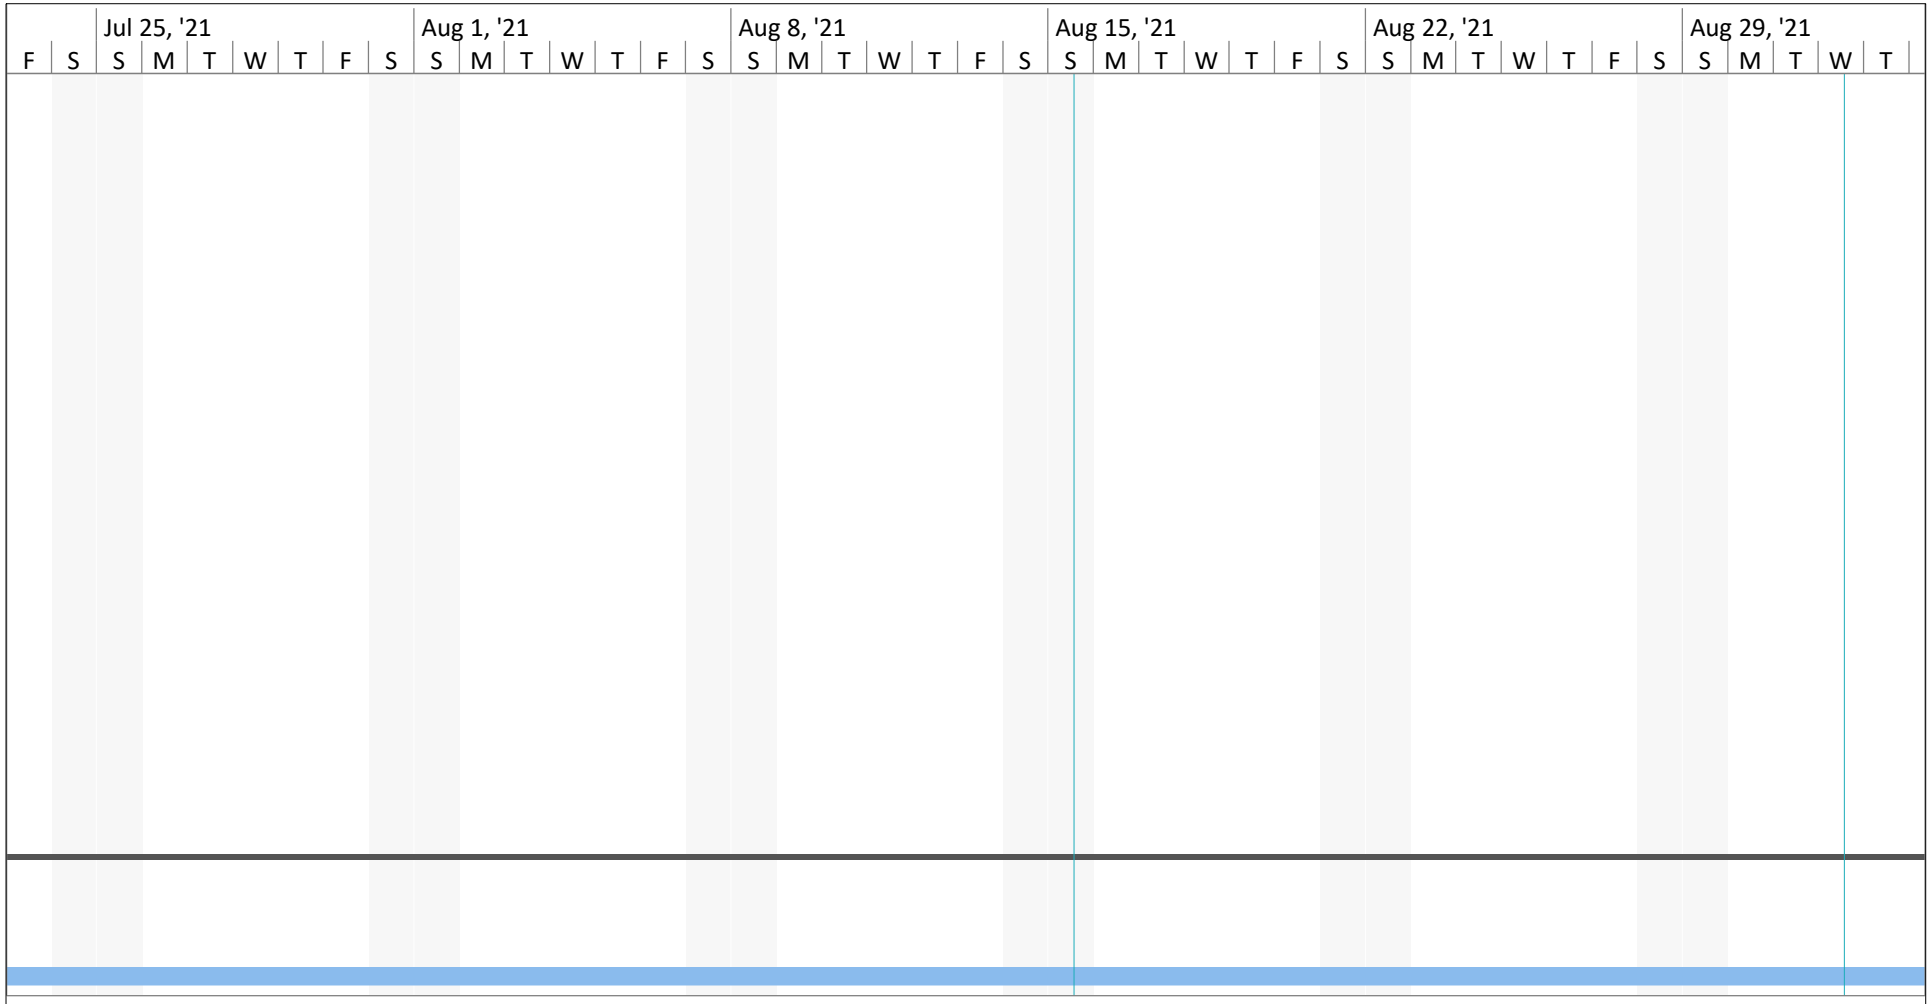


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

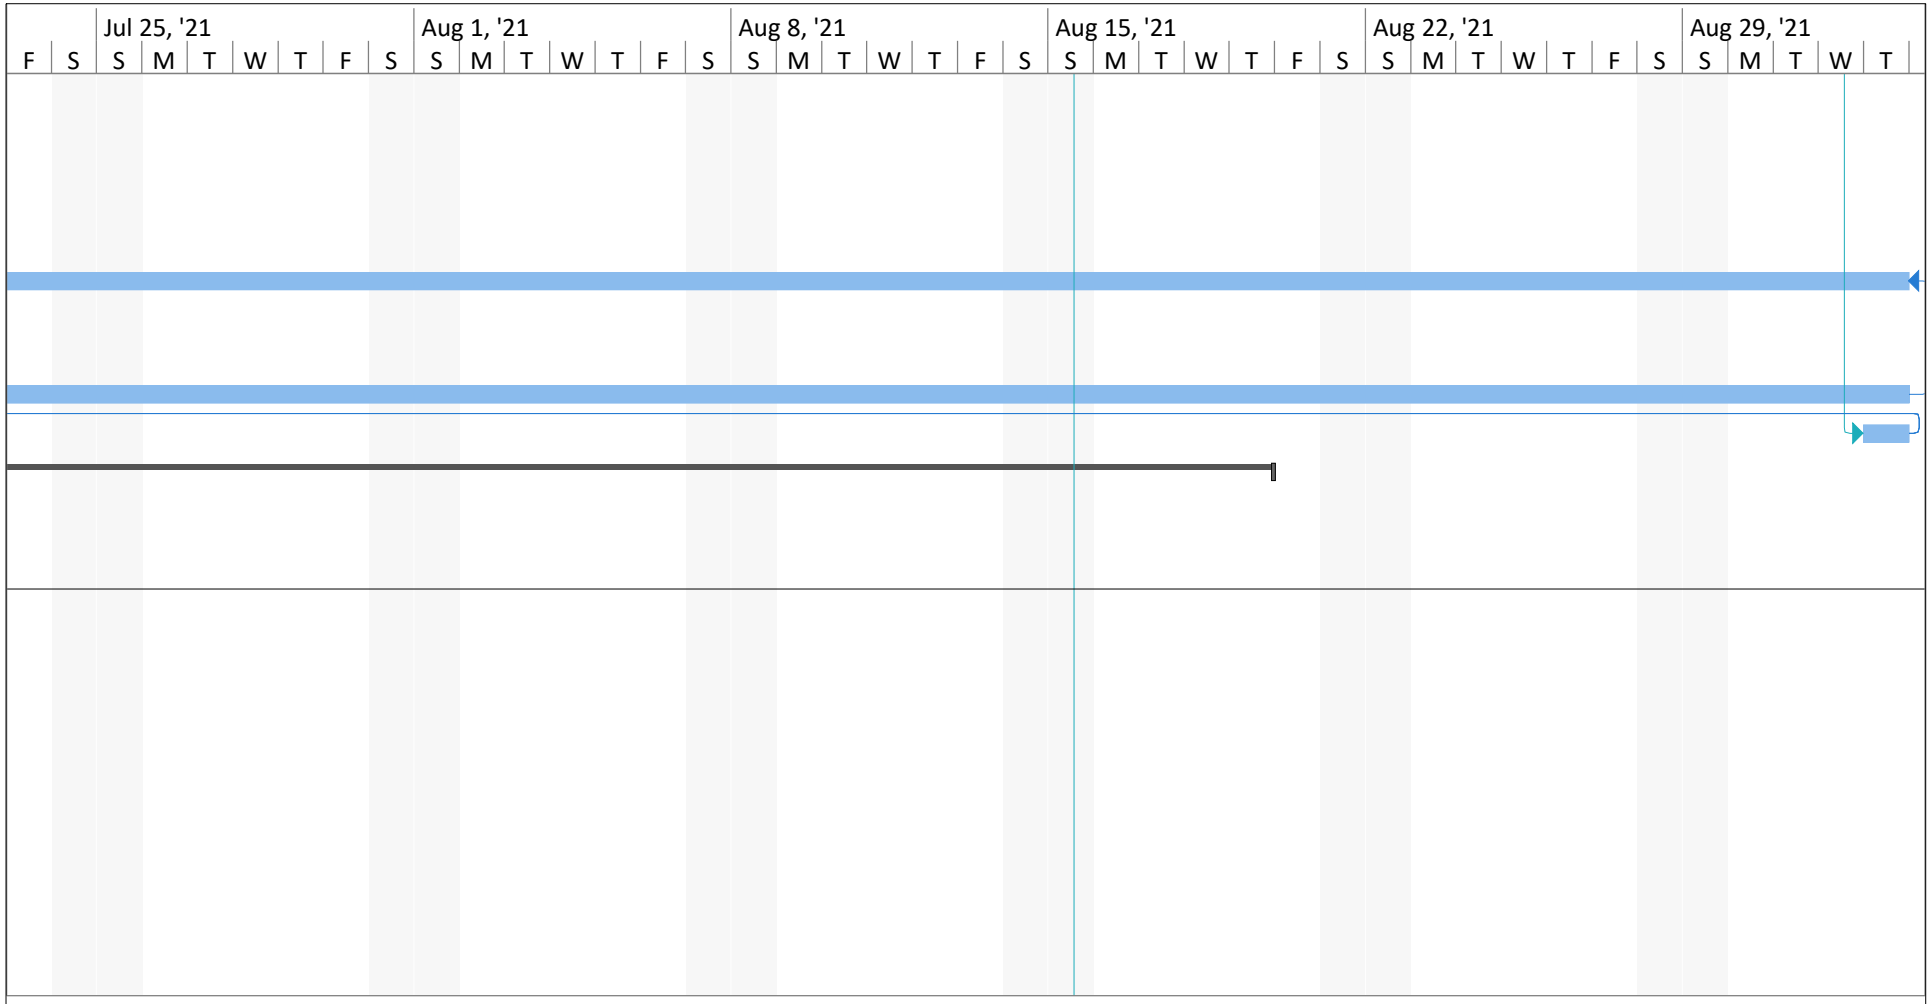


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

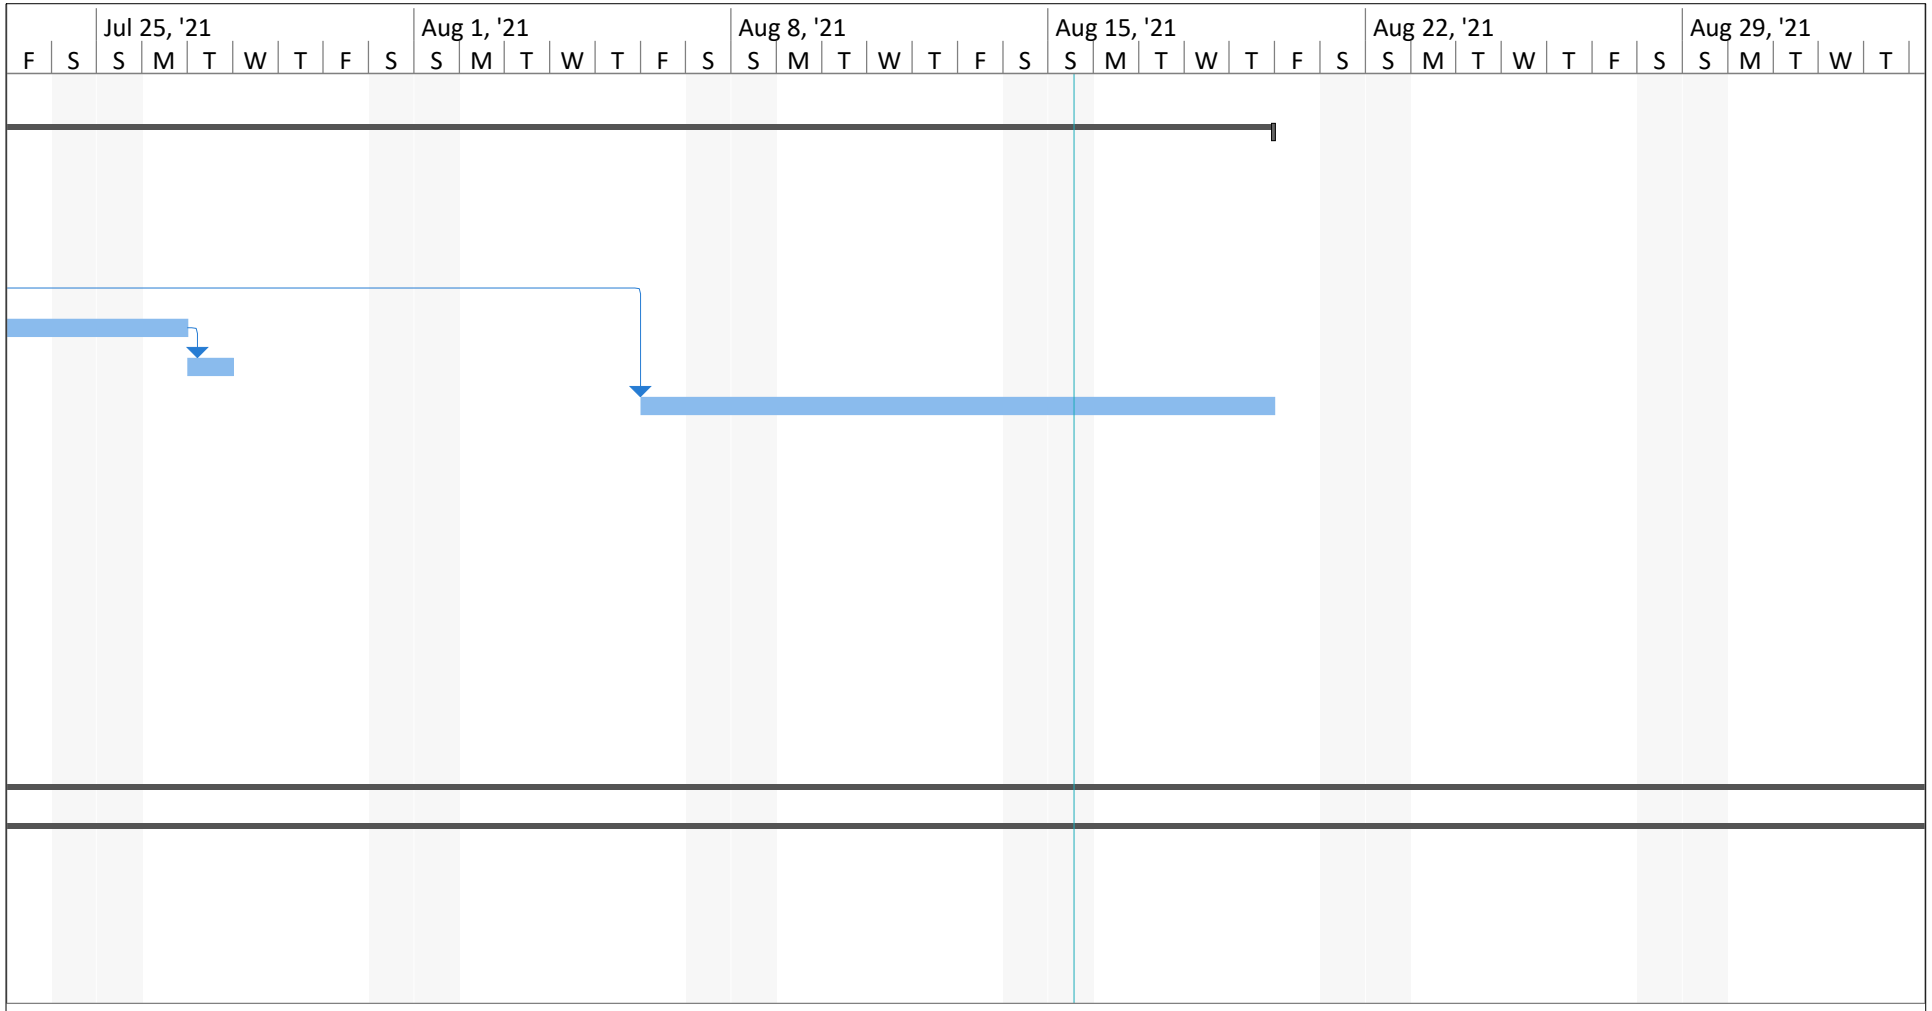


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

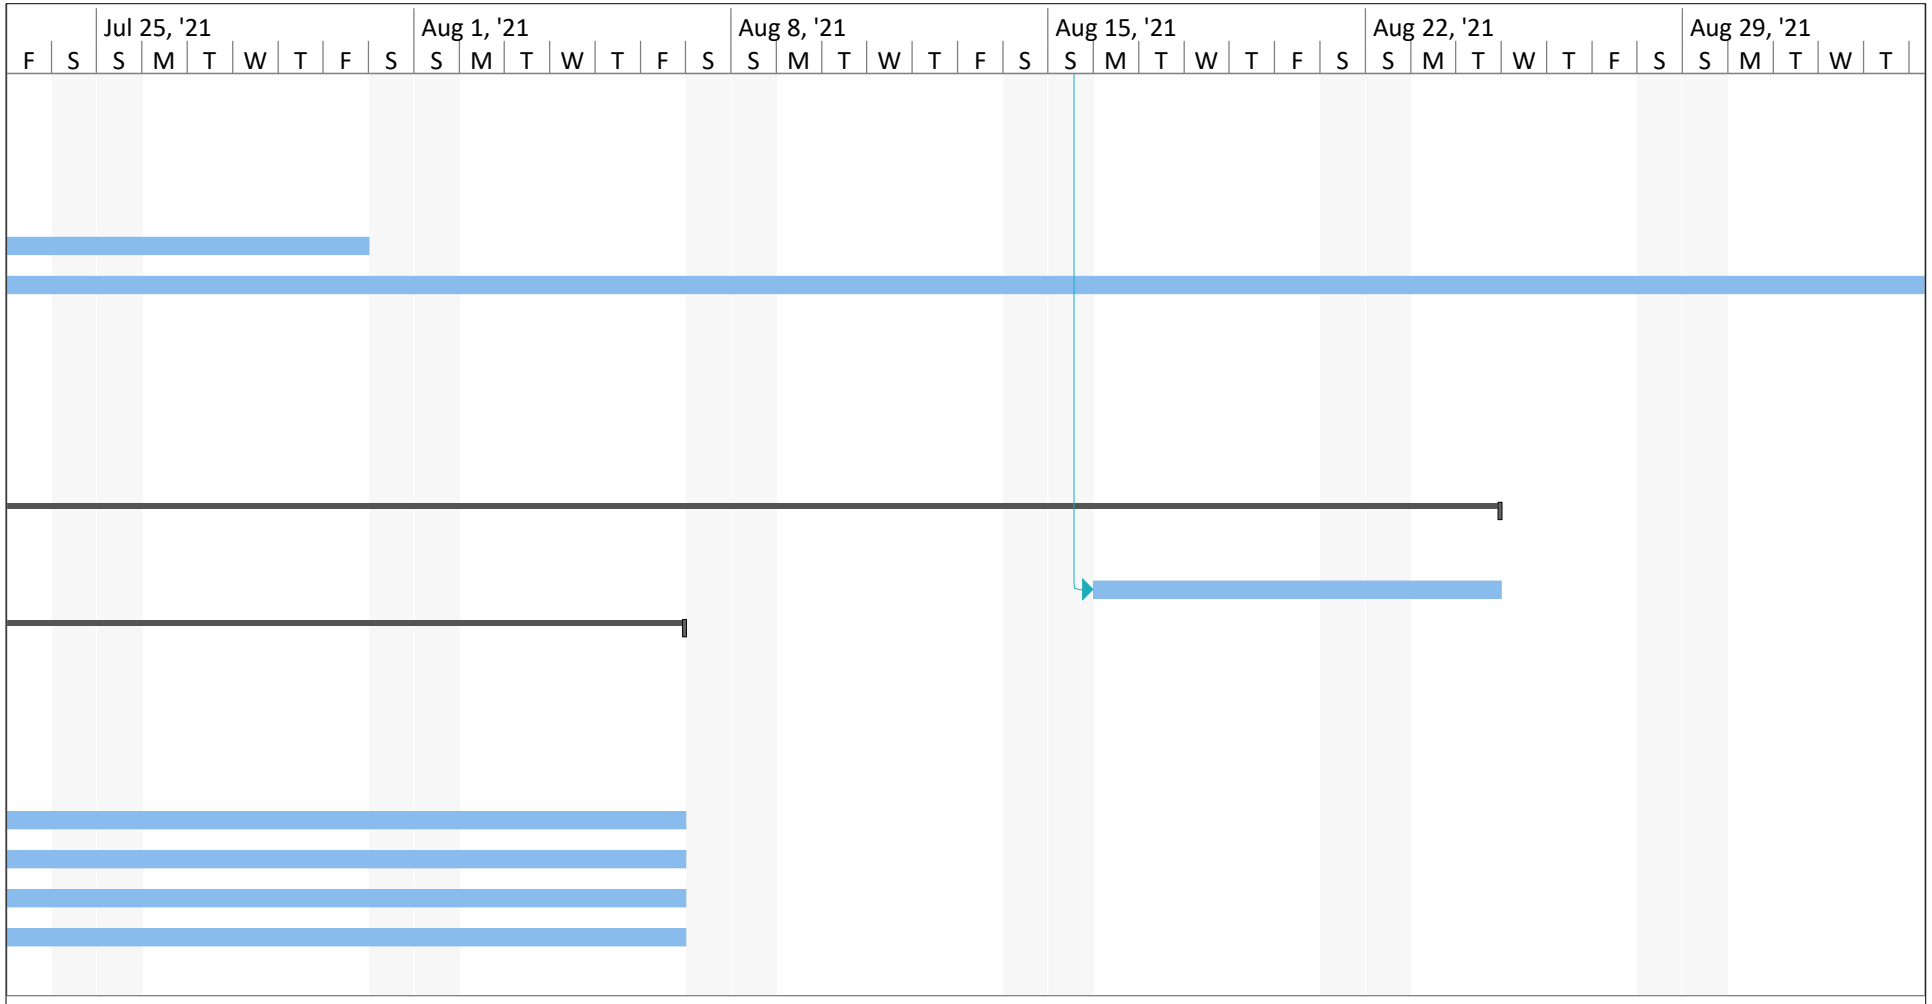


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |




Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

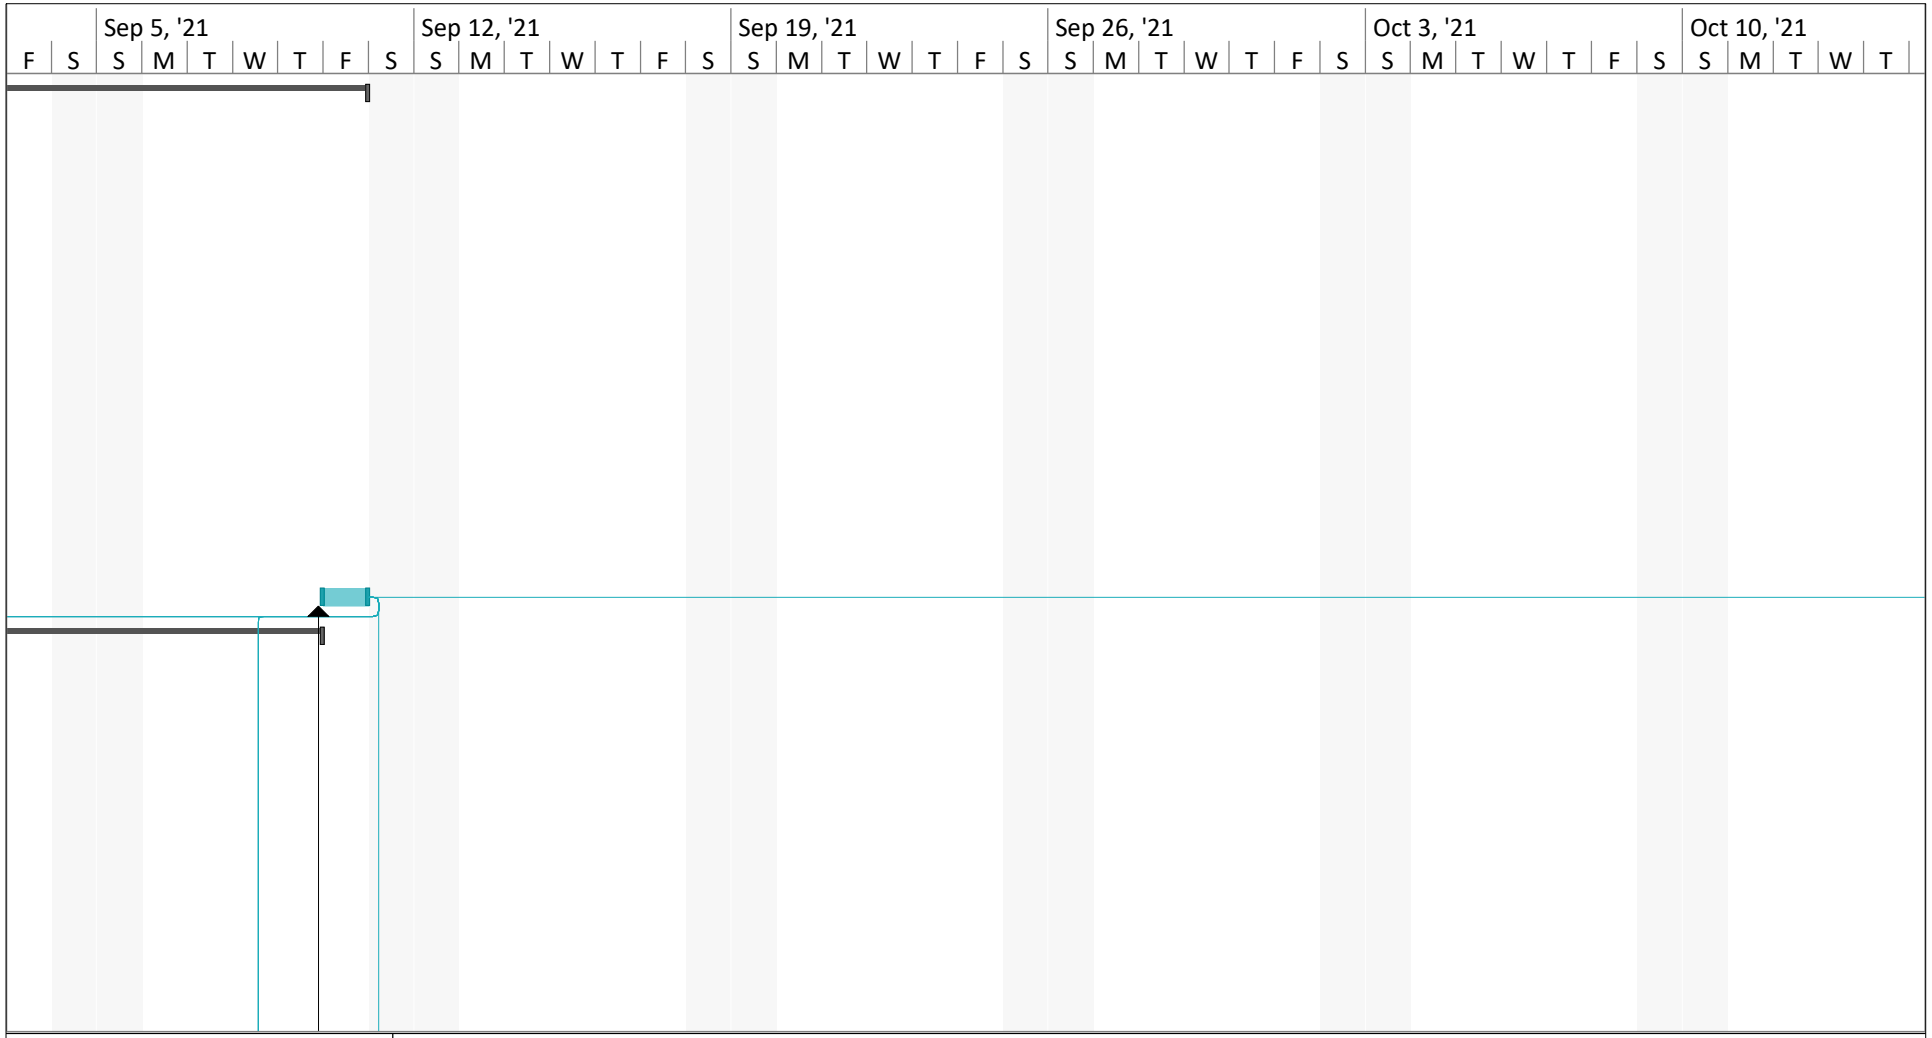


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

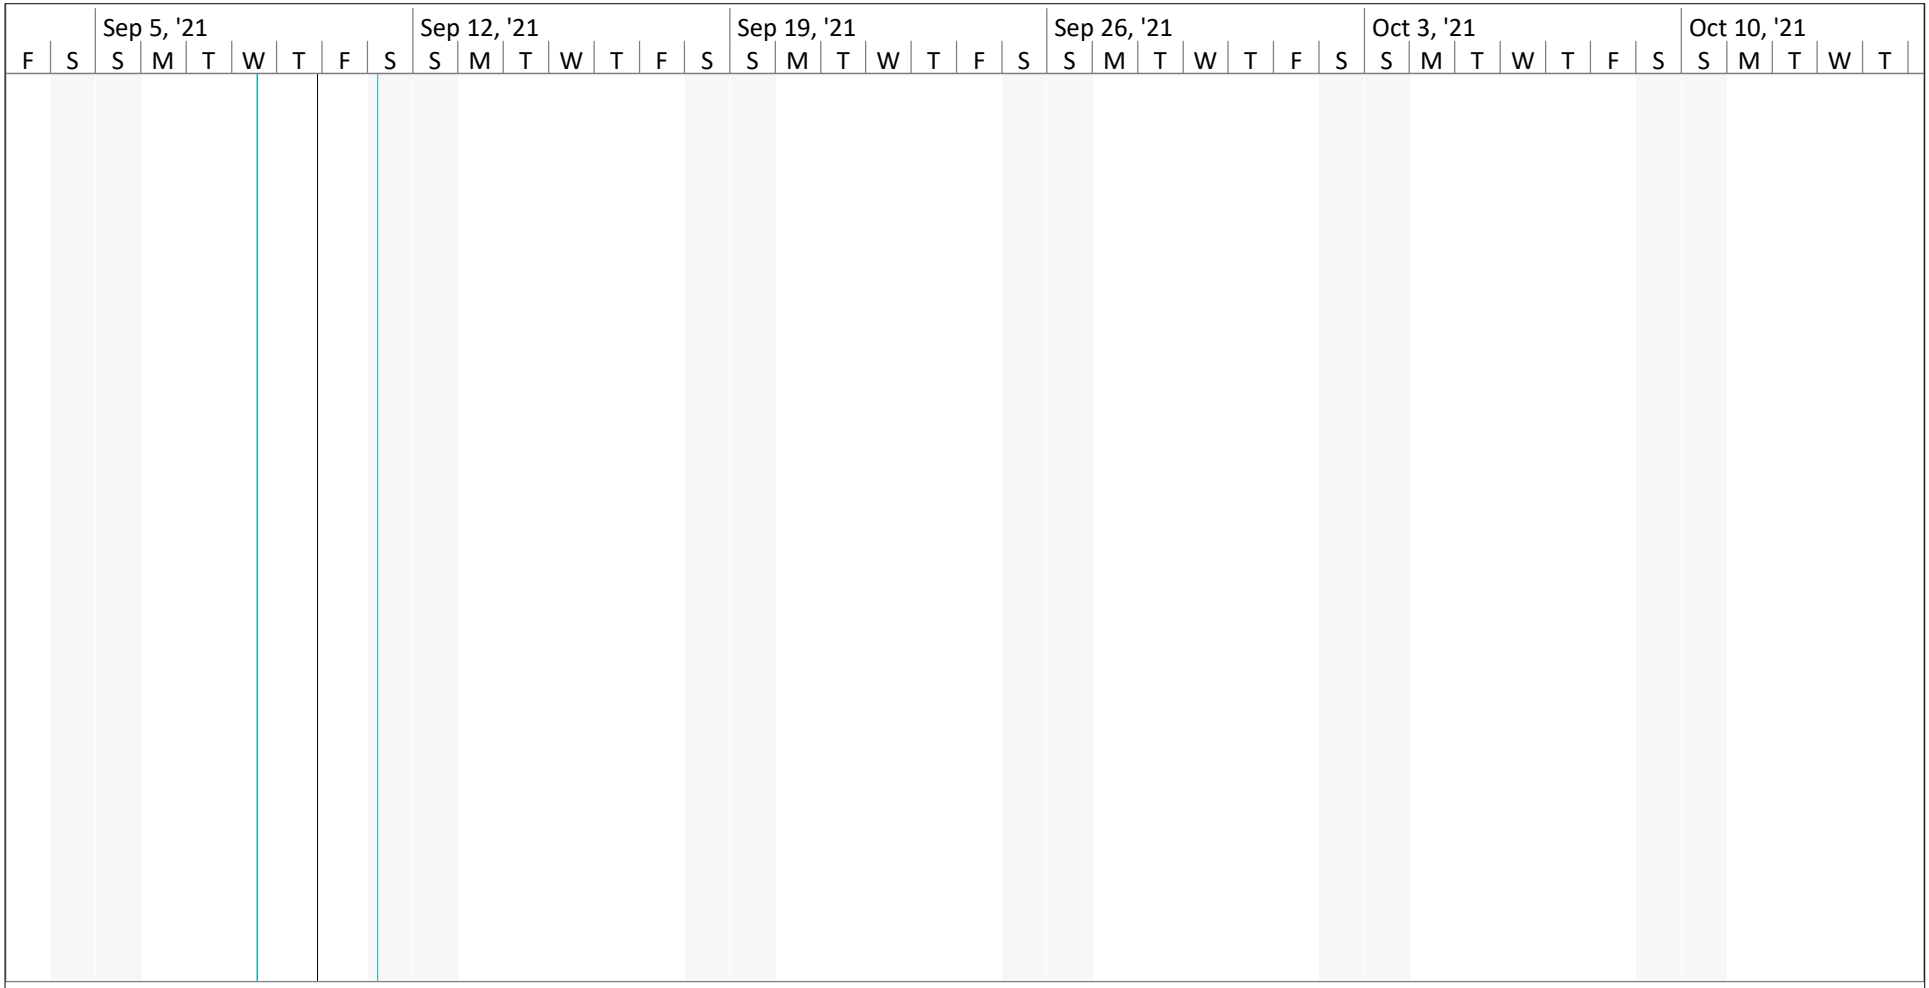


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

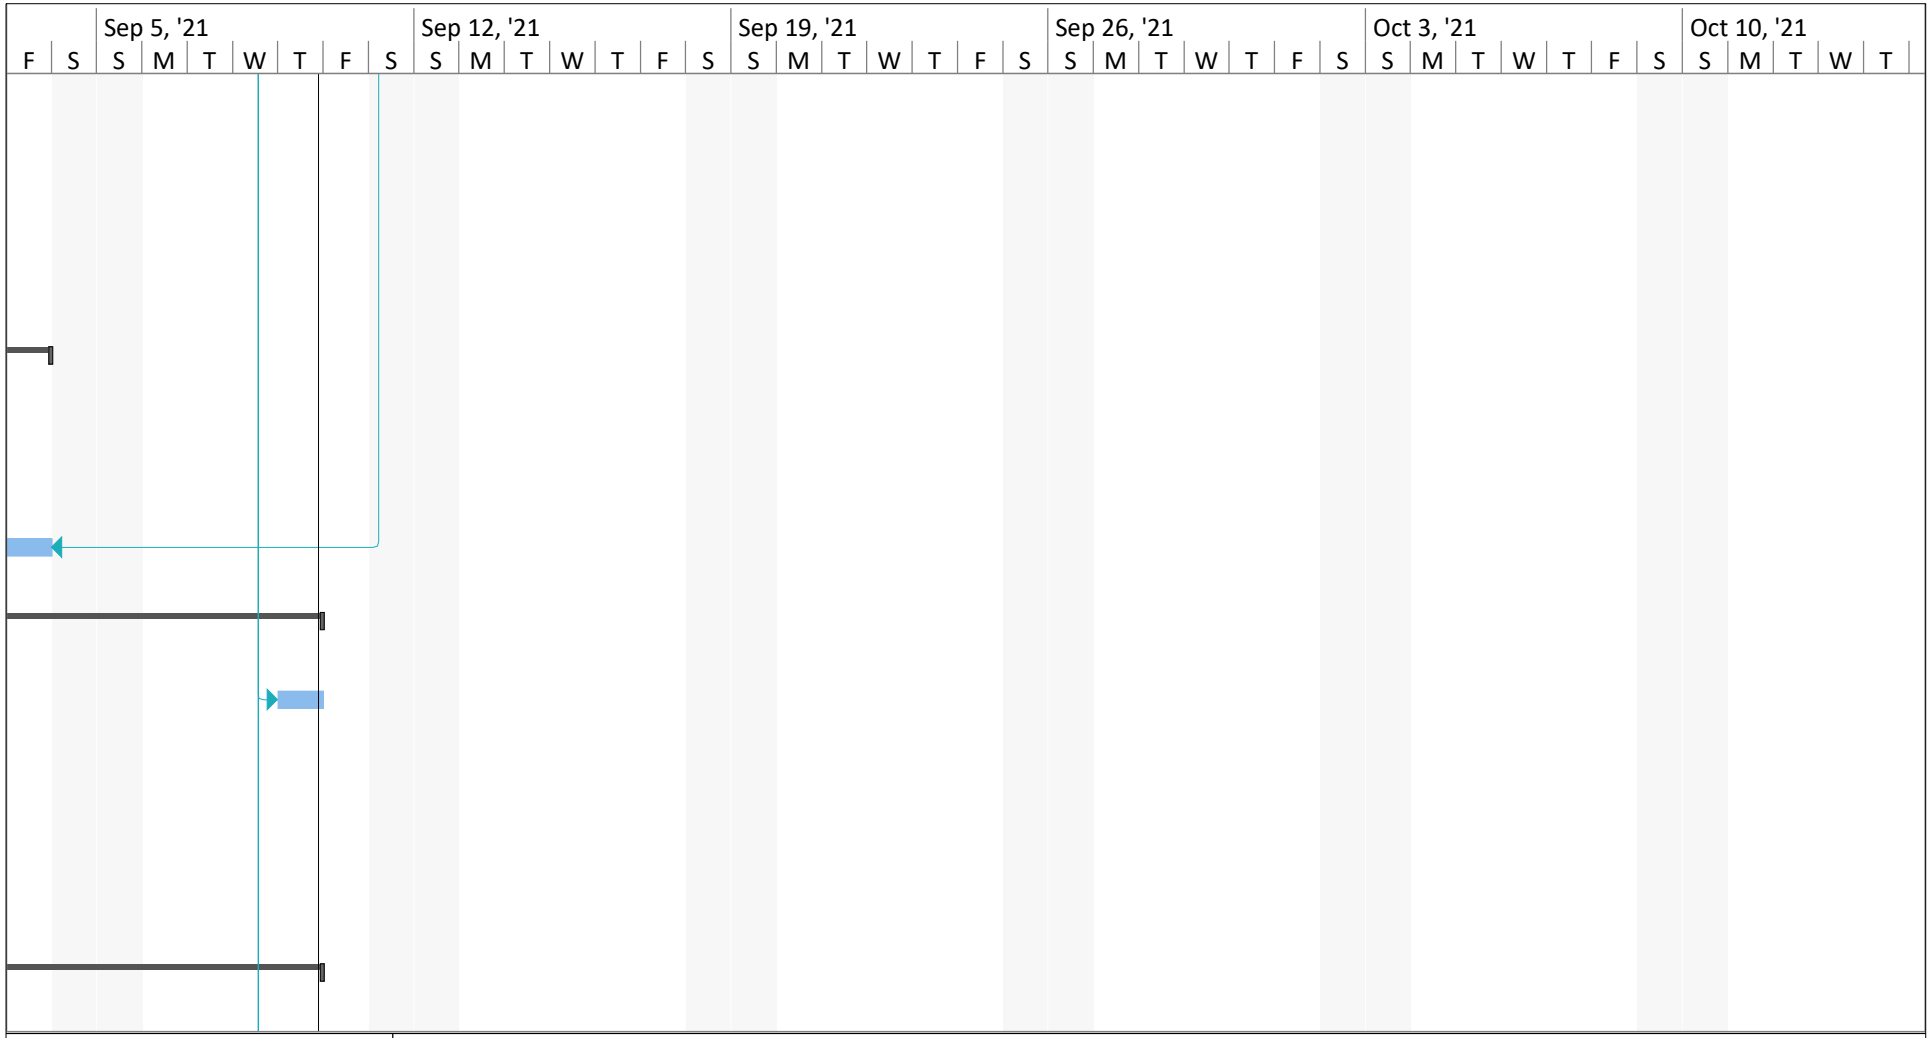


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

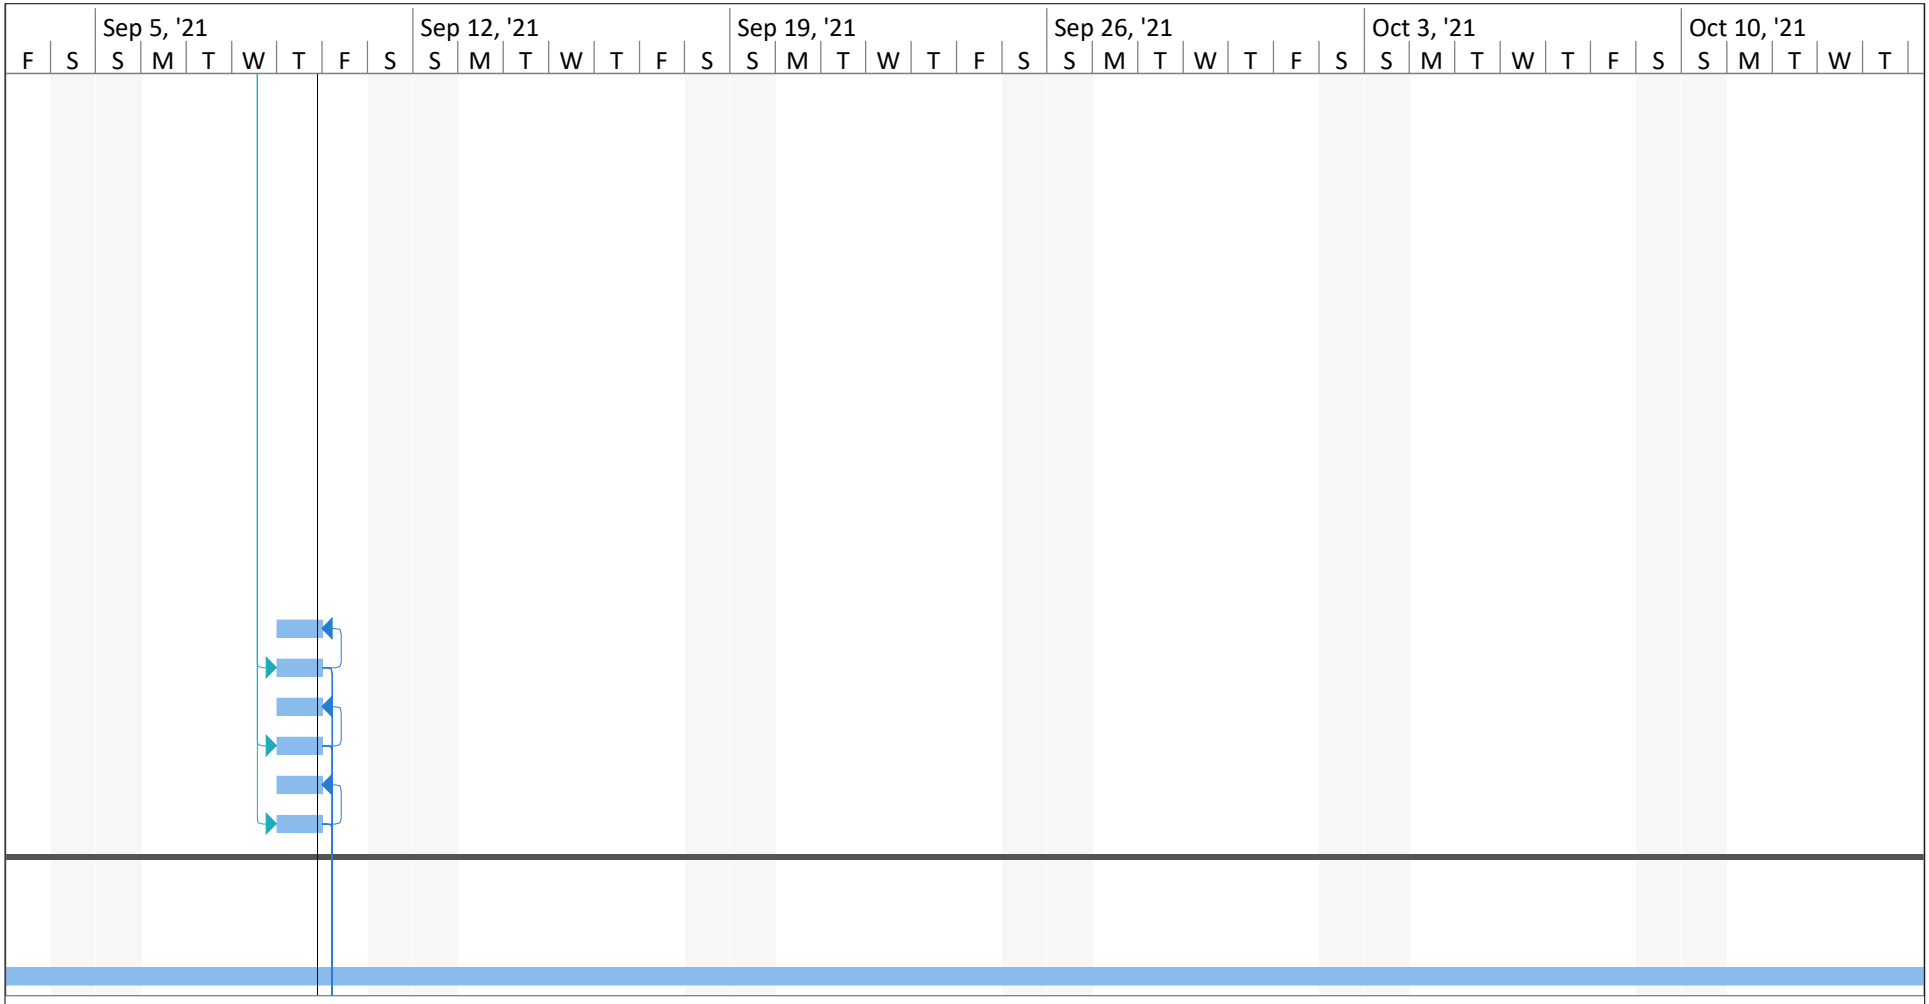


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

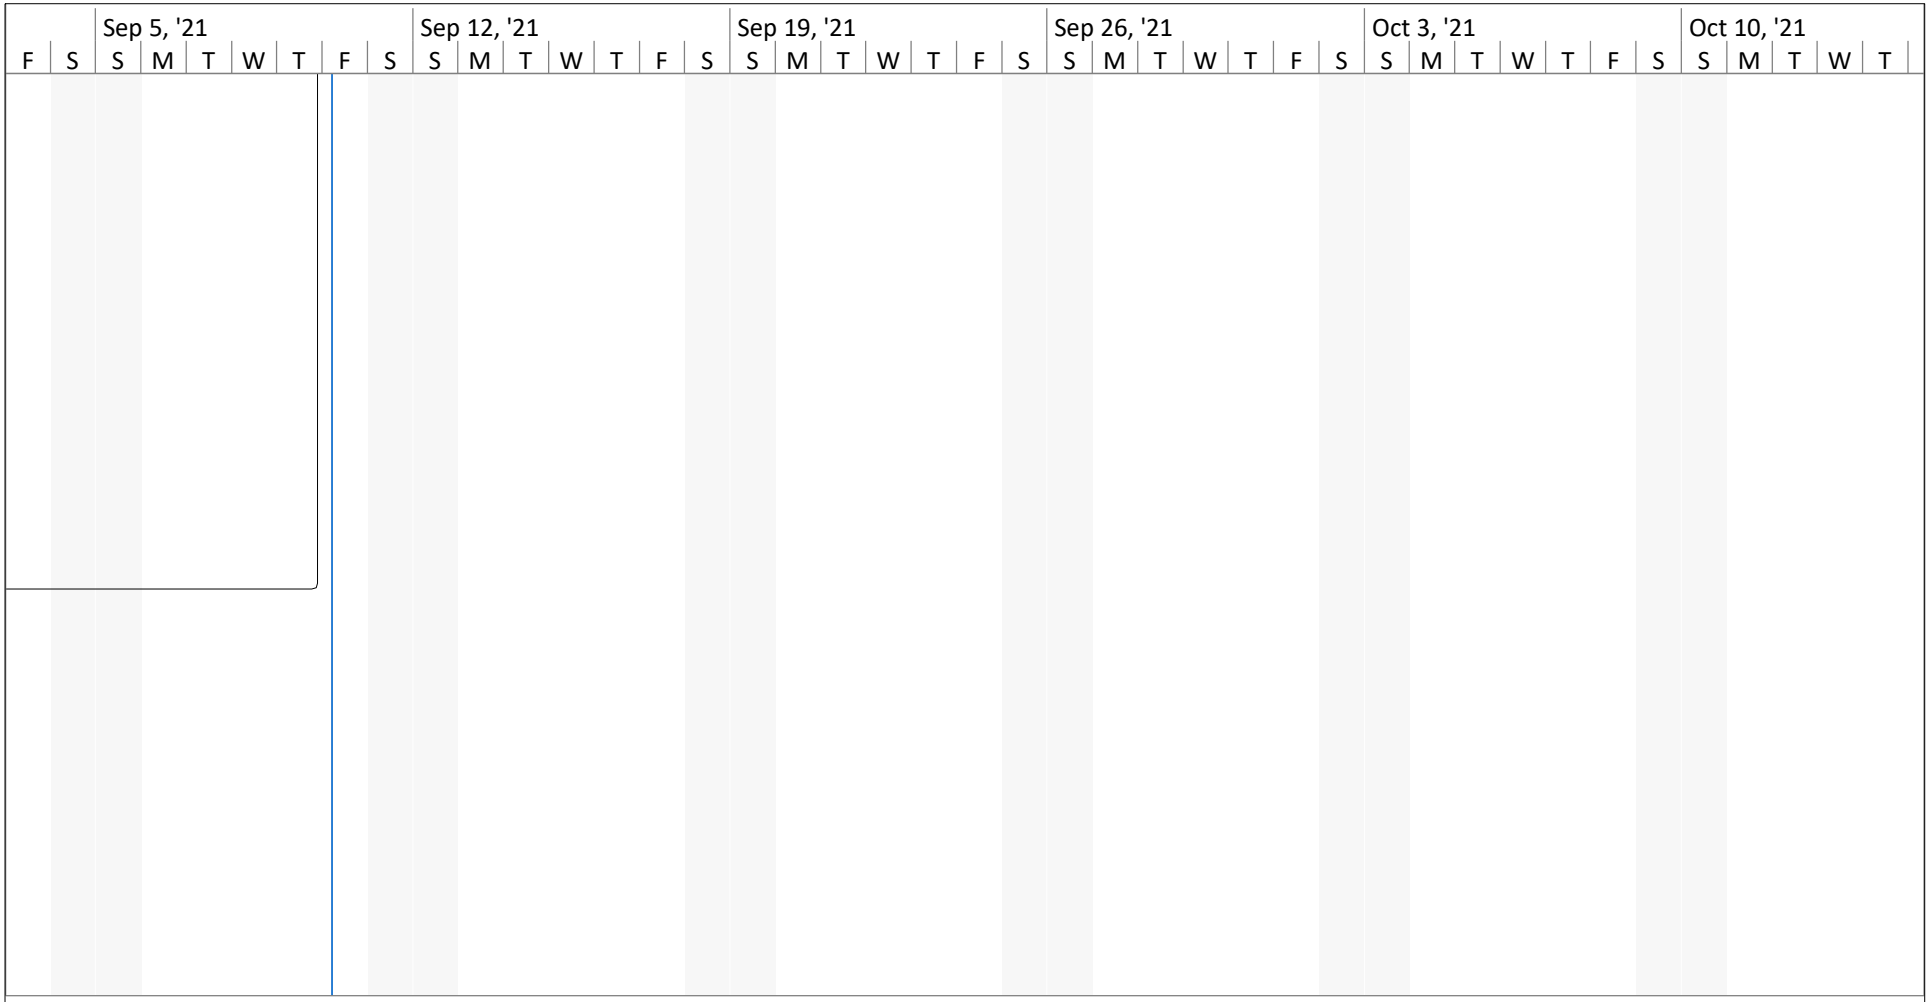


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

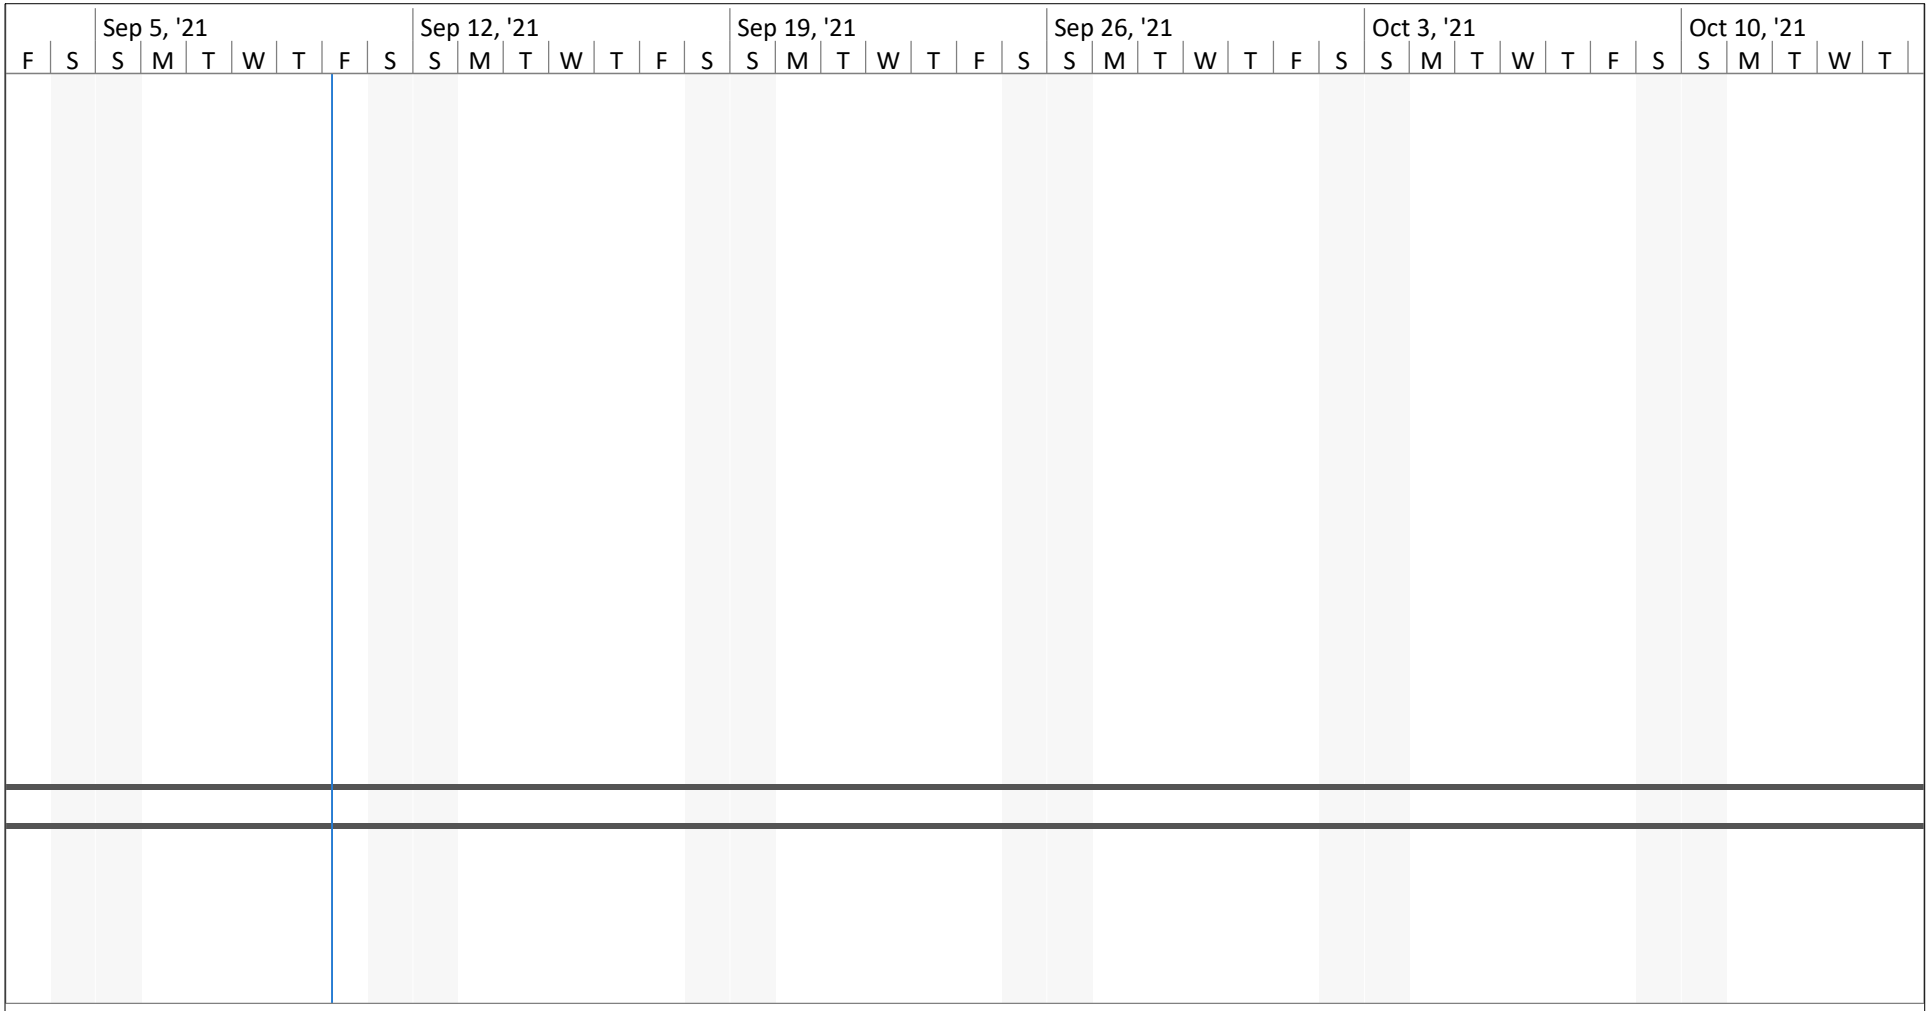


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

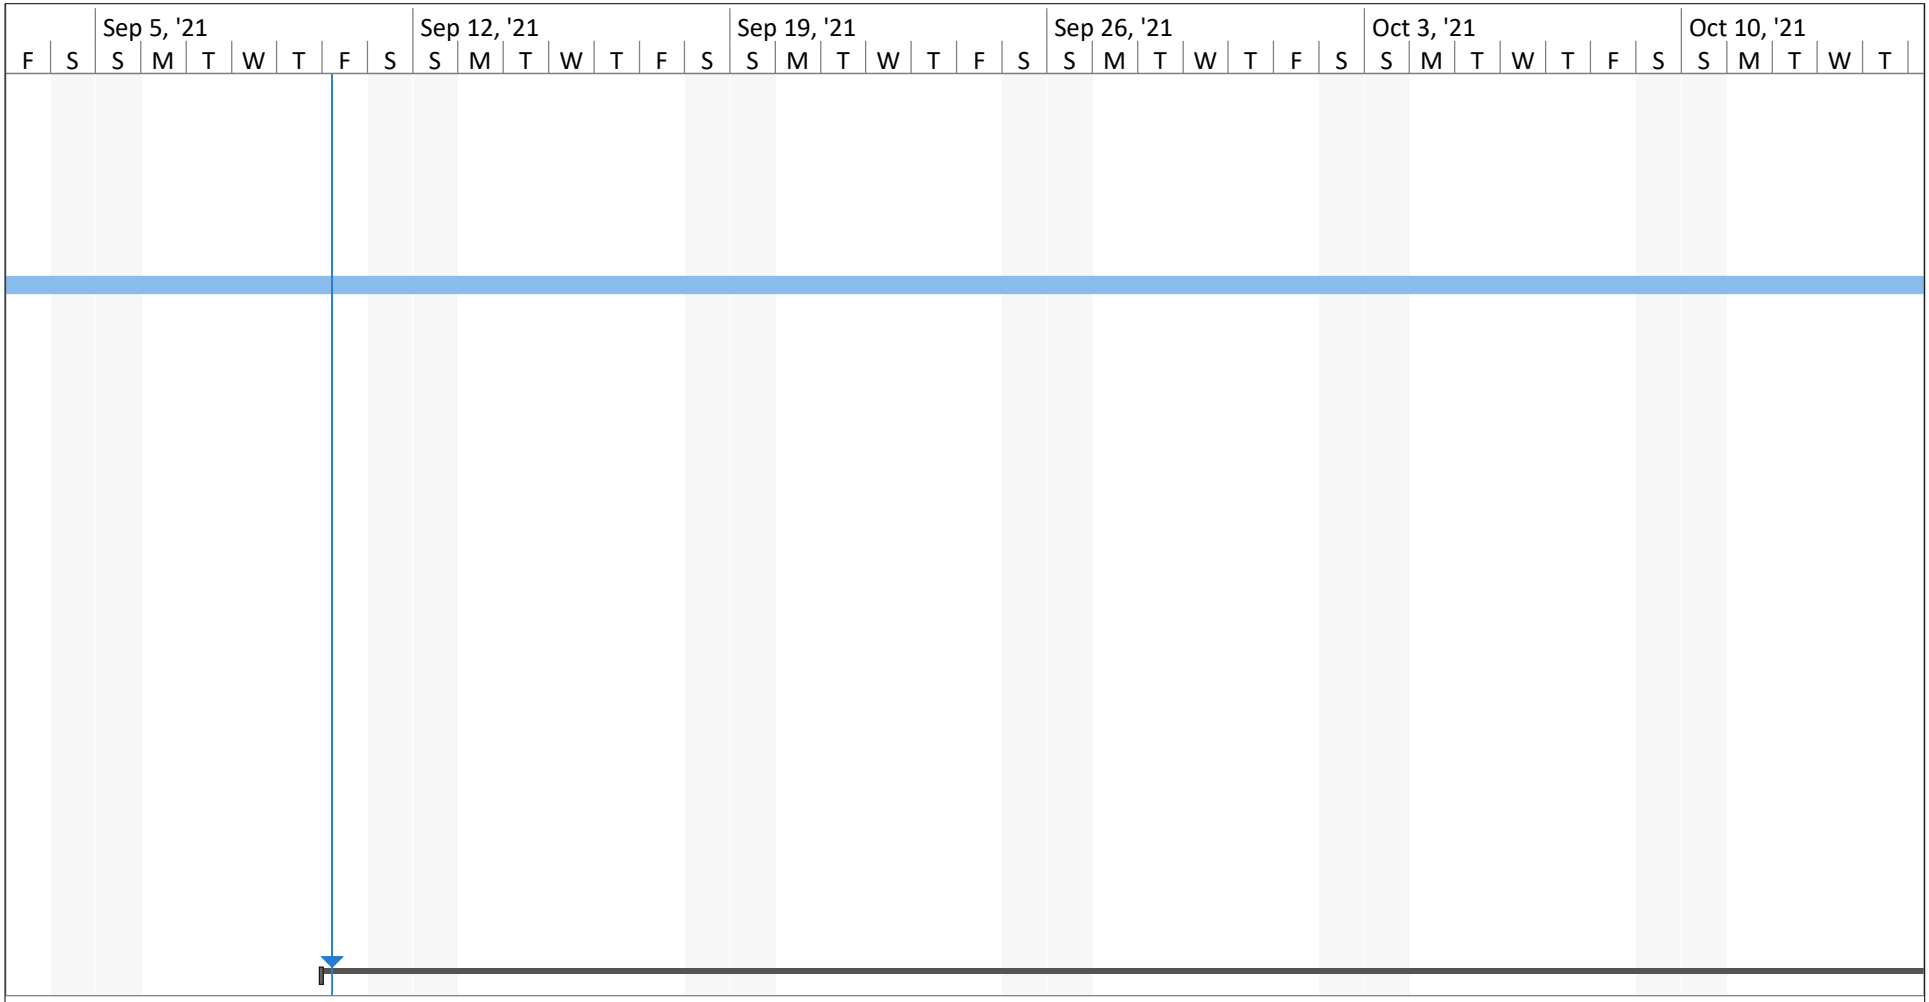


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

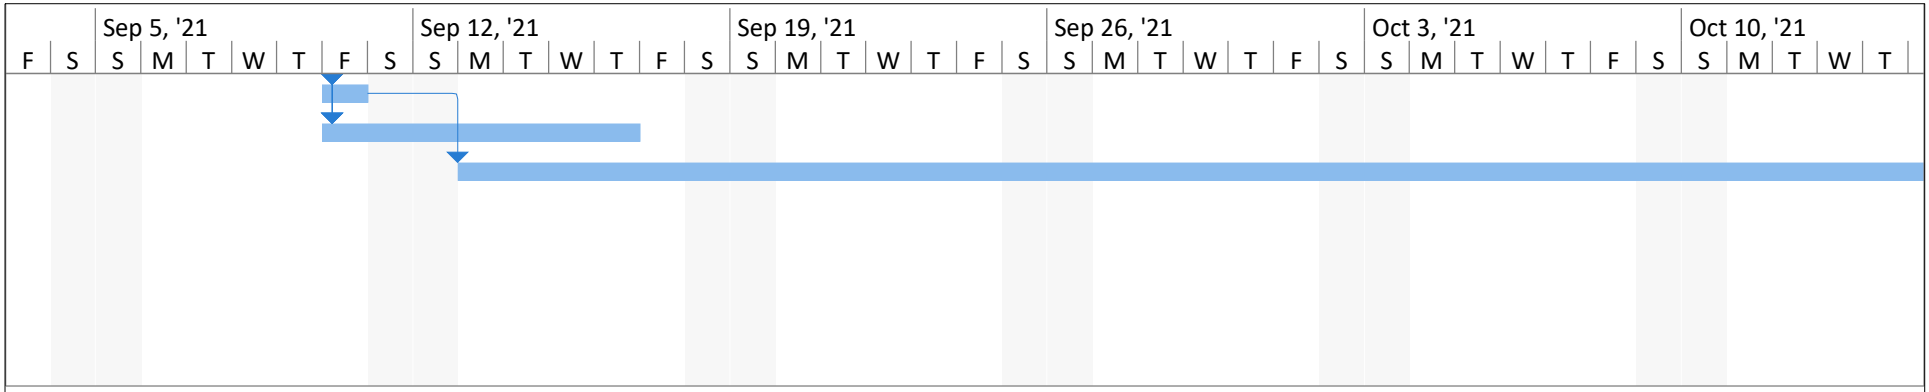


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

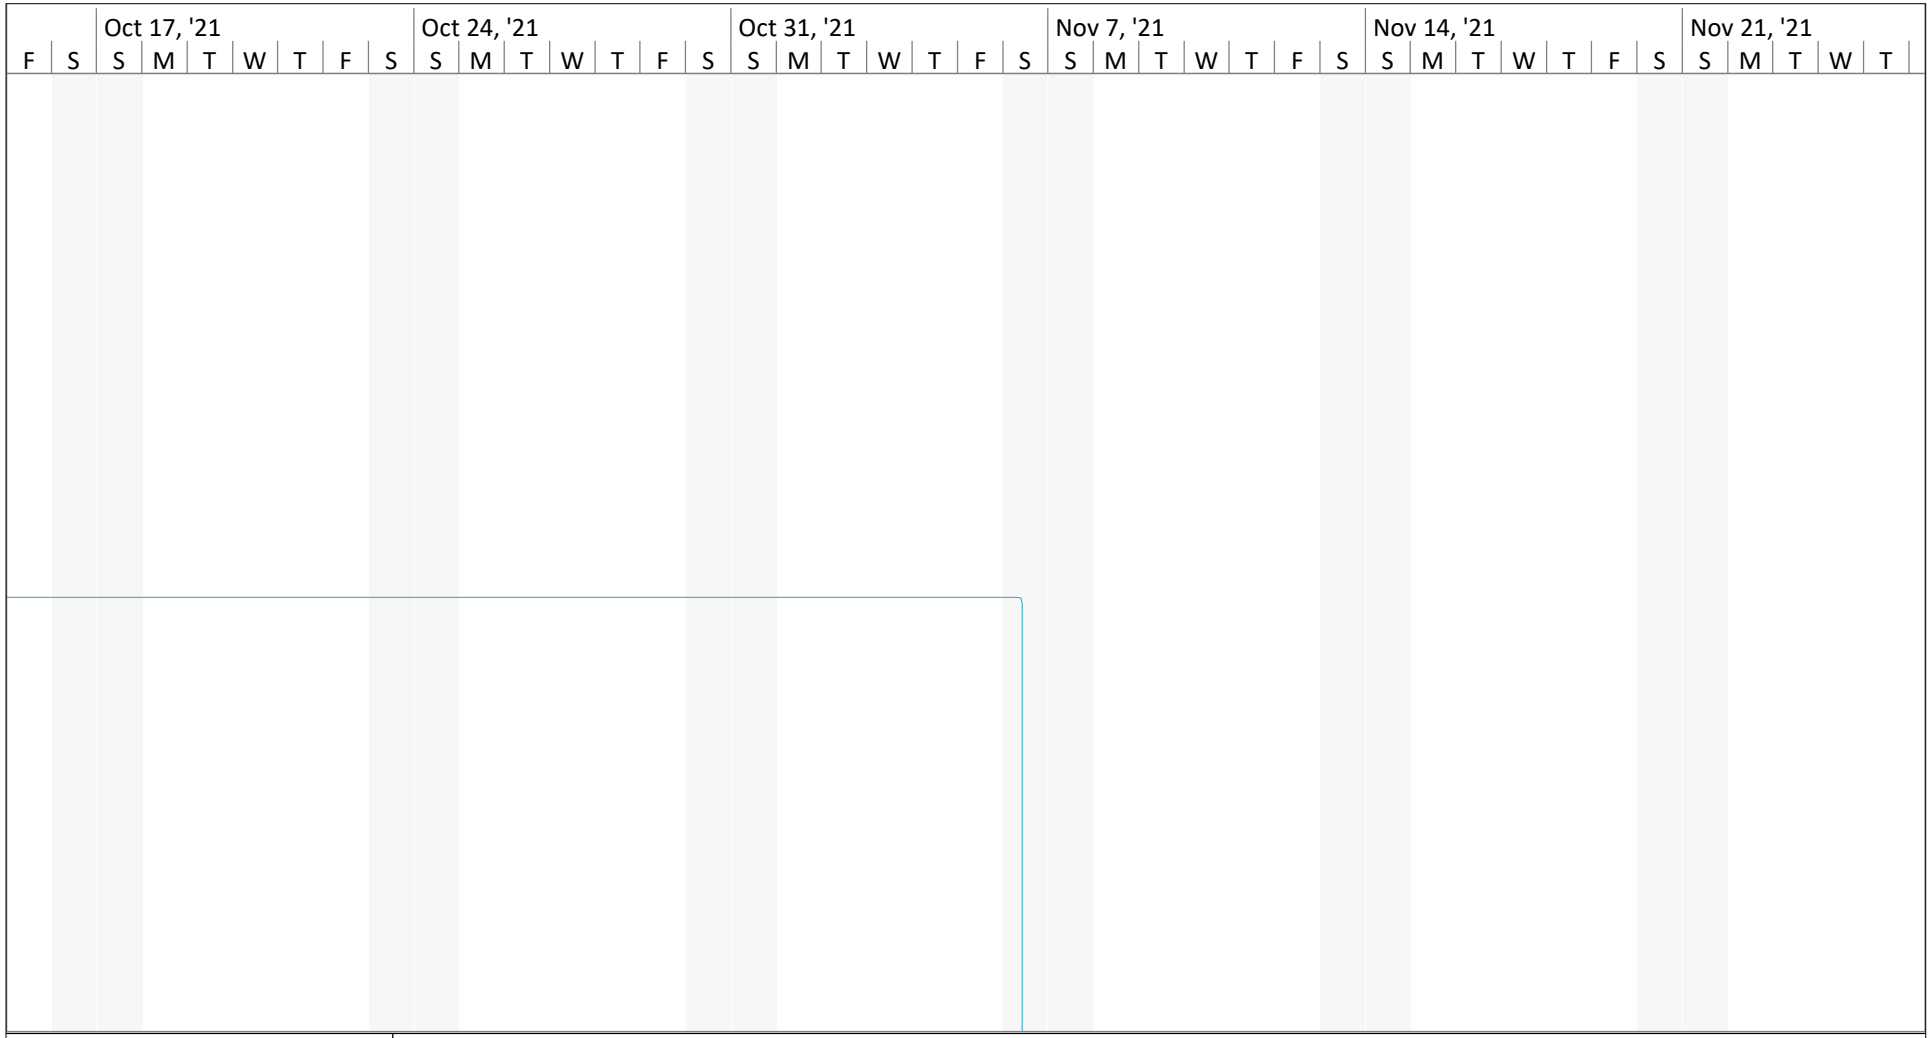


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

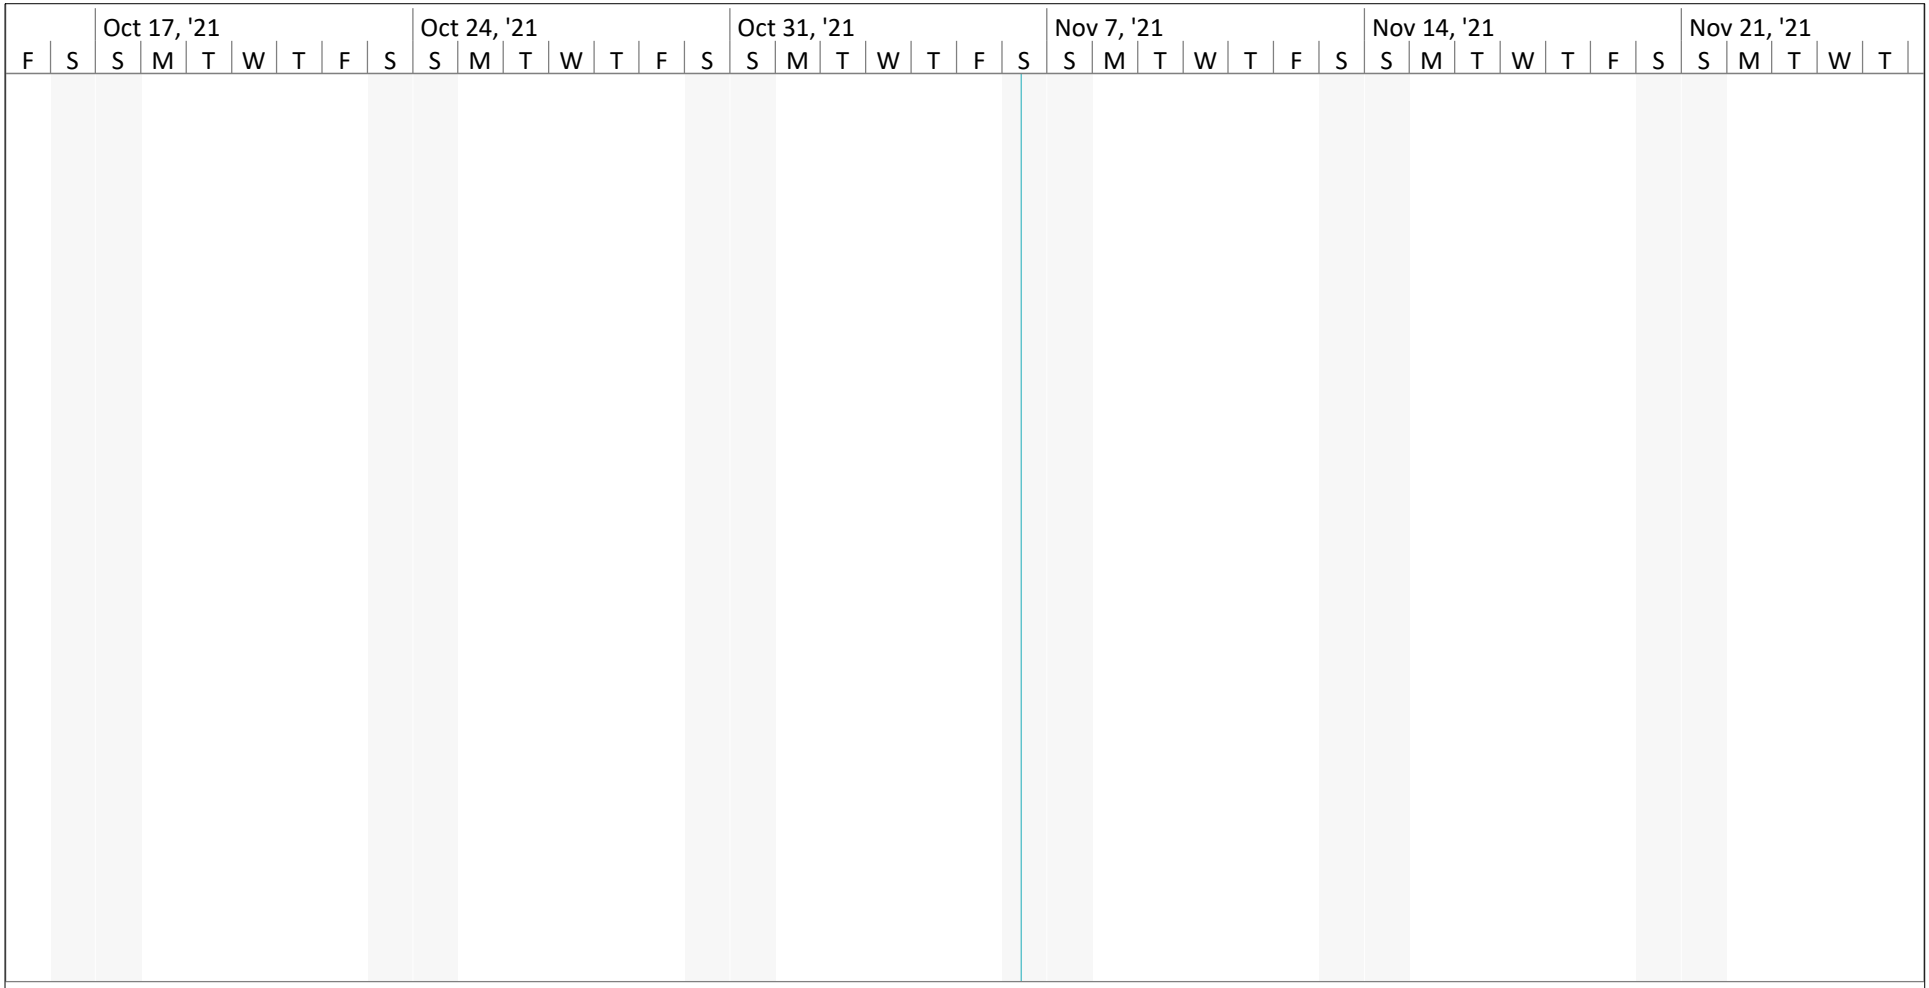


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

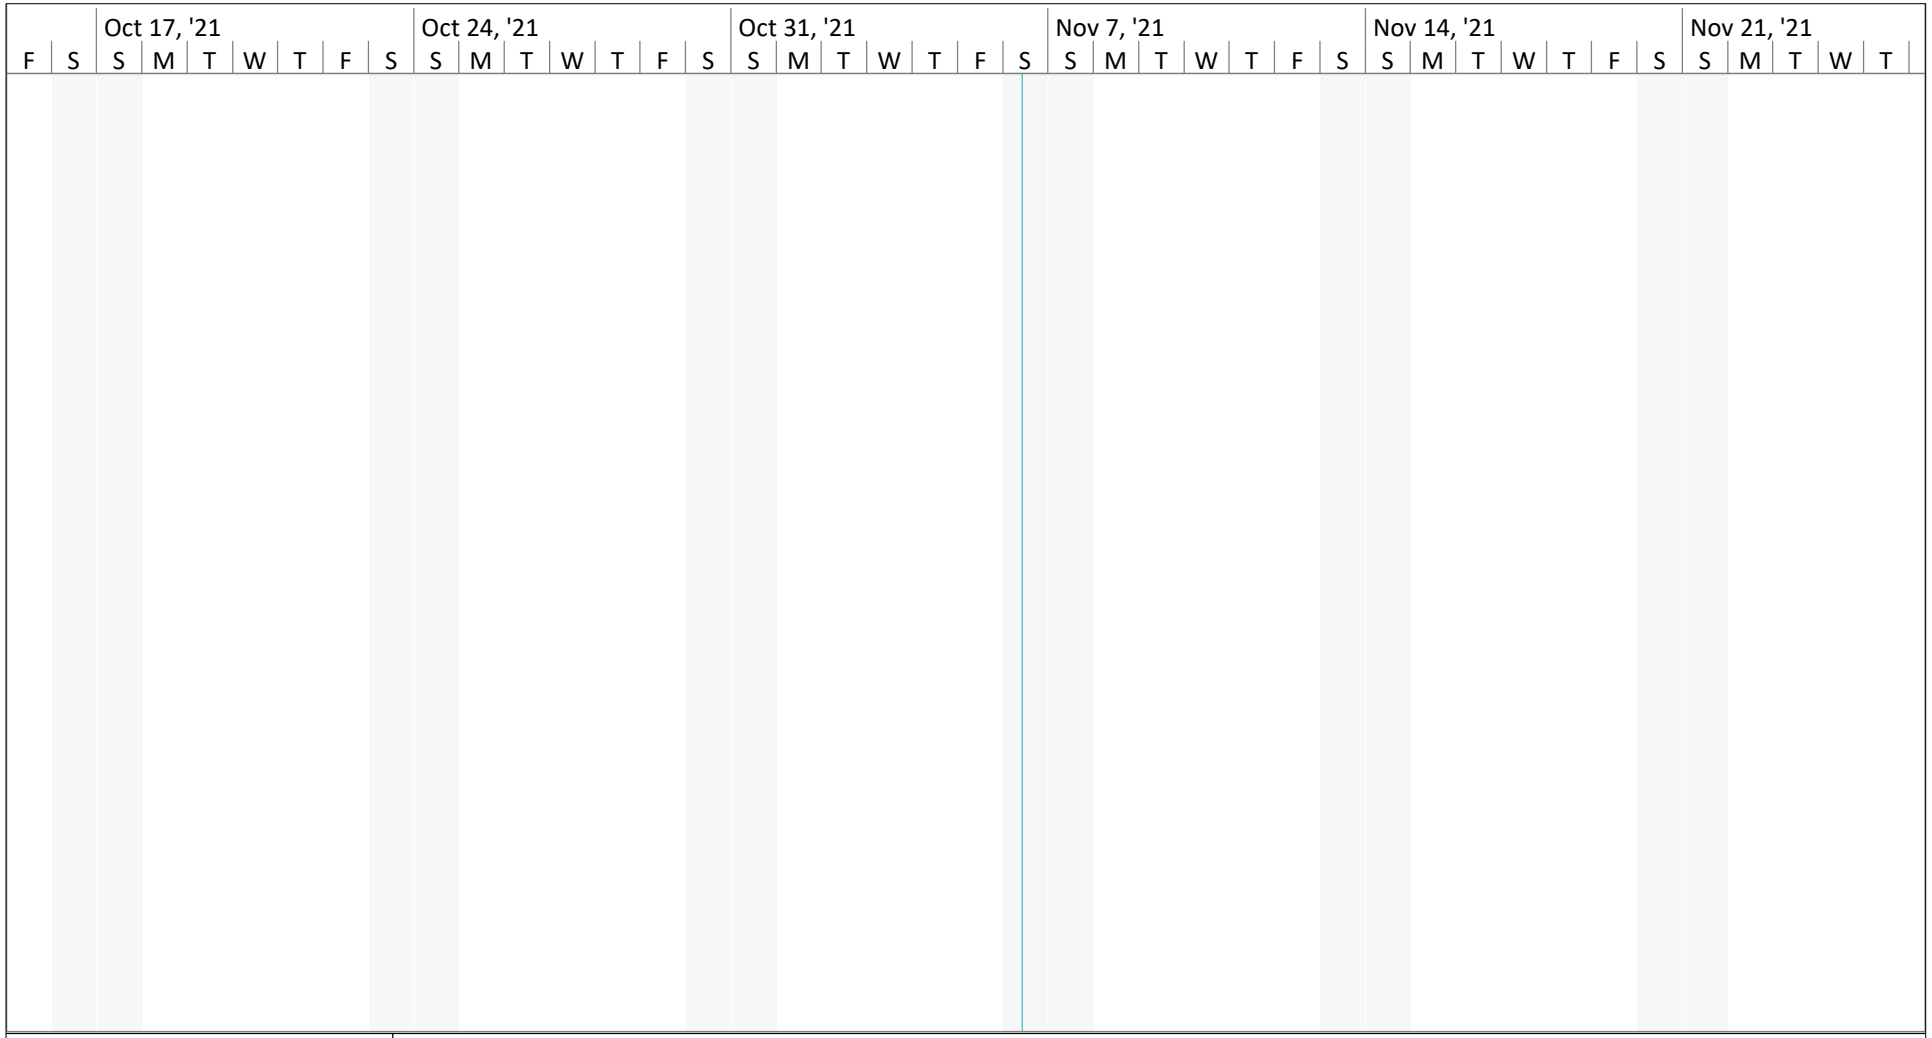


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

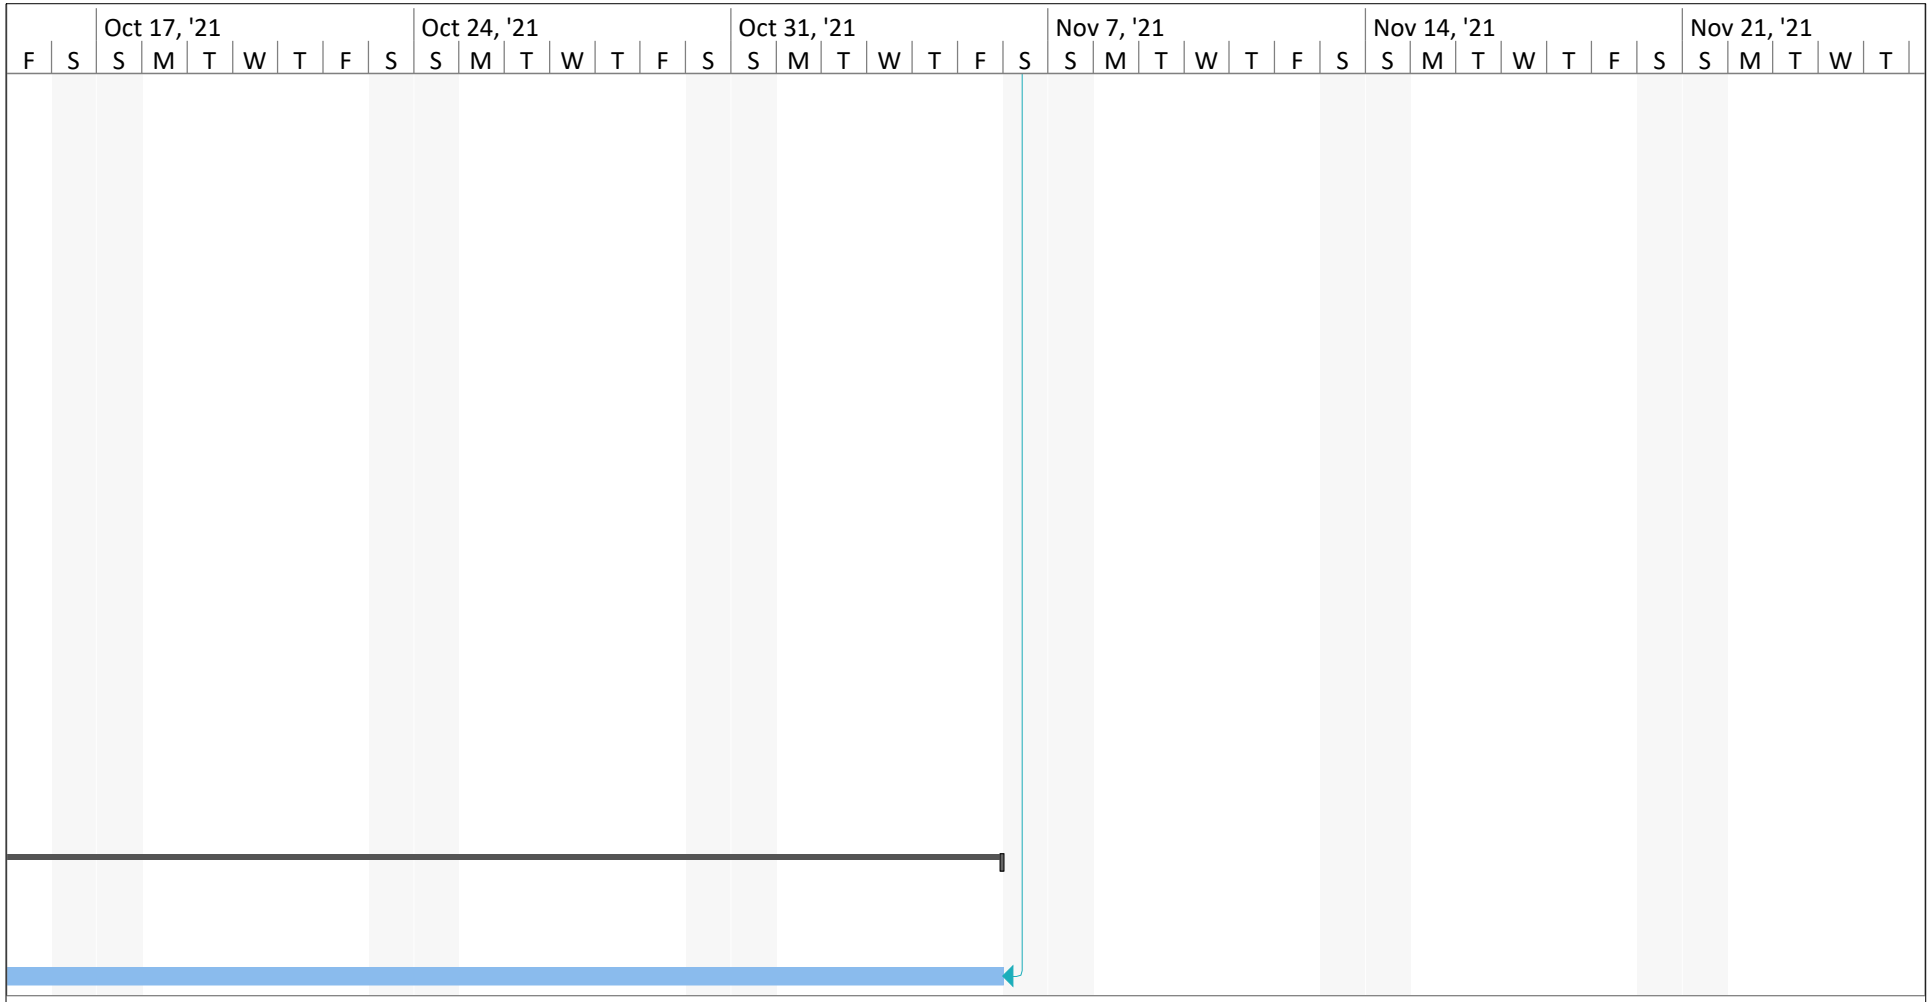


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

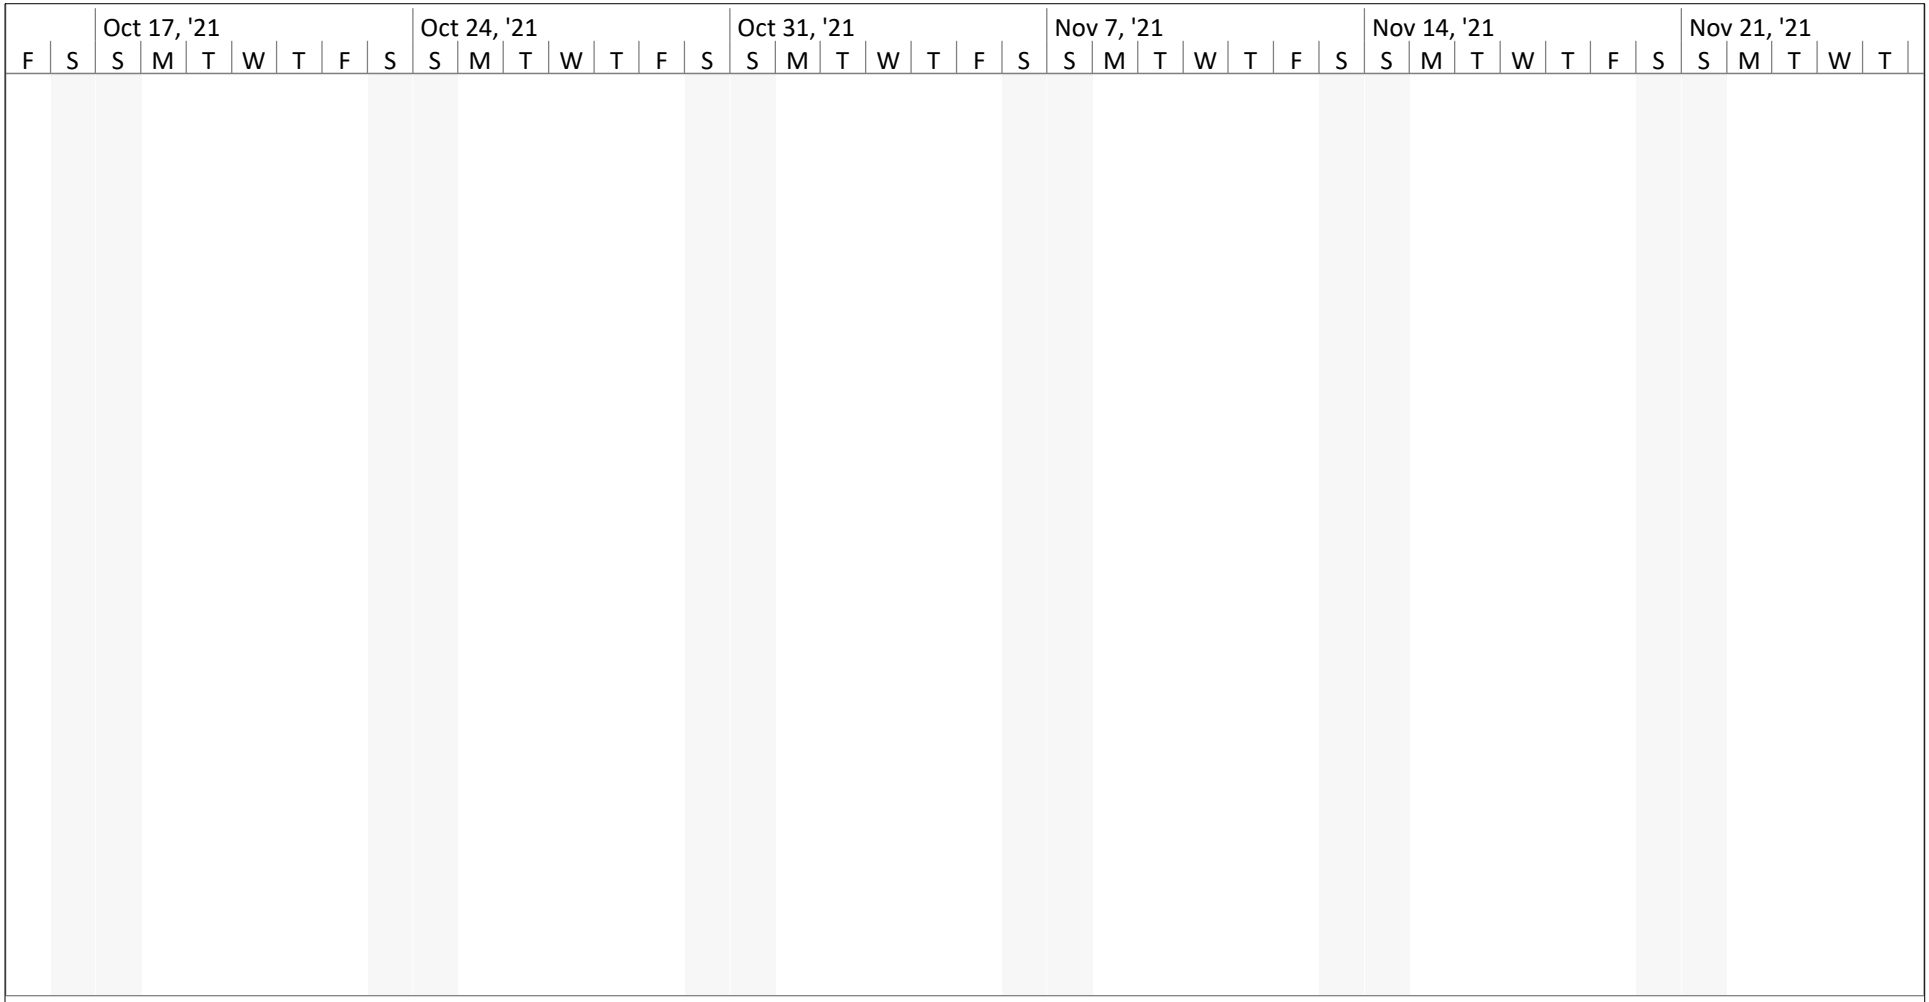


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

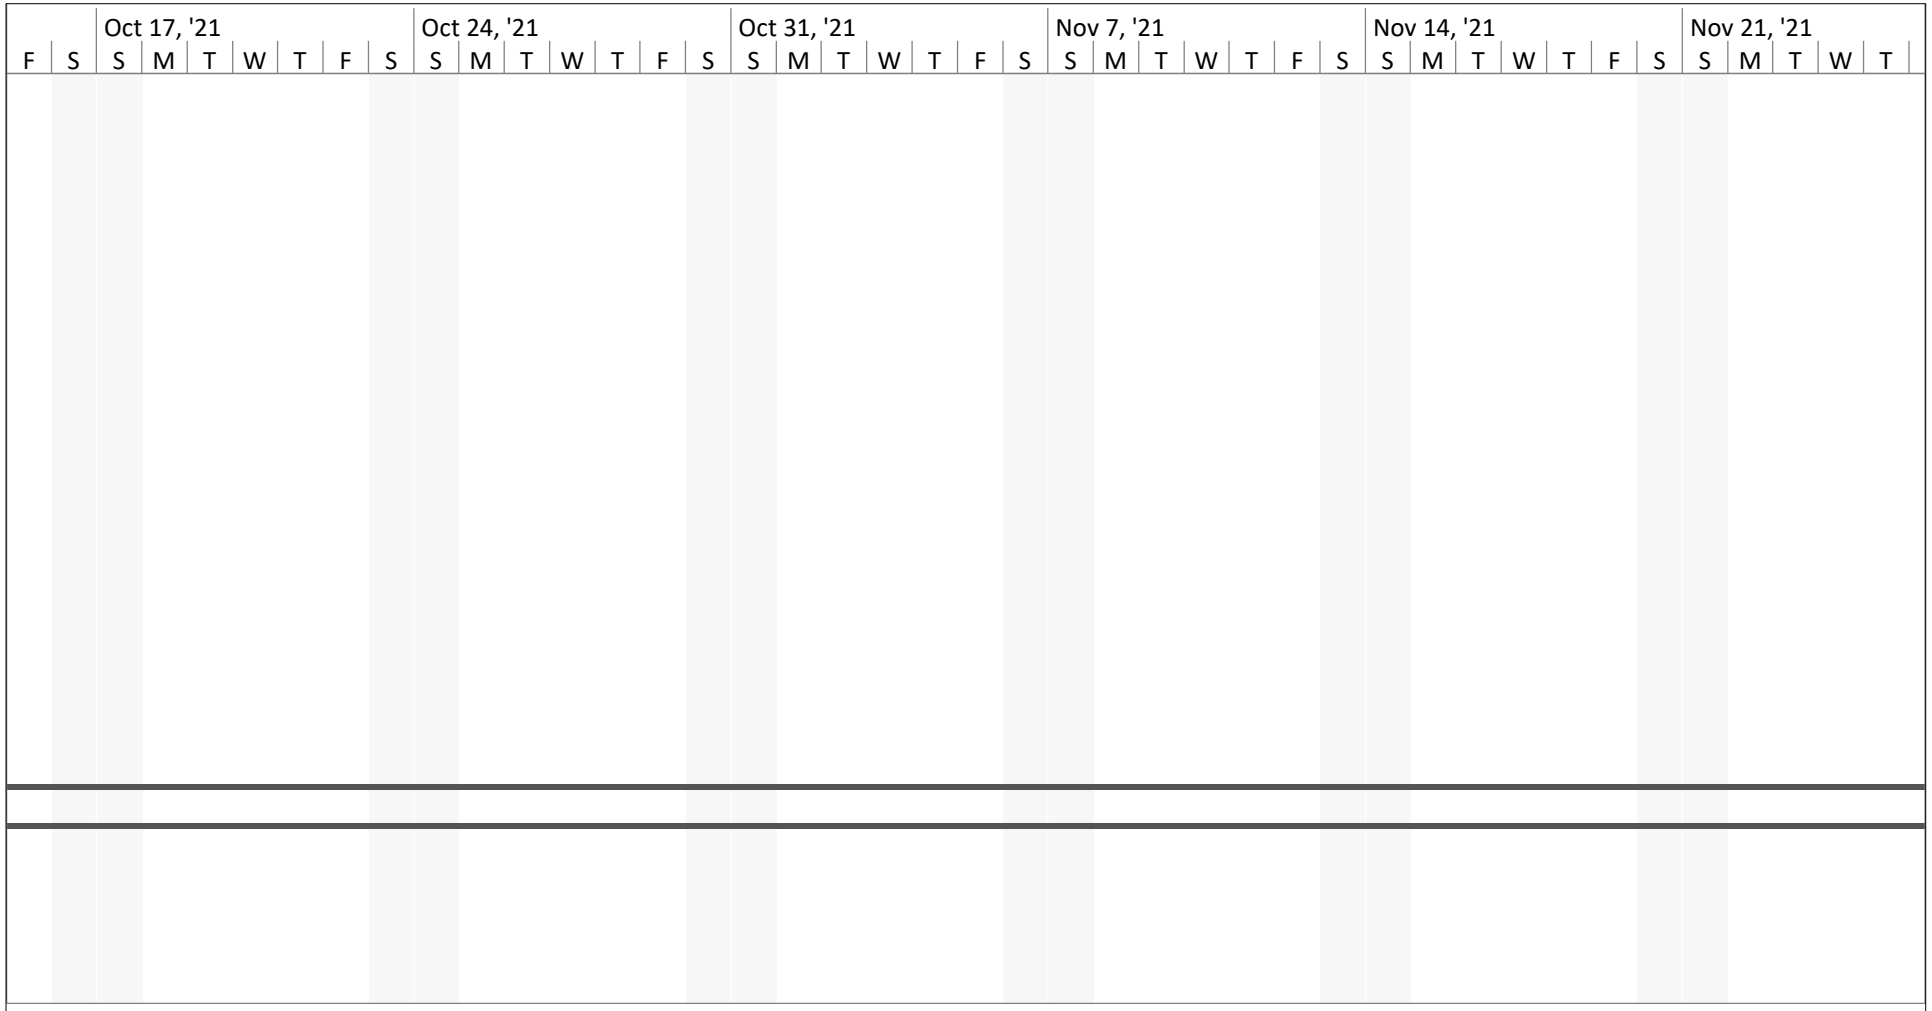


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

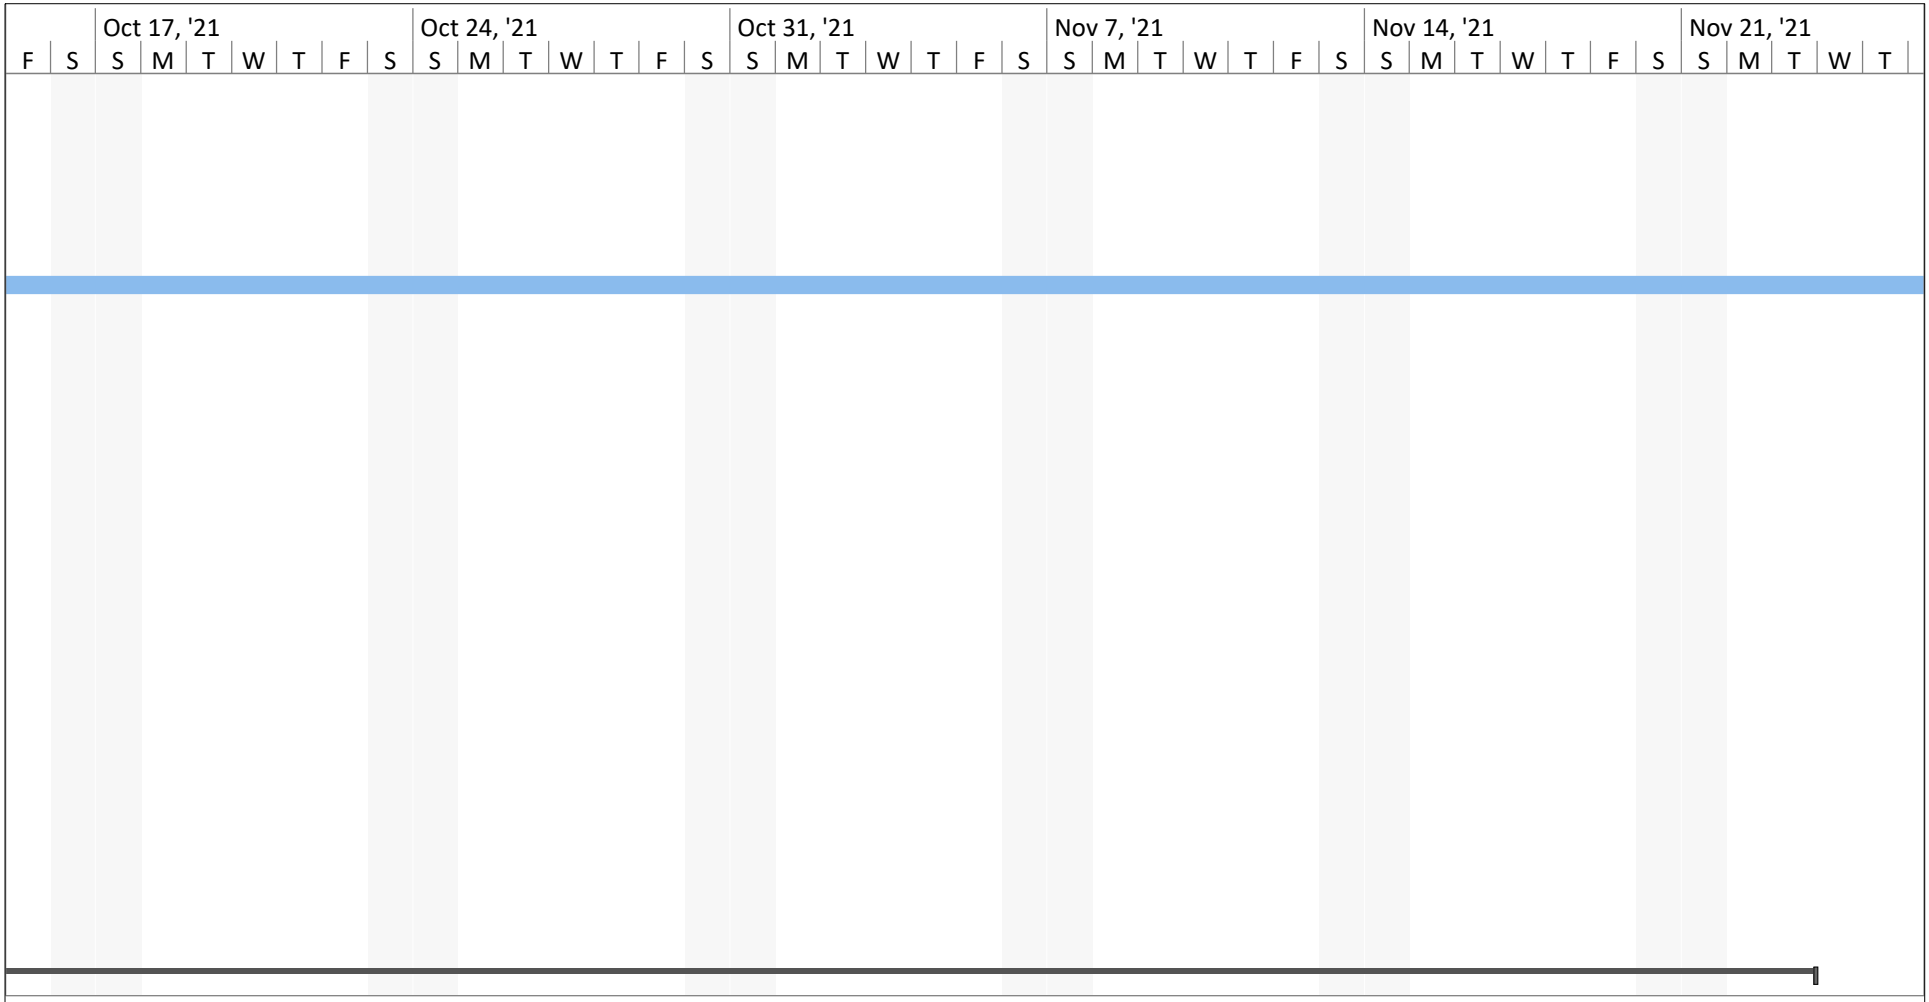


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

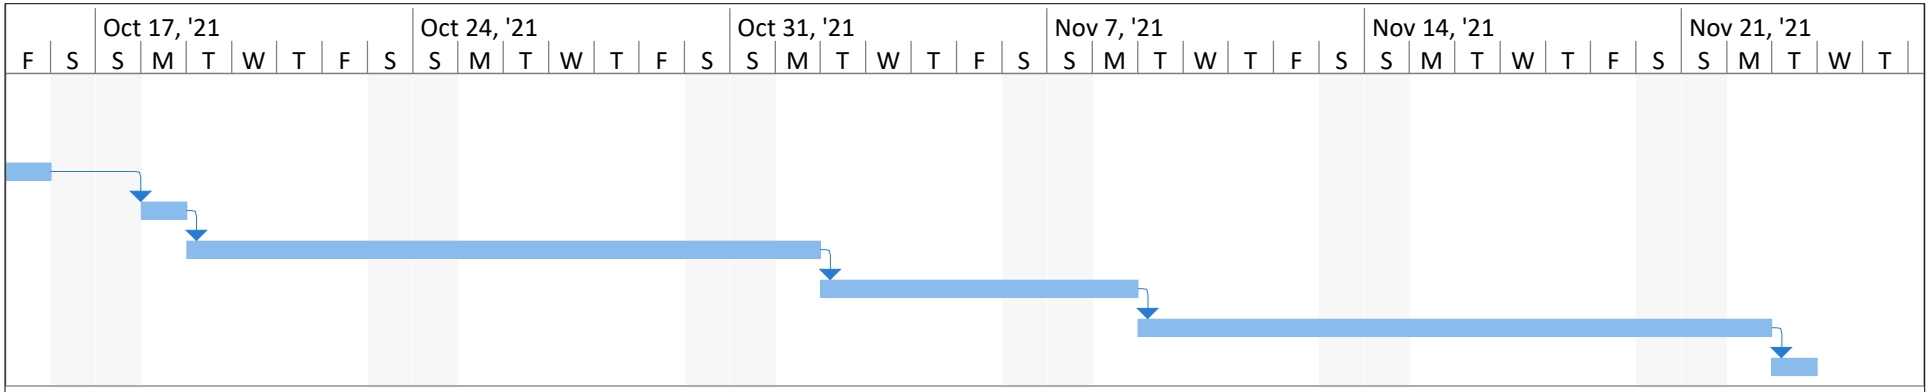


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

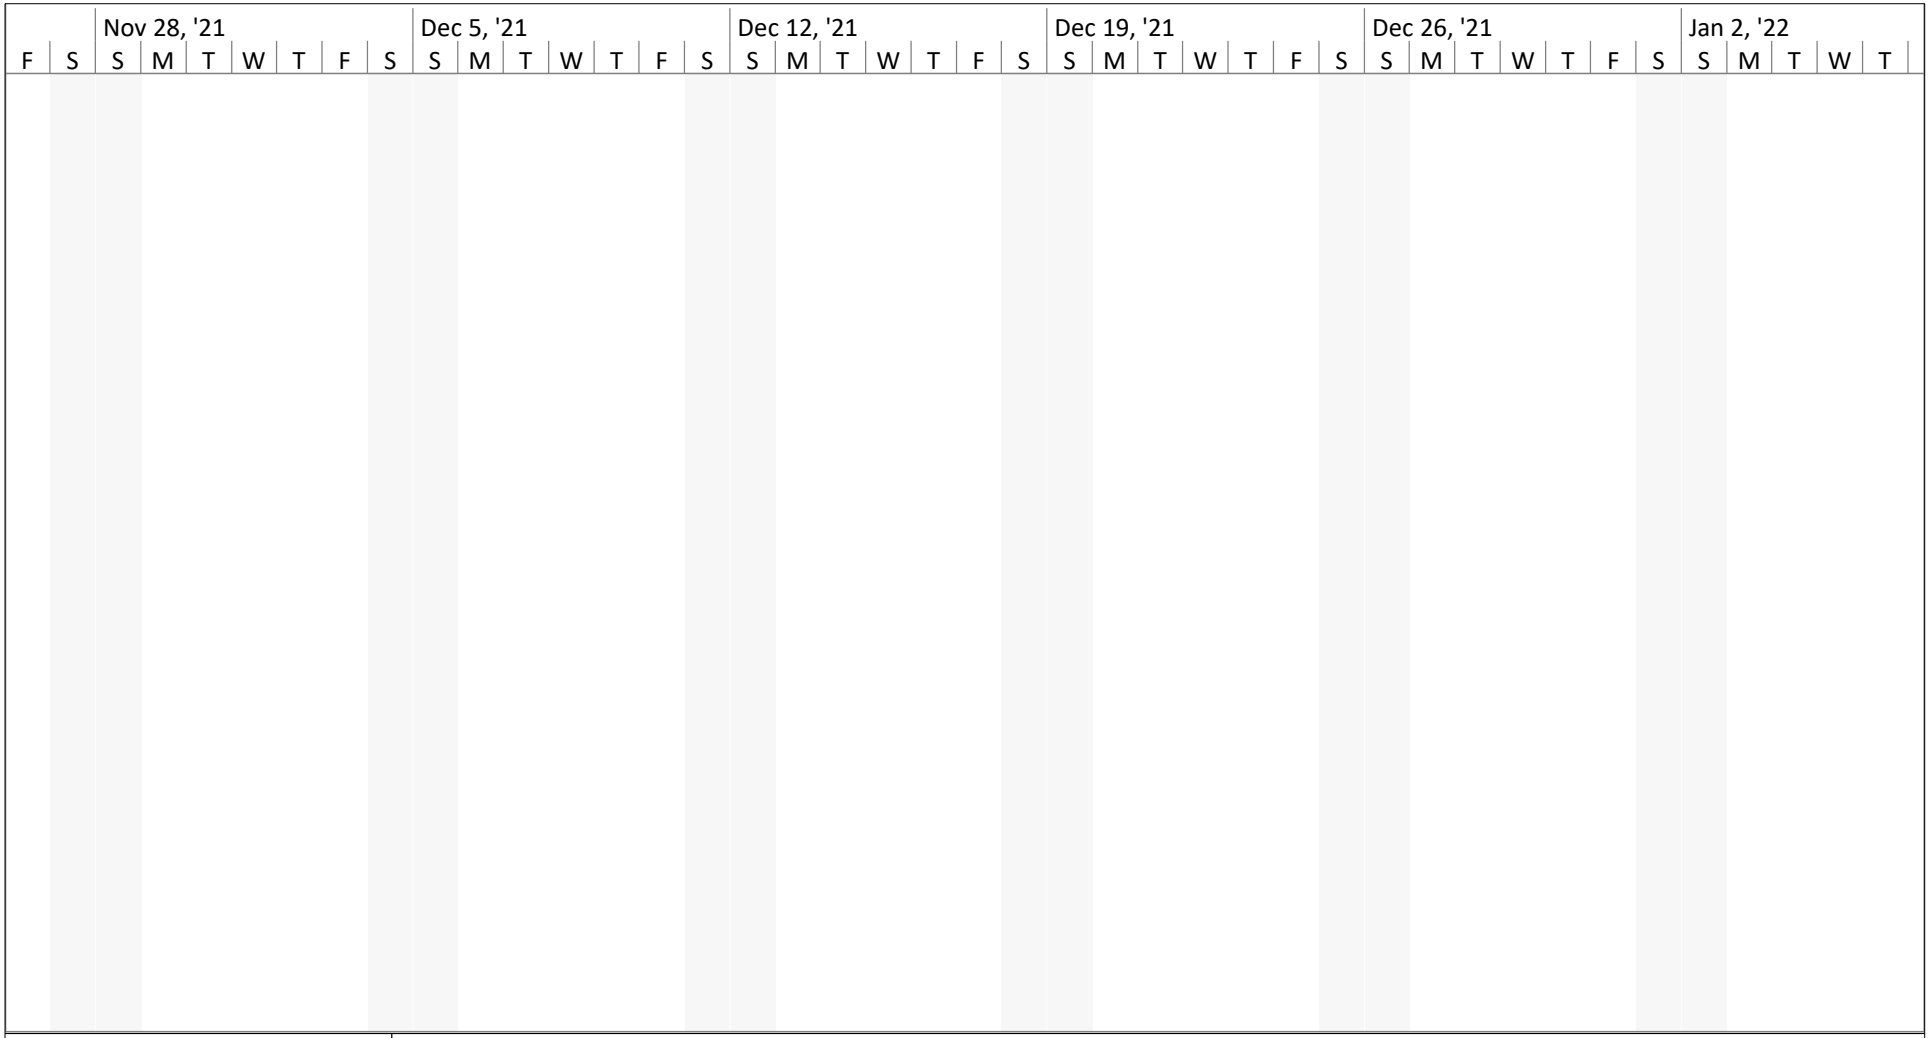


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

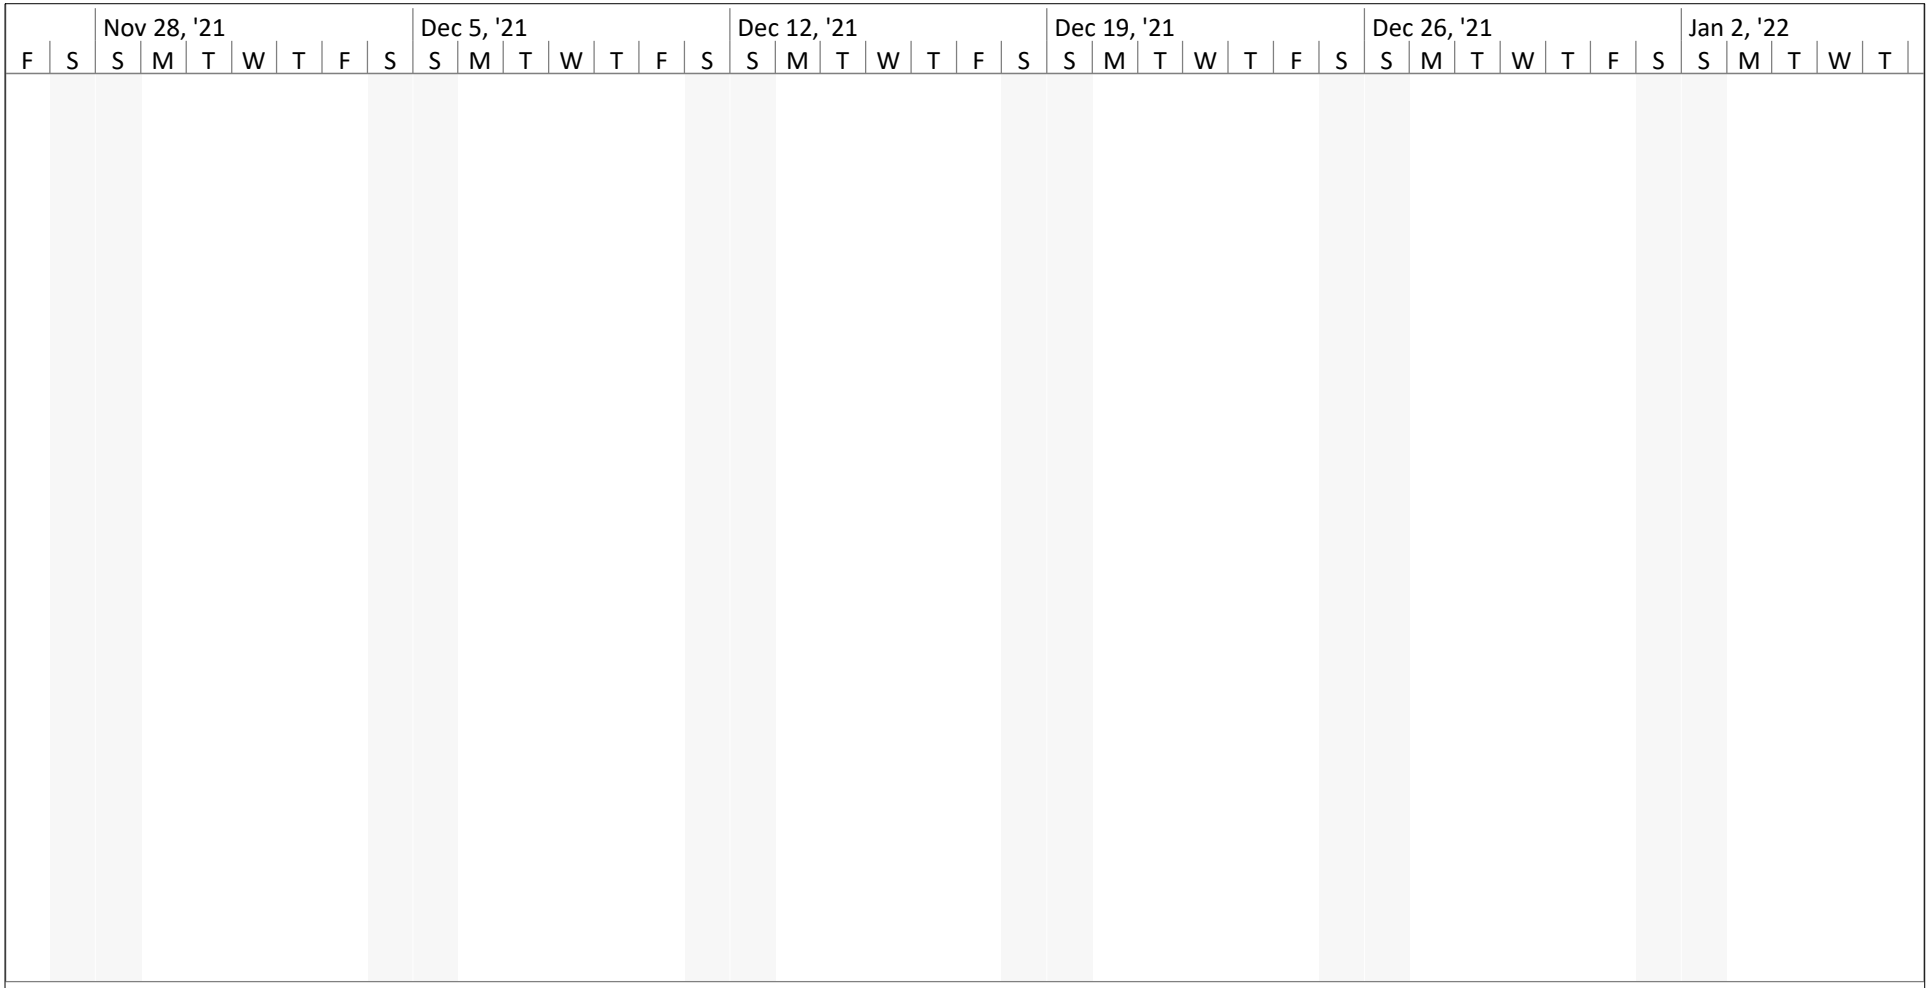


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

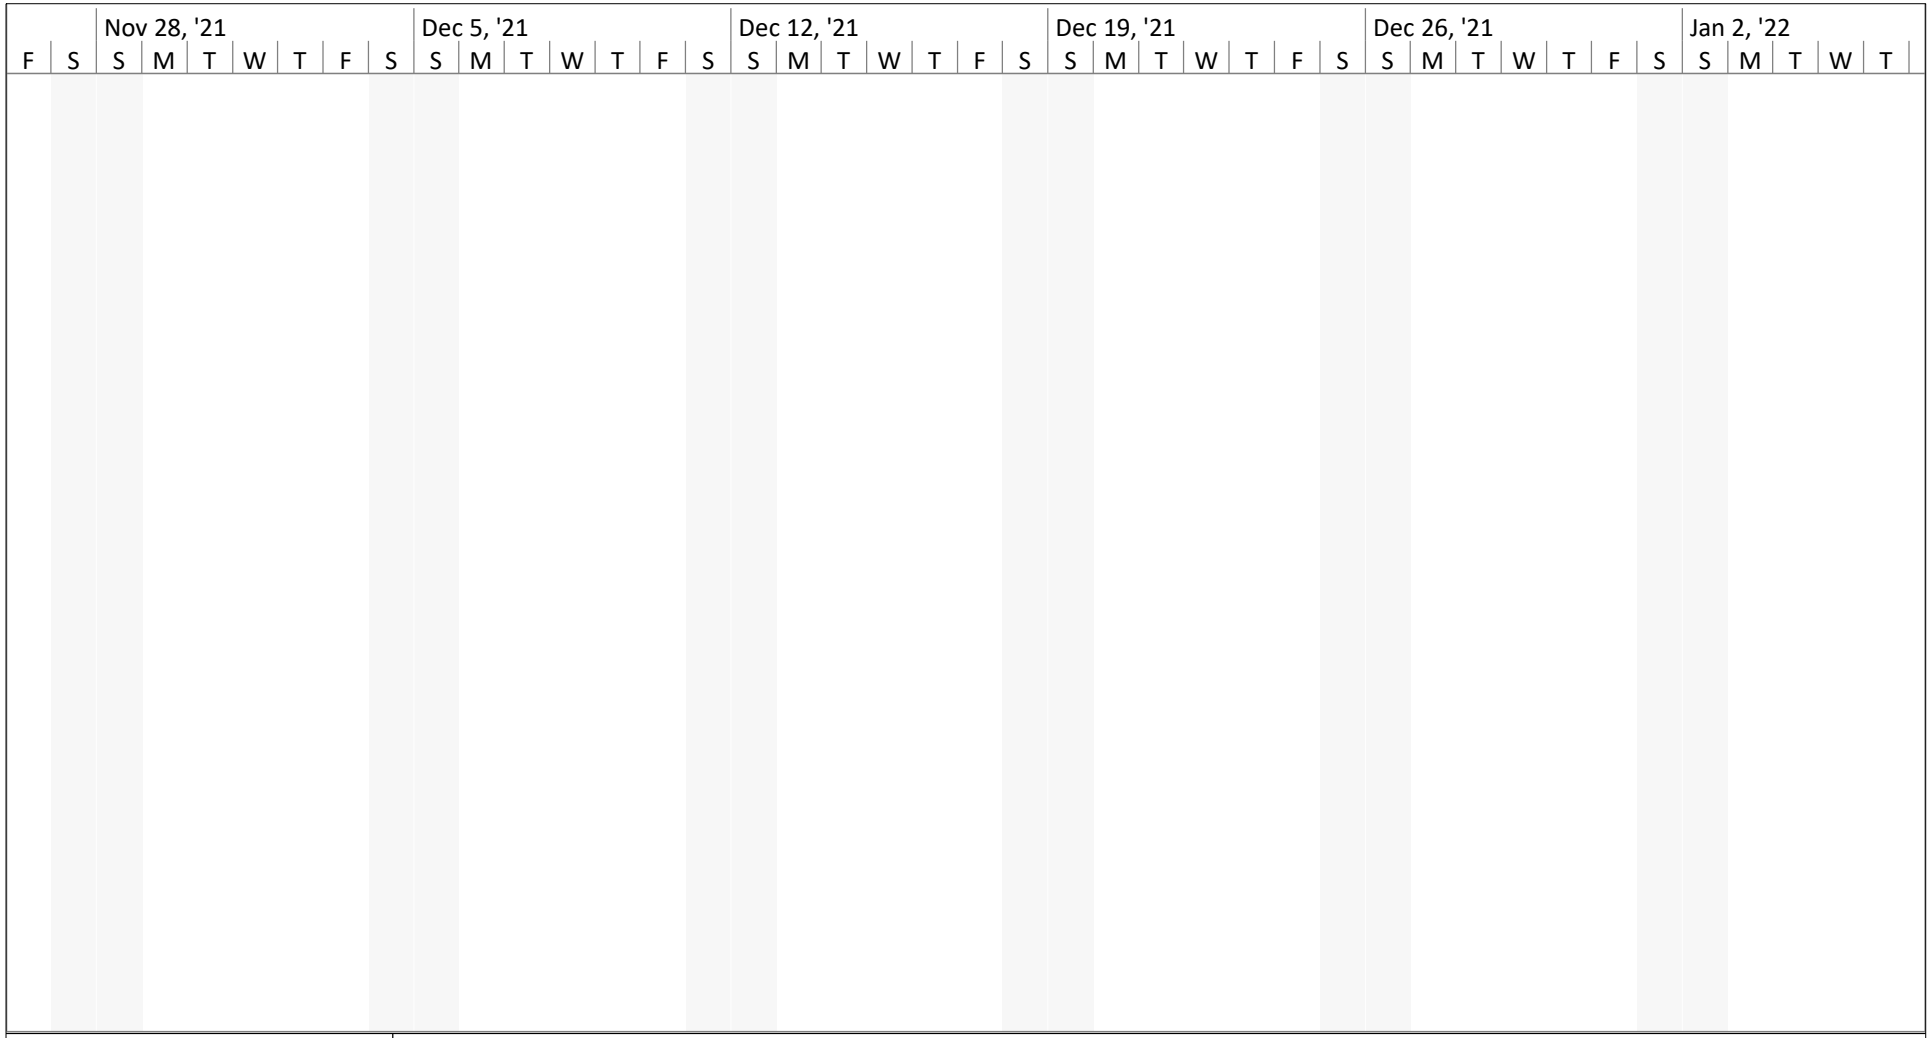


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

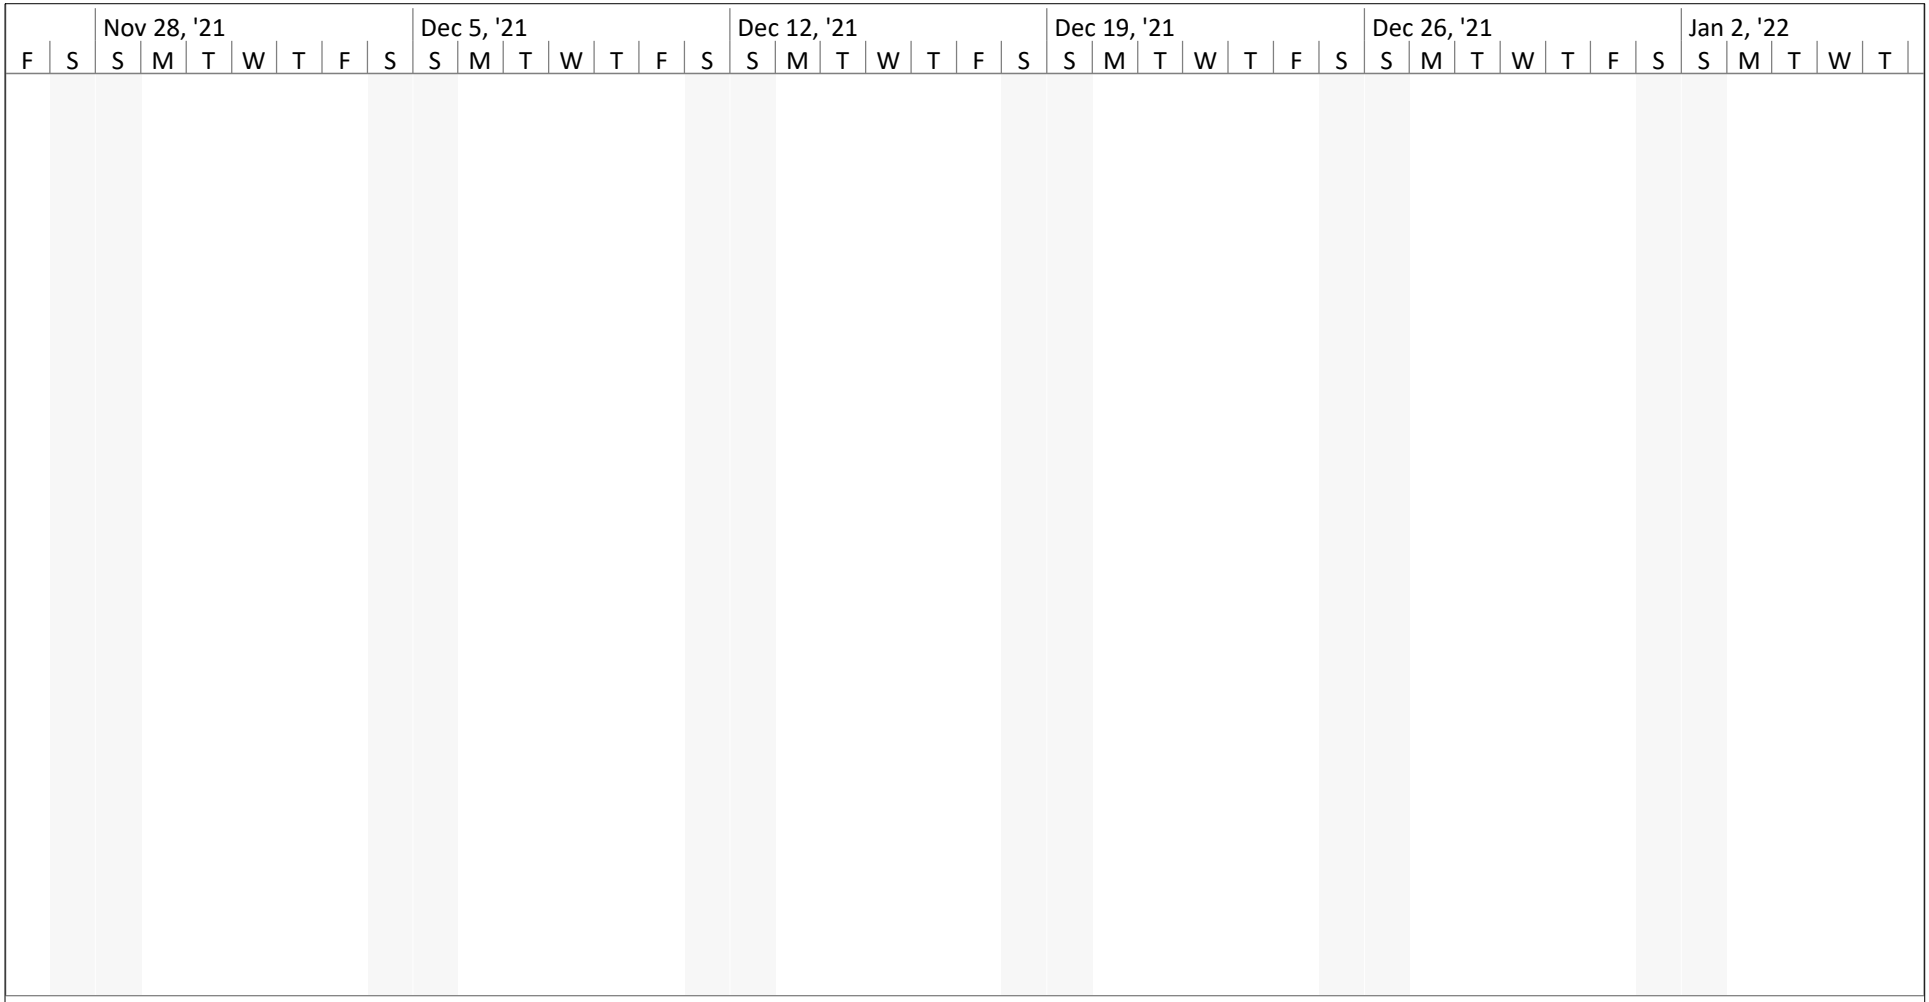


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

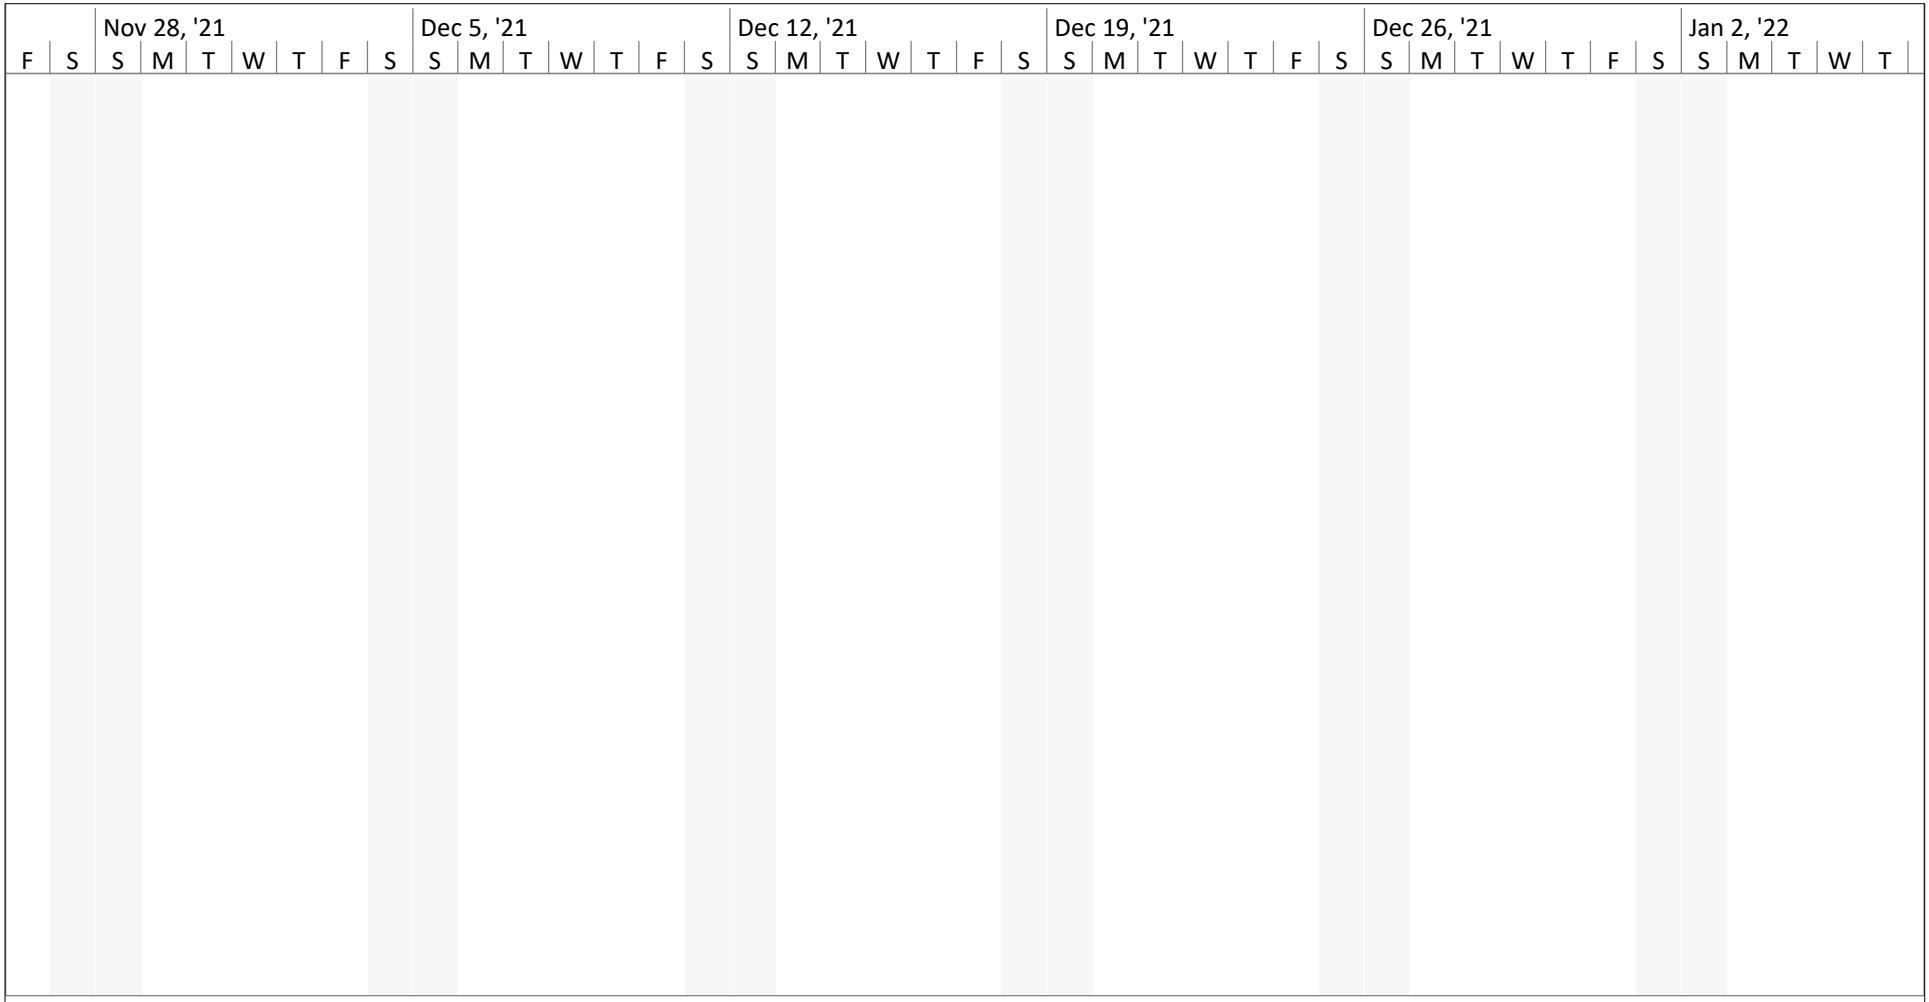


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

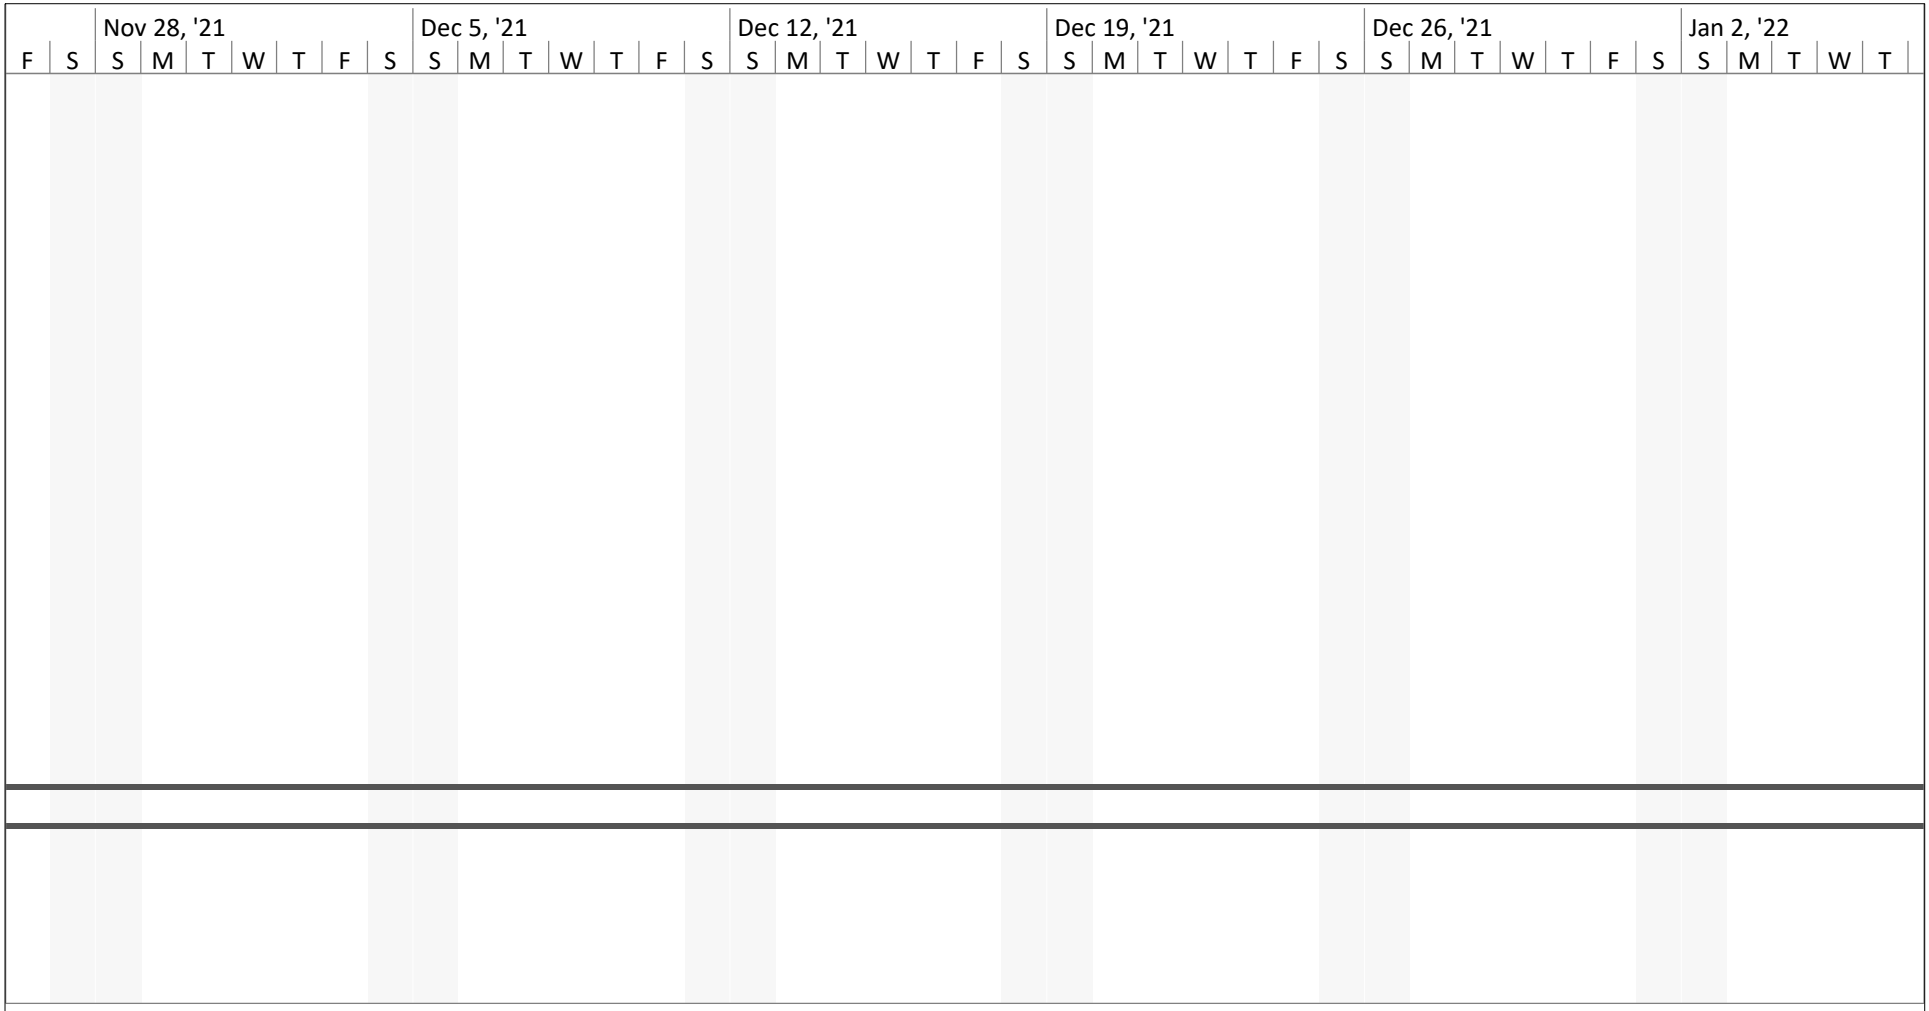


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

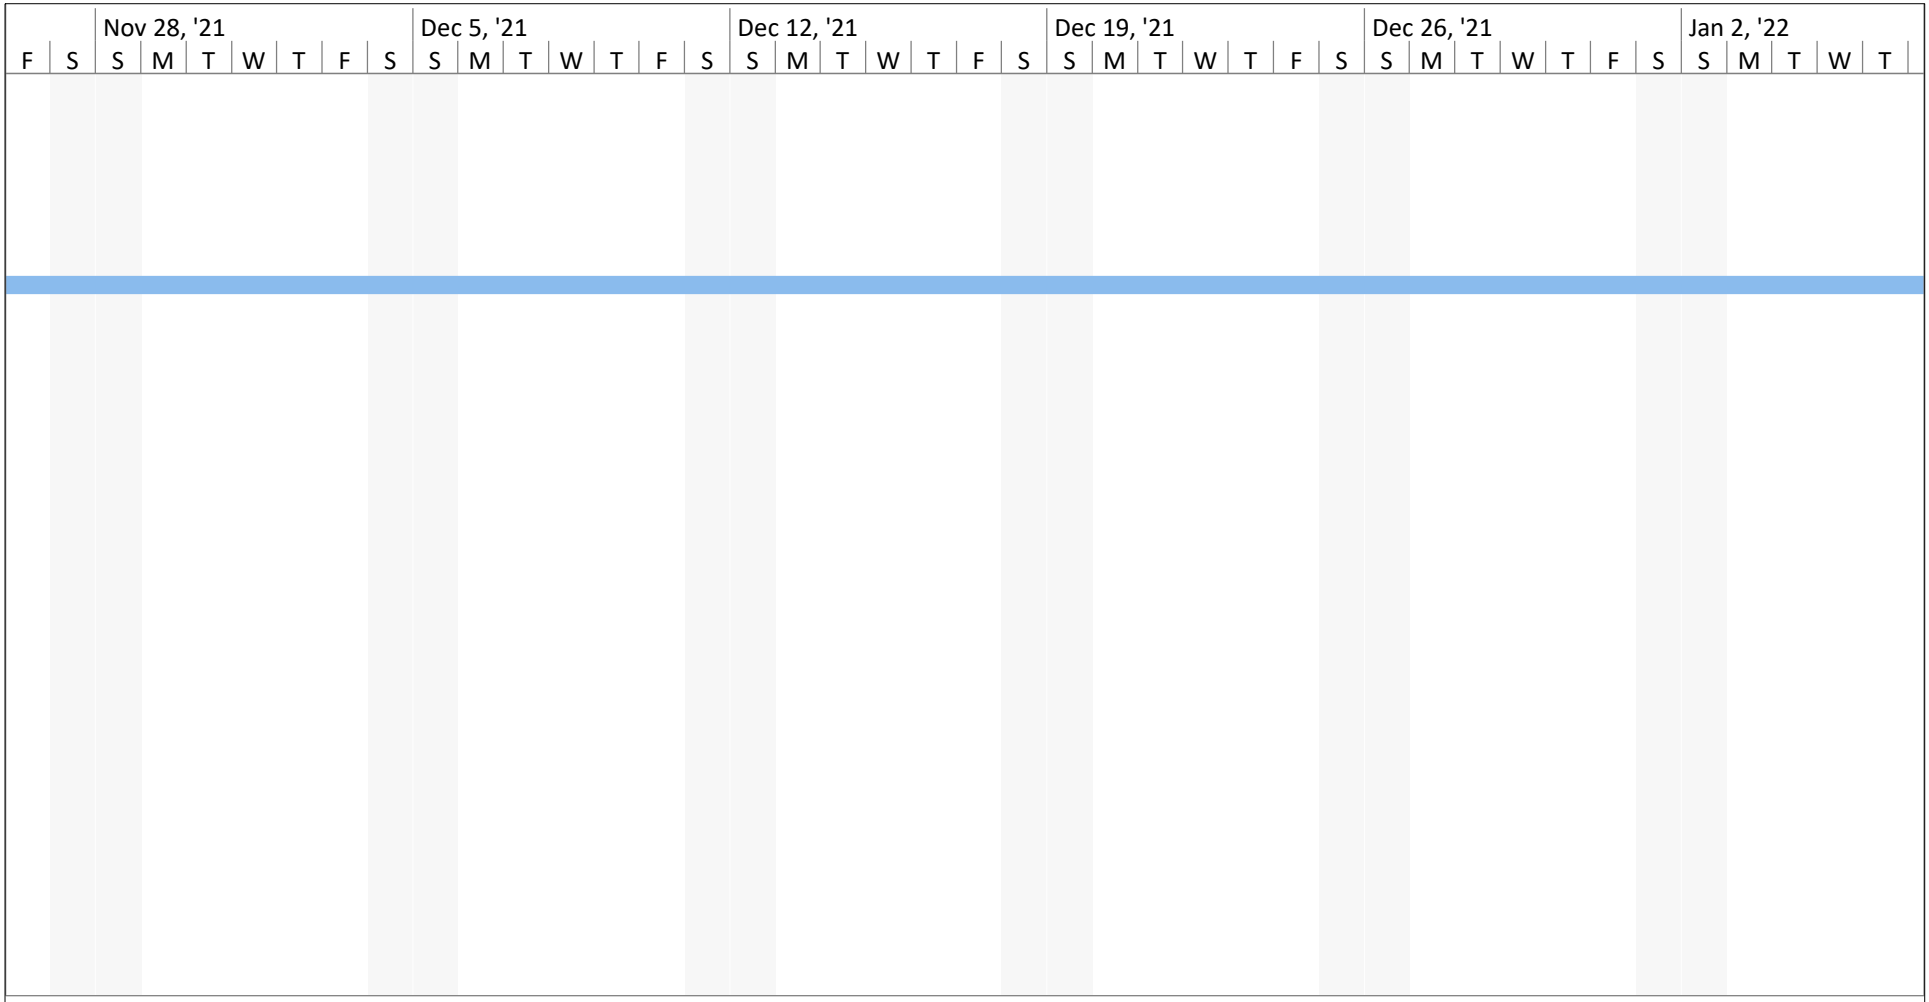


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |




Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

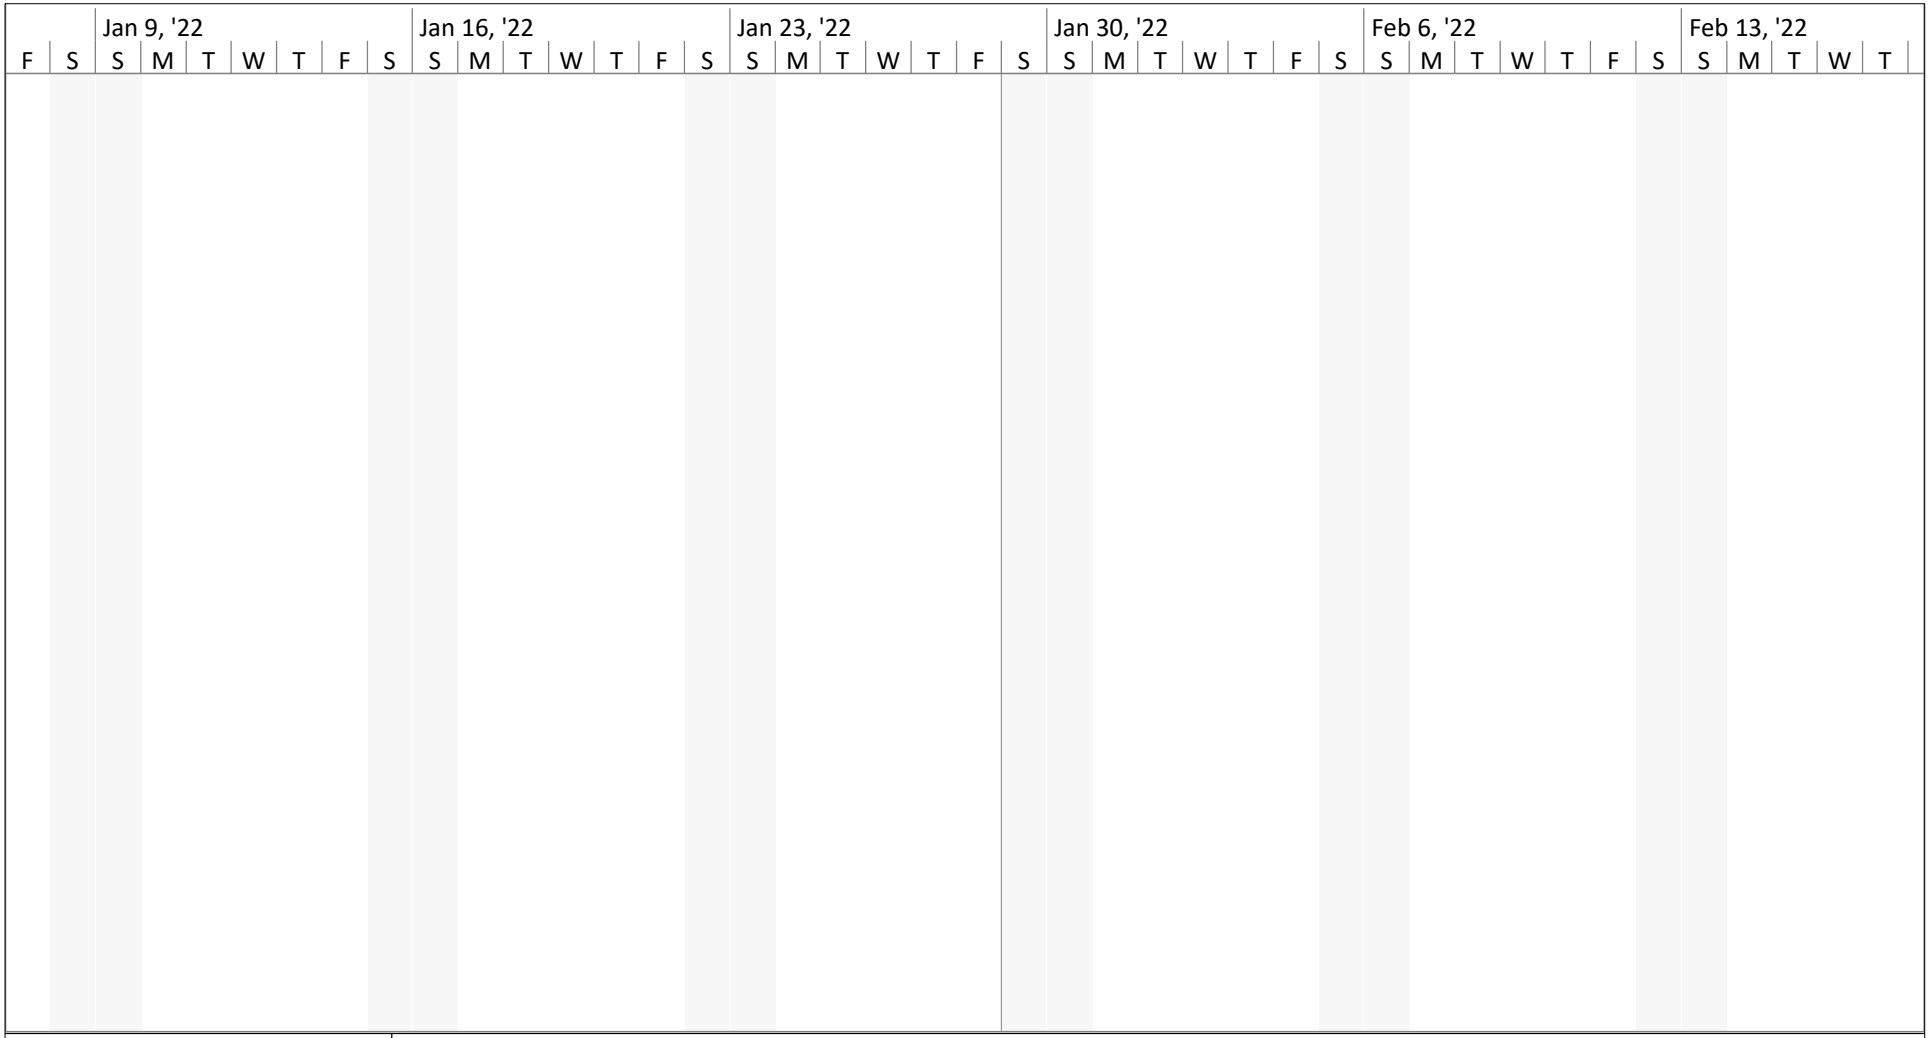


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

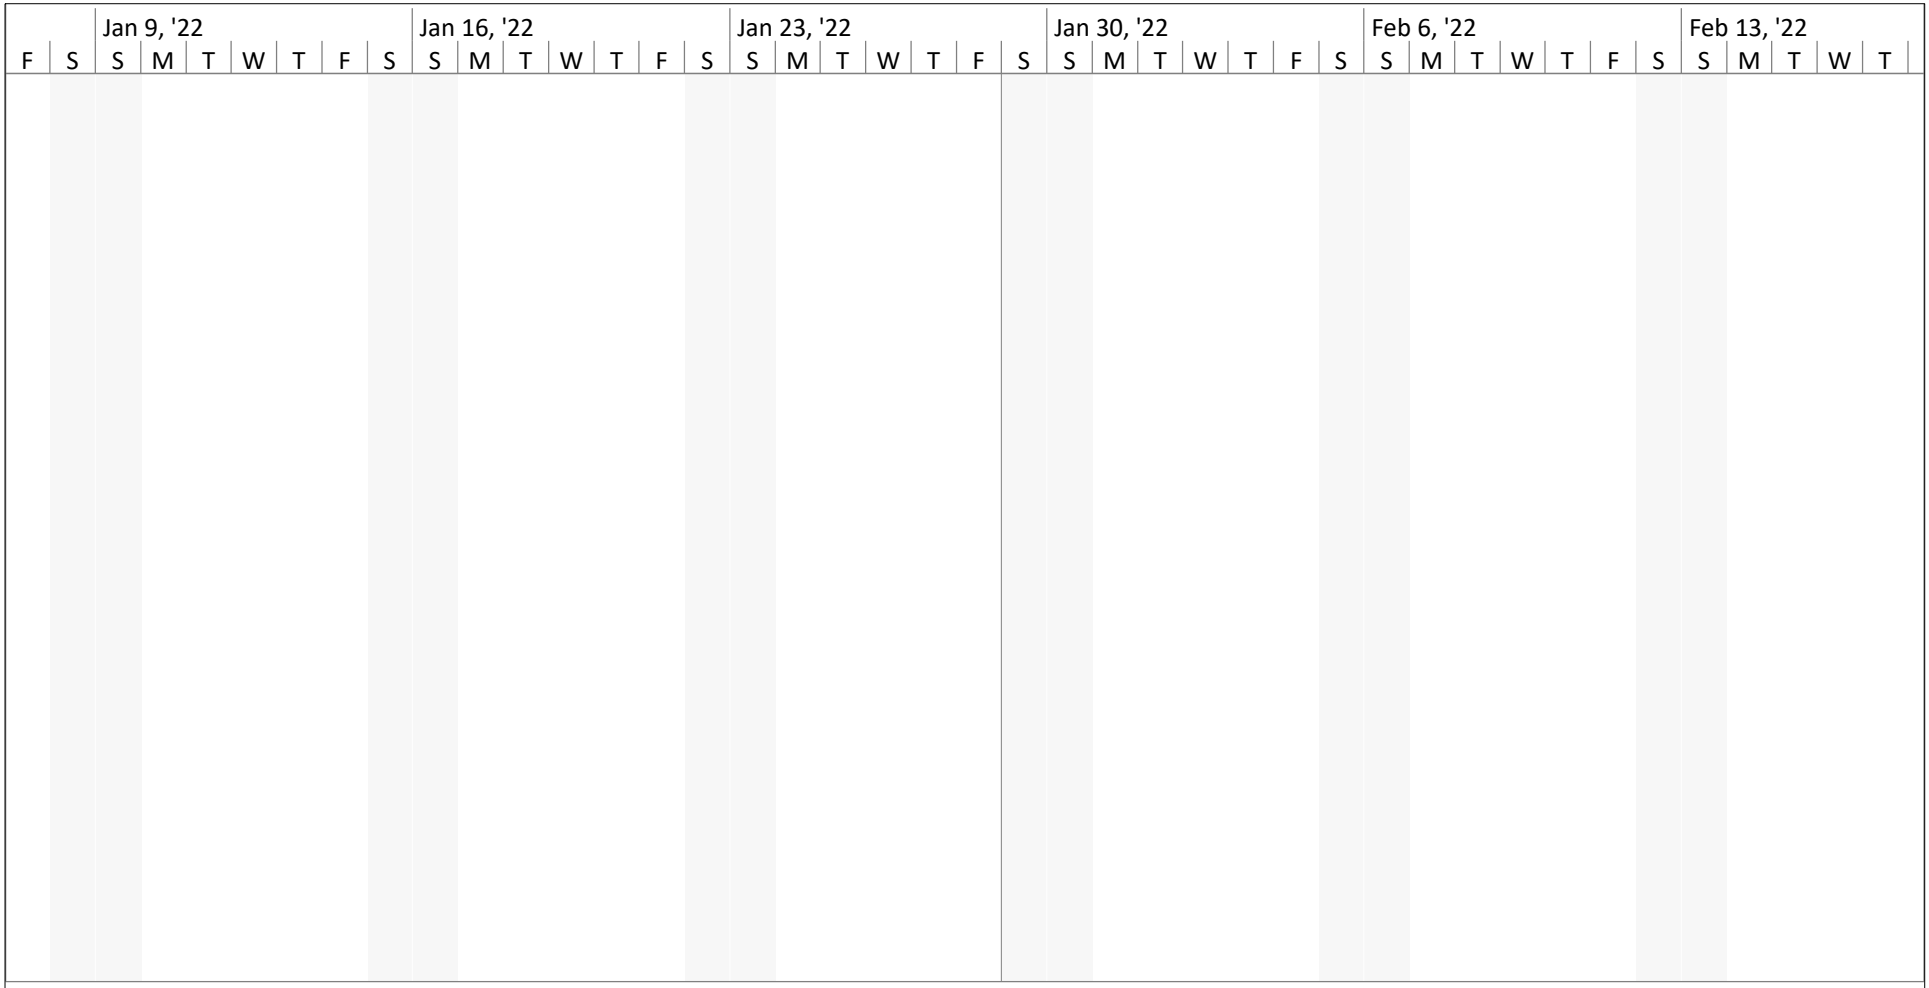


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

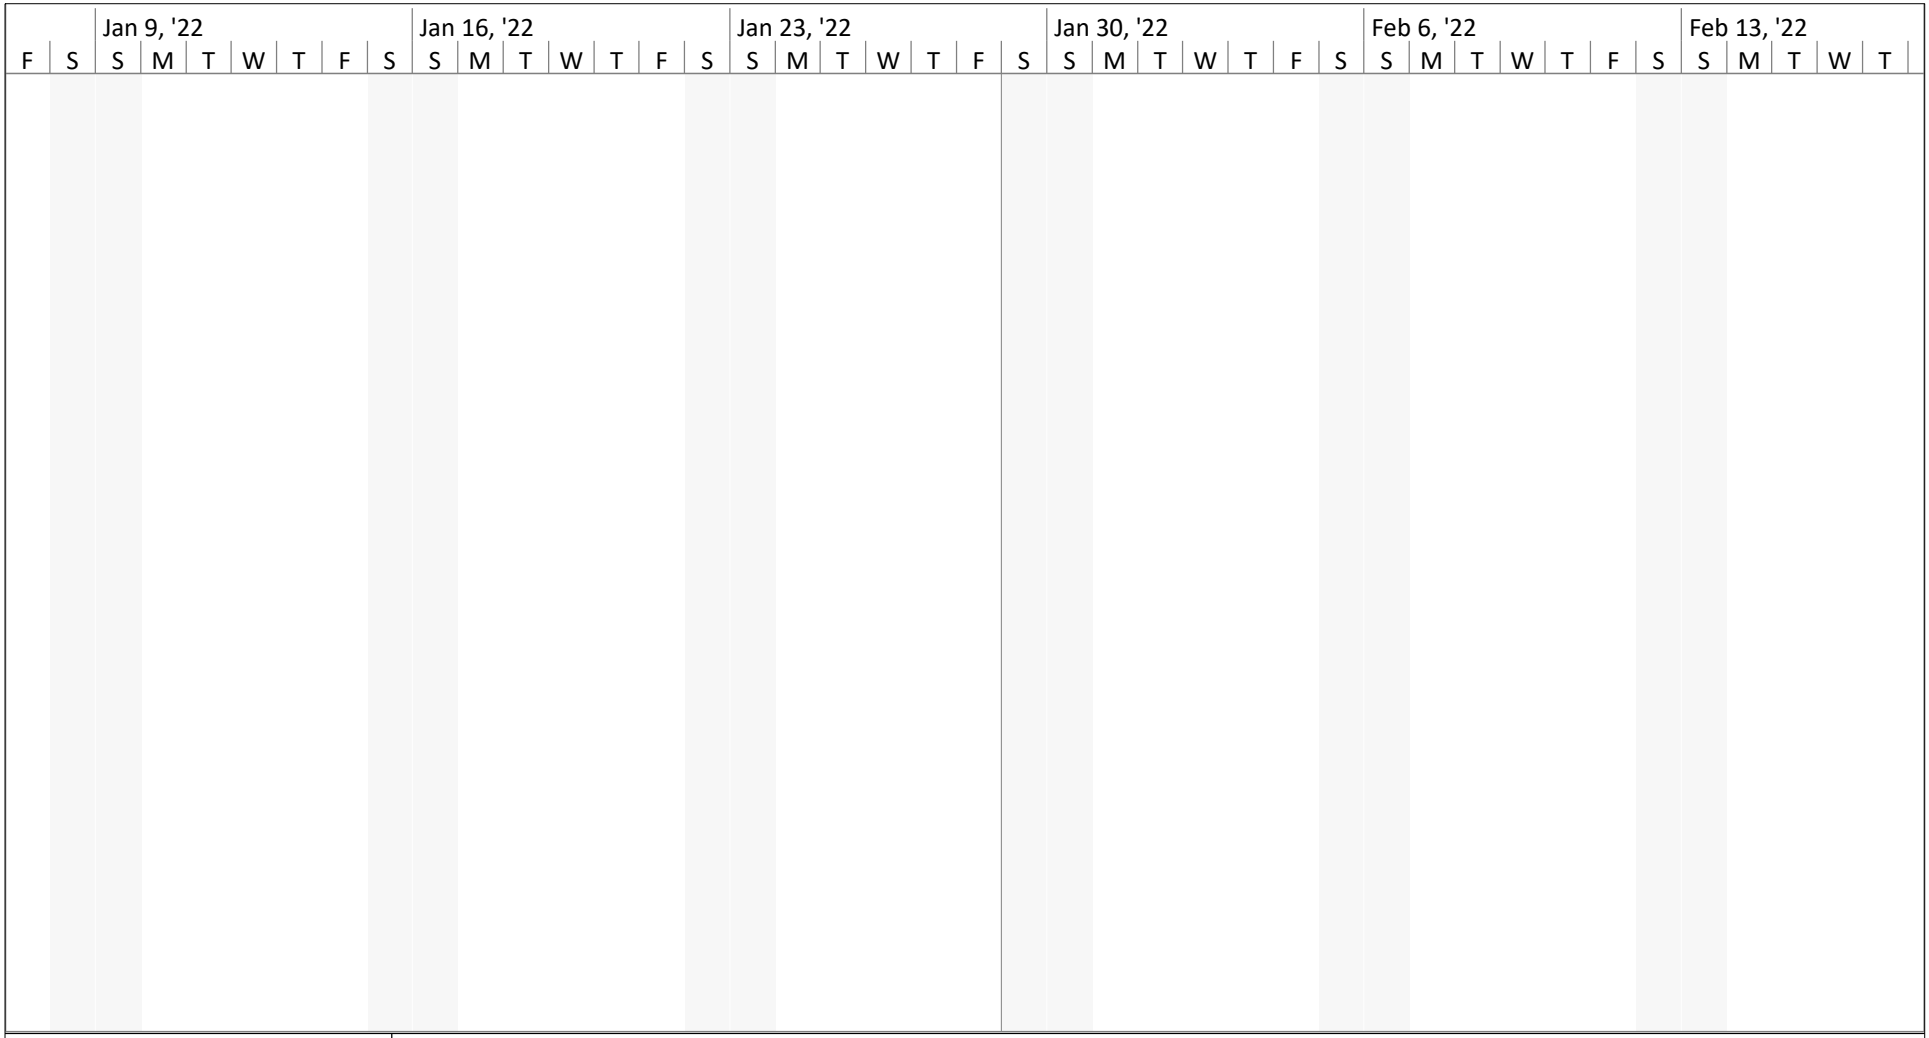


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

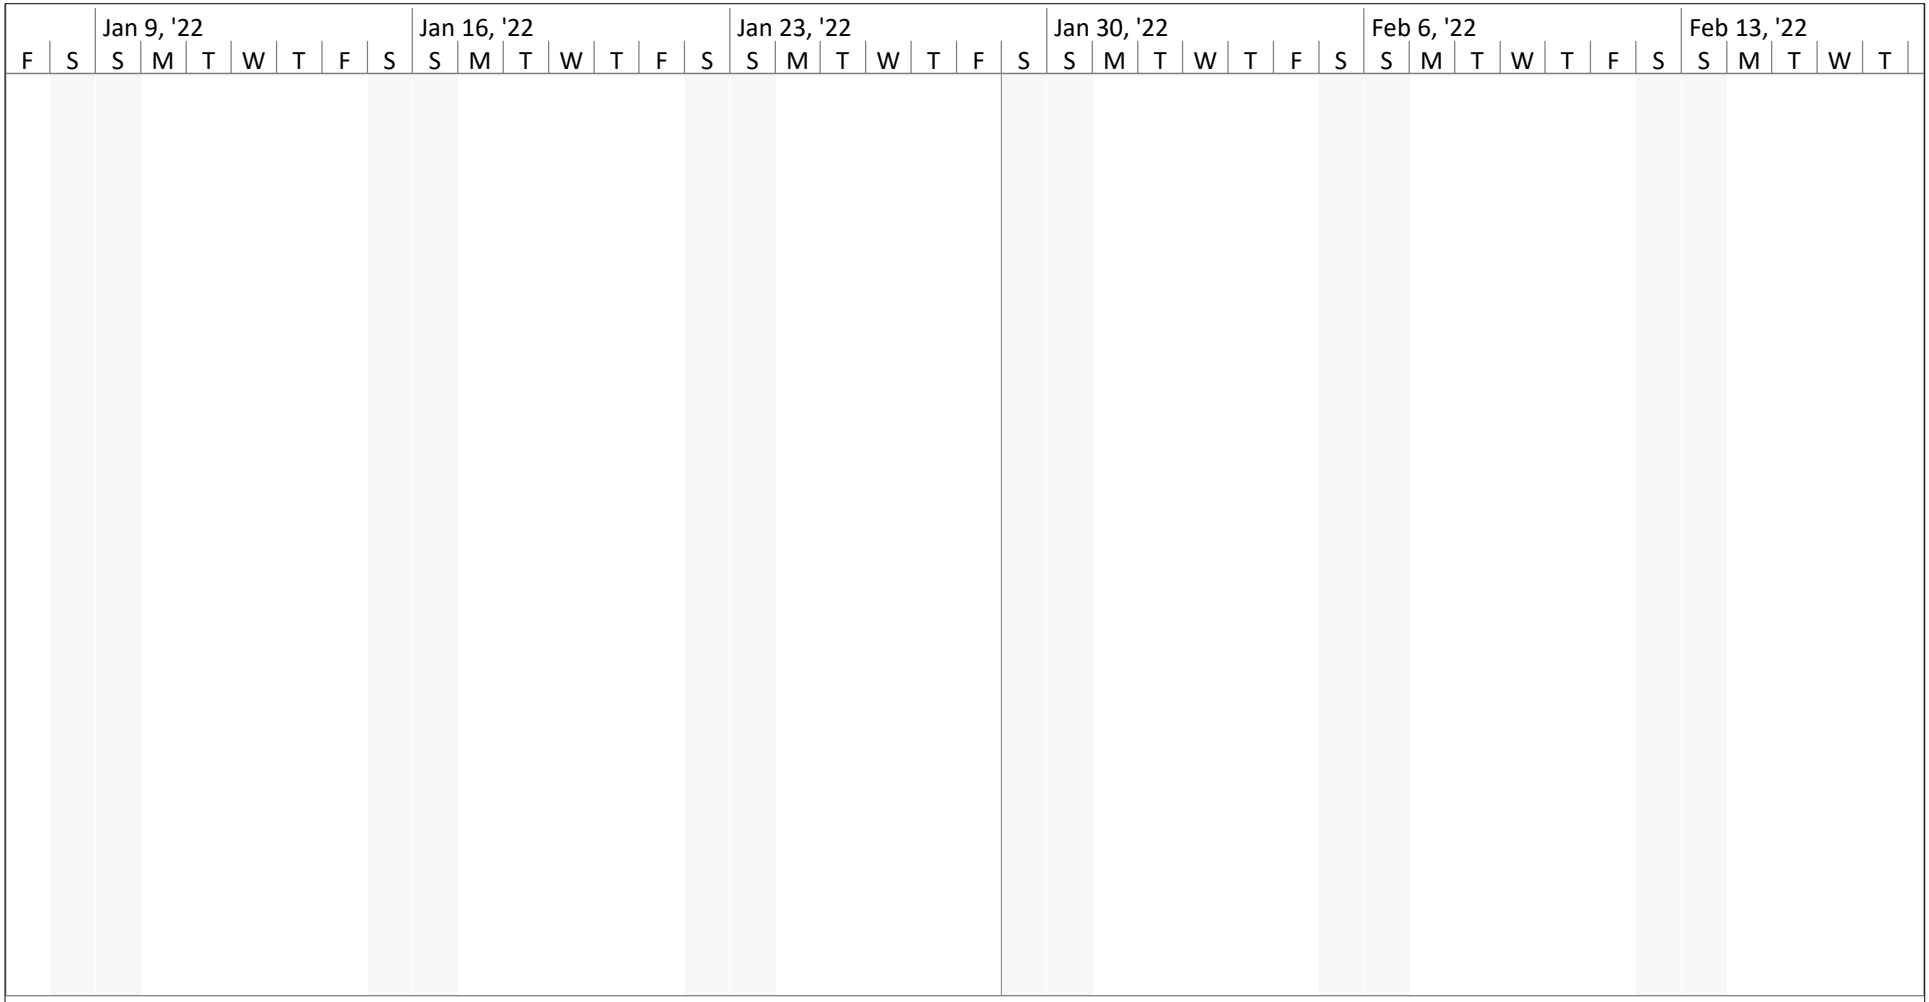


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

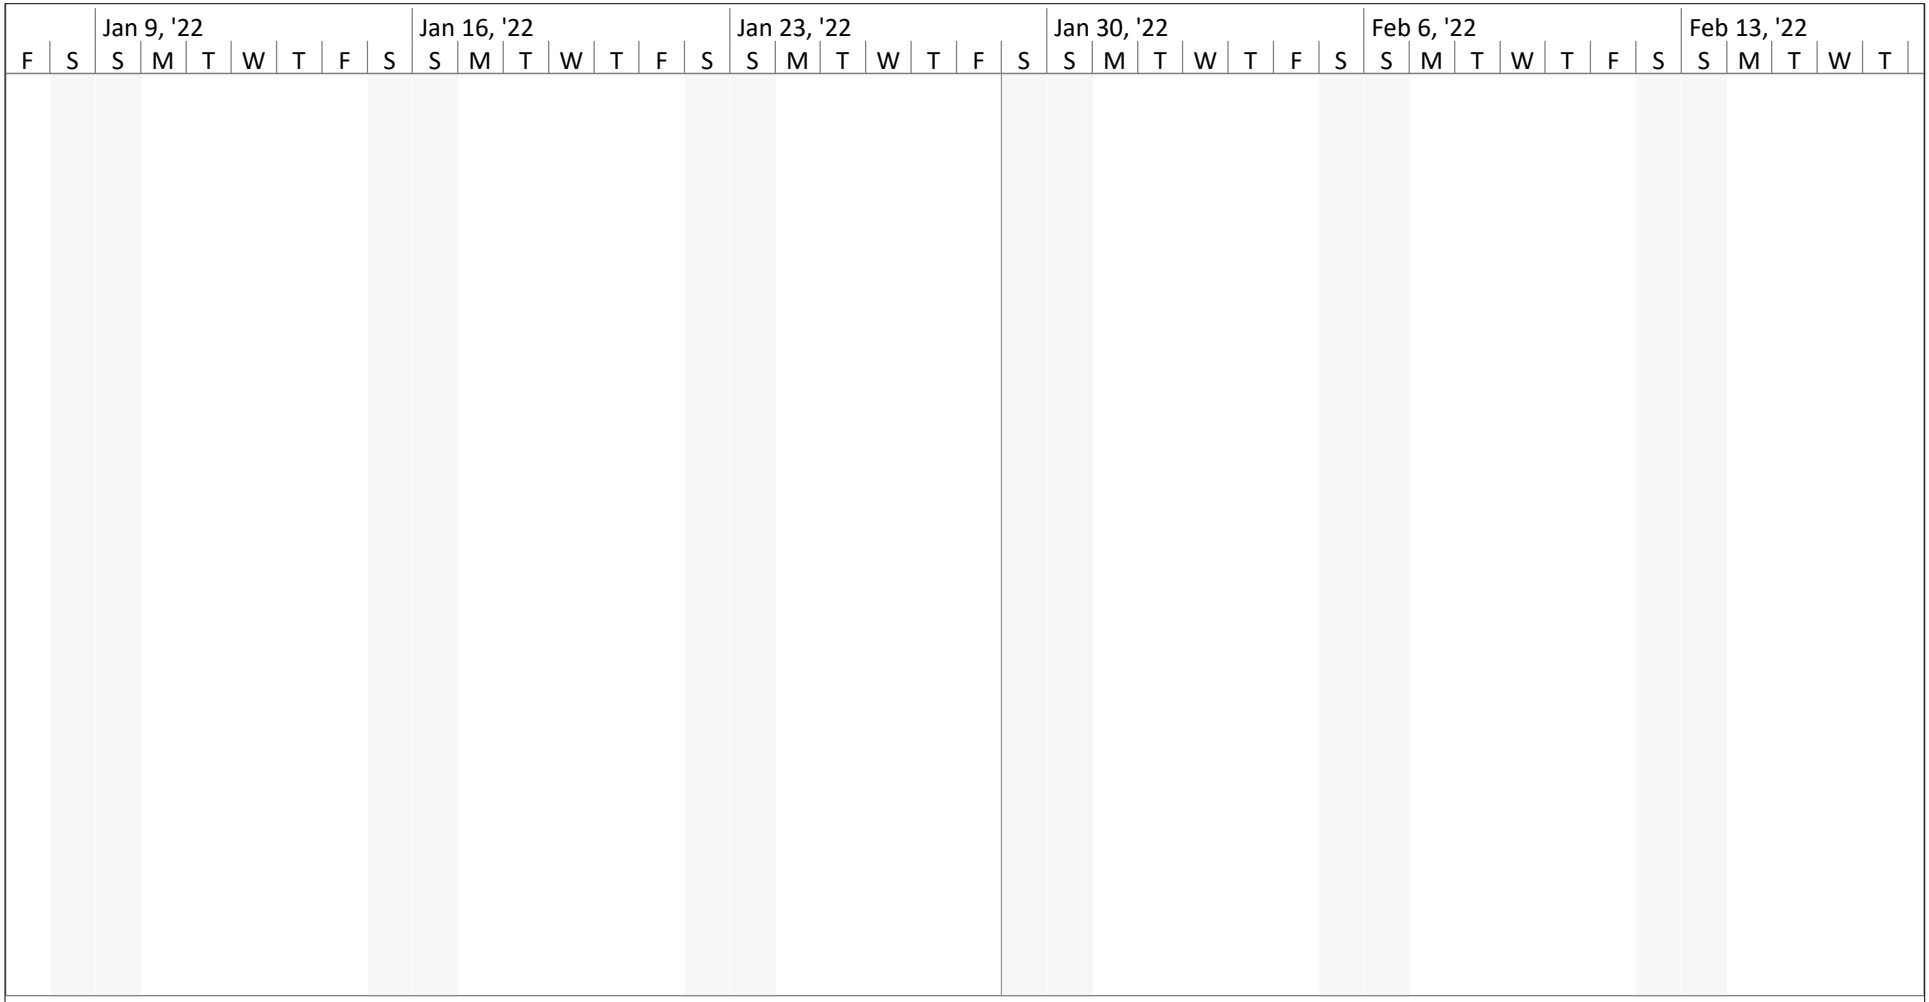


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

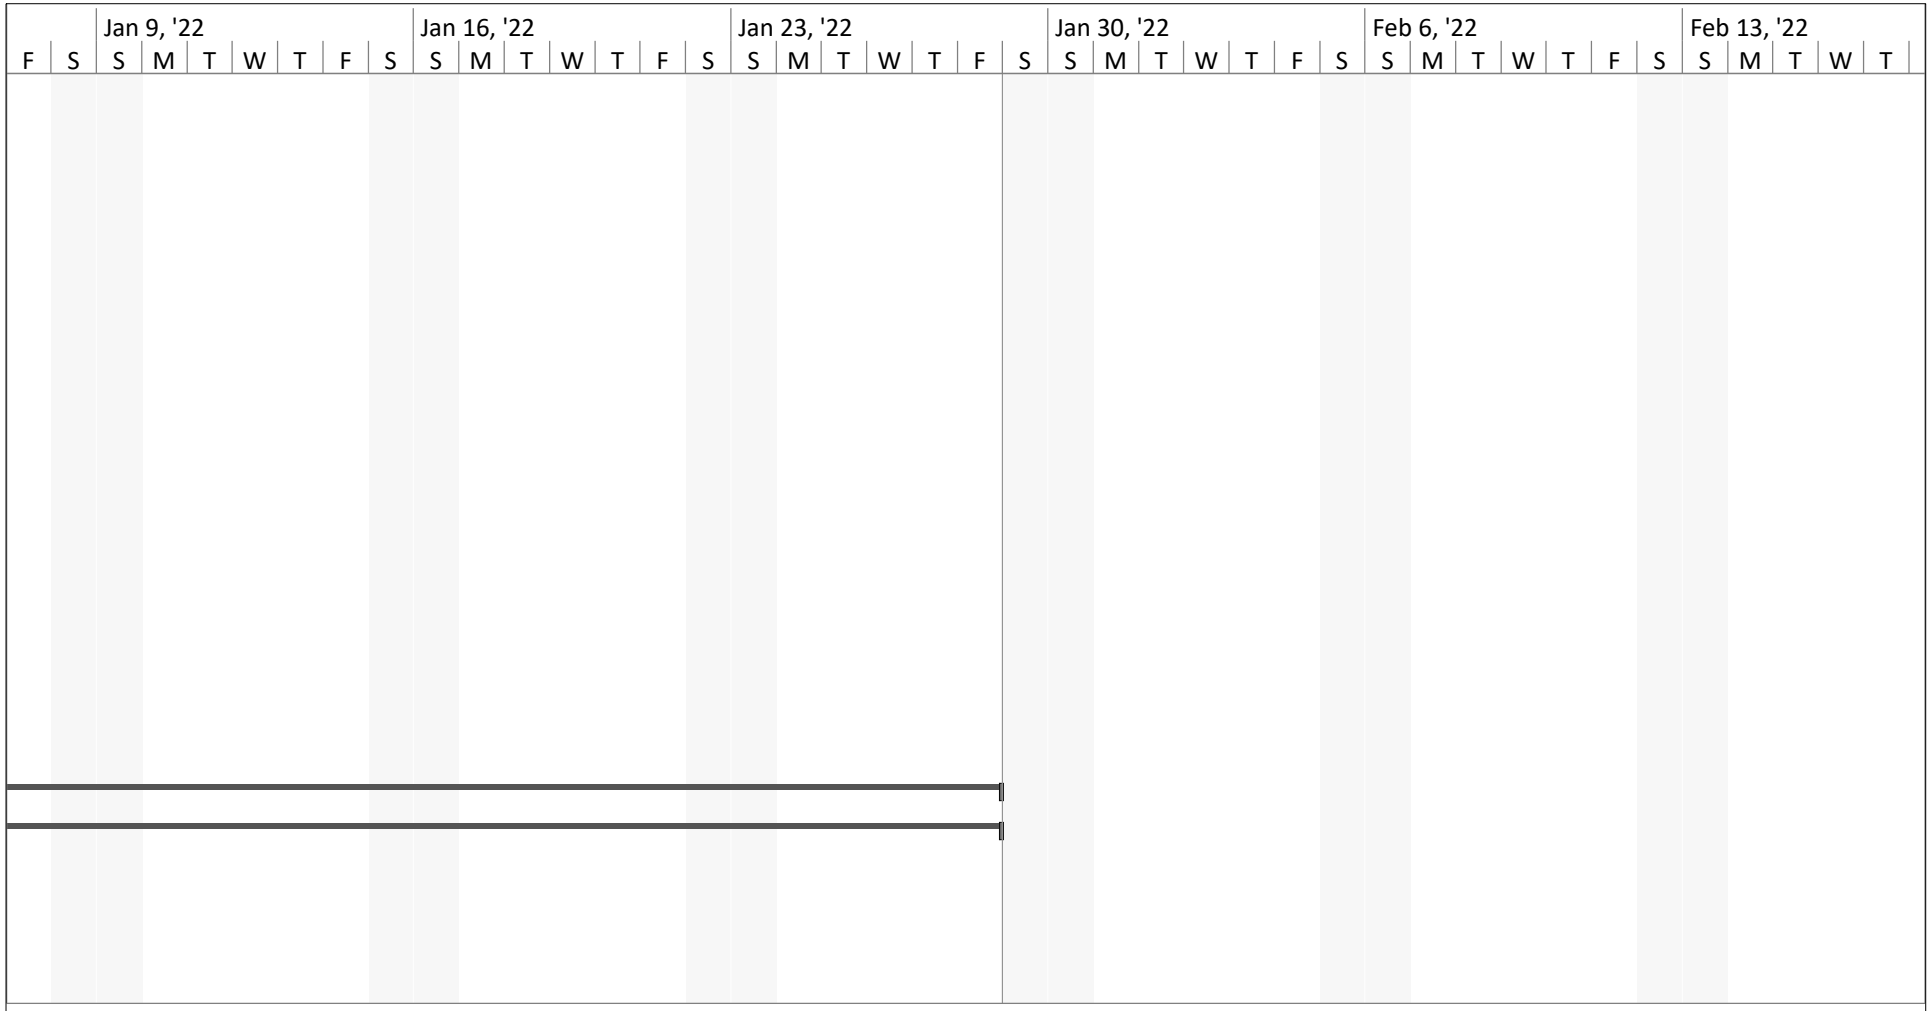


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |

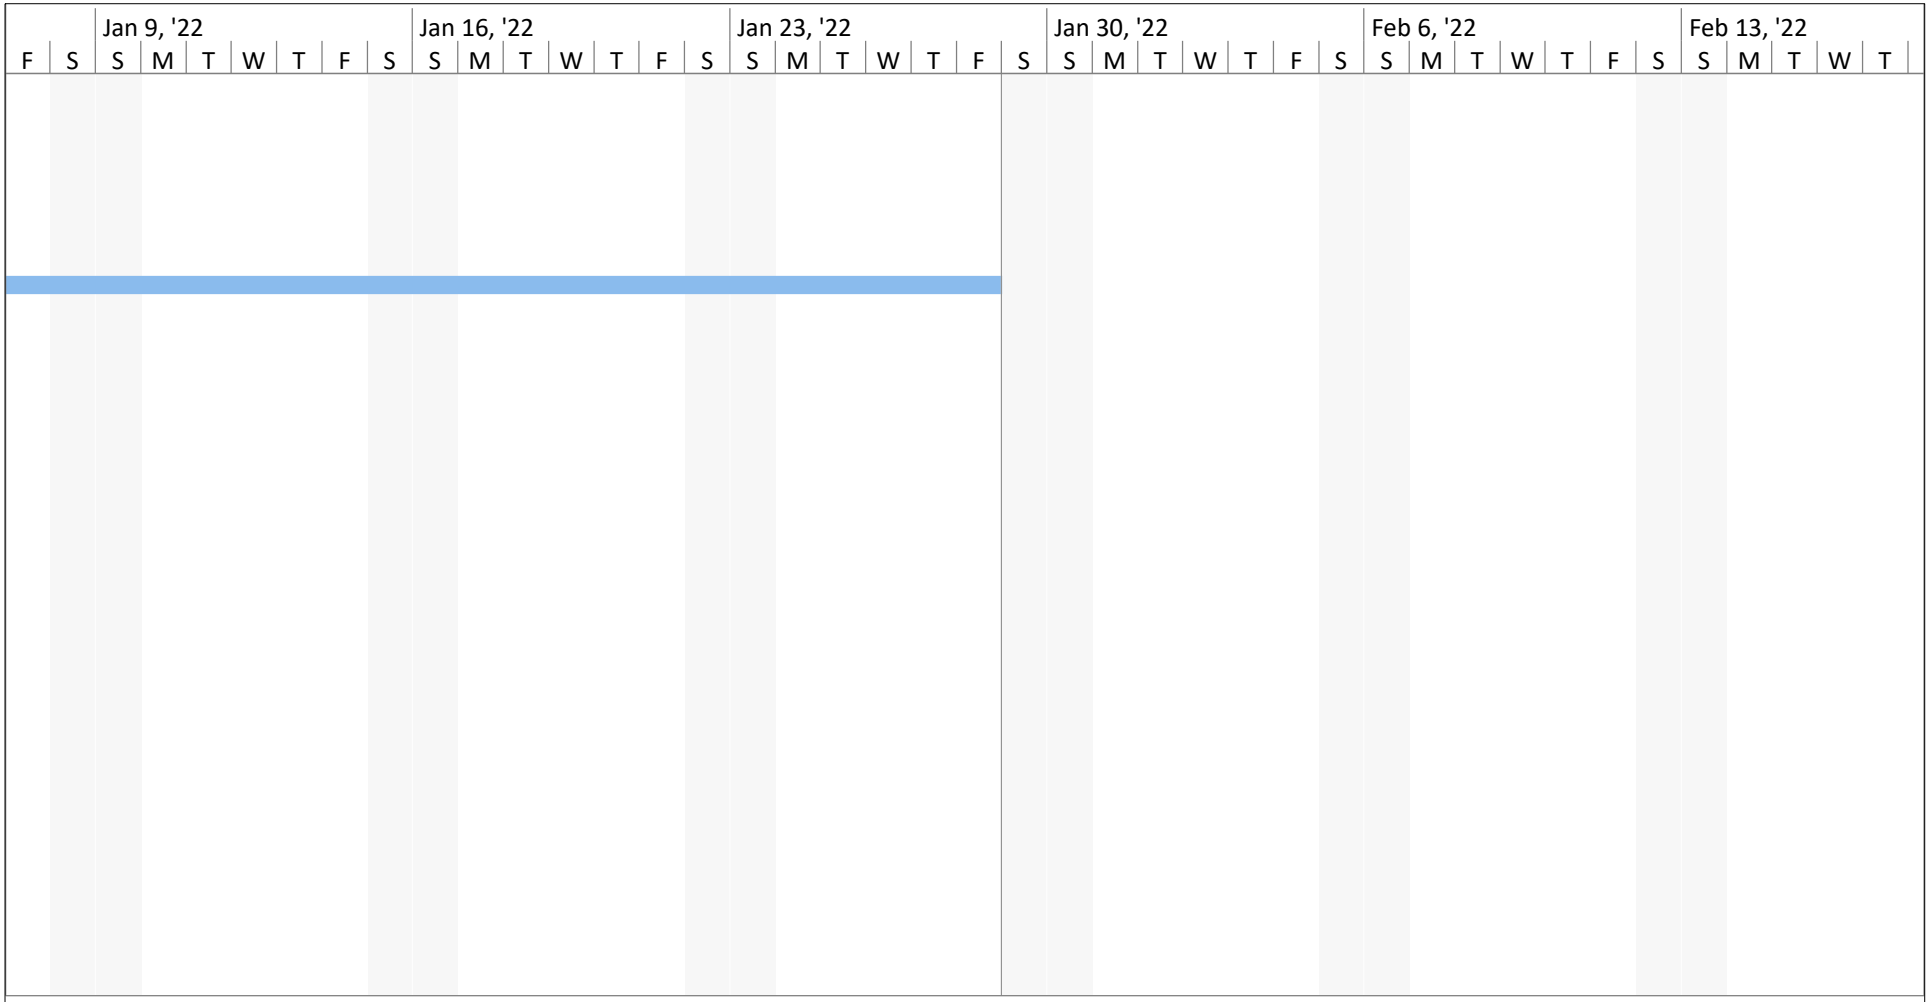


Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |




Project: Project WBS - Schedule
Date: Wed 2/24/21

| | | | | | |
|---|---|---|---|---|---|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Progress | |
| Project Summary | | Duration-only | | Manual Progress | |
| External Tasks | | Manual Summary Rollup | | | |
| External Milestone | | Manual Summary | | | |
